

Vegetation Clearing & Fauna Management Plan

*Economic Development
Queensland (EDQ)*

Vegetation clearing for Stage 1 development

CONTENTS

9216 E 02 VCFMP G -- Vegetation Clearing Notes
9216 E 03 VCFMP G -- Fauna Notes
9216 E 04 VCFMP H -- Detail Sheet Context
9216 E 05 - 17 VCFMP H -- Detail Sheets
9216 E 18 VCFMP H -- Clearing Direction
Appendix A -- Tree Schedule


**PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL**

Approval no: DEV2020/1099
Date: 25 AUGUST 2022



SHG Contact

Mr James Gautrey
Phone: (07) 3251 9458
Email: jamesgautrey@saundershavill.com

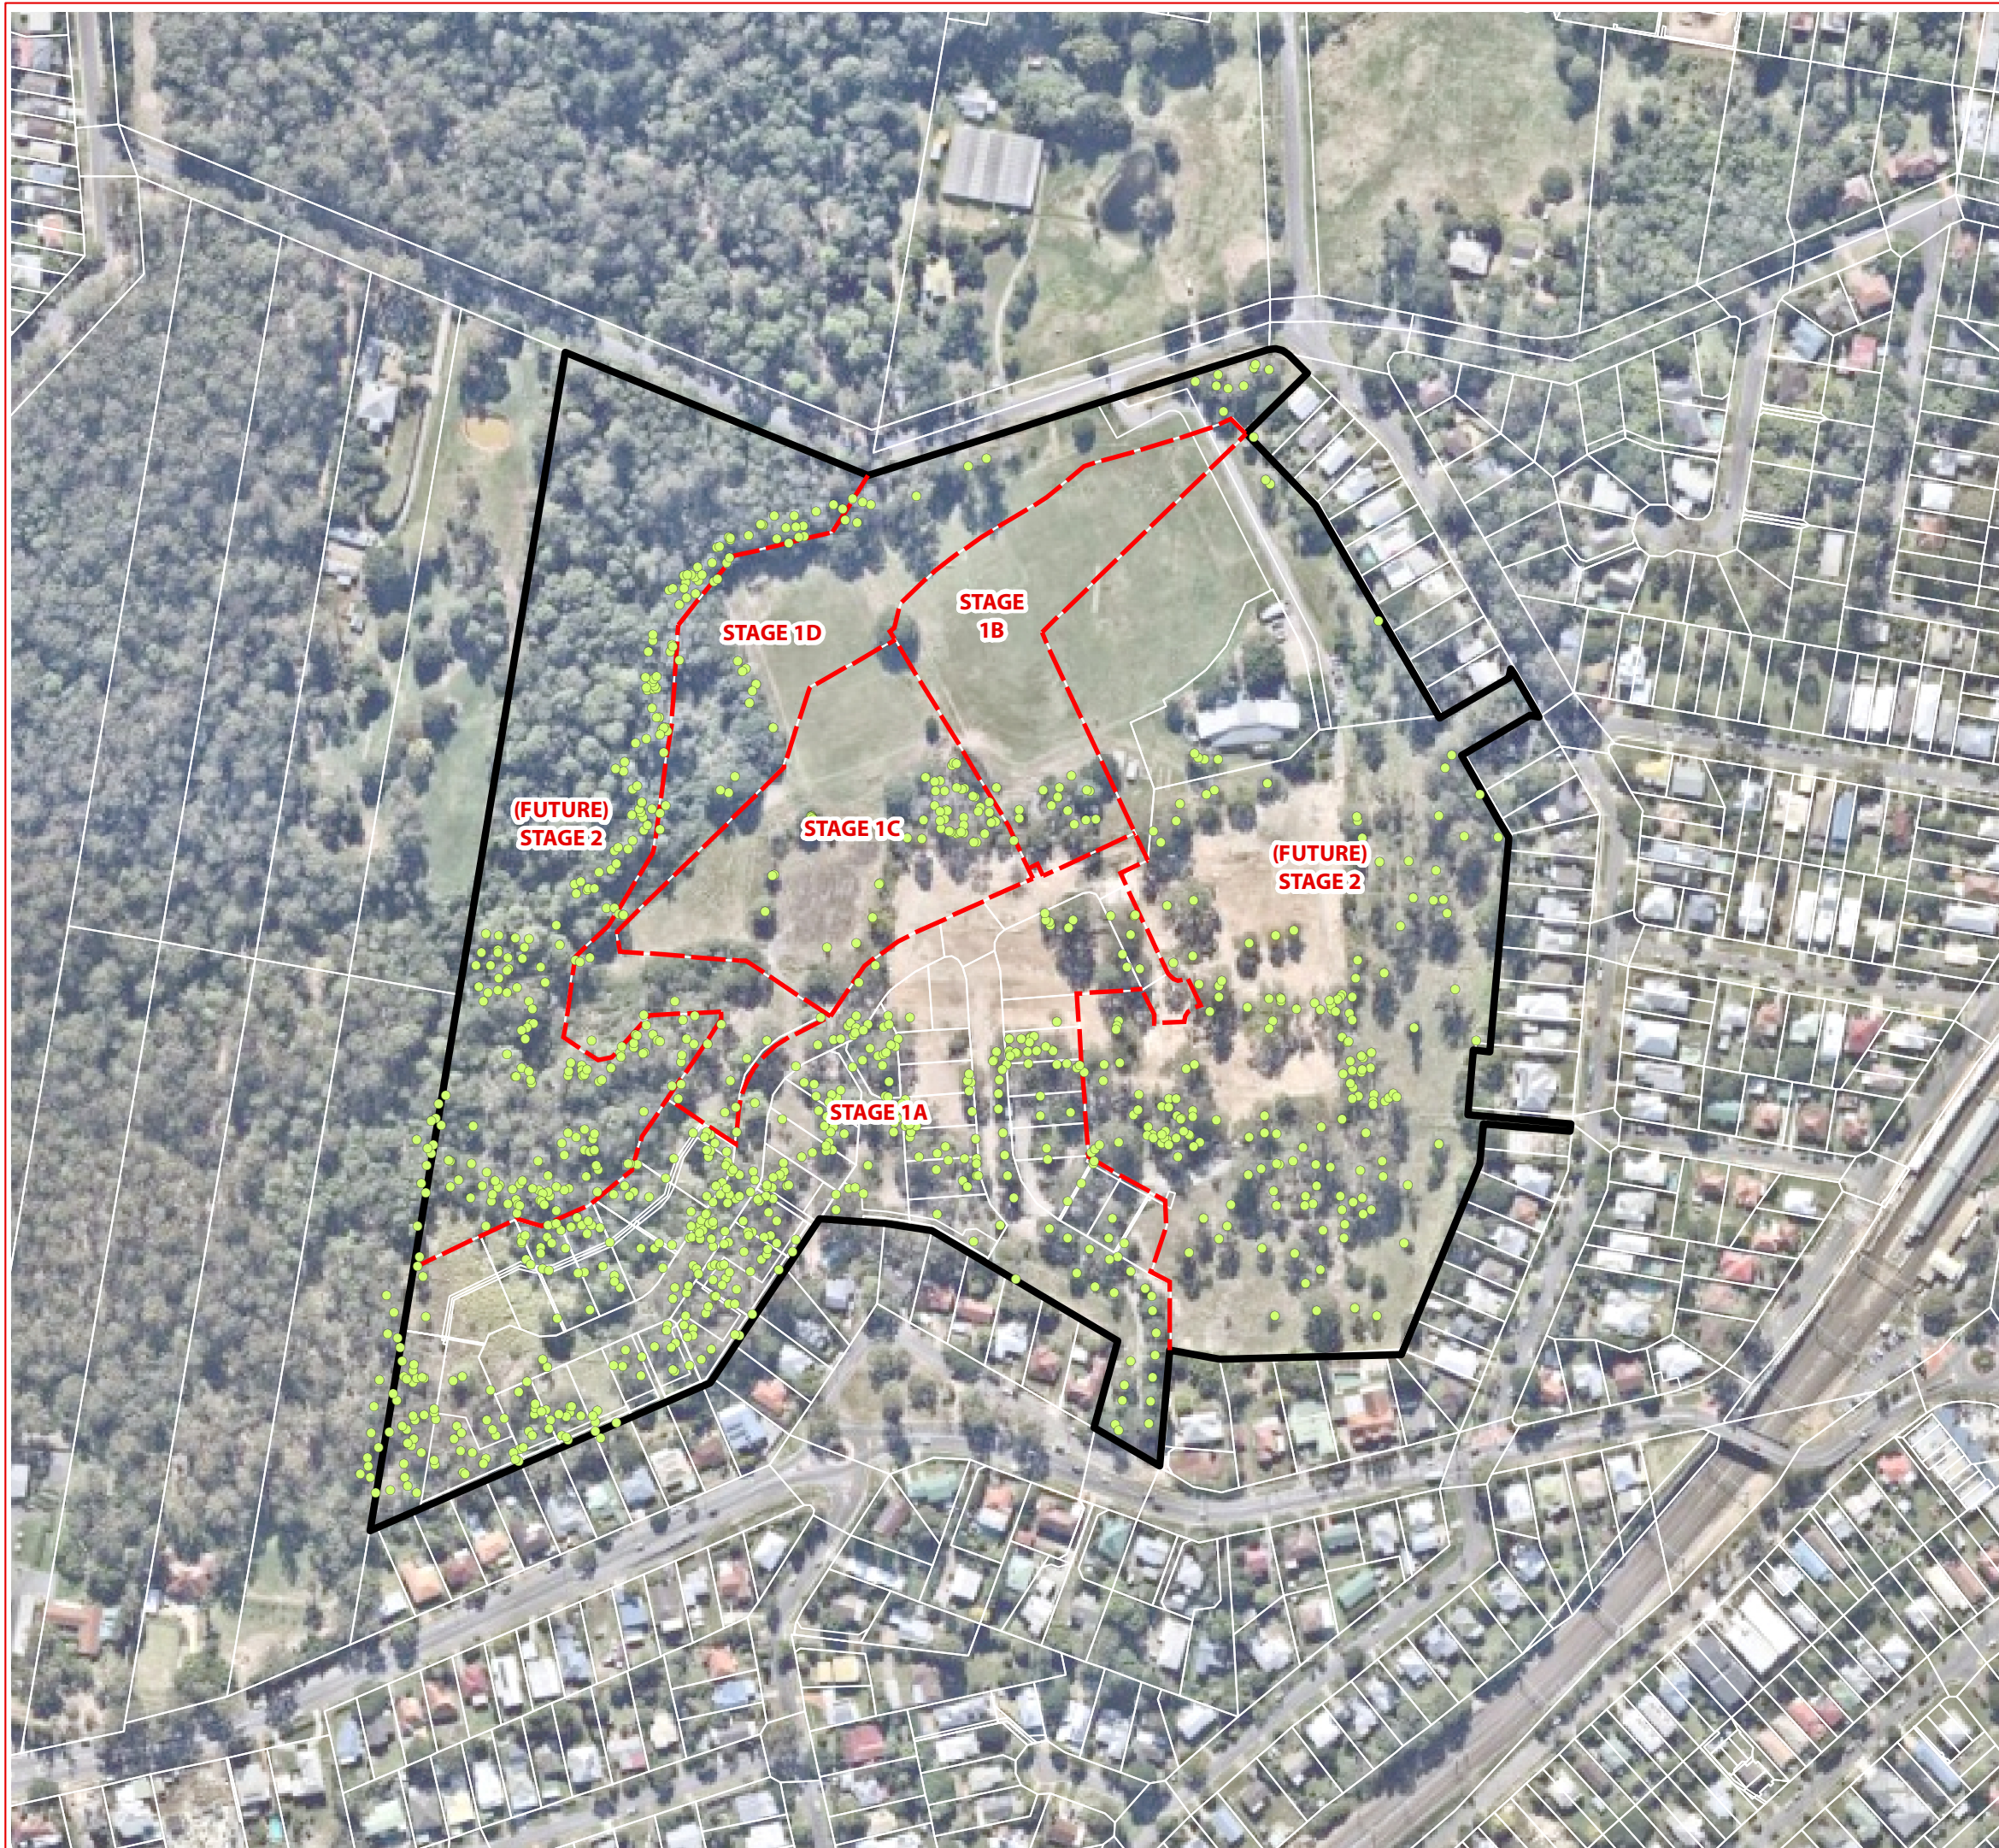

Vegetation Clearing and Fauna Management Plan - Notes

INTRODUCTION

The Environmental Management Division of the **Saunders Havill Group (SHG)** was engaged by **Economic Development Queensland (EDQ)** to prepare a Vegetation Clearing and Fauna Management Plan (VCFMP) for proposed Stage 1 development at 53 Seventeen Mile Rocks Road, Oxley (600/SP236626 & 551/SP142916).

The purpose of this plan is to manage the vegetation removal process and the protection of fauna species within proposed remediation areas. The clearing works will follow general principles for vegetation clearing documented on this sheet and *Sheet 3*.

This VCFMP has been produced by overlaying the following site datasets to determine impacts and disturbance on existing vegetation:

- 1. GPS accurate tree data including specimen details & features (SHG 2018-2020)
- 2. Survey accurate tree data (Land Partners 2018)
- 3. Site Remediation Layout Plans (Butler Partners 2020)
- 4. Staging layout Plan (Place Design Group 2020)

PROJECT MANAGEMENT

Vegetation management and its processes are an integral part of the construction and operational works phases. The site supervisor is responsible for all onsite works including overseeing vegetation clearing, health and safety of fauna and adhering to relevant conditions and guidelines and Australian Standards - Protection of Trees on Development Sites AS4970-2009 and Pruning of Amenity Trees AS4373-1996.

The project arborist (with minimum AQF Level 5 in Arboriculture and minimum 5 years’ experience) is responsible for: undertaking all appropriate arboricultural measures prior to the commencement of any earthworks on site to ensure the survival and long-term health of existing trees to be retained. These measures may include soil decompaction, soil aeration, fertilising, mulching, watering, root or crown reduction and hazard reduction or as otherwise determined by the arborist. The site arborist is also required to direct and supervise all works within TPZs of trees to be retained, and perform arboricultural care requirements where necessary.

SITE CONTACTS

Site and consulting contacts for queries relating to vegetation clearing include:

Client Contact: Economic Development Queensland Mr Kaush Singh Ph (07) 3452 7076	Environmental Contact: Saunders Havill Group Mr James Gautrey Ph (07) 3251 9458
Site Contractor: <i>To be advised</i>	Site Arborist: <i>To be advised</i>
Site Fauna spotter-catcher: <i>To be advised</i> (Refer to <i>Sheet 3</i> for responsibilities)	Site Bushfire Consultant: Land and Environment Consultants Mr Rob Janssen Ph 0466 714 833

CLEARING PHASES AND PROCESS

PHASE 1 - Tree Protection Fencing to be installed

Fencing to be installed prior to the commencement of any clearing works on the site. Tree protection fencing to be located at or beyond 12 x diameter at breast height (DBH) (AS4970-2009 Protection of trees on development sites)—unless approved by the appointed arborist.

PHASE 2 - Pre-start Meeting

Fencing shall be in place at the time of the official pre-start meeting for inspection and sign off by EDQ Officers.

PHASE 3 - Fauna Inspections and Management

Undertake necessary fauna management requirements prior to clearing works - as a minimum, this should include the specifications listed on sheet 3, and acknowledge specific EDQ approval requirements.

PHASE 4 - Undertake Bulk Clearing

Undertake wholesale removal of vegetation once approved for removal by a qualified fauna spotter.

Clearing will occur in the direction outlined in sheet 18 of this VCFMP, and managed by the appointed fauna spotter-catcher to allow all fauna unimpeded movement towards the proposed Public Open Space Area along western portion of site.

Vegetation clearing techniques:

- i. By utilising the most appropriate machinery and equipment during vegetation clearing, the probability of injury or death of wildlife during clearing can be significantly reduced or eliminated while still maintaining an efficient vegetation removal process.
- ii. Suggested techniques are as follows: (a) a vertical tree grab attachment on an excavator (30 tonne) can be used to pull entire trees in size up to 30-40cm diameter at a height measured at 1.3 metres above ground level and lay them down in a steady controlled fashion, allowing inspection by a fauna spotter-catcher (b) where large trees are too large for a vertical tree grab and have been identified, an elevated work platform or where practical, cherry picker should be used in conjunction with a chainsaw operator and fauna spotter-catcher. Alternatively, careful removal of hollow section from habitat tree and gentle lowering for inspection by fauna spotter-catcher (c) the use of bulldozers to clear vegetation is limited to vegetation that has been thoroughly inspected by a fauna spotter-catcher and is found to contain no fauna or potential habitat. Bulldozers are not to be used to push over large trees that contain hollows or other habitat features.

NOTE: Dogs are not permitted onsite at all times during construction. Construction works including clearing must occur between the hours of 6.30am and 6.30pm.

ACCESS AND STOCKPILING

A vegetation stockpiling location is to be designated in an easily accessible area outside of TPZs. Indicative vegetation stockpiling locations have been allocated at previously cleared locations near remediation areas, allowing for material to be easily delivered and stored. This location is subject to minor change according to cut/fill activities and intended location for reuse.

Cleared vegetation free of weeds is to be reused on or off the project site. Recycling techniques include mulching, tub-grinding, wood chipping and salvage (e.g. custom milling). Trees with identified hollows should have the hollow section preserved and should be suitably mounted on nearby or adjacent suitable trees.


MAINTENANCE

After tree clearing works on site, an analysis of the vegetation's health and growth should be undertaken by the project arborist to determine specific maintenance needs. Follow up maintenance works should be carried out on retained vegetation where required. If conditioned in the DA approval—the project arborist may be required to submit a report to EDQ detailing the measures undertaken during the construction period and any further work required post this period.


DYSCHORISTE DEPRESSA WEED CONTROL

24hrs prior to vegetation clearing commencing, *Dyschoriste depressa* is to be identified on-site by a suitably qualified professional and is to be treated via foliar spray. After vegetation clearing has been completed and prior to construction works commencing, an additional survey identifying *Dyschoriste depressa* is to be undertaken. If any additional locations of *Dyschoriste depressa* are identified, they are to be treated accordingly. Prior to plan sealing, certification of *Dyschoriste depressa* eradication within the development footprint is to be provided to EDQ.

Tree Protection Zone - Detail (not to scale)

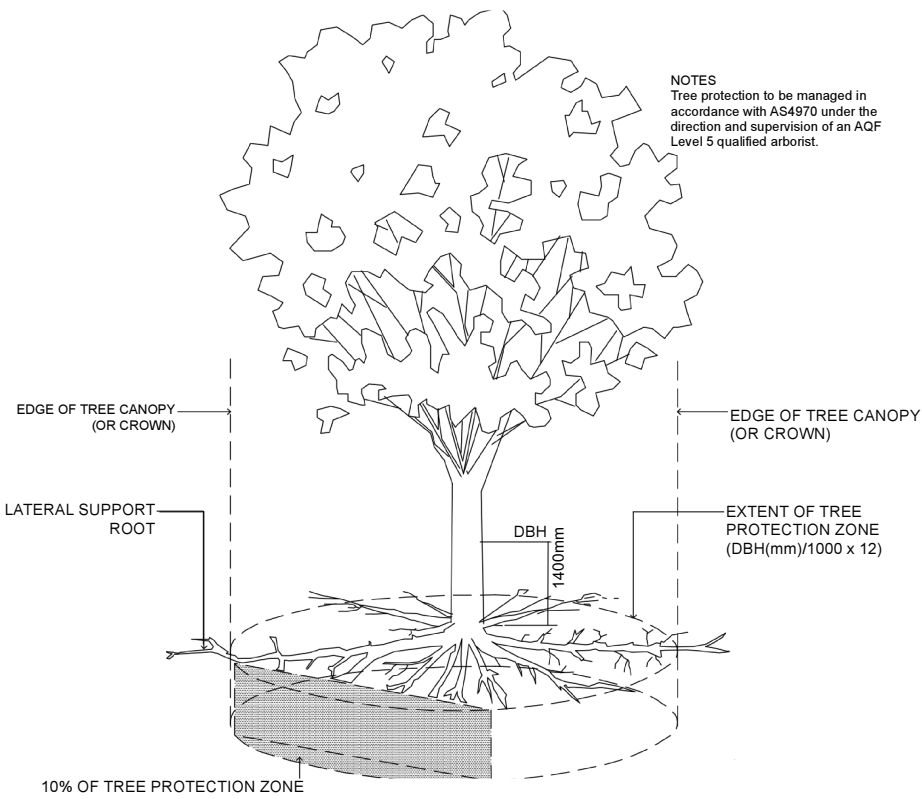

AS 4970 Tree Protection Fencing - Detail (not to scale)

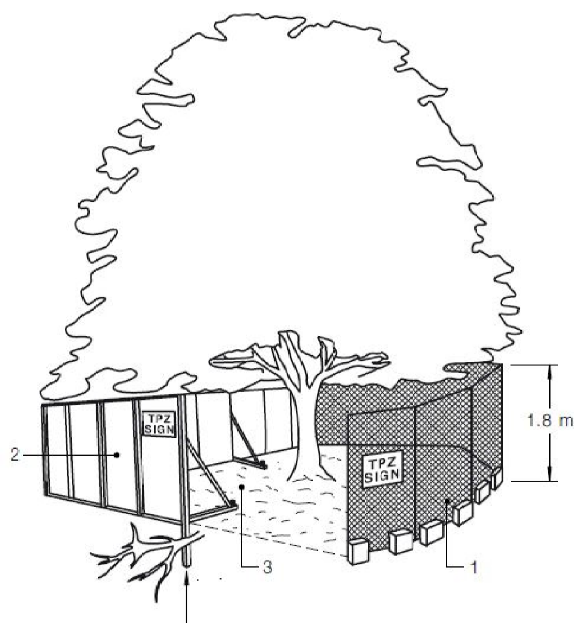

- LEGEND
- 1. Chain wire mesh panels with shade cloth (if required) attached, held in place with concrete feet.
 - 2. Alternative plywood or wooden paling fence. This fencing option also prevents building materials or soil entering the TPZ.
 - 3. Mulch installation across surface of TPZ (at the discretion of the Project Arborist). No Excavation, construction activity, grade changes, surface treatment or storage of materials of any kind is permitted with the TPZ.
 - 4. Bracing is permissible within the TPZ. Installation of supports should avoid damaging roots.

Vegetation Clearing and Fauna Management Plan - Fauna Management Notes

INTRODUCTION

The Fauna Management specification on this *VCFMP* is designed to protect native animals and control/manage impacts during the vegetation clearing works. The clearing area is located within Stage 1 of the development footprint. Thirty-eight fauna species were recorded during diurnal and nocturnal fauna surveys, comprising amphibian, bird, reptile and mammal species. The Vulnerable *Pteropus poliocephalus* (Grey-headed Flying-fox) were observed foraging onsite however no evidence of Koala or Powerful Owl was observed despite habitat mapping over the site / historic records in the vicinity of the site (refer to Ecological Assessment Report prepared by SHG 2020). The fauna management specifications and principles incorporated in this *VCFMP* applies generically to all native animals and focuses on avoiding conflicts and incorporating measures to minimize disturbance. Compliance with this section of the *VCFMP* is compulsory and incorporates the use of expert consultants including a Fauna Spotter (holding a valid Wildlife Rehabilitation Permit issued by the **Department of Environment and Science**).

FAUNA IMPACTS

Clearing of vegetation provides an obvious source of impact to existing habitat and animal safety. More specifically the existing vegetation provides habitat, movement and protection opportunities for some fauna through both regrowth and canopy trees. These opportunities are to be altered during and post vegetation clearing works.

CONSTRUCTION IMPACTS

- Direct removal of site vegetation
- Loss of habitat
- Noise, vibration and dust
- Erosion and sedimentation
- Threats associated with open cuts etc. and fauna entrapment
- Loss of food sources
- Excavation/compaction/changes in ground levels
- Altering hydrological flows
- Fragmentation of habitat

OPERATIONAL IMPACTS

- Weed introduction (garden escapees)
- Increased hydrology with increased hardstand
- Altering of run-off chemical and nutrient components (quality)
- Barriers to fauna movement
- Vehicles and pedestrian movement and trespass
- Introduction of domestic and predatory species

Fauna Management Schedule

1.0 PRE CLEARING				
Ref:	Management Item	Responsibility	Timing	Reporting
1.1	TEMPORARY FENCING Prior to the commencement of works and to be inspected by the site Environmental Coordinator—Delineate areas where vegetation is proposed to be retained with exclusion fencing to prevent accidental felling. Clearing is to be undertaken in accordance with AS 4970-2009 Protection of Trees on Development Sites. ▪ Fencing shall be fauna friendly ▪ No clearing, stockpiling, site access, earthworks, storage, etc. is to occur within the temporary protection fencing. ▪ Only approved weed management works to occur within the temporary protection fencing ▪ Fencing to be reinstated immediately if damaged or knocked down, any damage to retained trees to be immediately reported to Project Arborist. ▪ Fencing to remain until the completion of all site works.	SITE SUPERVISOR	Prior to the commencement of clearing	Inspected by EDQ or the Environmental Site Coordinator
1.2	CONTRACTOR EDUCATION & AWARENESS All site contractors and subcontractors will be made aware of their responsibilities to protect native fauna. The Fauna Management notes on this VCFMP is provided as a working document to assist on-site management and protection of native animals. This generally will form part of education and training on a broader work place health and safety but as a minimum will include: ▪ Copy of VCFMP kept on-site (Site Office). ▪ General education and awareness notification of contractors and sub-contractors involved in activities potentially impacting native animals as part of site induction – contractors must know the location of the VCFMP, key phone numbers and who to report to if they breach the VCFMP. A list of relevant contact phone numbers as listed on these drawings is kept in a visible and accessible location in the site office.	SITE SUPERVISOR / THE PROPONENT	Prior to the commencement of clearing and as part of the site induction for new staff and sub-contractors	SITE SUPERVISOR
2.0 VEGETATION CLEARING				
2.1	SPOTTER / RELOCATOR Immediately prior to the commencement of clearing of native vegetation a daily visual inspection of the area must be carried out by the fauna spotter-catcher. Furthermore, the fauna spotter-catcher is to be present on site during all clearing operations to supervise and direct clearing works, and to respond to any situations that may arise in relation to fauna. In the event of an animal being located, a suitable buffer area (as determined by the fauna spotter-catcher) should be established around the animal's location that excludes machinery until it has relocated at its own accord (usually overnight). If an animal requires relocating this must be undertaken by a suitable qualified fauna expert recognized by the Department of Environment & Science . For some fauna, specific permit requirements may apply. If vegetation is left stockpiled overnight, the fauna spotter-catcher must inspect the vegetation prior to chipping or removal from site. Any native fauna orphaned or injured by the development process must be reported to the Department of Environment & Science (1300 130 372) or RSPCA (1300 264 625). The Site Supervisor is responsible for the safe management of site fauna and implementation of these specific fauna requirements.	SITE SUPERVISOR	Prior to the commencement, and during clearing	Inspected by EDQ or the Environmental Site Coordinator
2.2	SPECIFIC KOALA MANAGEMENT NOTES A Koala Spotter is a person who holds a tertiary qualification in Biology or Zoology, or who is demonstrably experienced in the identification and location of Koalas in their natural habitat. For example, a koala keeper employed by a licensed Wildlife exhibitor (i.e. a zoo) may be capable of demonstrating competence in locating Koala's. Prior to the commencement and during felling operations, it is the responsibility of the Koala spotter to be present at the site of felling operations identify any tree at the site within which a Koala is present, as well as any tree that has a crown which is intermeshed or overlapping with such a tree; and advise the person who is authorised to conduct the felling operation, or that persons' representative, of the precise location of each such tree Management Item.	SITE SUPERVISOR	Prior to the commencement, and during clearing	Inspected by EDQ or the Environmental Site Coordinator
2.3	CLEARING PATTERN / FAUNA FLUSHING Clearing occurs once the fauna spotter-catcher gives sign off the site is clear of significant native species. The intended clearing directions is towards the proposed Public Open Space Area along western portion of site. Clearing direction is subject to amendment by the fauna spotter-catcher. At the completion of operational works, and prior to the sealing of survey plans for the relevant stage, the fauna spotter-catcher must provide certification to EDQ officers that all works were undertaken in accordance with these fauna management requirements and specific EDQ requirements.	SITE SUPERVISOR	Prior to the commencement, and during clearing	Inspected by EDQ or the Environmental Site Coordinator



ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND OR TOLD LOCATIONS OF ALL SERVICES.

REFERENCES:

AS4970-2009 Protection of trees on development sites

Ecological Assessment Report (SHG 2020)

AMENDMENTS:

Issue	Date	Description	Checked
B	30/03/2020	Update 1	JG
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	20/08/2020	Update 6	JG

PROJECT:

STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)



PLAN OF:
Vegetation Clearing & Fauna
Management Plan


DATE: 20/08/2020

CHECKED: JG

CLIENT REF: 9216

DRAWN: MC

DRAWING No.: 9216 E 03 VCFMP G

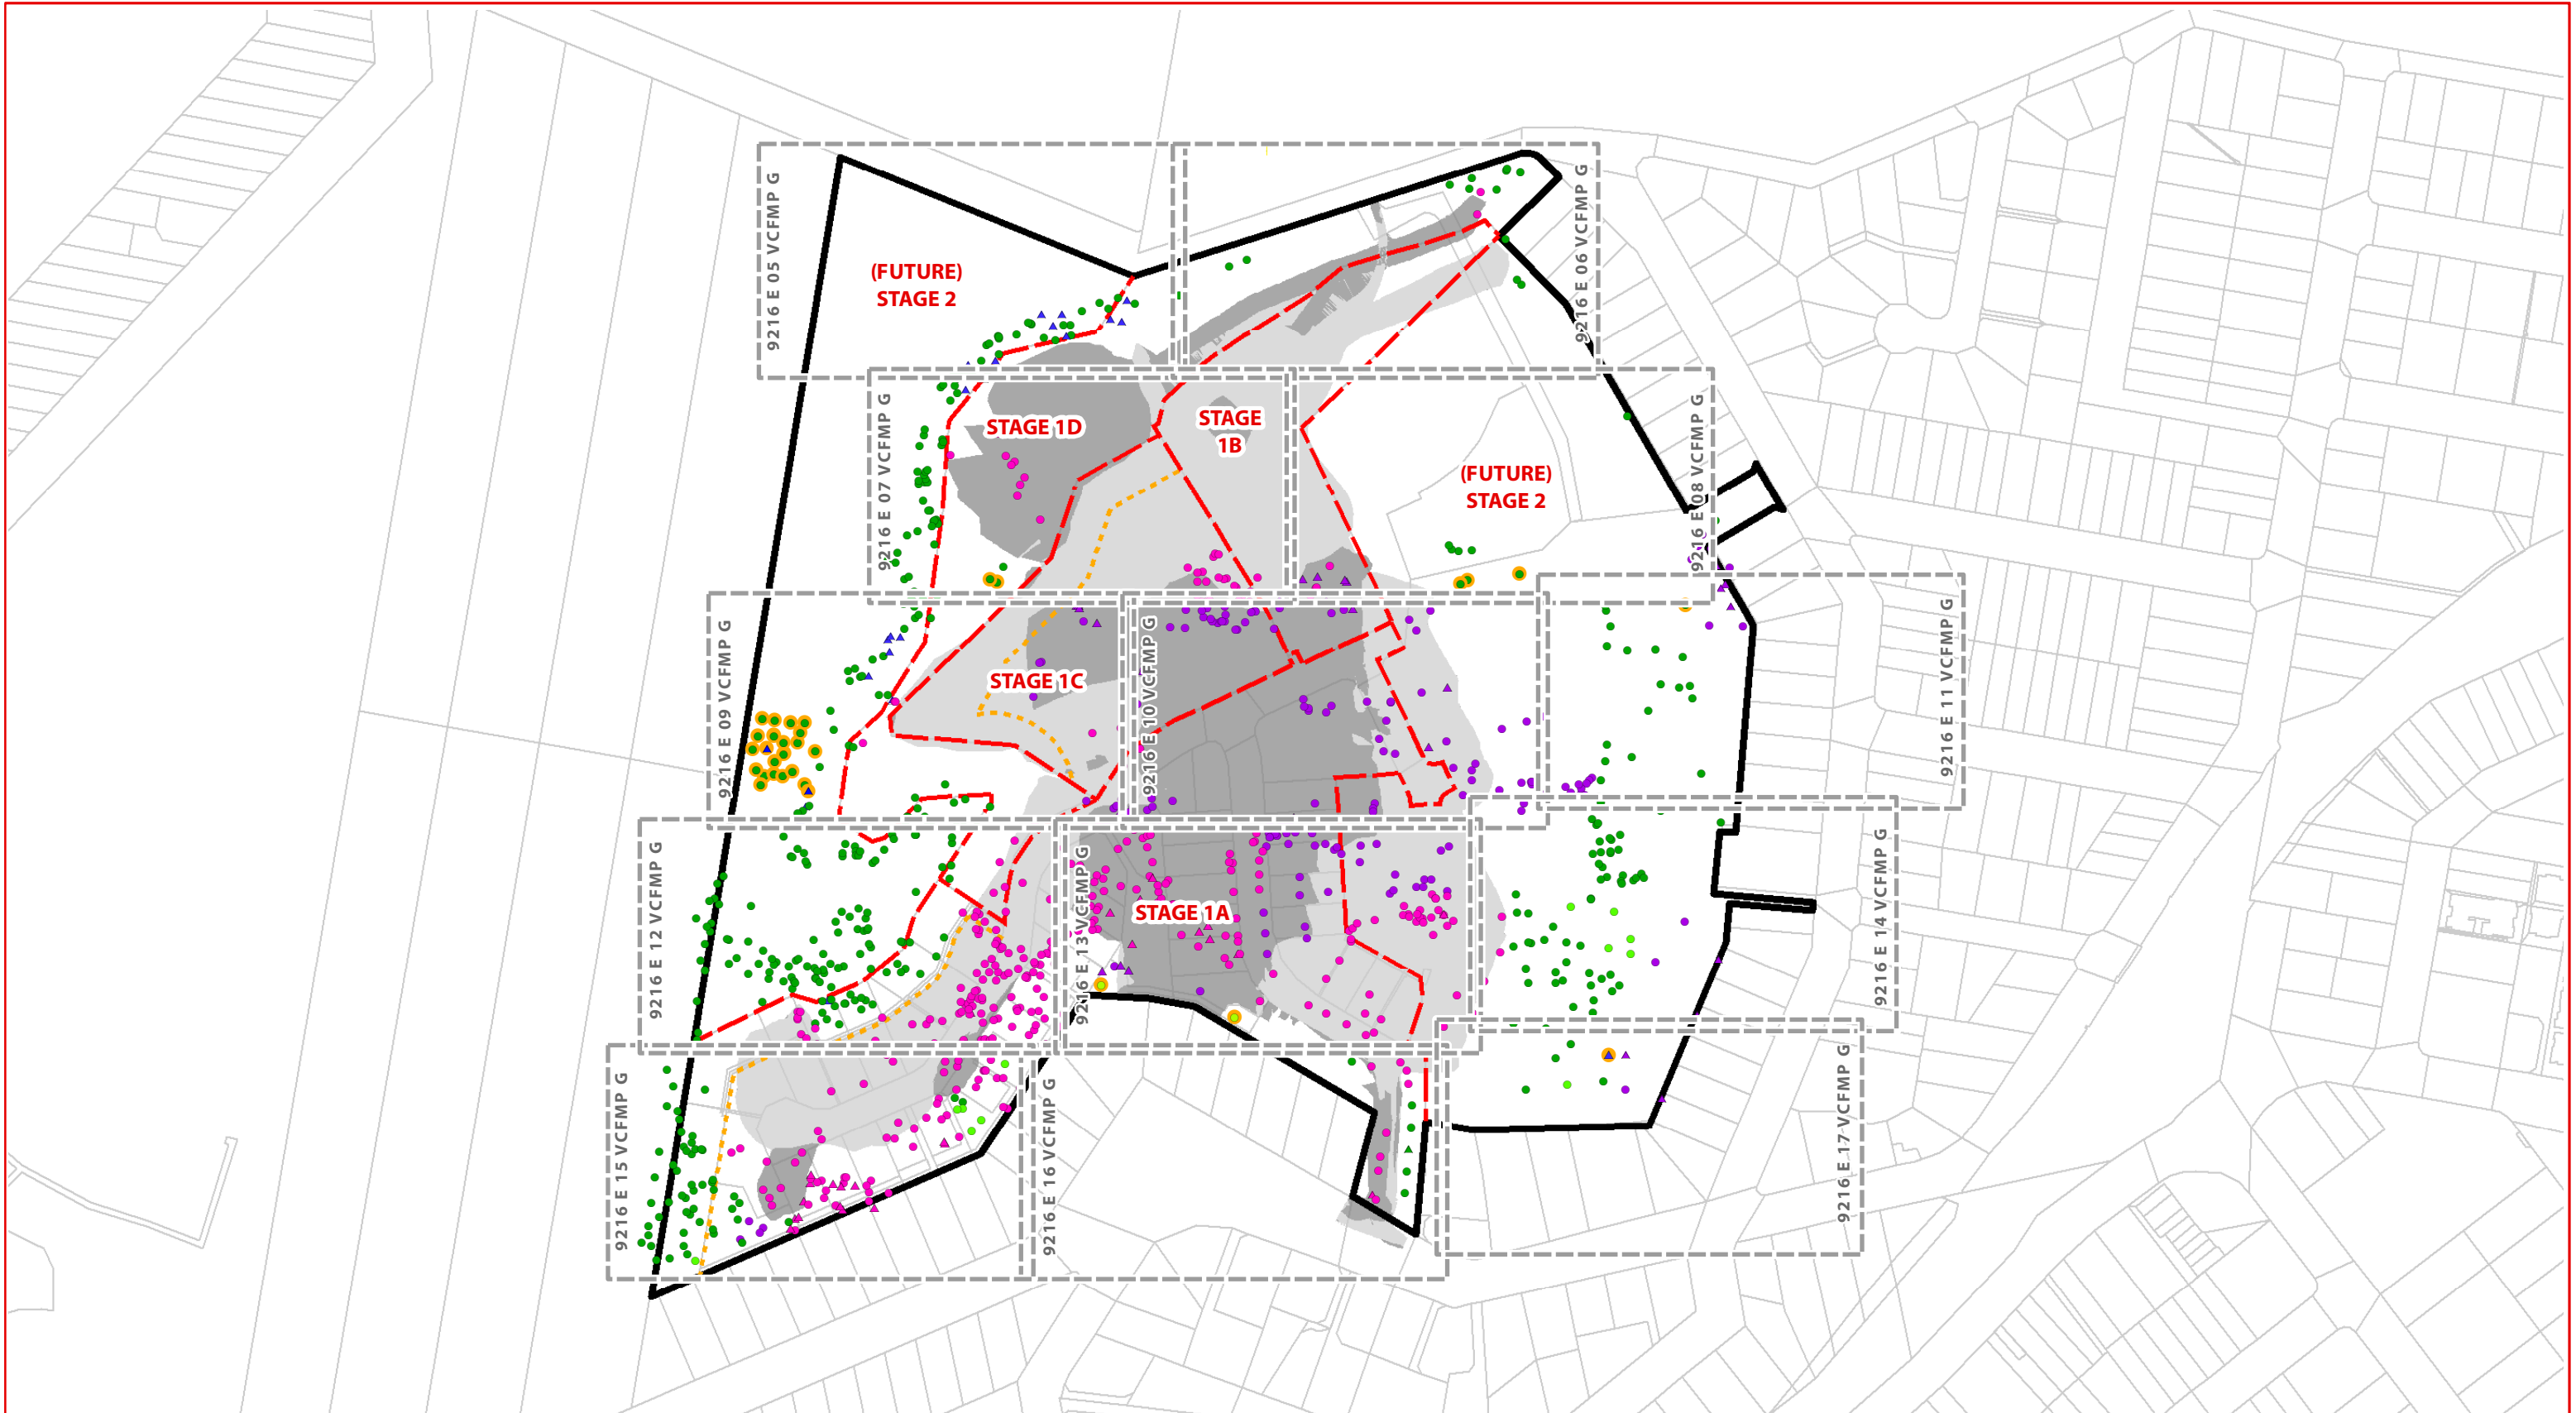

- Native tree to remove during tree clearing for remediation works
- Weed tree to remove during tree clearing for remediation works
- Native tree to remove during tree clearing for Stage 1
- Weed tree to remove during tree clearing for Stage 1
- Native tree to retain during tree clearing for Stage 1
- Exotic tree to retain during tree clearing for Stage 1
- Significant tree to be retained during tree clearing for Stage 1
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan
- Retention during clearing for remediations works subject to works extent / requirements
- Dead tree / stag
- Project Site
- Stage Boundary
- Indicative Bushfire Setback
- Extent of cut
- Extent of fill

Vegetation Clearing & Fauna Management Plan - Detail sheet context



CLIENT:
ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)

0 10 20 40 60 80 100 m


AMENDMENTS:			
Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management

PLAN OF:
Vegetation Clearing & Fauna Management Plan

DATE: 26/07/2022	CHECKED: JG
CLIENT REF: 9216	DRAWN: MP
DRAWING No.: 9216 E 04 VCFMP H	

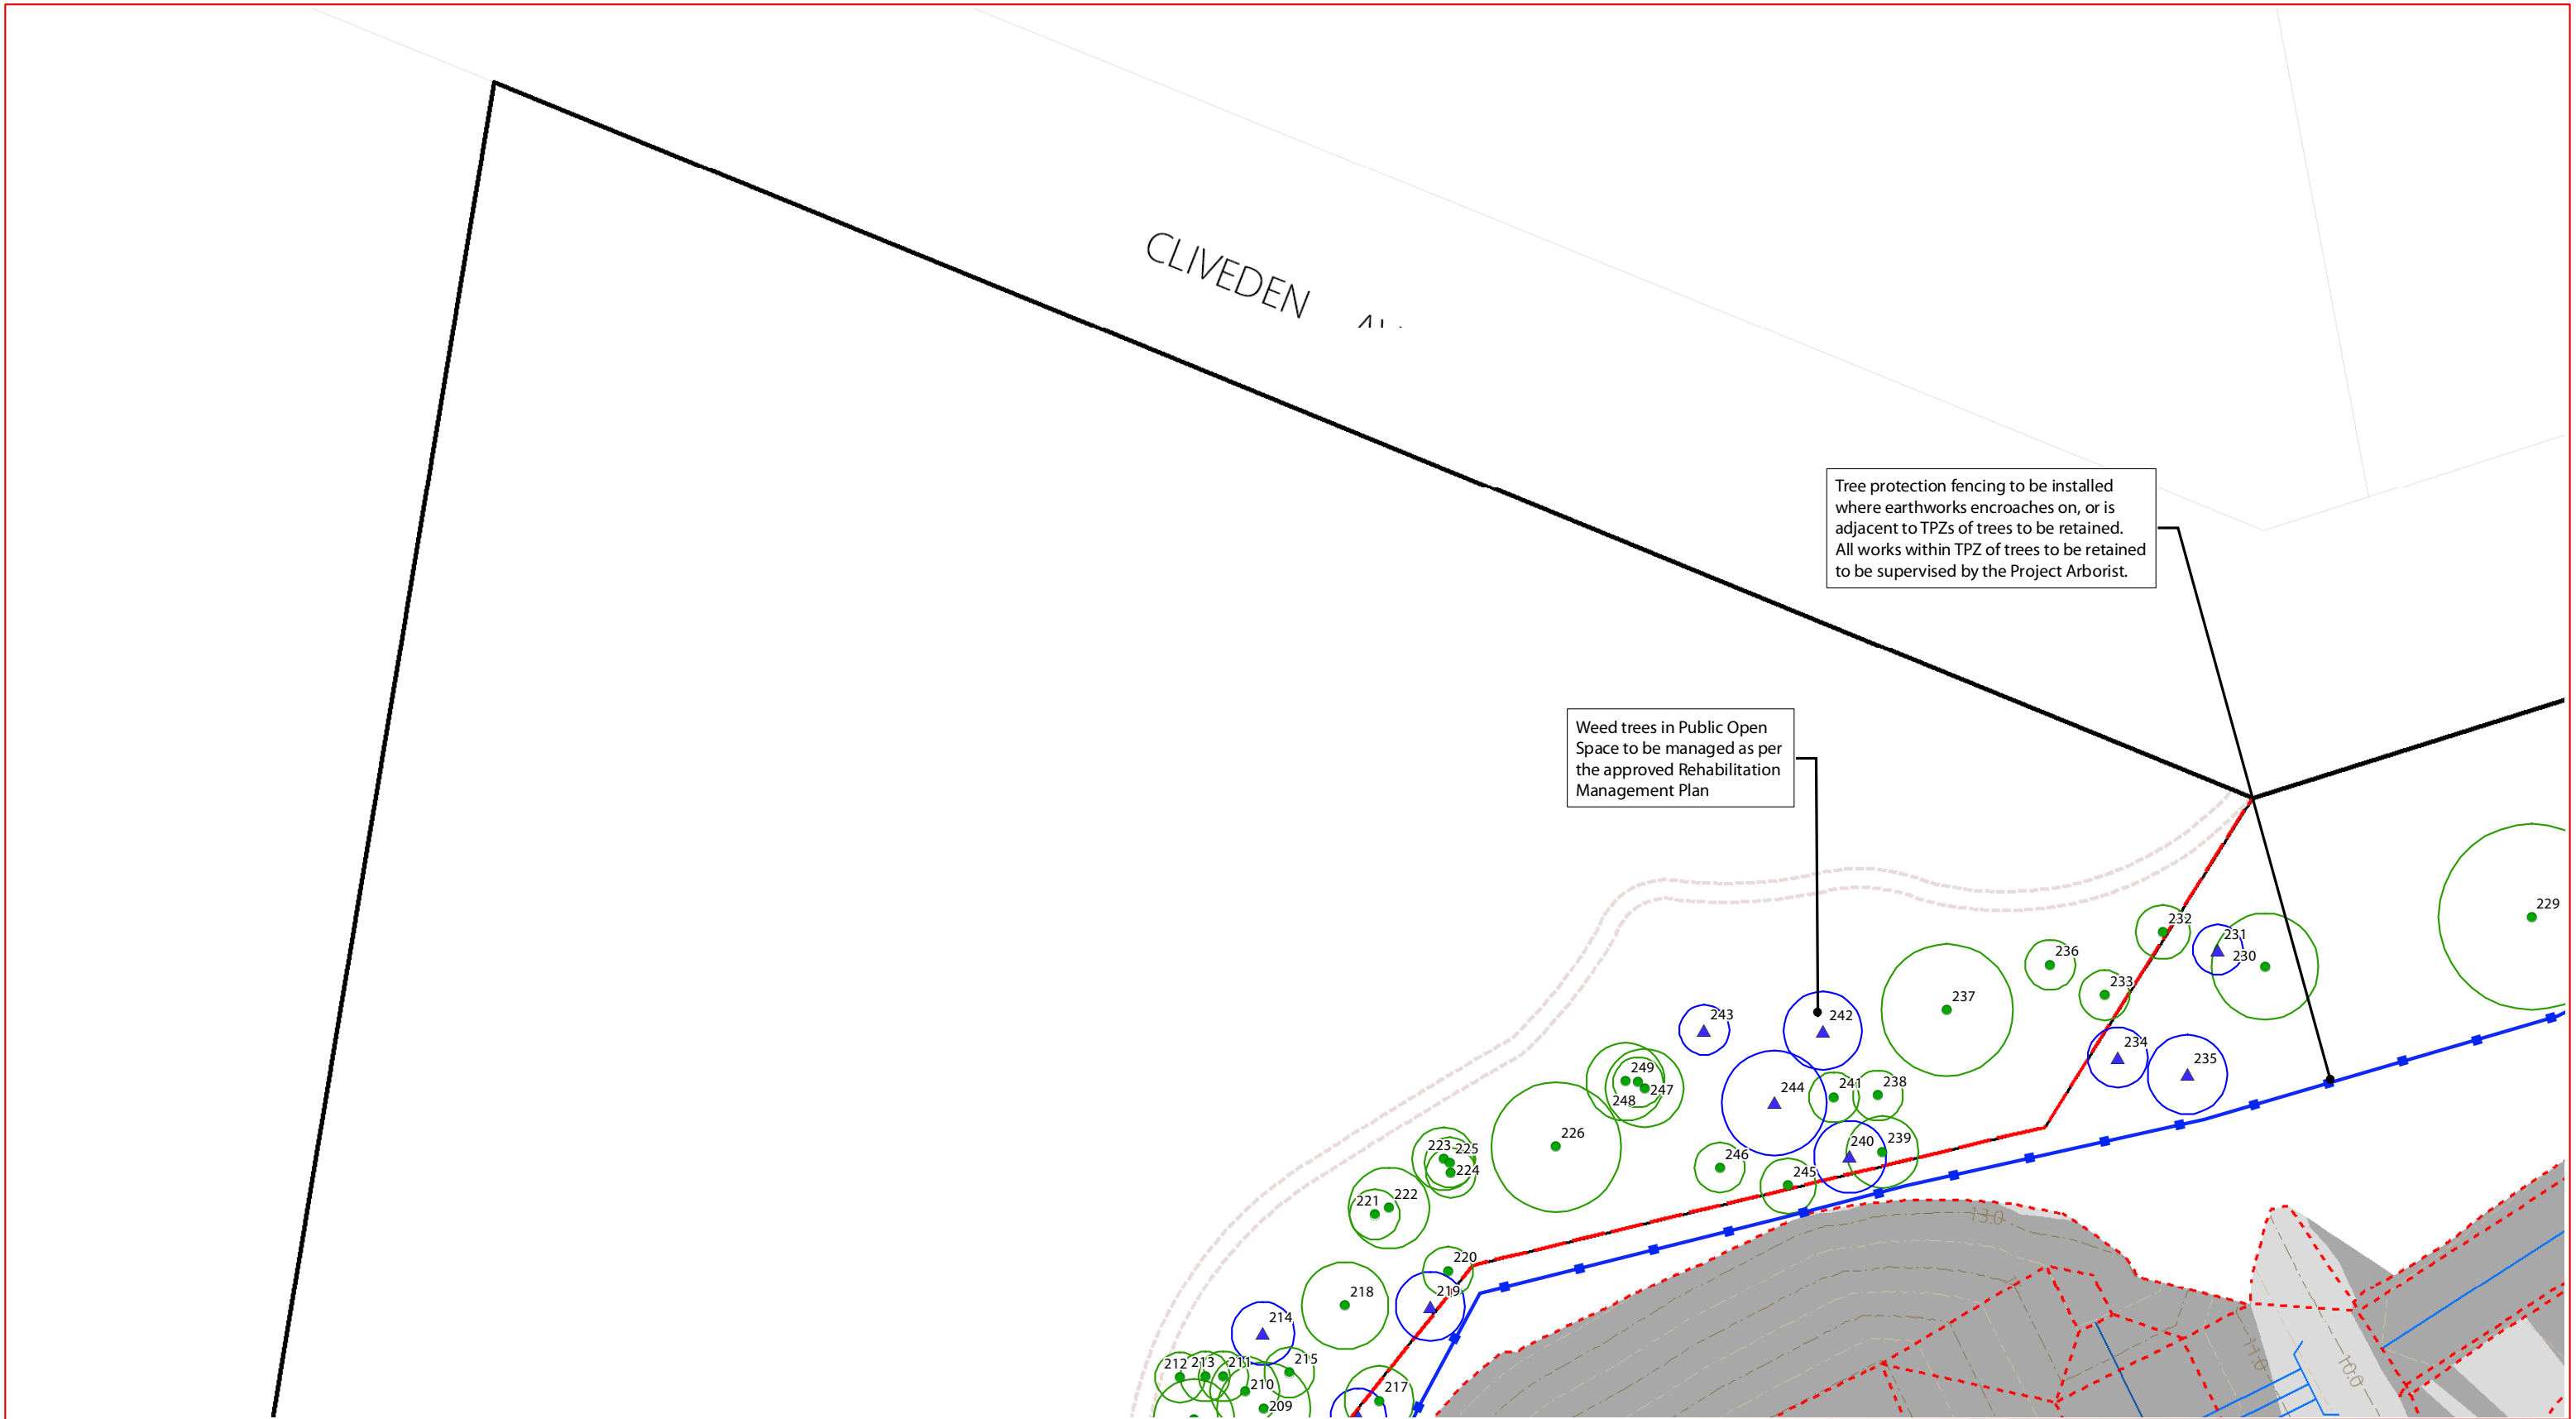

Tree protection fencing to be installed where earthworks encroaches on, or is adjacent to TPZs of trees to be retained. All works within TPZ of trees to be retained to be supervised by the Project Arborist.

Weed trees in Public Open Space to be managed as per the approved Rehabilitation Management Plan

- Native tree to remove during tree clearing for remediation works (w/TPZ)
- Weed tree to remove during tree clearing for remediation works (w/TPZ)
- Native tree to remove during tree clearing for Stage 1 (w/TPZ)
- Weed tree to remove during tree clearing for Stage 1 (w/TPZ)
- Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)
- Dead tree / stag
- Retention during clearing for remediations works subject to works extent / requirements
- Project Site
- Stage Boundary
- Survey / DCDB
- Design layout
- Easement
- Building Envelope
- Indicative Bushfire Setback
- Batter - Top / Toe
- Tree Protection Fence
- Scour protection
- Retaining wall
- Water
- Sewer
- Stormwater
- Electricity
- Bio basin
- Footpath
- Road design
- Future stage design
- Major design contours
- Minor design contours
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - Detail sheet 5



CLIENT:
ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.


REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)

0 5 10 20 30 m

AMENDMENTS:			
Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management			
PLAN OF: Vegetation Clearing & Fauna Management Plan			
DATE	26/07/2022	CHECKED:	JG
CLIENT REF:	9216	DRAWN:	MP
DRAWING No.:	9216 E 5 VCFMP H		

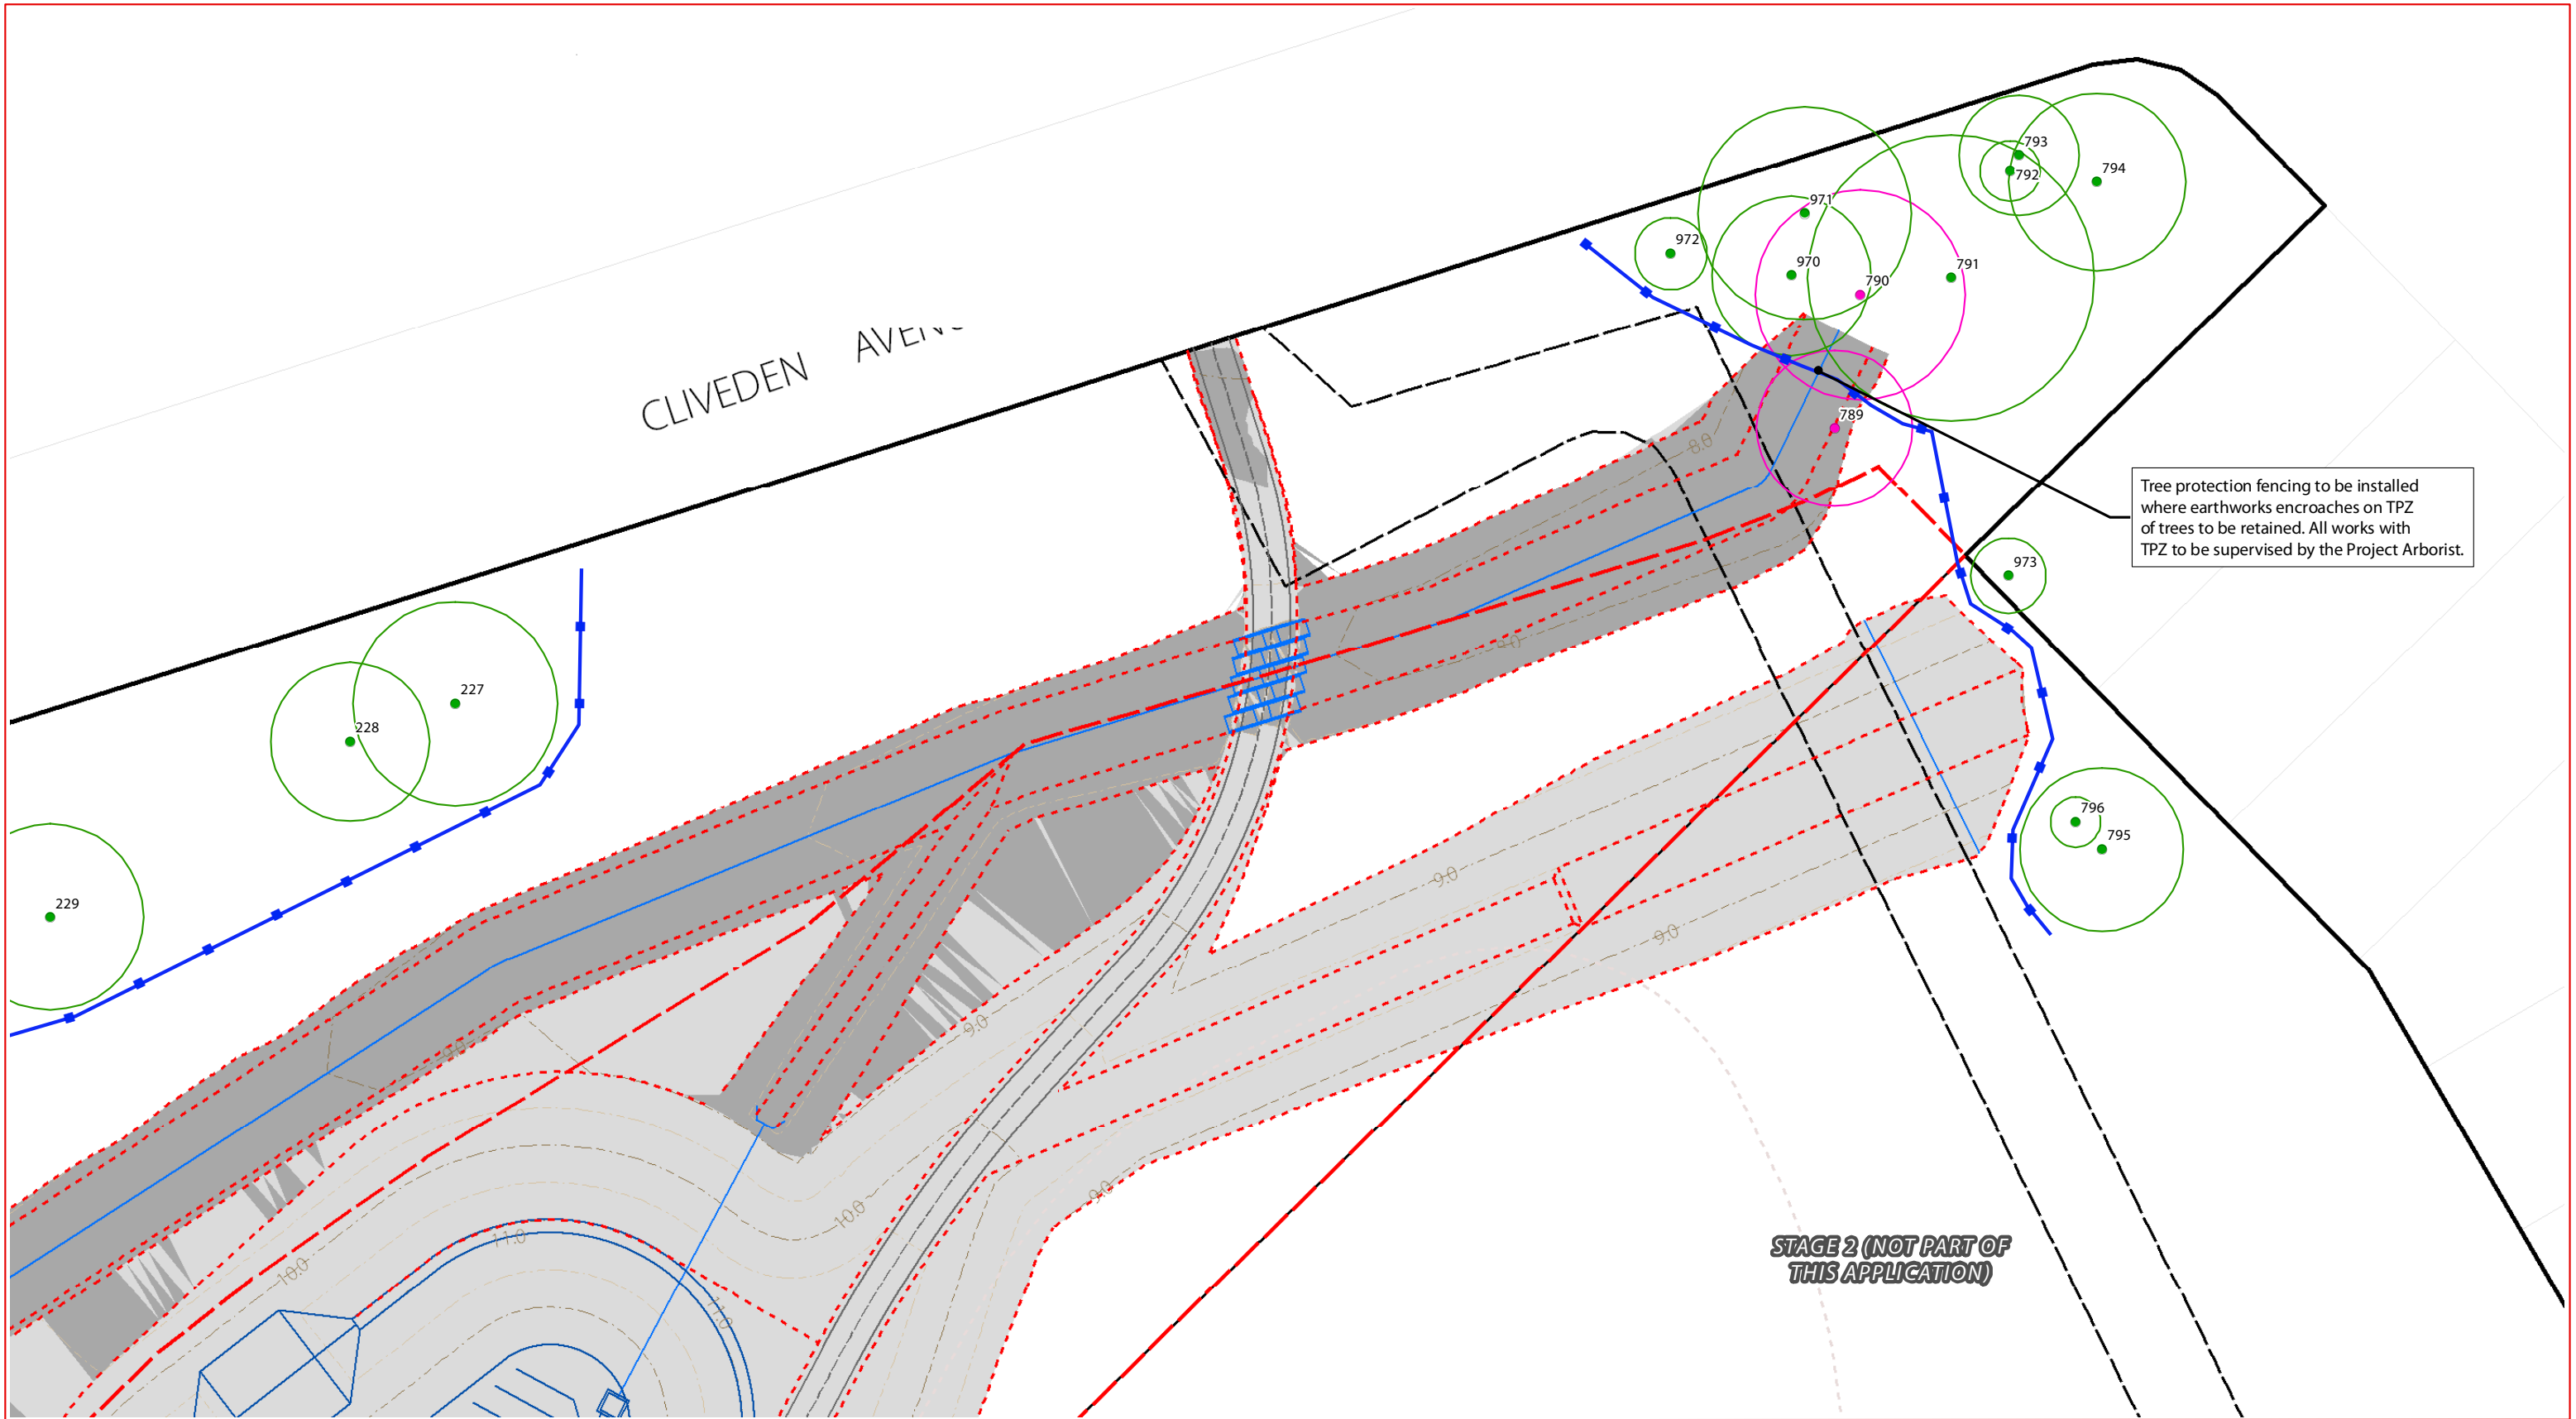

- Native tree to remove during tree clearing for remediation works (w/TPZ)

Weed tree to remove during tree clearing for Stage 1 (w/TPZ)

Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)

Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)

Dead tree / stag

Retention during clearing for remediations works subject to works extent / requirements

Project Site

Stage Boundary

Survey / DCDB

Design layout

Easement

Building Envelope

Indicative Bushfire Setback

Batter - Top / Toe

Tree Protection Fence

Scour protection

Retaining wall

Water

Sewer

Stormwater

Electricity

Bio basin

Footpath

Road design

Future stage design

Major design contours

Minor design contours

Extent of cut

Extent of fill

Vegetation stockpile location (indicative)
- # Vegetation Clearing & Fauna Management Plan - Detail sheet 6
- saunders havill group

ECONOMIC DEVELOPMENT QUEENSLAND (EDQ)

CLIENT:

ECONOMIC DEVELOPMENT QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:

Engineering / layout drawings (Butler Partners, KN Group 2020)

AMENDMENTS:

Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:

STAGE 1 SEVENTEEN MILE ROCKS ROAD OXLEY (600SP236626 / 551SP142916)

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE: 26/07/2022

CHECKED: JG


CLIENT REF: 9216

DRAWN: MP

DRAWING No.: 9216 E 6 VCFMP H

0 5 10 20 30 m

1:500 @ A3

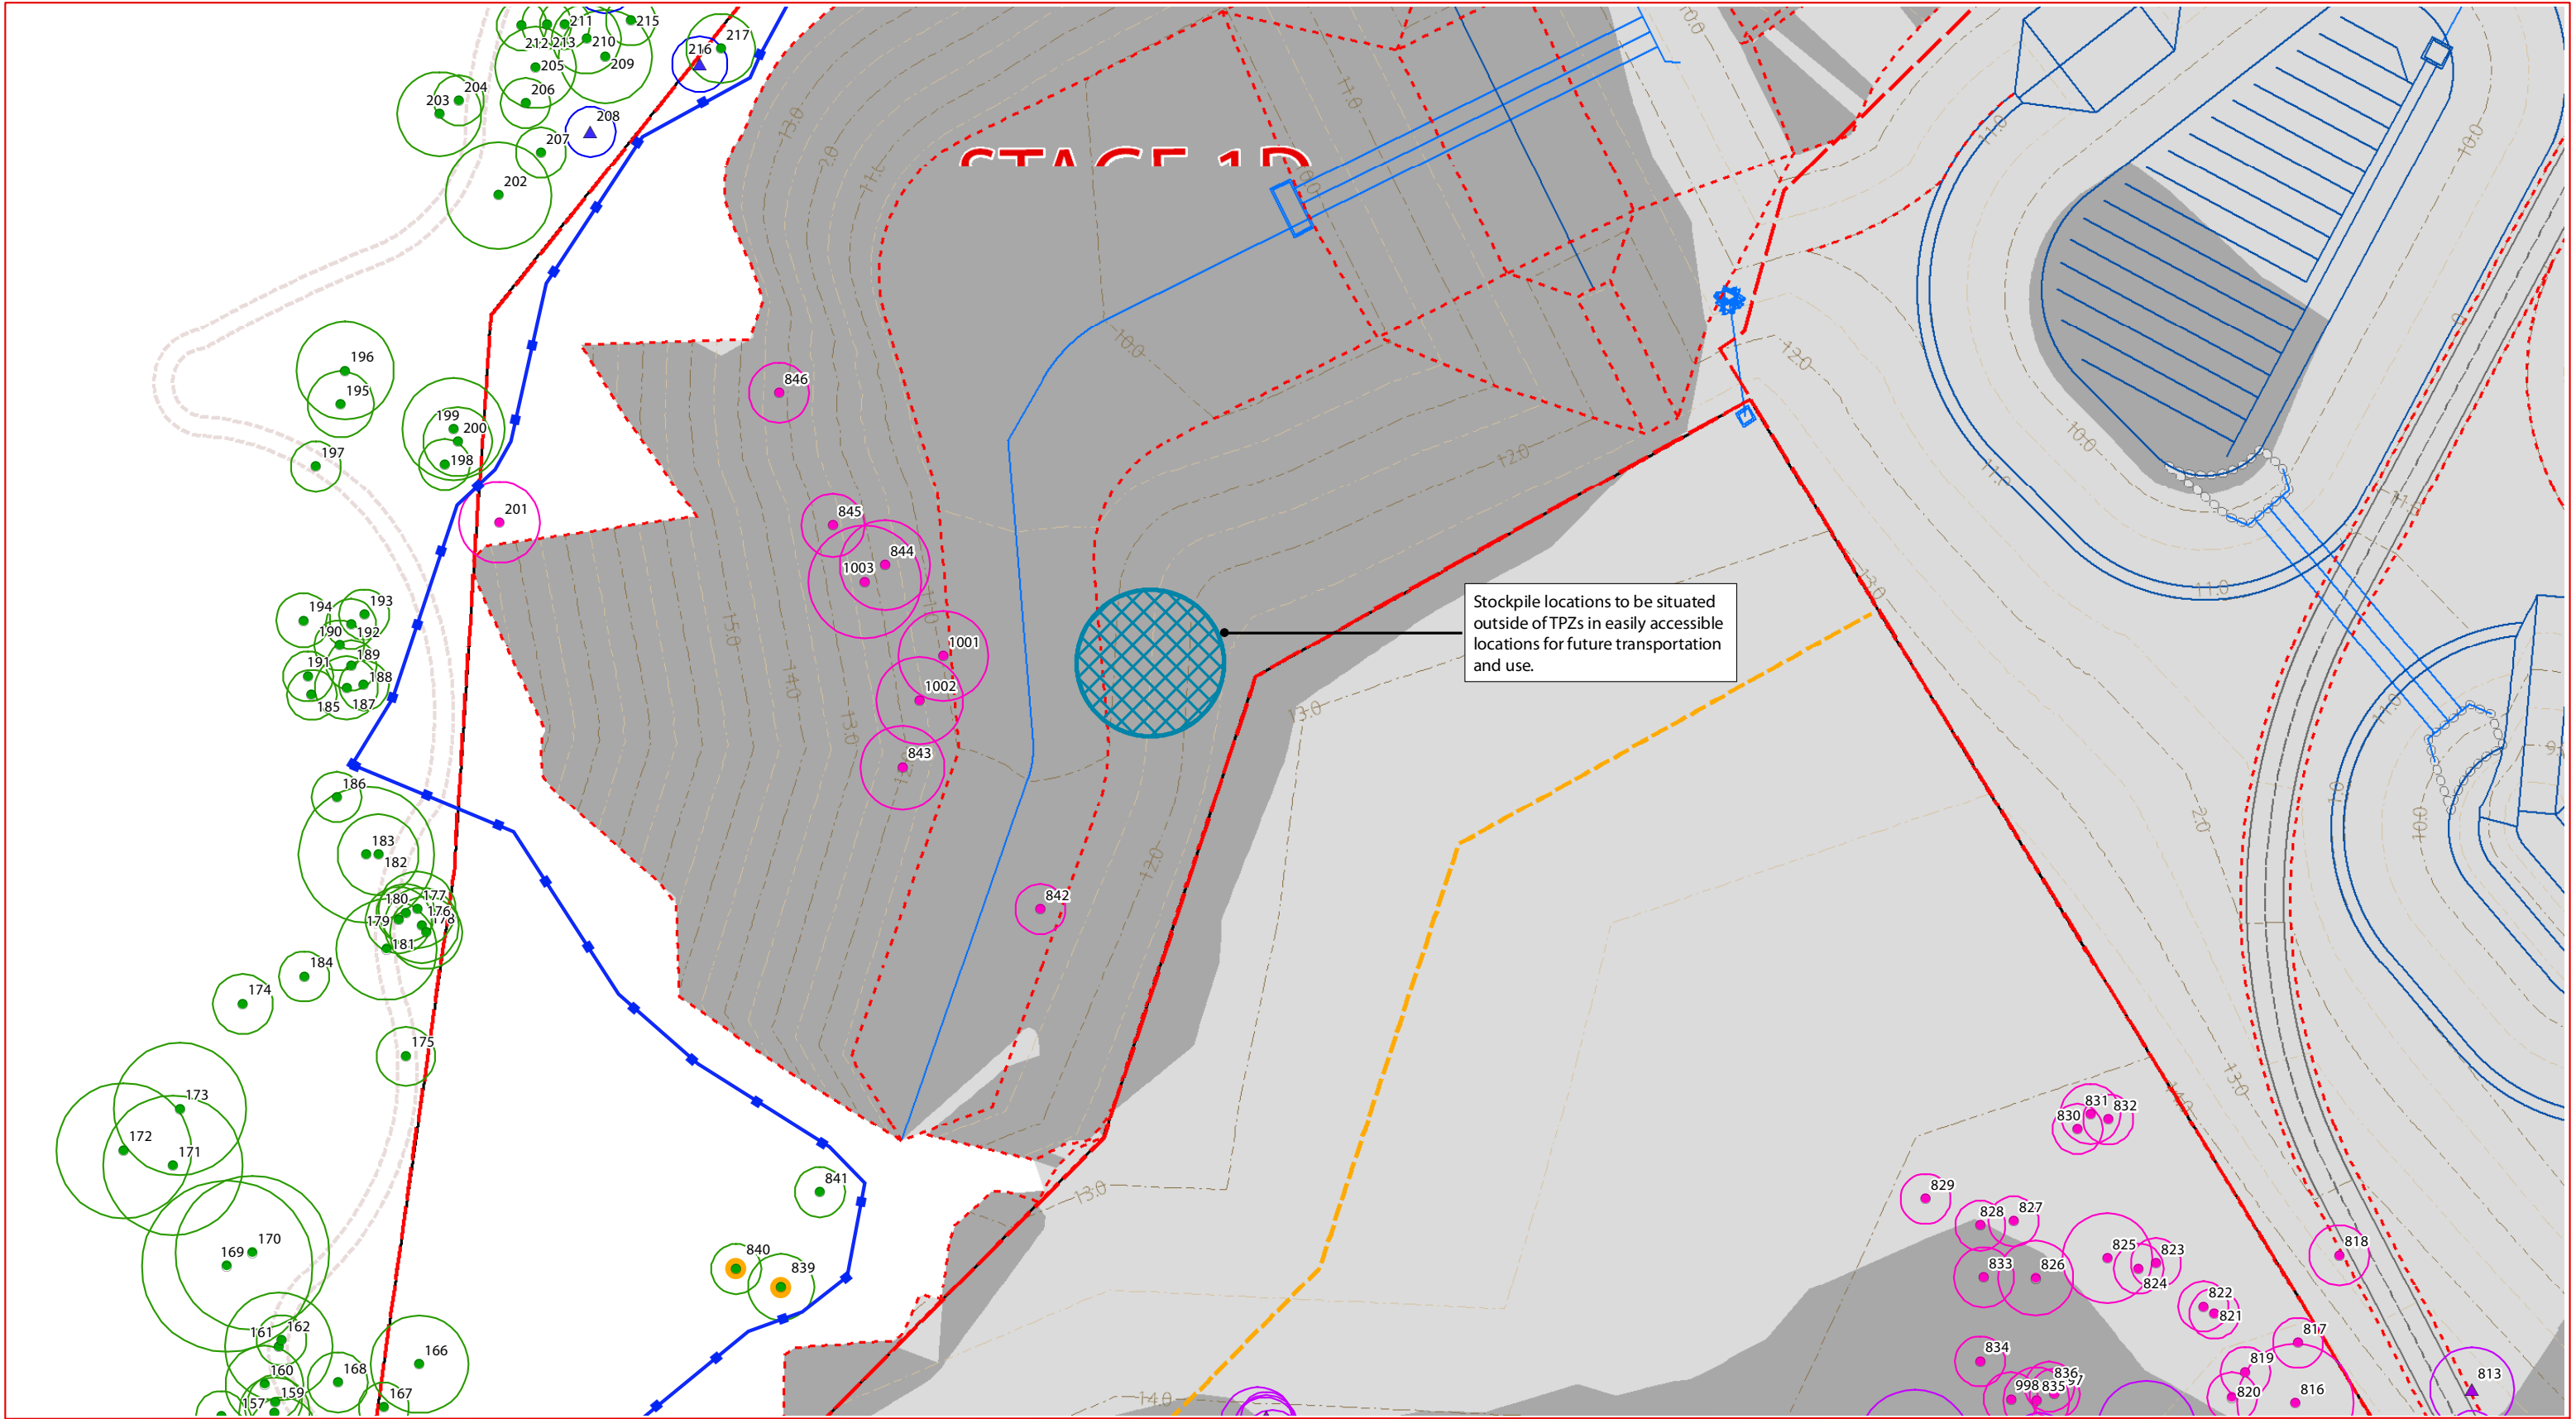

- Native tree to remove during tree clearing for remediation works (w/TPZ)
- Weed tree to remove during tree clearing for remediation works (w/TPZ)
- Native tree to remove during tree clearing for Stage 1 (w/TPZ)
- Weed tree to remove during tree clearing for Stage 1 (w/TPZ)
- Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)
- Dead tree / stag
- Retention during clearing for remediations works subject to works extent / requirements
- Project Site
- Stage Boundary
- Survey / DCDB
- Design layout
- Easement
- Building Envelope
- Indicative Bushfire Setback
- Batter - Top / Toe
- Tree Protection Fence
- Scour protection
- Retaining wall
- Water
- Sewer
- Stormwater
- Electricity
- Bio basin
- Footpath
- Road design
- Future stage design
- Major design contours
- Minor design contours
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - Detail sheet 7



CLIENT:
ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.


REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)

0 5 10 20 30 m

AMENDMENTS:			
Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	HS
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management			
PLAN OF: Vegetation Clearing & Fauna Management Plan			
DATE	26/07/2022	CHECKED:	JG
CLIENT REF:	9216	DRAWN:	MP
DRAWING No.:	9216 E 7 VCFMP H		

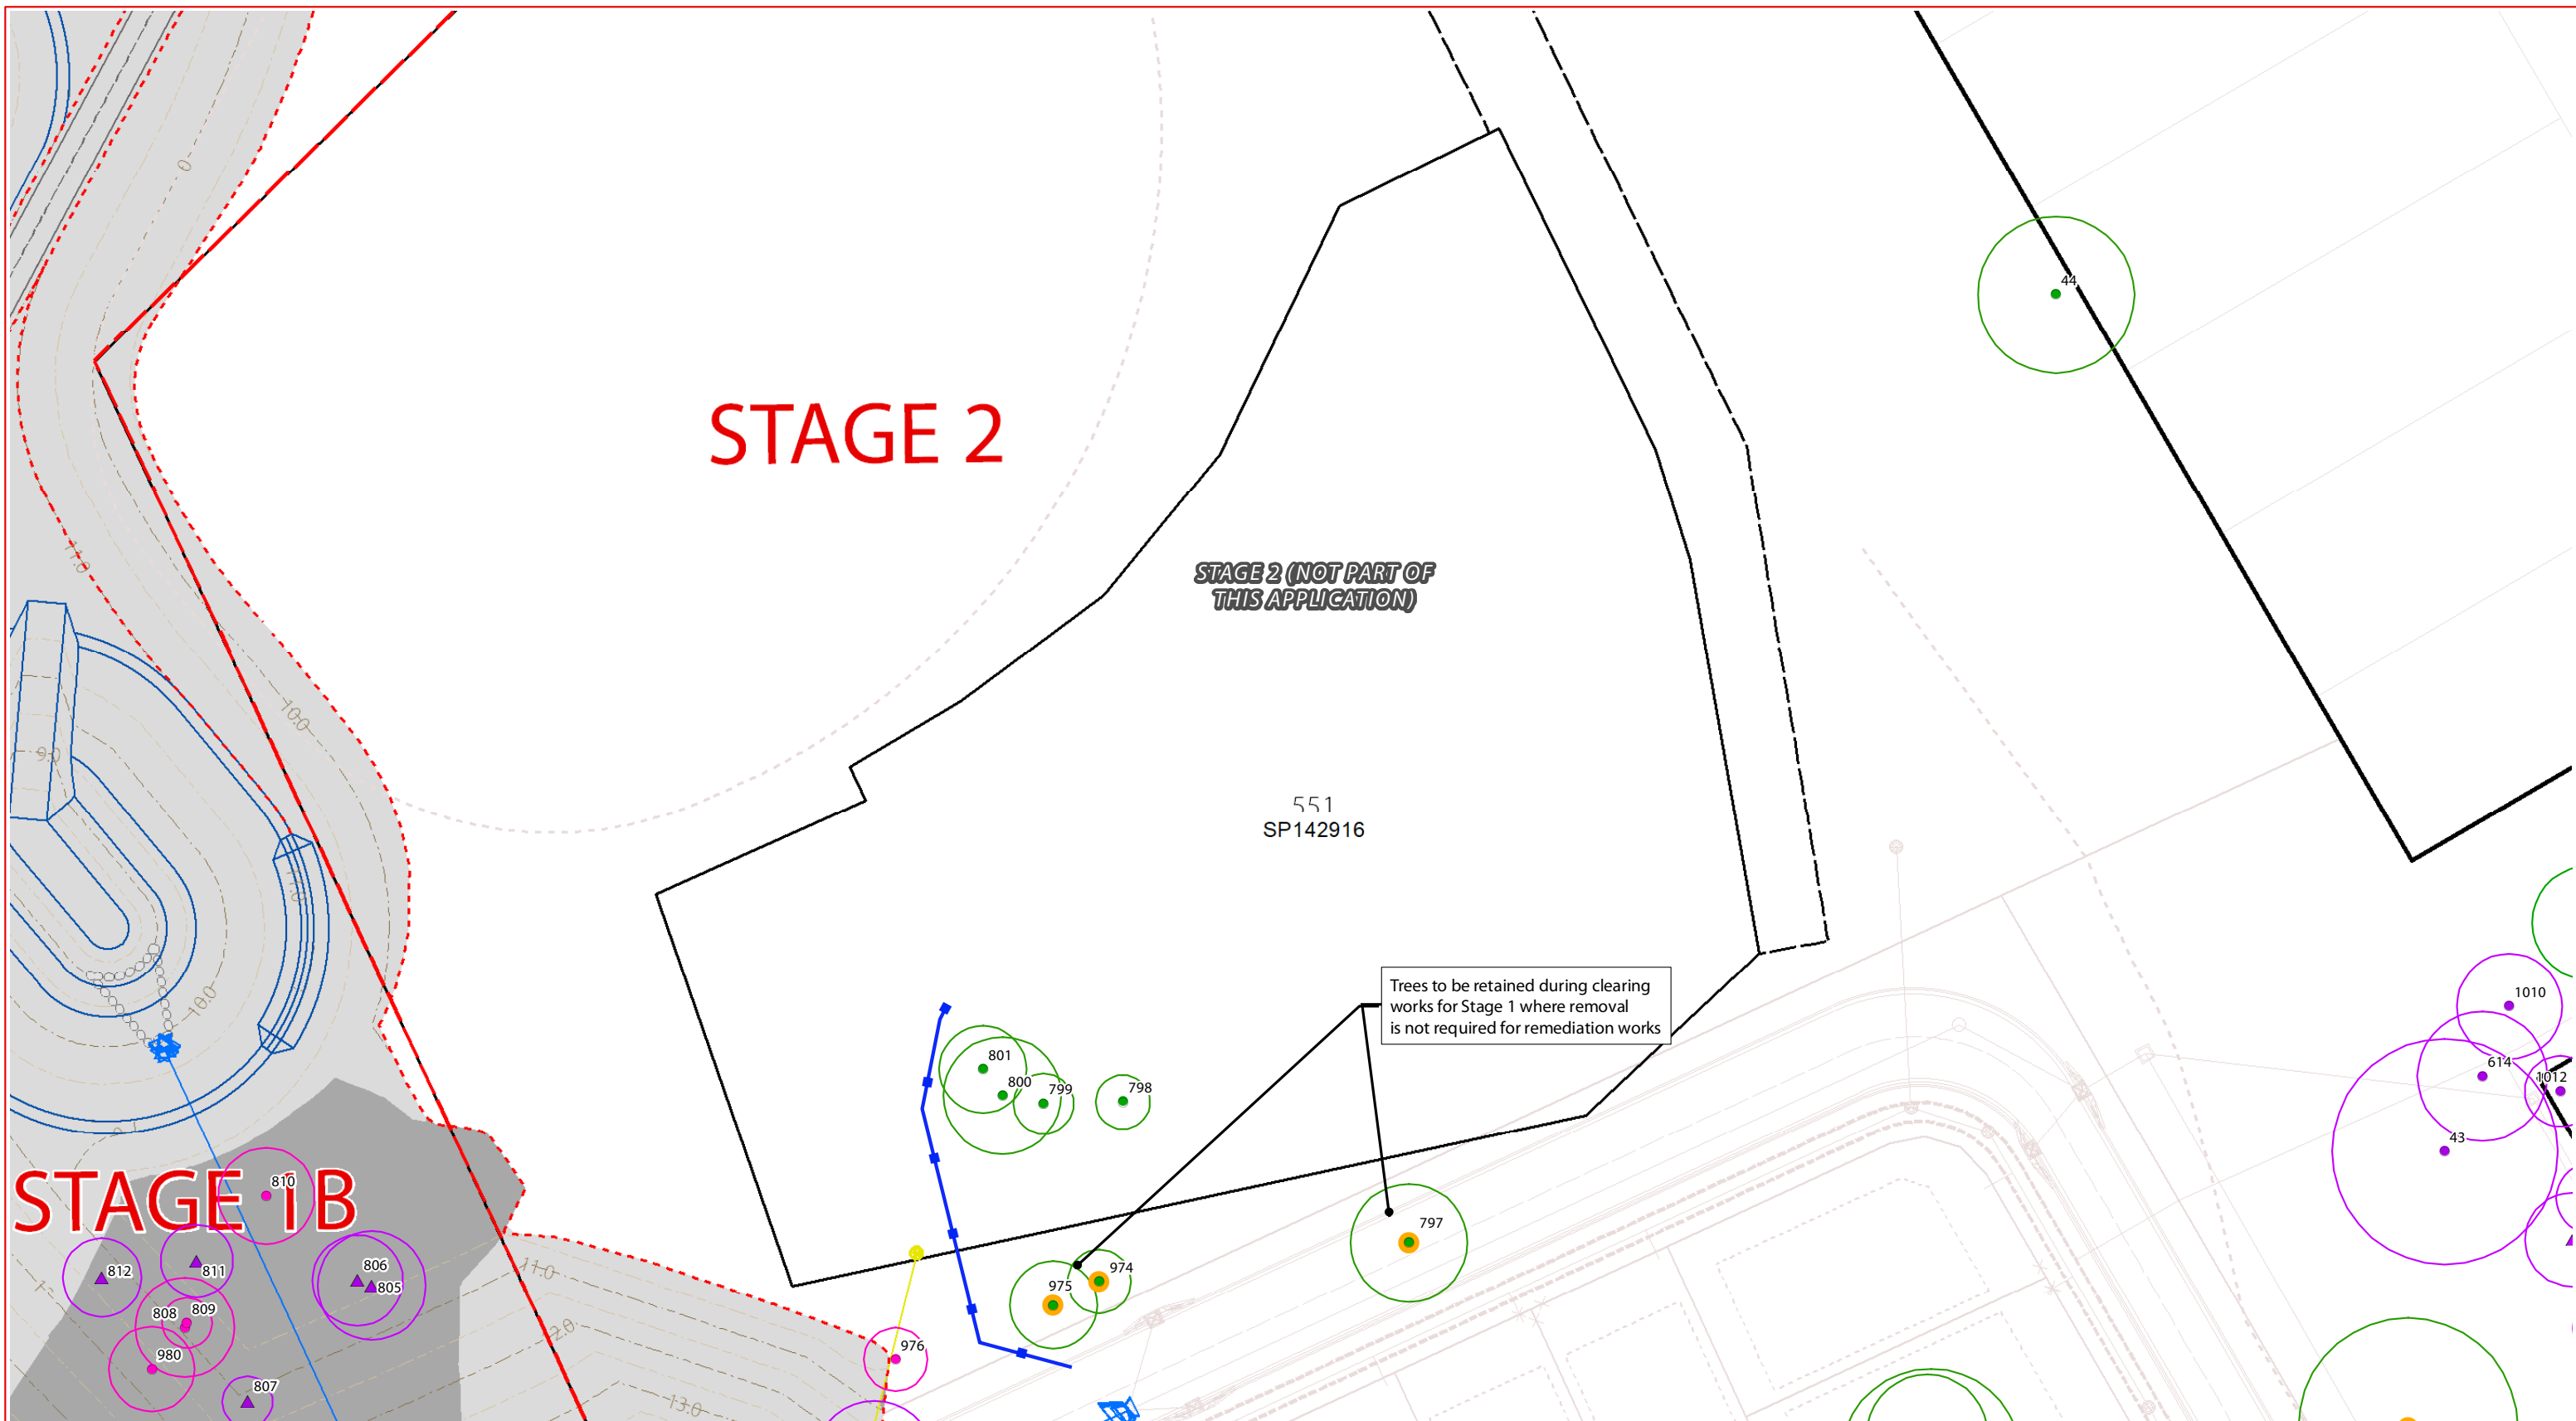

Vegetation Clearing & Fauna Management Plan - *Detail sheet 8*



CLIENT:

ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Engineering / layout drawings
(Butler Partners, KN Group 2020)



AMENDMENTS:

Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:

STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)


 environmental management

PLAN OF:
Vegetation Clearing & Fauna
Management Plan

DATE: 26/07/2022	CHECKED: JG
------------------	-------------

CLIENT REF.: 9216	DRAWN: MP
-------------------	-----------

1:500 @ A3

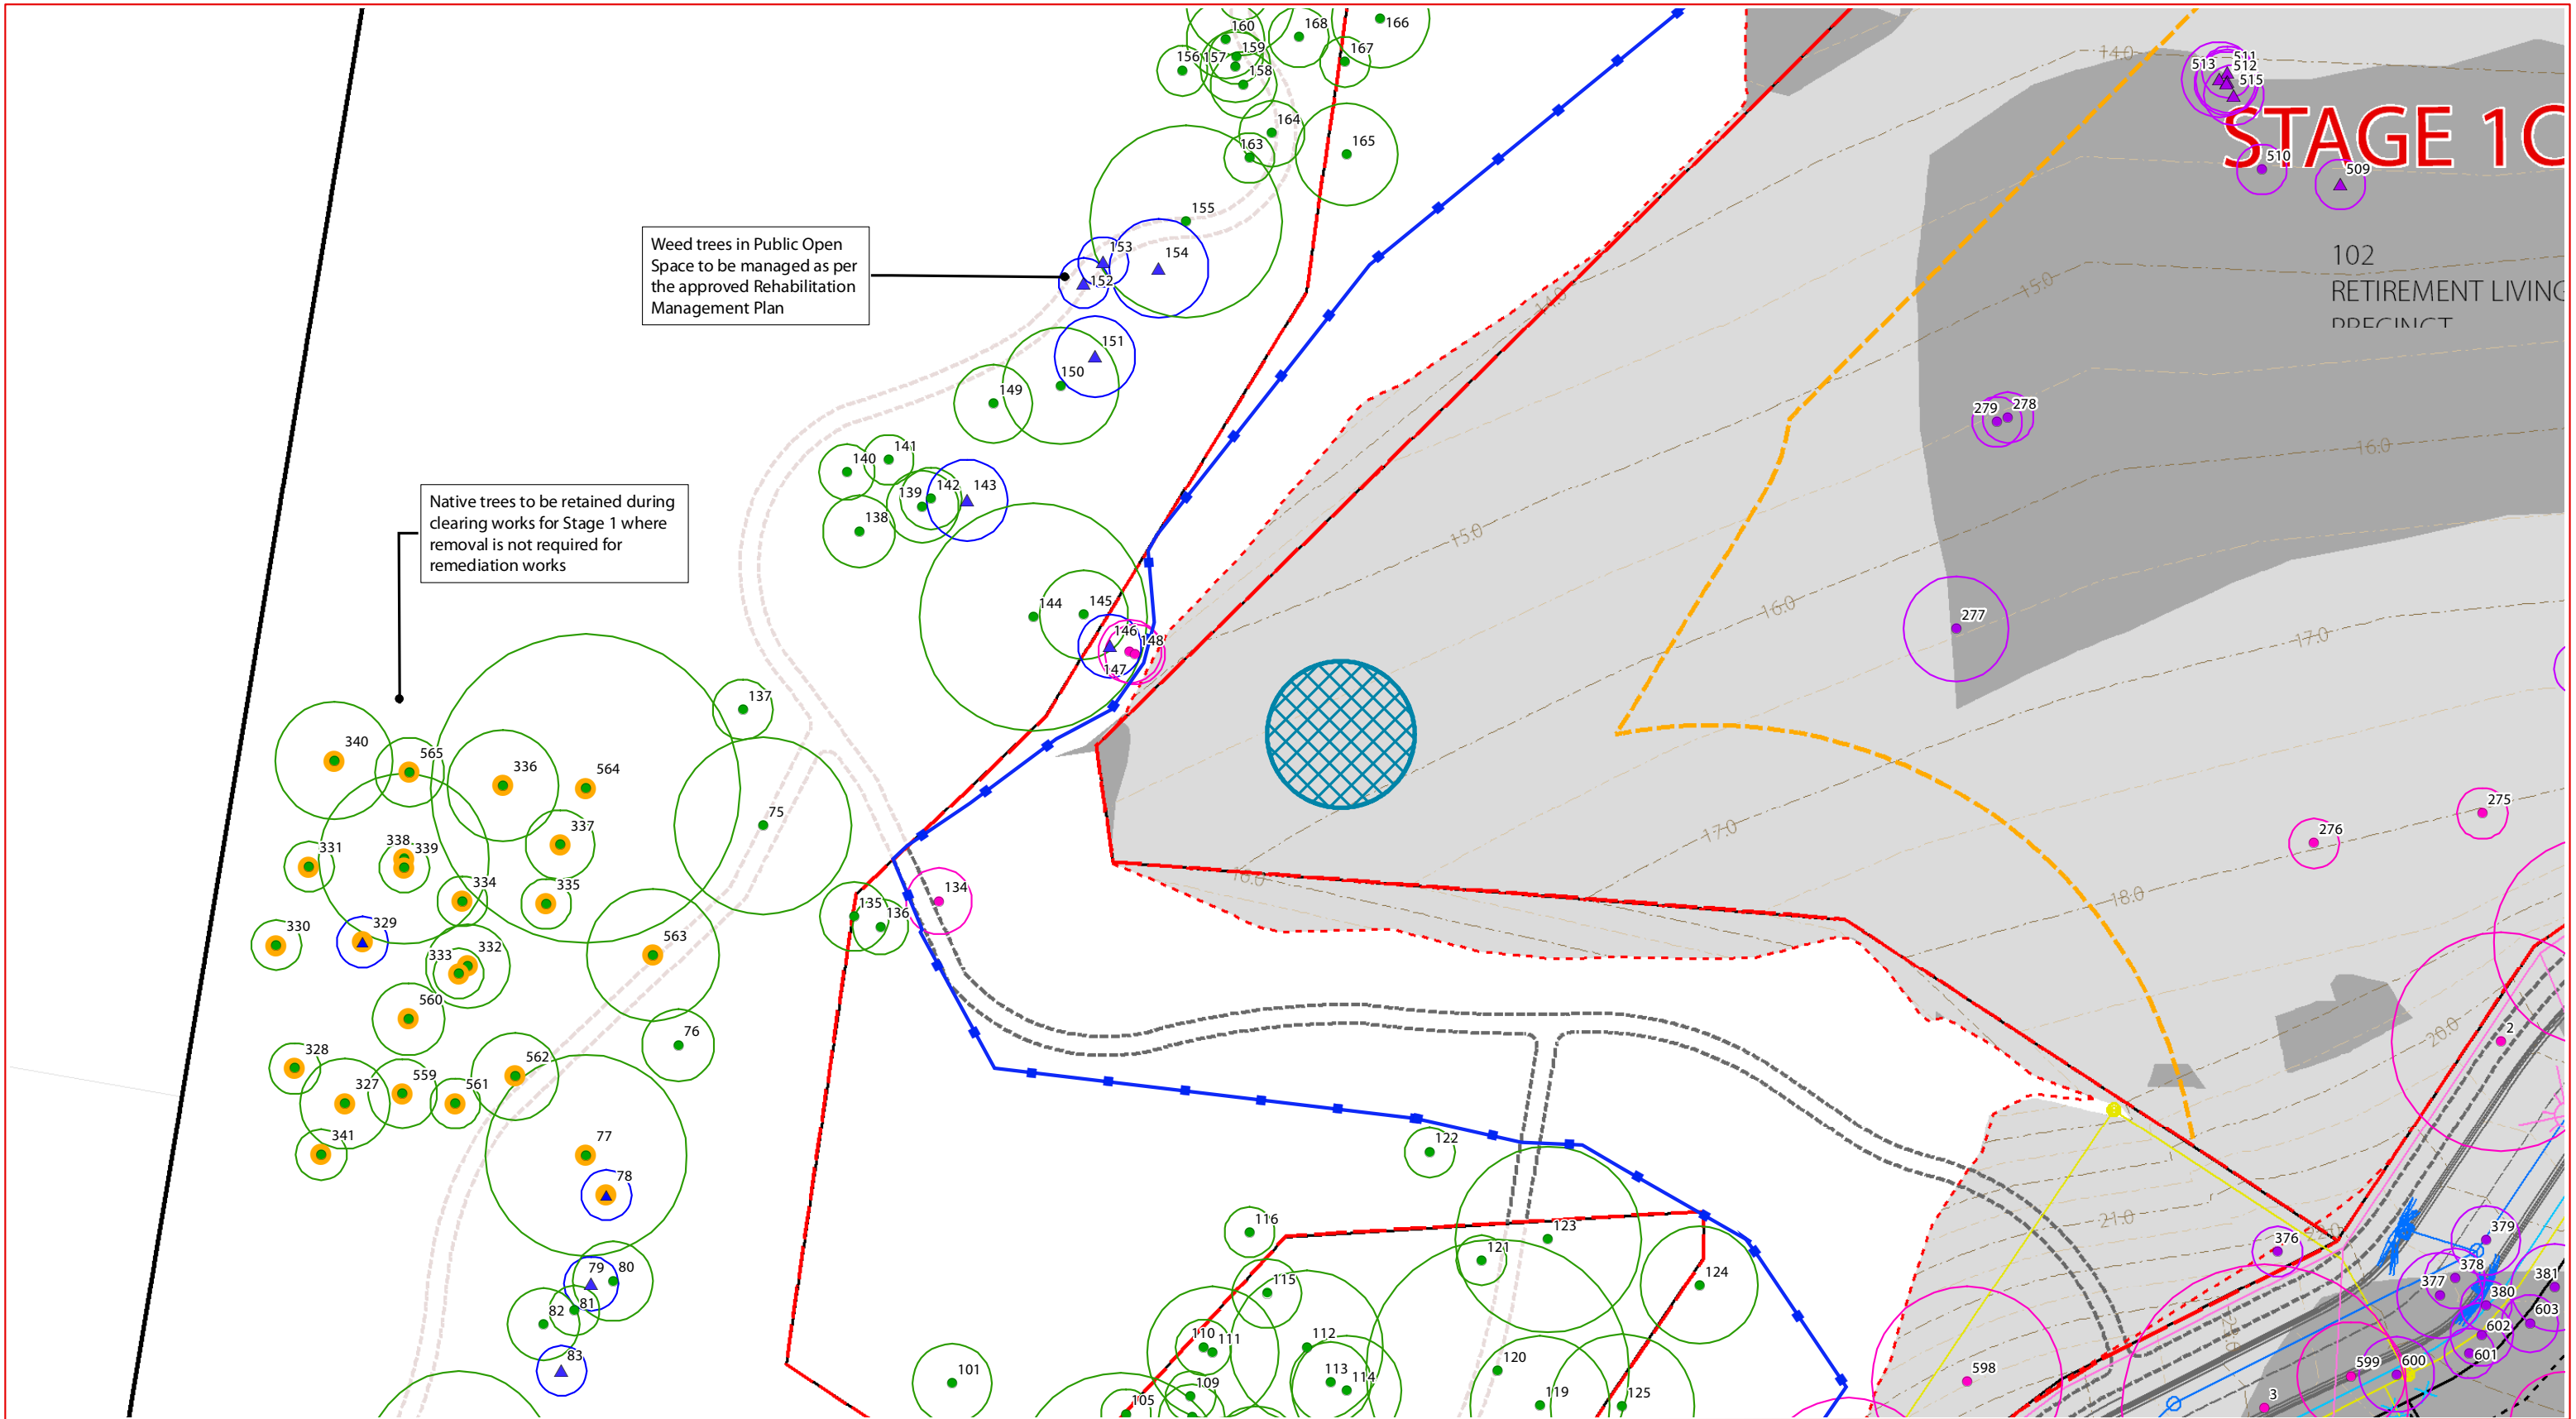

- Native tree to remove during tree clearing for remediation works (w/TPZ)
- Weed tree to remove during tree clearing for Stage 1 (w/TPZ)
- Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)
- Dead tree / stag
- Retention during clearing for remediations works subject to works extent / requirements
- Project Site
- Stage Boundary
- Survey / DCDB
- Design layout
- Easement
- Building Envelope
- Indicative Bushfire Setback
- Batter - Top / Toe
- Tree Protection Fence
- Scour protection
- Retaining wall
- Water
- Sewer
- Stormwater
- Electricity
- Bio basin
- Footpath
- Road design
- Future stage design
- Major design contours
- Minor design contours
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - Detail sheet 9



CLIENT:
ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)



0 5 10 20 30 m

AMENDMENTS:			
Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

1:500 @ A3

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management
PLAN OF:
Vegetation Clearing & Fauna
Management Plan
DATE: 26/07/2022 CHECKED: JG
CLIENT REF: 9216 DRAWN: MP
DRAWING No.: 9216 E 9 VCFMP H



- Native tree to remove during tree clearing for remediation works (w/TPZ)

Weed tree to remove during tree clearing for Stage 1 (w/TPZ)

Native tree to remove during tree clearing for Stage 1 (w/TPZ)

Weed tree to remove during tree clearing for remediation works (w/TPZ)

Native tree to retain during tree clearing for Stage 1 (w/TPZ)

Exotic tree to retain during tree clearing for Stage 1 (w/TPZ)

Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)

Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)

Dead tree / stag

Retention during clearing for remediations works subject to works extent / requirements

Project Site

Stage Boundary

Survey / DCDB

Design layout

Easement

Building Envelope

Indicative Bushfire Setback

Batter - Top / Toe

Tree Protection Fence

Scour protection

Retaining wall

Water

Sewer

Stormwater

Electricity

Bio basin

Footpath

Road design

Future stage design


Major design contours

Minor design contours

Extent of cut

Extent of fill

Vegetation stockpile location (indicative)
- ## Vegetation Clearing & Fauna Management Plan - Detail sheet 10
-
- CLIENT:
**ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)**
- DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.
- REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)
-
-
- | AMENDMENTS: | | | |
|-------------|------------|---------------------|---------|
| Issue | Date | Description | Checked |
| C | 1/05/2020 | Update 2 | JG |
| D | 8/06/2020 | Update 3 | JG |
| E | 22/06/2020 | Update 4 | JG |
| F | 13/08/2020 | Update 5 | HS |
| G | 18/09/2020 | Update 6 - Approved | JG |
| H | 26/07/2022 | Update 7 | JG |
- PROJECT:
**STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)**
- | environmental management | | | |
|---|-------------------|----------|----|
| PLAN OF:
Vegetation Clearing & Fauna Management Plan | | | |
| DATE | 26/07/2022 | CHECKED: | JG |
| CLIENT REF: | 9216 | DRAWN: | MP |
| DRAWING No.: | 9216 E 10 VCFMP H | | |

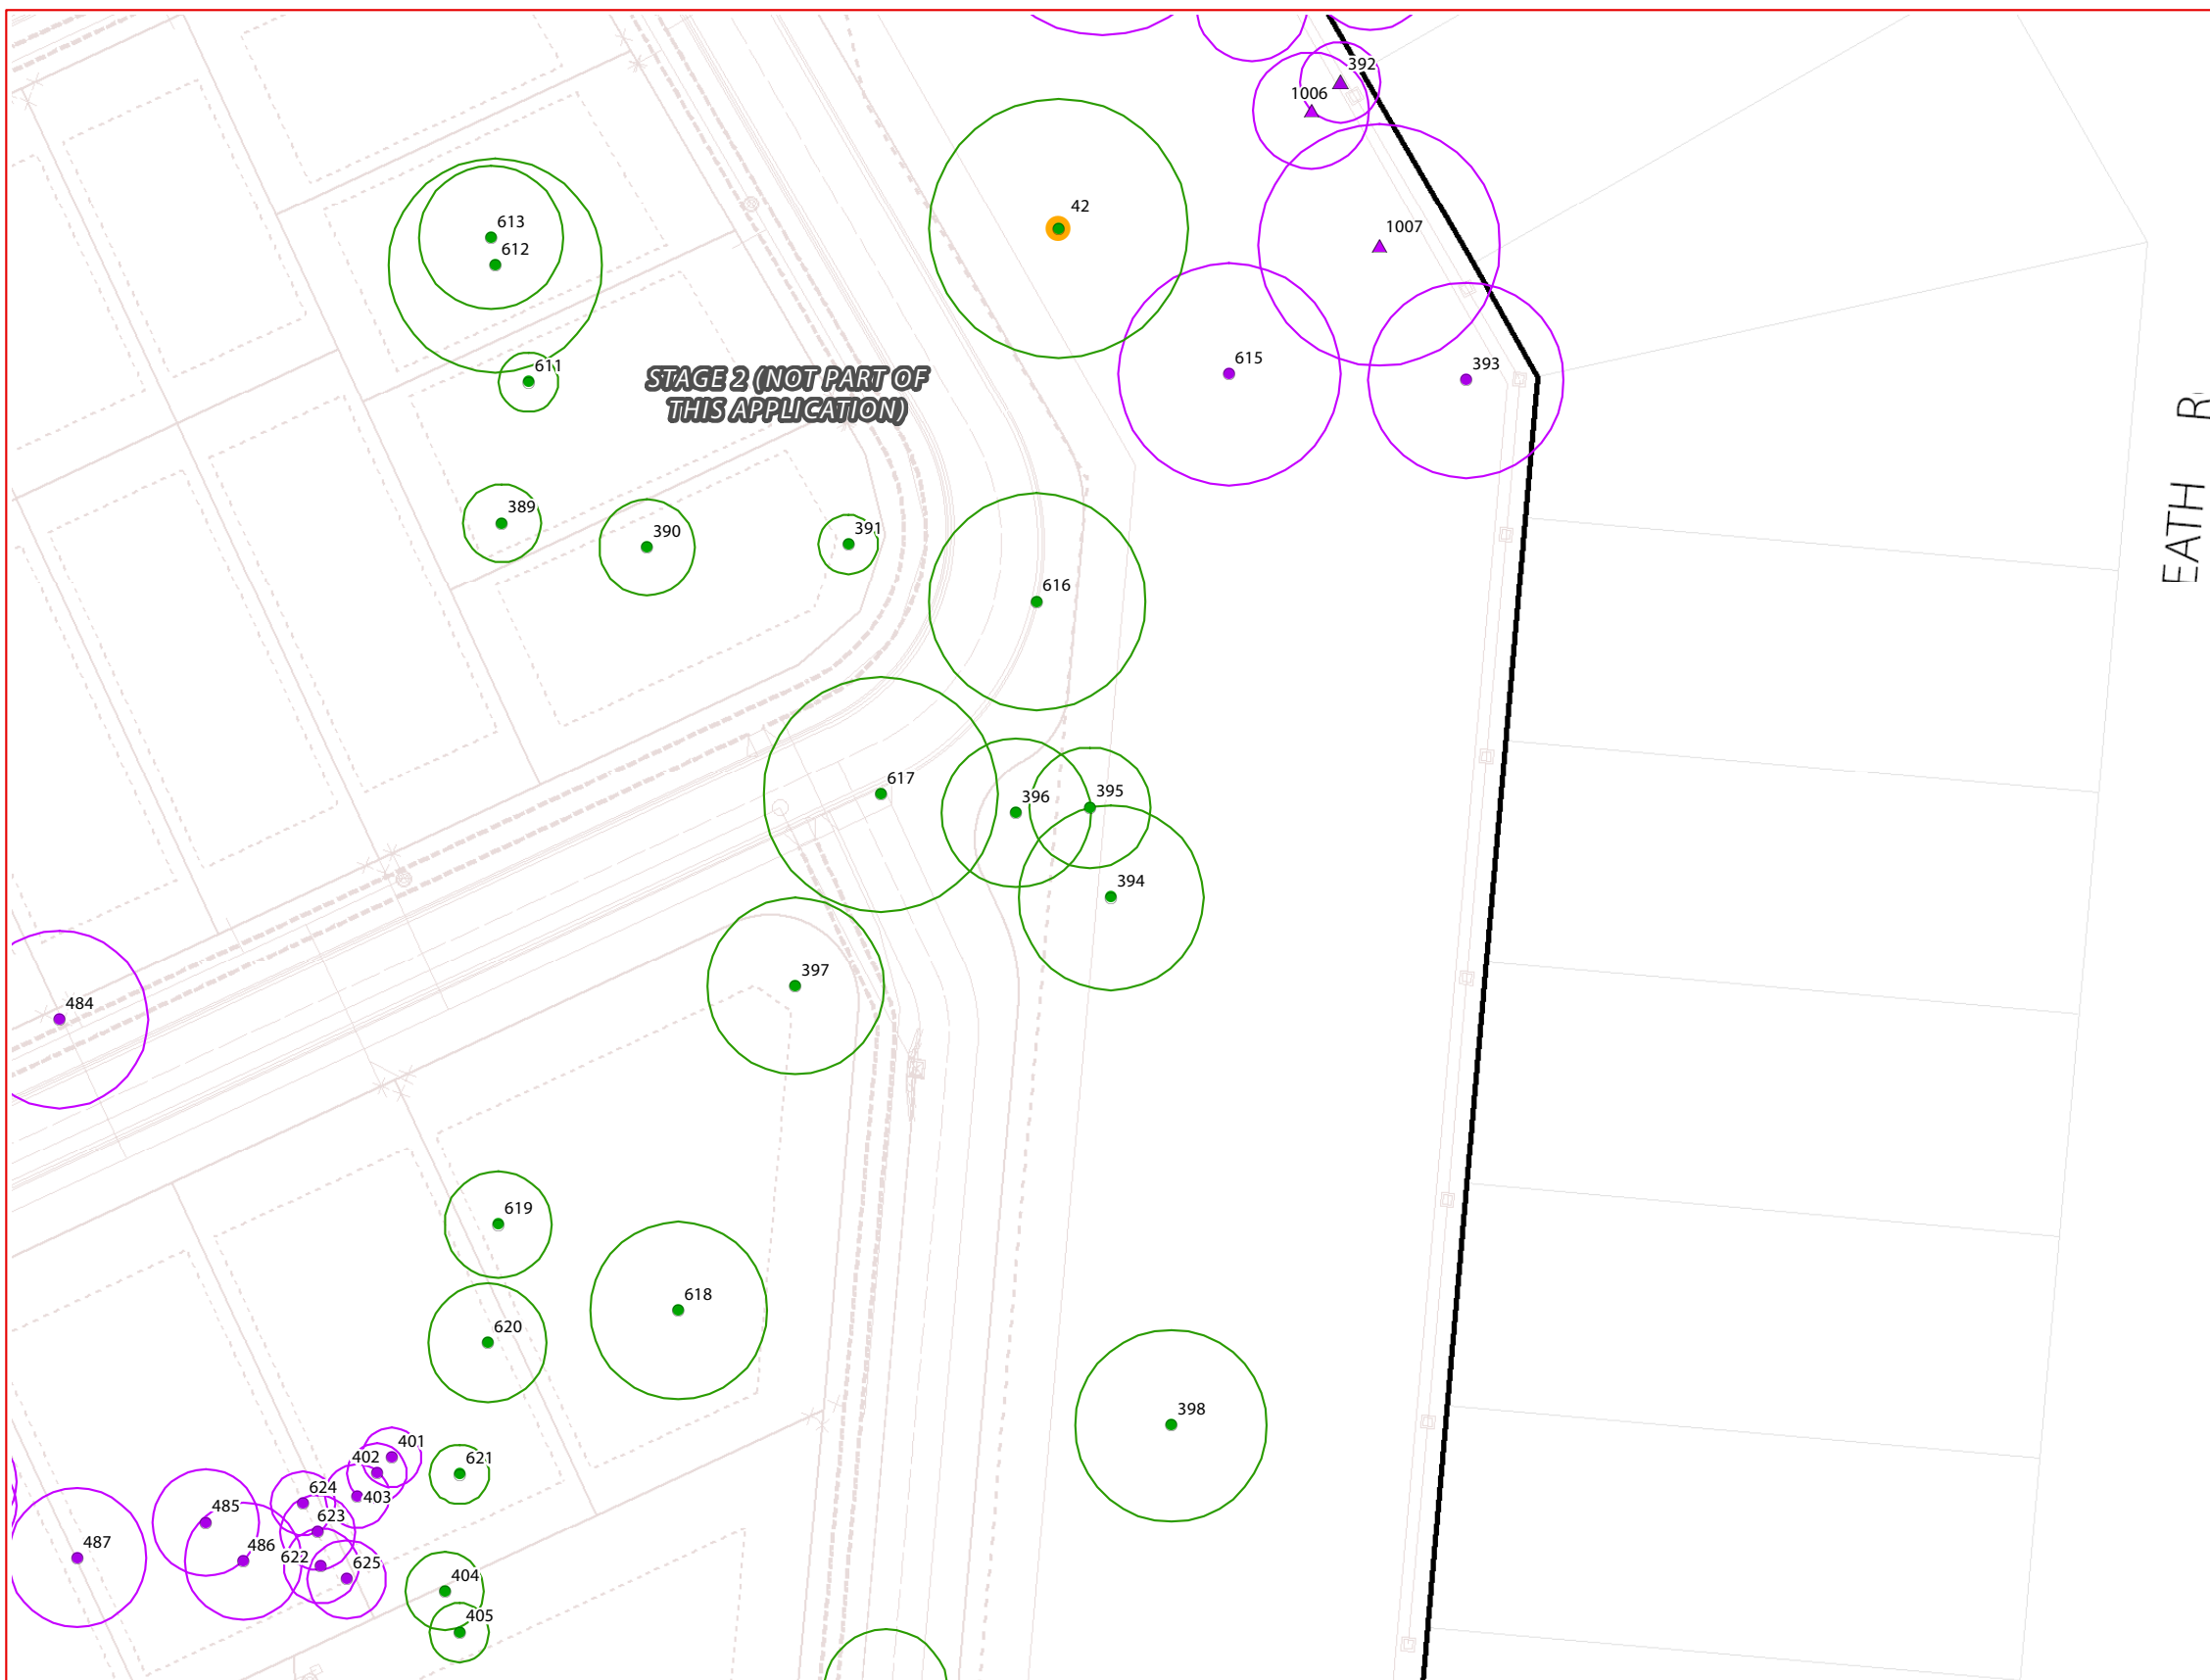

EATH R

- | | | | | | | | |
|--|--|---|---|---|--|---|--|
|  Native tree to remove during tree clearing for remediation works (w/TPZ) |  Weed tree to remove during tree clearing for Stage 1 (w/TPZ) |  Significant tree to be retained during tree clearing for Stage 1 (w/TPZ) |  Retention during clearing for remediations works subject to works extent / requirements | Easement | Retaining wall | Bio basin |  Extent of cut |
|  Weed tree to remove during tree clearing for remediation works (w/TPZ) |  Native tree to retain during tree clearing for Stage 1 (w/TPZ) |  Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ) | Project Site | Building Envelope | Water | Footpath |  Extent of fill |
|  Native tree to remove during tree clearing for Stage 1 (w/TPZ) |  Exotic tree to retain during tree clearing for Stage 1 (w/TPZ) |  Dead tree / stag | Stage Boundary | Indicative Bushfire Setback | Sewer | Road design |  Vegetation stockpile location (indicative) |
| | | | Survey / DCDB | Batter - Top / Toe | Stormwater | Future stage design | |
| | | | Design layout | Tree Protection Fence | Electricity | Major design contours | |
| | | | | Scour protection | | Minor design contours | |

Vegetation Clearing & Fauna Management Plan - *Detail sheet 11*



CLIENT:

ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Engineering / layout drawings
(Butler Partners, KN Group 2020)



1:500 @ A3

AMENDMENTS:

Issue	Date	Description	Checker
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:

STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

 environmental management

PLAN OF:
Vegetation Clearing & Fauna
Management Plan

DATE: 26/07/2022	CHECKED: JG
------------------	-------------

CLIENT REF: 9216	DRAWN: MP
------------------	-----------

DRAWING No.: 9216 E 11 VCFMP H



- Native tree to remove during tree clearing for remediation works (w/TPZ)
- Weed tree to remove during tree clearing for Stage 1 (w/TPZ)
- Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)
- Dead tree / stag
- Retention during clearing for remediations works subject to works extent / requirements
- Project Site
- Stage Boundary
- Survey / DCDB
- Design layout
- Easement
- Building Envelope
- Indicative Bushfire Setback
- Batter - Top / Toe
- Tree Protection Fence
- Scour protection
- Retaining wall
- Water
- Sewer
- Stormwater
- Electricity
- Bio basin
- Footpath
- Road design
- Future stage design
- Major design contours
- Minor design contours
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - Detail sheet 13



CLIENT:

ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

REFERENCES:

Engineering / layout drawings
(Butler Partners, KN Group 2020)



0 5 10 20 30 m

AMENDMENTS:

Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG


PROJECT:

STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management

PLAN OF:
Vegetation Clearing & Fauna
Management Plan

DATE: 26/07/2022
CLIENT REF: 9216
DRAWING No.: 9216 E 13 VCFMP H
CHECKED: JG
DRAWN: MP

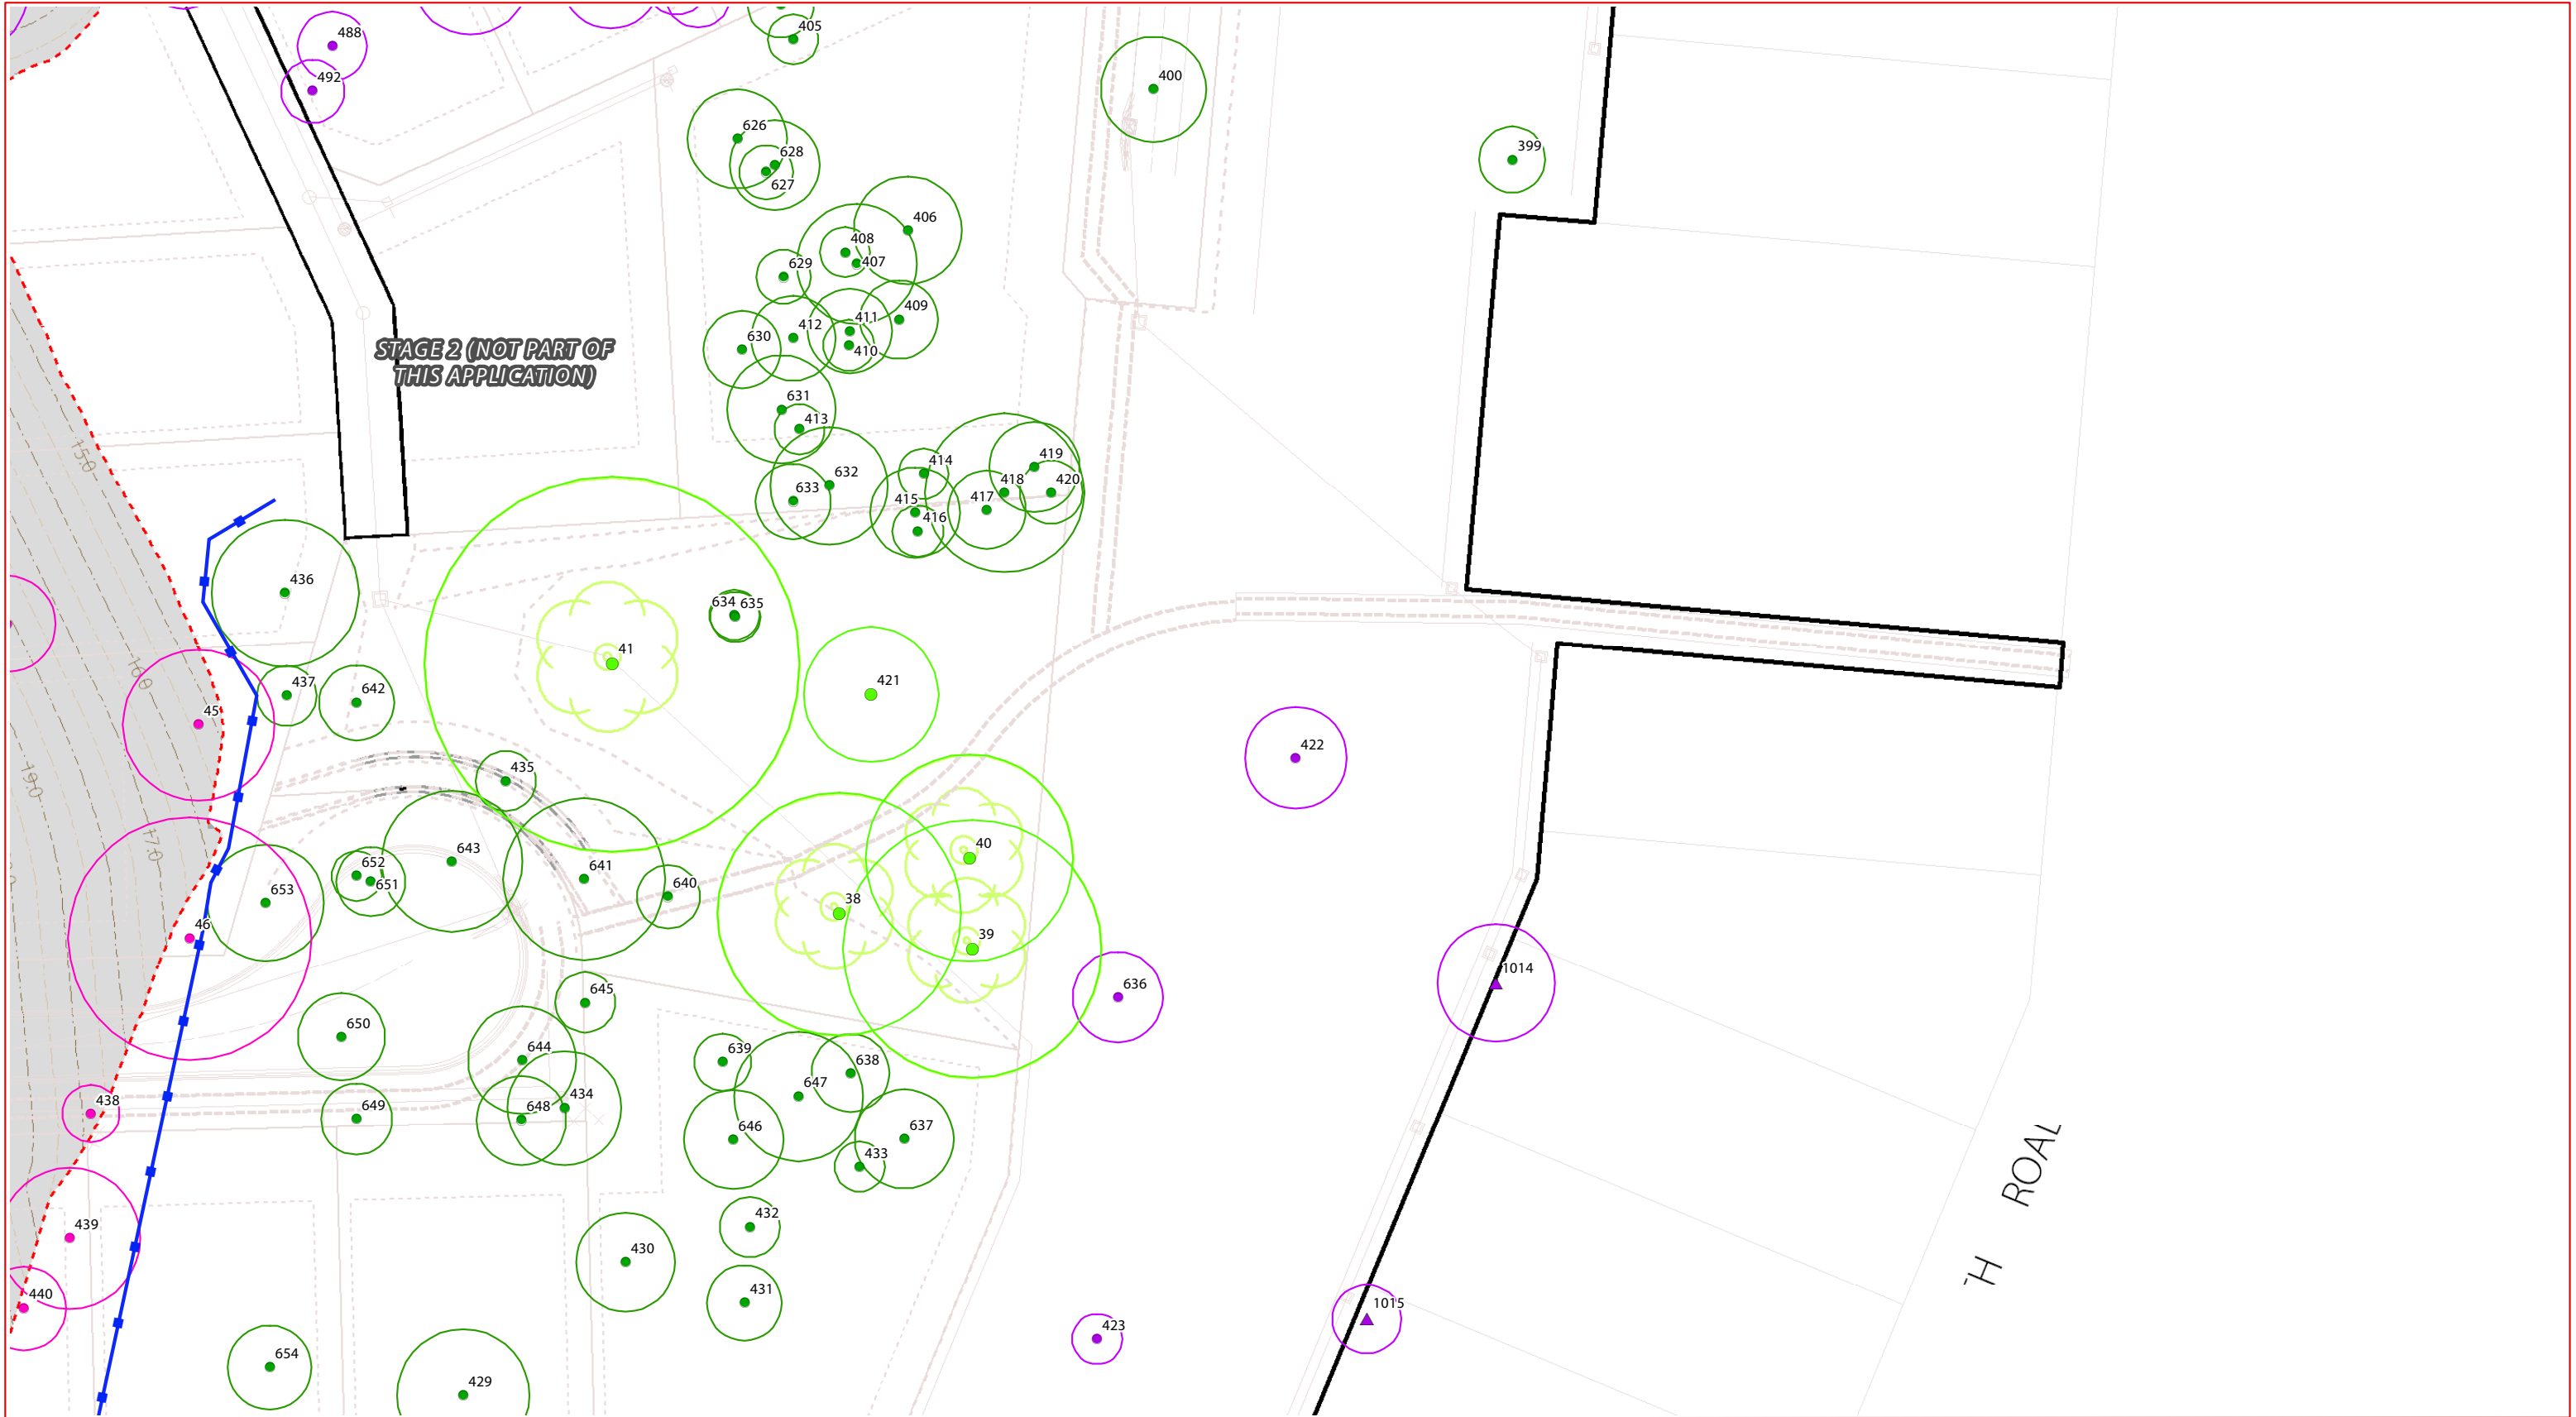

- Native tree to remove during tree clearing for remediation works (w/TPZ)
- Weed tree to remove during tree clearing for remediation works (w/TPZ)
- Native tree to remove during tree clearing for Stage 1 (w/TPZ)
- Native tree to retain during tree clearing for Stage 1 (w/TPZ)
- Exotic tree to retain during tree clearing for Stage 1 (w/TPZ)
- Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)
- Dead tree / stag
- Retention during clearing for remediations works subject to works extent / requirements
- Project Site
- Stage Boundary
- Survey / DCDB
- Design layout
- Easement
- Building Envelope
- Indicative Bushfire Setback
- Batter - Top / Toe
- Tree Protection Fence
- Scour protection
- Retaining wall
- Water
- Sewer
- Stormwater
- Electricity
- Bio basin
- Footpath
- Road design
- Future stage design
- Major design contours
- Minor design contours
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - Detail sheet 14



CLIENT:
ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)

0 5 10 20 30 m


AMENDMENTS:			
Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management


PLAN OF:
Vegetation Clearing & Fauna Management Plan

DATE	26/07/2022	CHECKED:	JG
CLIENT REF:	9216	DRAWN:	MP
DRAWING No.:	9216 E 14 VCFMP H		



- ## Vegetation Clearing & Fauna Management Plan - *Detail sheet 16*



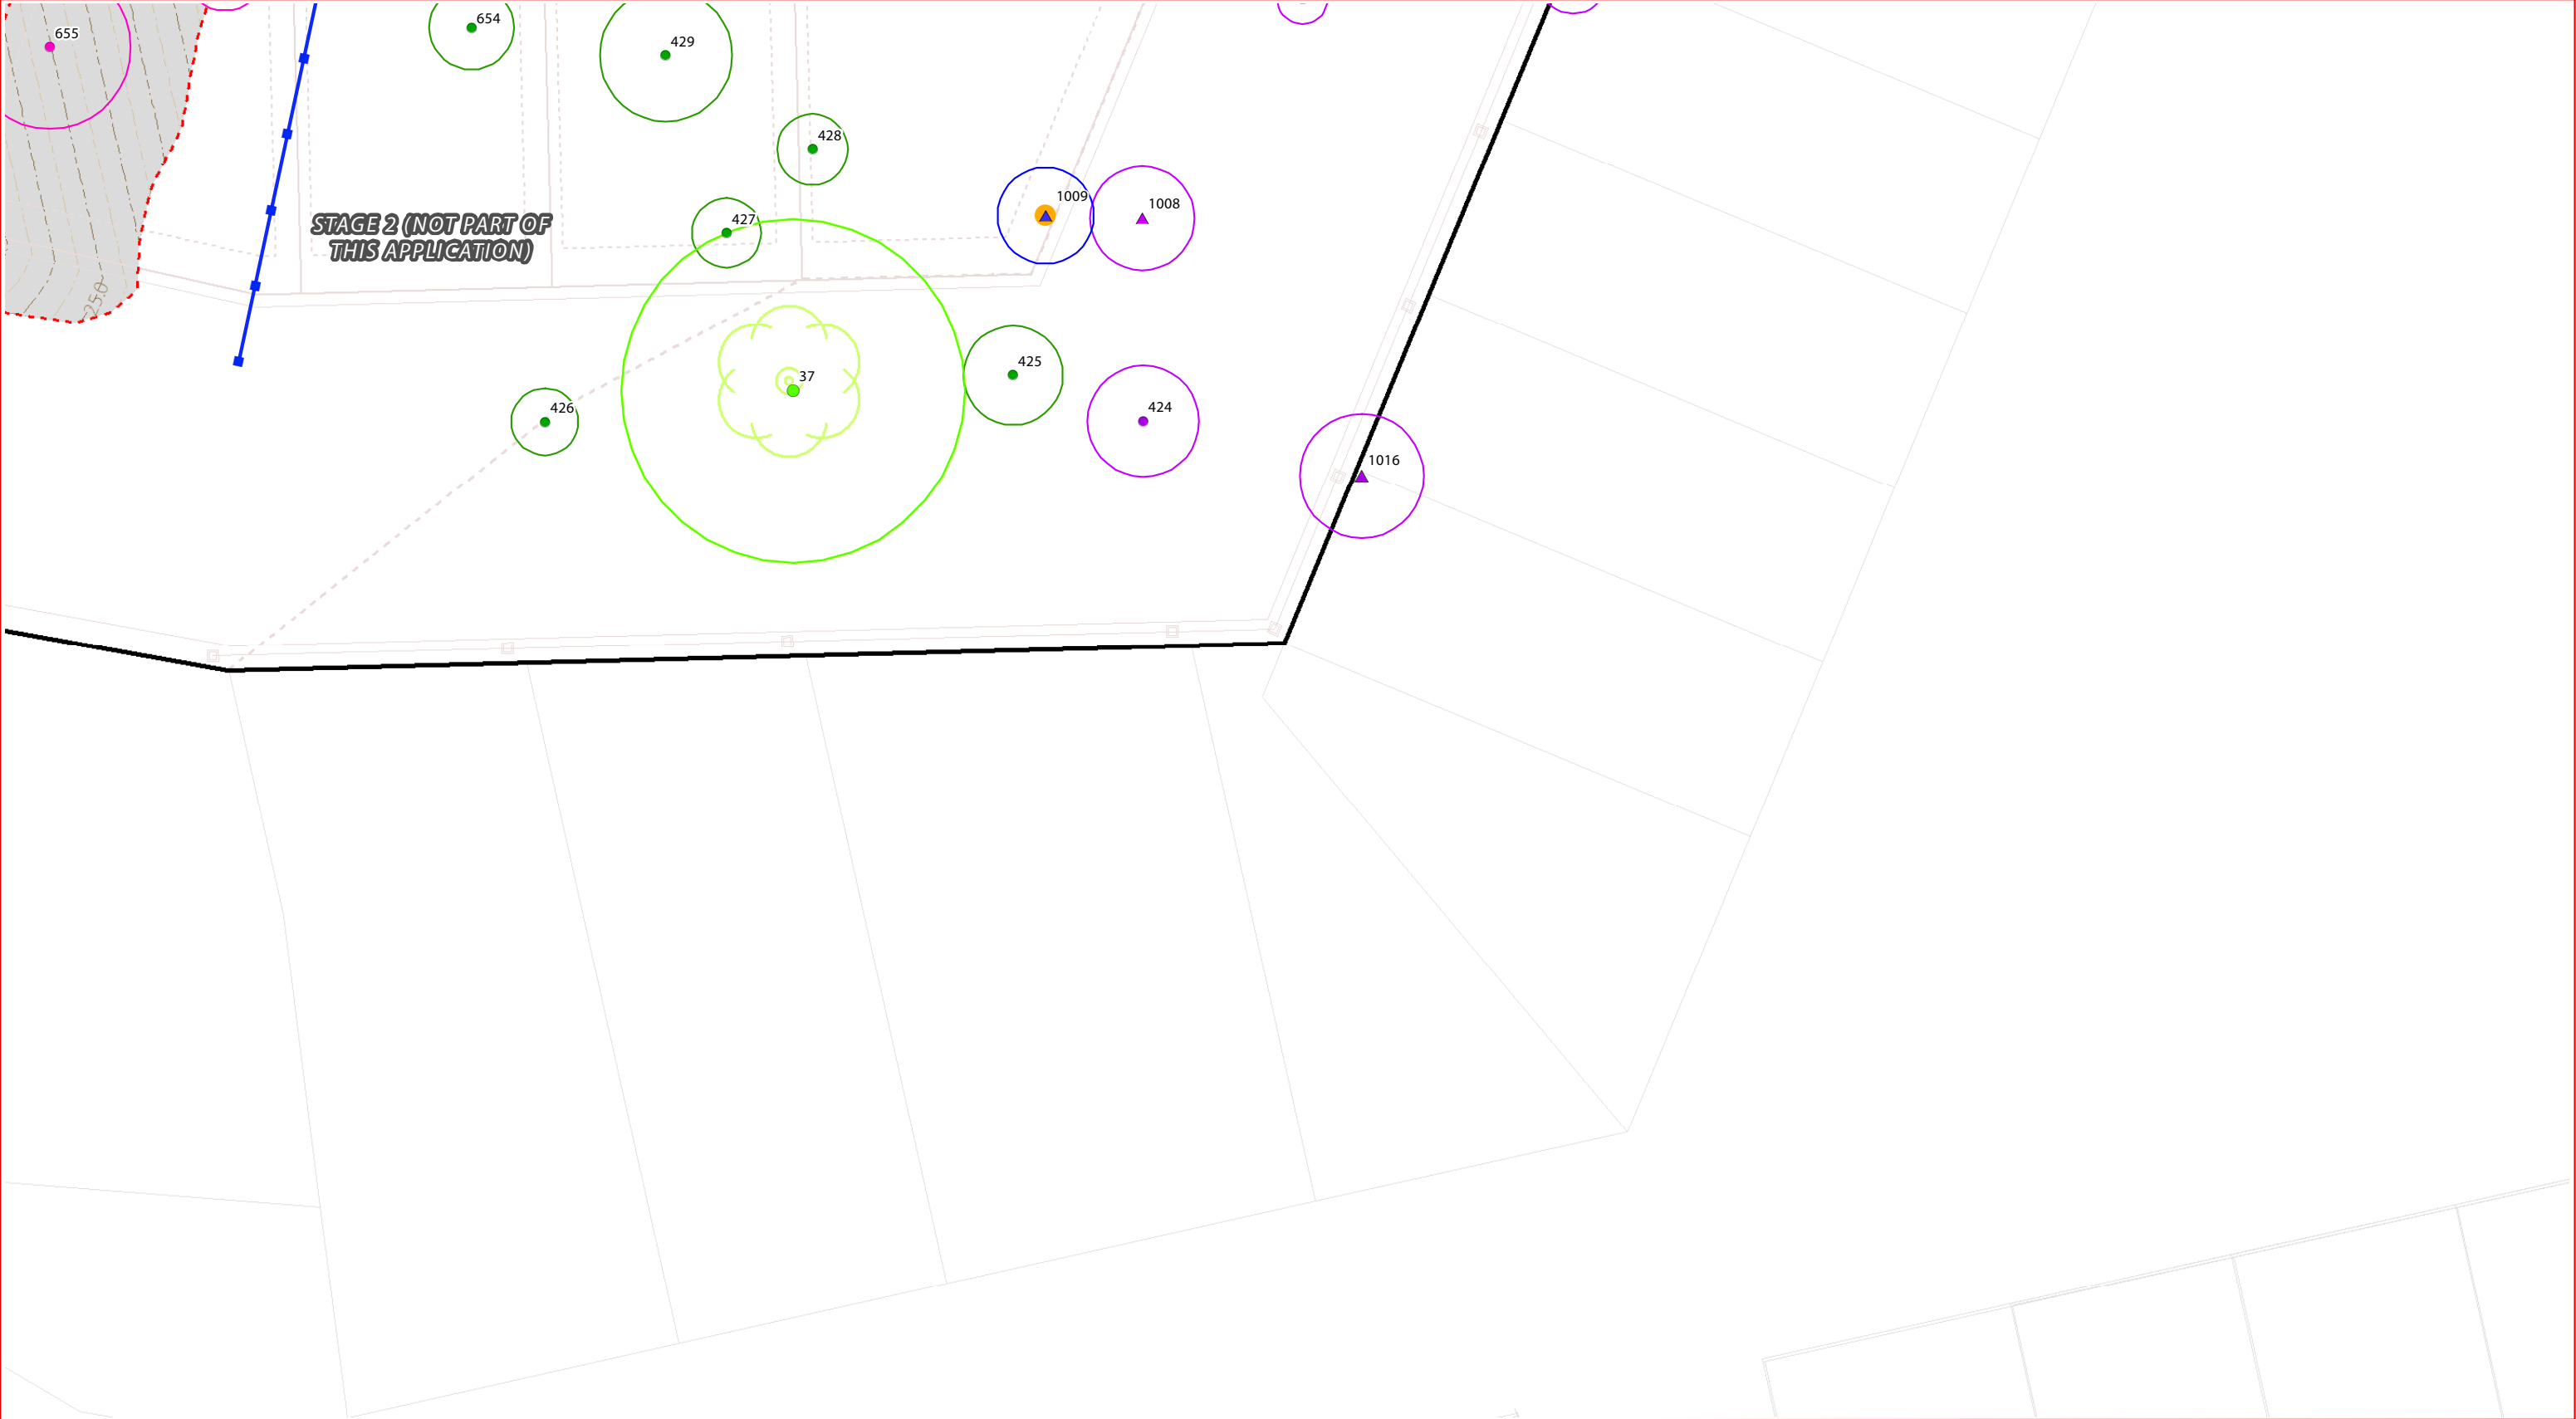

- Native tree to remove during tree clearing for remediation works (w/TPZ)

Weed tree to remove during tree clearing for remediation works (w/TPZ)

Native tree to remove during tree clearing for Stage 1 (w/TPZ)

Weed tree to remove during tree clearing for Stage 1 (w/TPZ)

Native tree to retain during tree clearing for Stage 1 (w/TPZ)

Exotic tree to retain during tree clearing for Stage 1 (w/TPZ)

Significant tree to be retained during tree clearing for Stage 1 (w/TPZ)

Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan (w/TPZ)

Dead tree / stag

Retention during clearing for remediations works subject to works extent / requirements

Project Site

Stage Boundary

Survey / DCDB

Design layout

Easement

Building Envelope

Indicative Bushfire Setback

Batter - Top / Toe

Tree Protection Fence

Scour protection

Retaining wall

Water

Sewer

Stormwater

Electricity

Bio basin

Footpath

Road design

Future stage design

Major design contours

Minor design contours

Extent of cut

Extent of fill

Vegetation stockpile location (indicative)

Vegetation Clearing & Fauna Management Plan - *Detail sheet 17*

saunders havill group

CLIENT:

ECONOMIC DEVELOPMENT QUEENSLAND (EDQ)

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, ERECTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:

Engineering / layout drawings (Butler Partners, KN Group 2020)

AMENDMENTS:

Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG
D	8/06/2020	Update 3	JG
E	22/06/2020	Update 4	JG
F	13/08/2020	Update 5	HS
G	18/09/2020	Update 6 - Approved	JG
H	26/07/2022	Update 7	JG

0 5 10 20 30

m

1:500 @ A3


PROJECT:

STAGE 1 SEVENTEEN MILE ROCKS ROAD OXLEY (600SP236626 / 551SP142916)

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE	26/07/2022	CHECKED:	JG
CLIENT REF:	9216	DRAWN:	MP
DRAWING No.:	9216 E 17 VCFMP H		

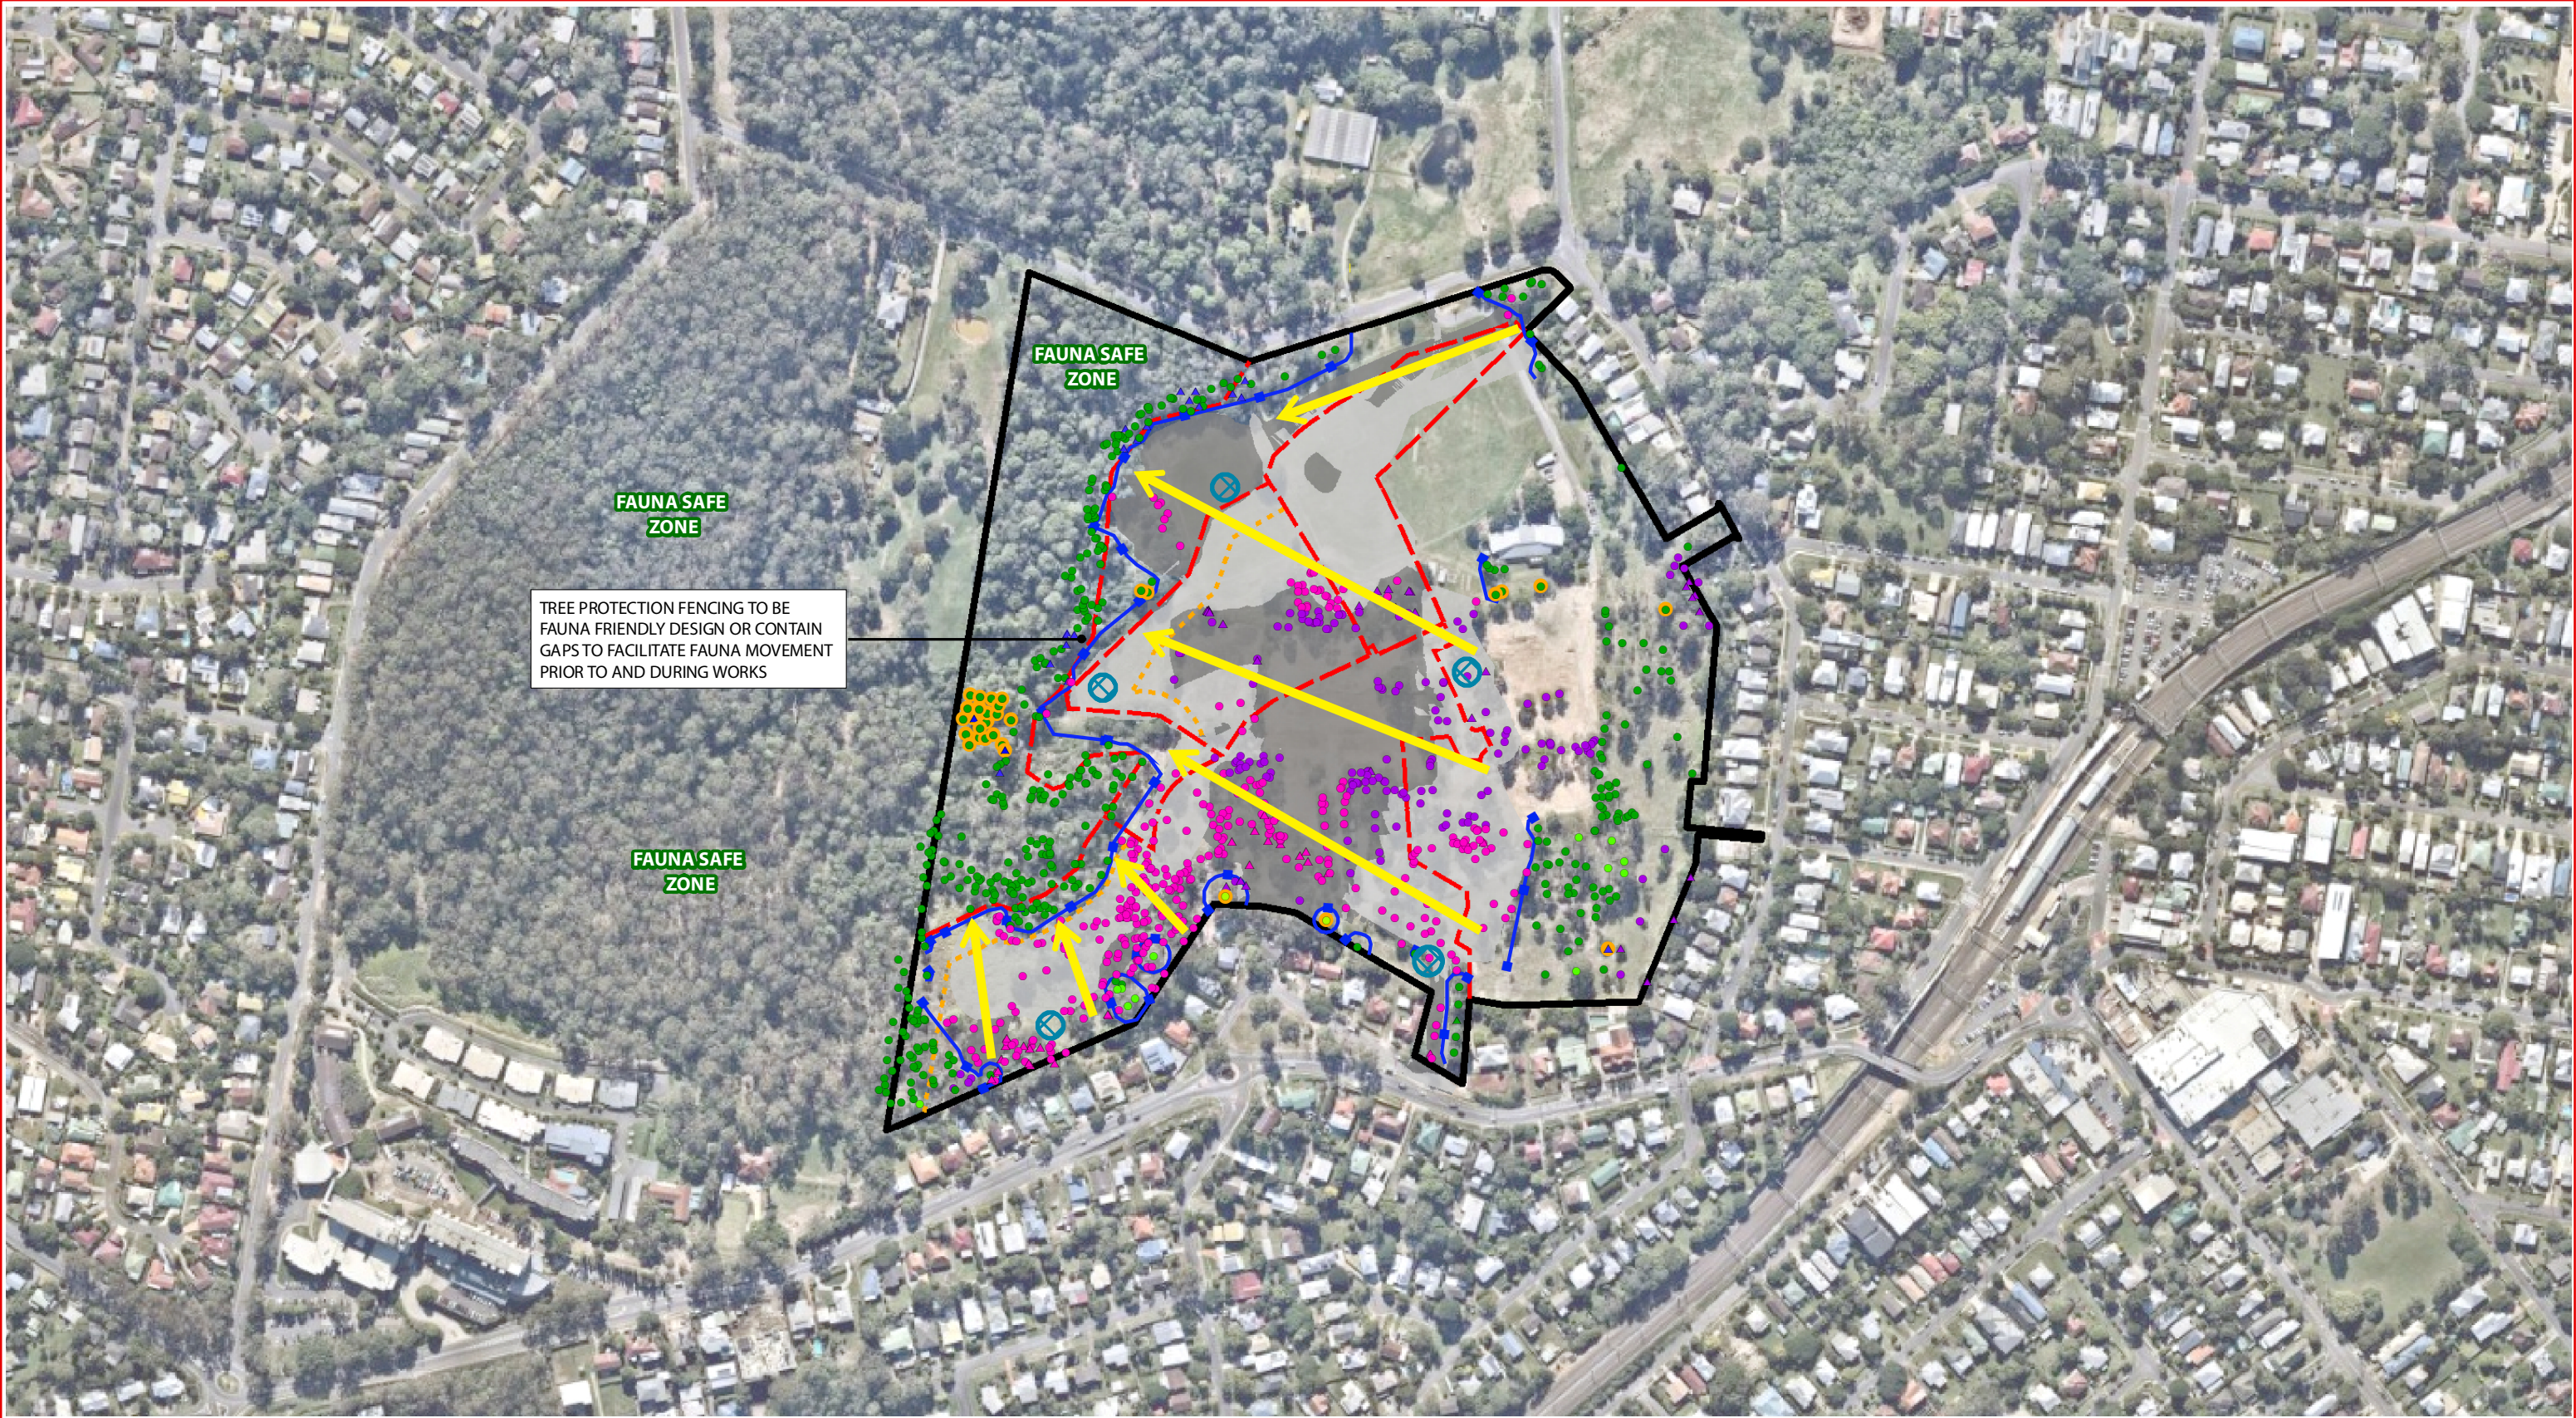

- Native tree to remove during tree clearing for remediation works
- Weed tree to remove during tree clearing for remediation works
- Native tree to remove during tree clearing for Stage 1
- Weed tree to remove during tree clearing for Stage 1
- Native tree status in Bushfire Protection Zone subject to Project Arborist and Bushfire Consultant certification
- Native tree to retain during tree clearing for Stage 1
- Exotic tree to retain during tree clearing for Stage 1
- Significant tree to be retained during tree clearing for Stage 1
- Weed tree in Public Open Space Reserve to be managed as per approved Rehabilitation Management Plan
- Retention during clearing for remediations works subject to works extent / requirements
- Dead tree / stag
- Project Site
- Stage Boundary
- Indicative Bushfire Setback
- Tree Protection Fence
- Extent of cut
- Extent of fill
- Vegetation stockpile location (indicative)
- Vegetation clearing direction

Vegetation Clearing & Fauna Management Plan - *Clearing Direction*



ECONOMIC DEVELOPMENT
QUEENSLAND (EDQ)

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:
Engineering / layout drawings
(Butler Partners, KN Group 2020)



0 25 50 100 150 200 250 300 m 1:4,000 @ A3

AMENDMENTS:	Issue	Date	Description	Checked
C	1/05/2020	Update 2	JG	
D	8/06/2020	Update 3	JG	
E	22/06/2020	Update 4	JG	
F	13/08/2020	Update 5	HS	
G	18/09/2020	Update 6 - Approved	JG	
H	26/07/2022	Update 7	JG	

PROJECT:
STAGE 1
SEVENTEEN MILE ROCKS ROAD
OXLEY
(600SP236626 / 551SP142916)

environmental management	
PLAN OF: Vegetation Clearing & Fauna Management Plan	
DATE: 26/07/2022	CHECKED: JG
CLIENT REF: 9216	DRAWN: MP
DRAWING No.: 9216 E 18 VCFMP H	

Specimen Details										Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
1	<i>Ficus macrophylla</i>	Moreton Bay Fig	580	290, 260	699	12.0	14.0	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
2	<i>Eucalyptus siderophloia</i>	Grey Ironbark	730		730	25.0	14.0	8.8	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
3	<i>Eucalyptus siderophloia</i>	Grey Ironbark	955		955	26.0	10.0	11.5	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
4	<i>Corymbia citriodora</i>	Spotted Gum	810		810	27.0	14.0	9.7	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
5	<i>Corymbia citriodora</i>	Spotted Gum	570		570	27.0	12.0	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
6	<i>Corymbia citriodora</i>	Spotted Gum	570		570	27.0	11.0	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Retain subject to remediation	
7	<i>Flindersia australis</i>	Crows Ash	300		300	11.0	5.0	3.6	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
8	<i>Flindersia australis</i>	Crows Ash	510		510	12.0	7.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
9	<i>Flindersia australis</i>	Crows Ash	295		295	11.0	5.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
10	<i>Jacaranda mimosifolia</i>	Jacaranda	495		495	10.0	16.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
11	<i>Flindersia australis</i>	Crows Ash	440		440	15.0	7.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
12	<i>Flindersia australis</i>	Crows Ash	590		590	17.0	8.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
13	<i>Flindersia australis</i>	Crows Ash	535		535	17.0	7.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
14	<i>Delonix regia</i>	Poinciana	400	325	515	9.0	12.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
15	<i>Flindersia australis</i>	Crows Ash	430	395, 235	629	17.0	9.0	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
16	<i>Flindersia australis</i>	Crows Ash	630		630	18.0	10.0	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
17	<i>Flindersia australis</i>	Crows Ash	495		495	17.0	9.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
18	<i>Flindersia australis</i>	Crows Ash	420		420	18.0	8.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
19	<i>Flindersia australis</i>	Crows Ash	170		170	8.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
20	<i>Flindersia australis</i>	Crows Ash	510		510	14.0	8.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
21	<i>Flindersia australis</i>	Crows Ash	345		345	15.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
22	<i>Flindersia australis</i>	Crows Ash	350		350	13.0	9.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
23	<i>Flindersia australis</i>	Crows Ash	410		410	17.0	9.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
24	<i>Flindersia australis</i>	Crows Ash	175		175	9.0	4.0	2.1	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
25	<i>Flindersia australis</i>	Crows Ash	500		500	16.0	8.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
26	<i>Flindersia australis</i>	Crows Ash	350		350	13.0	7.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
27	<i>Flindersia australis</i>	Crows Ash	275		275	12.0	5.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
28	<i>Flindersia australis</i>	Crows Ash	210		210	8.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
29	<i>Jagera pseudorhus</i>	Foambark Tree	200	160, 135	290	9.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
30	<i>Flindersia australis</i>	Crows Ash	265		265	11.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
31	<i>Flindersia australis</i>	Crows Ash	320		320	11.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
32	<i>Flindersia australis</i>	Crows Ash	200		200	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
33	<i>Flindersia australis</i>	Crows Ash	165		165	9.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
34	<i>Flindersia australis</i>	Crows Ash	185		185	10.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
35	<i>Flindersia australis</i>	Crows Ash	260		260	11.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
36	<i>Flindersia australis</i>	Crows Ash	245		245	11.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
37	<i>Eucalyptus propinqua</i>	Grey Gum	1140		1140	34.0	16.0	13.7	3.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Retain stage 1	
38	<i>Eucalyptus tereticornis</i>	Forest Red Gum	810		810	33.0	12.0	9.7	3.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	

Specimen Details									Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
39	<i>Eucalyptus tereticornis</i>	Forest Red Gum	860		860	27.0	14.0	10.3	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
40	<i>Eucalyptus tereticornis</i>	Forest Red Gum	690		690	27.0	12.0	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
41	<i>Eucalyptus tereticornis</i>	Forest Red Gum	1480		1480	37.0	22.0	15.0	3.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
42	<i>Eucalyptus siderophloia</i>	Grey Ironbark	540	490	729	23.0	11.0	8.8	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
43	<i>Eucalyptus siderophloia</i>	Grey Ironbark	750		750	26.0	14.0	9.0	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Remove remediation works	
44	<i>Grevillea robusta</i>	Silky Oak	520		520	21.0	8.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
45	<i>Eucalyptus microcorys</i>	Tallowwood	505		505	22.0	12.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
46	<i>Eucalyptus siderophloia</i>	Grey Ironbark	765	265	810	27.0	14.0	9.7	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
47	<i>Eucalyptus siderophloia</i>	Grey Ironbark	680		680	29.0	12.0	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Remove Stage 1	
48	<i>Corymbia citriodora</i>	Spotted Gum	1065		1065	34.0	14.0	12.8	3.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
49	<i>Corymbia citriodora</i>	Spotted Gum	525		525	27.0	11.0	6.3	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
50	<i>Corymbia citriodora</i>	Spotted Gum	550		550	30.0	8.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
51	<i>Eucalyptus siderophloia</i>	Grey Ironbark	680		680	34.0	10.0	8.2	2.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
52	<i>Corymbia citriodora</i>	Spotted Gum	820		820	36.0	14.0	9.8	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
53	<i>Corymbia citriodora</i>	Spotted Gum	380		380	32.0	8.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
54	<i>Corymbia citriodora</i>	Spotted Gum	365		365	26.0	9.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
55	<i>Corymbia citriodora</i>	Spotted Gum	365		365	26.0	9.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
56	<i>Corymbia trachyphloia</i>	Brown Bloodwood	260		260	12.0	5.0	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
57	<i>Corymbia citriodora</i>	Spotted Gum	720		720	34.0	14.0	8.6	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
58	<i>Corymbia citriodora</i>	Spotted Gum	580		580	30.0	11.0	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
59	<i>Corymbia citriodora</i>	Spotted Gum	700		700	34.0	14.0	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
60	<i>Corymbia citriodora</i>	Spotted Gum	670		670	32.0	12.0	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
61	<i>Corymbia citriodora</i>	Spotted Gum	550		550	32.0	10.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
62	<i>Eucalyptus grandis</i>	Flooded Gum	790		790	26.0	12.0	9.5	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
63	<i>Corymbia citriodora</i>	Spotted Gum	485		485	25.0	12.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
64	<i>Corymbia citriodora</i>	Spotted Gum	580		580	32.0	12.0	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
65	<i>Corymbia citriodora</i>	Spotted Gum	600		600	32.0	9.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
66	<i>Corymbia citriodora</i>	Spotted Gum	570		570	32.0	12.0	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
67	<i>Corymbia citriodora</i>	Spotted Gum	485		485	25.0	11.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
68	<i>Eucalyptus siderophloia</i>	Grey Ironbark	960		960	36.0	16.0	11.5	3.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
69	<i>Lophostemon confertus</i>	Brush Box	530		530	17.0	12.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
70	<i>Eucalyptus siderophloia</i>	Grey Ironbark	820	540	982	34.0	12.0	11.8	3.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain stage 1	
71	<i>Eucalyptus siderophloia</i>	Grey Ironbark	575		575	32.0	12.0	6.9	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
72	<i>Eucalyptus siderophloia</i>	Grey Ironbark	670		670	29.0	14.0	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
73	<i>Eucalyptus siderophloia</i>	Grey Ironbark	530		530	28.0	12.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
74	<i>Corymbia citriodora</i>	Spotted Gum	575		575	28.0	12.0	6.9	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
75	<i>Lophostemon confertus</i>	Brush Box	590		590	16.0	10.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
76	<i>Eucalyptus moluccana</i>	Gum Topped Box	240		240	16.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
77	<i>Eucalyptus moluccana</i>	Gum Topped Box	670		670	26.0	12.0	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
78	<i>Celtis sinensis</i>	Chinese Elm	165		165	10.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP (remediation)	
79	<i>Celtis sinensis</i>	Chinese Elm	180		180	10.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
80	<i>Acacia disparrima</i>	Hickory Wattle	265		265	10.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
81	<i>Alphitonia excelsa</i>	Soap Tree	140		140	11.0	4.0	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
82	<i>Acacia disparrima</i>	Hickory Wattle	240		240	11.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
83	<i>Celtis sinensis</i>	Chinese Elm	155		155	9.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
84	<i>Lophostemon confertus</i>	Brush Box	620		620	15.0	8.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
85	<i>Lophostemon confertus</i>	Brush Box	420		420	16.0	7.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
86	<i>Lophostemon confertus</i>	Brush Box	445		445	16.0	6.0	5.3	2.4	Regular	-																		

Specimen Details									Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
88	<i>Eucalyptus siderophloia</i>	Grey Ironbark	260		260	16.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
89	<i>Acacia disparrima</i>	Hickory Wattle	160		160	11.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
90	<i>Lophostemon confertus</i>	Brush Box	150		150	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
91	<i>Eucalyptus siderophloia</i>	Grey Ironbark	250		250	14.0	5.0	3.0	1.8	One-sided	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
92	<i>Eucalyptus siderophloia</i>	Grey Ironbark	460		460	22.0	7.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
93	<i>Eucalyptus siderophloia</i>	Grey Ironbark	465		465	23.0	7.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
94	<i>Commersonia bartramia</i>	Brown Kurrajong	220	140, 130, 130	319	11.0	6.0	3.8	2.0	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
95	<i>Lophostemon confertus</i>	Brush Box	165		165	11.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
96	<i>Eucalyptus siderophloia</i>	Grey Ironbark	235		235	22.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
97	<i>Auranticarpa rhombifolia</i>	Pittosporum	130		130	11.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
98	<i>Eucalyptus siderophloia</i>	Grey Ironbark	245		245	18.0	5.0	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
99	<i>Jagera pseudorhus</i>	Foambark Tree	180		180	11.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
100	<i>Eucalyptus siderophloia</i>	Grey Ironbark	495		495	23.0	14.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Retain stage 1	
101	<i>Glochidion ferdinandi</i>	Cheese Tree	265		265	10.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
102	<i>Jagera pseudorhus</i>	Foambark Tree	125		125	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
103	<i>Acacia disparrima</i>	Hickory Wattle	235		235	10.0	5.0	2.8	1.8	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
104	<i>Lophostemon confertus</i>	Brush Box	580	400	705	20.0	14.0	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
105	<i>Commersonia bartramia</i>	Brown Kurrajong	125		125	7.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
106	<i>Acacia disparrima</i>	Hickory Wattle	220		220	12.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
107	<i>Eucalyptus siderophloia</i>	Grey Ironbark	310		310	13.0	4.0	3.7	2.0	Regular	-	-	-	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
108	<i>Jagera pseudorhus</i>	Foambark Tree	125		125	9.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
109	<i>Alphitonia excelsa</i>	Soap Tree	130		130	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
110	<i>Acacia leiocalyx</i>	Early Flowering Black Wattle	185		185	9.0	5.0	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
111	<i>Eucalyptus siderophloia</i>	Grey Ironbark	440		440	23.0	10.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Retain stage 1	
112	<i>Eucalyptus siderophloia</i>	Grey Ironbark	510		510	24.0	11.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
113	<i>Eucalyptus siderophloia</i>	Grey Ironbark	270		270	23.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
114	<i>Lophostemon confertus</i>	Brush Box	365		365	17.0	7.0	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
115	<i>Commersonia bartramia</i>	Brown Kurrajong	160	165	230	9.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
116	<i>Alphitonia excelsa</i>	Soap Tree	150		150	9.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
117	<i>Eucalyptus siderophloia</i>	Grey Ironbark	500		500	27.0	14.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Retain stage 1	
118	<i>Eucalyptus siderophloia</i>	Grey Ironbark	240	140	278	17.0	6.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
119	<i>Eucalyptus siderophloia</i>	Grey Ironbark	465		465	23.0	9.0	5.6	2.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
120	DEAD/STAG		620	620	877	17.0	7.0	10.5	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-	Retain stage 1	
121	<i>Eucalyptus siderophloia</i>	Grey Ironbark	165		165	12.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
122	<i>Eucalyptus siderophloia</i>	Grey Ironbark	165		165	12.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
123	<i>Eucalyptus siderophloia</i>	Grey Ironbark	620		620	23.0	14.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
124	<i>Eucalyptus siderophloia</i>	Grey Ironbark	390		390	17.0	8.0	4.7	2.2	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
125	<i>Eucalyptus siderophloia</i>	Grey Ironbark	480		480	18.0	9.0	5.8	2.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
126	<i>Eucalyptus siderophloia</i>	Grey Ironbark	270		270	17.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
127	<i>Eucalyptus siderophloia</i>	Grey Ironbark	230		230	16.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
128	<i>Acacia disparrima</i>	Hickory Wattle	390		390	12.0	8.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
129	<i>Glochidion ferdinandi</i>	Cheese Tree	160	120, 100	224	9.0	5.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
130	<i>Lophostemon suaveolens</i>	Swmap Box	210		210	11.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
131	<i>Alphitonia excelsa</i>	Soap Tree	165		165	8.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
132	<i>Alphitonia excelsa</i>	Soap Tree	150		150	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
133	<i>Flindersia schottiana</i>	Bumpy Ash	650		650	22.0	11.0	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
134	<i>Alphitonia excelsa</i>	Soap Tree	220		220	12.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-			

Specimen Details									Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
137	<i>Alphitonia excelsa</i>	Soap Tree	200		200	11.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
138	<i>Acacia disparrima</i>	Hickory Wattle	240		240	13.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	Both	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
139	<i>Acacia disparrima</i>	Hickory Wattle	240		240	12.0	4.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
140	<i>Acacia disparrima</i>	Hickory Wattle	185		185	11.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
141	<i>Acacia disparrima</i>	Hickory Wattle	165		165	12.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
142	<i>Acacia disparrima</i>	Hickory Wattle	205		205	11.0	2.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
143	<i>Corymbia torelliana</i>	Cadaghi	270		270	13.0	5.0	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
144	<i>Lophostemon confertus</i>	Swamp Box	760		760	20.0	8.0	9.1	2.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
145	<i>Jagera pseudorhus</i>	Foambark Tree	180	140, 125, 140	295	11.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
146	<i>Corymbia torelliana</i>	Cadaghi	210		210	9.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
147	<i>Lophostemon confertus</i>	Brush Box	210		210	12.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
148	<i>Lophostemon confertus</i>	Brush Box	200		200	10.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
149	<i>Acacia disparrima</i>	Hickory Wattle	260		260	12.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
150	<i>Auranticarpa rhombifolia</i>	Pittosporum	370	120	389	16.0	7.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
151	<i>Schinus terebinthifolius</i>	Broadleaved Pepper Tree	240	120	268	8.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
152	<i>Corymbia torelliana</i>	Cadaghi	150		150	11.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
153	<i>Corymbia torelliana</i>	Cadaghi	130		130	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
154	<i>Corymbia torelliana</i>	Cadaghi	330		330	16.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
155	<i>Lophostemon confertus</i>	Brush Box	640		640	17.0	8.0	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
156	<i>Acacia leiocalyx</i>	Early Flowering Black Wattle	125		125	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
157	<i>Acacia disparrima</i>	Hickory Wattle	235		235	12.0	4.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
158	<i>Acacia disparrima</i>	Hickory Wattle	220		220	12.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
159	<i>Acacia leiocalyx</i>	Early Flowering Black Wattle	180		180	11.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
160	<i>Lophostemon confertus</i>	Brush Box	260		260	14.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
161	<i>Lophostemon confertus</i>	Brush Box	360		360	15.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
162	<i>Acacia leiocalyx</i>	Early Flowering Black Wattle	160		160	11.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
163	<i>Stenocarpus sinuatus</i>	Wheel of Fire	160		160	11.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
164	<i>Auranticarpa rhombifolia</i>	Pittosporum	165	110, 90	218	11.0	5.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
165	<i>Acacia disparrima</i>	Hickory Wattle	340		340	12.0	6.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
166	<i>Jagera pseudorhus</i>	Foambark Tree	230	230	325	13.0	6.0	3.9	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
167	<i>Mallotus philippensis</i>	Red Kamala	135		135	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
168	<i>Auranticarpa rhombifolia</i>	Pittosporum	200		200	12.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
169	<i>Lophostemon confertus</i>	Brush Box	570		570	17.0	8.0	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
170	<i>Lophostemon confertus</i>	Brush Box	460	120, 140, 130	512	12.0	5.0	6.1	2.5	Regular	-	-	-	-	Lopped	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-	Retain stage 1	
171	<i>Lophostemon confertus</i>	Brush Box	465		465	17.0	8.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
172	<i>Lophostemon confertus</i>	Brush Box	450		450	20.0	6.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
173	<i>Lophostemon confertus</i>	Brush Box	380	150, 100, 130	440	16.0	5.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
174	<i>Auranticarpa rhombifolia</i>	Pittosporum	200		200	9.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
175	<i>Acacia leiocalyx</i>	Early Flowering Black Wattle	195		195	9.0	5.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
176	<i>Acacia disparrima</i>	Hickory Wattle	250		250	13.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
177	<i>Acacia disparrima</i>	Hickory Wattle	220	130	256	13.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
178	<i>Acacia disparrima</i>	Hickory Wattle	180	160	241	12.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
179	<i>Acacia disparrima</i>	Hickory Wattle	155	135, 80	221	11.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
180	<i>Acacia disparrima</i>	Hickory Wattle	195		195	12.0	4.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
181	<i>Acacia disparrima</i>	Hickory Wattle	210	170, 200	336	11.0	5.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
182	<i>Acacia disparrima</i>	Hickory Wattle	200	180	269	12.0	3.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
183	<i>Acacia disparrima</i>	Hickory Wattle	230	190, 230, 250	452	12.0	6.0	5.4	2.4	Regular	-	-	-	-	-	Typ													

Specimen Details									Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
186	<i>Alphitonia excelsa</i>	Soap Tree	165		165	12.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
187	<i>Alphitonia excelsa</i>	Soap Tree	210		210	10.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
188	<i>Alphitonia excelsa</i>	Soap Tree	165		165	10.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
189	<i>Alphitonia excelsa</i>	Soap Tree	145		145	9.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
190	<i>Alphitonia excelsa</i>	Soap Tree	130		130	9.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
191	<i>Alphitonia excelsa</i>	Soap Tree	130		130	9.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
192	<i>Alphitonia excelsa</i>	Soap Tree	140		140	9.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
193	<i>Alphitonia excelsa</i>	Soap Tree	160		160	10.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
194	<i>Alphitonia excelsa</i>	Soap Tree	180		180	10.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
195	<i>Alphitonia excelsa</i>	Soap Tree	220		220	11.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
196	<i>Lophostemon confertus</i>	Brush Box	230	230	325	17.0	8.0	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
197	<i>Alphitonia excelsa</i>	Soap Tree	160		160	9.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
198	<i>Acacia disparrima</i>	Hickory Wattle	170		170	11.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
199	<i>Acacia disparrima</i>	Hickory Wattle	340		340	15.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
200	<i>Acacia disparrima</i>	Hickory Wattle	230		230	12.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
201	<i>Acacia disparrima</i>	Hickory Wattle	270		270	12.0	3.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Remove Stage 1	
202	<i>Acacia disparrima</i>	Hickory Wattle	230	200, 180	354	12.0	5.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
203	<i>Acacia disparrima</i>	Hickory Wattle	280		280	11.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
204	<i>Alphitonia excelsa</i>	Soap Tree	145		145	11.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
205	<i>Acacia disparrima</i>	Hickory Wattle	270		270	12.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
206	<i>Lophostemon suaveolens</i>	Swamp Box	145		145	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
207	<i>Alphitonia excelsa</i>	Soap Tree	130		130	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
208	<i>Corymbia torelliana</i>	Cadaghi	150		150	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
209	<i>Acacia disparrima</i>	Hickory Wattle	310		310	11.0	6.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
210	<i>Angophora leiocarpa</i>	Early Flowering Black Wattle	230		230	16.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
211	<i>Corymbia citriodora</i>	Spotted Gum	130		130	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
212	<i>Alphitonia excelsa</i>	Soap Tree	160		160	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
213	<i>Acacia disparrima</i>	Hickory Wattle	160		160	11.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
214	<i>Corymbia torelliana</i>	Cadaghi	210		210	12.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
215	<i>Acacia disparrima</i>	Hickory Wattle	140		140	9.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
216	<i>Corymbia torelliana</i>	Cadaghi	185		185	10.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
217	<i>Acacia disparrima</i>	Hickory Wattle	230		230	11.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
218	<i>Lophostemon confertus</i>	Brush Box	290		290	12.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
219	<i>Corymbia torelliana</i>	Cadaghi	230		230	10.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
220	<i>Alphitonia excelsa</i>	Soap Tree	130		130	9.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
221	<i>Lophostemon confertus</i>	Brush Box	120		120	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
222	<i>Acacia disparrima</i>	Hickory Wattle	270		270	12.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
223	<i>Lophostemon confertus</i>	Brush Box	210		210	12.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
224	<i>Alphitonia excelsa</i>	Soap Tree	130		130	9.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
225	<i>Lophostemon confertus</i>	Brush Box	135		135	9.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
226	<i>Acacia disparrima</i>	Hickory Wattle	330	280	433	10.0	6.0	5.2	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
227	<i>Eucalyptus tereticornis</i>	Forest Red Gum	680		680	22.0	9.0	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
228	<i>Eucalyptus tereticornis</i>	Forest Red Gum	530		530	17.0	8.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
229	<i>Eucalyptus tereticornis</i>	Forest Red Gum	620		620	23.0	12.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
230	<i>Eucalyptus siderophloia</i>	Grey Ironbark	355		355	19.0	10.0	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Retain stage 1	
231	<i>Corymbia torelliana</i>	Cadaghi	165		165	10.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
232	<i>Acacia disparrima</i>	Hickory Wattle	180		180	11.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
233	<i>Alphitonia excelsa</i>	Soap Tree	145		145	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
234	<																												

Specimen Details									Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value							
235	<i>Corymbia torelliana</i>	Cadaghi	265		265	13.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Weed tree - refer RMP	
236	<i>Alphitonia excelsa</i>	Soap Tree	145		145	10.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
237	<i>Acacia disparrima</i>	Hickory Wattle	280	180, 200, 160, 130	440	12.0	7.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
238	<i>Alphitonia excelsa</i>	Soap Tree	155		155	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
239	<i>Acacia disparrima</i>	Hickory Wattle	240		240	10.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
240	<i>Corymbia torelliana</i>	Cadaghi	240		240	13.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Weed tree - refer RMP	
241	<i>Lophostemon suaveolens</i>	Swamp Box	165		165	11.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
242	<i>Corymbia torelliana</i>	Cadaghi	260		260	11.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Weed tree - refer RMP	
243	<i>Corymbia torelliana</i>	Cadaghi	145		145	10.0	1.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Weed tree - refer RMP	
244	<i>Corymbia torelliana</i>	Cadaghi	350		350	14.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Weed tree - refer RMP	
245	<i>Lophostemon confertus</i>	Brush Box	185		185	10.0	4.0	2.2	1.6	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
246	<i>Lophostemon suaveolens</i>	Swamp Box	145		145	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
247	<i>Acacia disparrima</i>	Hickory Wattle	260		260	10.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
248	<i>Lophostemon confertus</i>	Brush Box	150		150	10.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	
249	<i>Acacia disparrima</i>	Hickory Wattle	260		260	11.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	Retain stage 1	

Tree Schedule - Job 9216 53 Seventeen Mile Rocks Road, Oxley (The Minister for Economic Development Queensland) 25/08/2020																																
Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value									
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes		
250	Melaleuca bracteata	Black Tea Tree	340		340	107	9.0	6.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	Remove remediation works		
251	Acacia disparrima	Hickory Wattle	340		340	107	6.0	4.0	4.1	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	-	Typical	-	-	-	-	-	-	-	Remove remediation works	
252	Casuarina cunninghamiana	River She-oak	230	200	305	96	12.0	4.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
253	Eucalyptus microcorys	Tallowwood	400		400	126	22.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
254	Eucalyptus propinqua	Northern Grey Gum	340	320	467	147	24.0	10.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	-	-	Remove remediation works	
255	Melaleuca leucadendra	Weeping Paperbark	350		350	110	10.0	7.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
256	Melaleuca quinquenervia	Broad-leaf Paperbark	420	400, 280	644	202	16.0	8.0	7.7	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
257	Eucalyptus saligna	Sydney Blue Gum	340		340	107	20.0	8.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
258	Corymbia torelliana	Cadaghi	380		380	119	20.0	12.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
259	Eucalyptus propinqua	Northern Grey Gum	400		400	126	22.0	10.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
260	Grevillea robusta	Silky Oak	330		330	104	16.0	8.0	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
261	Eucalyptus microcorys	Tallowwood	500		500	157	22.0	12.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
262	Eucalyptus propinqua	Northern Grey Gum	520		520	163	24.0	12.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	-	-	Remove remediation works	
263	Eucalyptus microcorys	Tallowwood	820		820	258	22.0	14.0	9.8	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
264	Melaleuca viminalis	Weeping Bottlebrush	240	190	306	96	8.0	4.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
265	Lophostemon confertus	Brush Box	160		160	50	7.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
266	Melaleuca linariifolia	Snow In Summer	220	130, 110	278	87	4.0	3.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
267	Brachychiton acerifolius	Illawara Flame Tree	180		180	57	6.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
268	Eucalyptus microcorys	Tallowwood	150		150	47	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
269	Brachychiton acerifolius	Illawara Flame Tree	200		200	63	6.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
270	Lophostemon confertus	Brush Box	320		320	101	8.0	5.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
271	Euodia elleryana	Corkwood	160		160	50	9.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
272	Eucalyptus microcorys	Tallowwood	540		540	170	26.0	14.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
273	Acacia concurrens	Black Wattle	180		180	57	6.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
274	Eucalyptus siderophloia	Grey Ironbark	490		490	154	24.0	12.0	5.9	2.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
275	Acacia concurrens	Black Wattle	170		170	53	5.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
276	Eucalyptus siderophloia	Grey Ironbark	130		130	41	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
277	Lophostemon confertus	Brush Box	350		350	110	6.0	4.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
278	Acacia concurrens	Black Wattle	170		170	53	6.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
279	Acacia concurrens	Black Wattle	160		160	50	6.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove remediation works	
280	Alphitonia excelsa	Soap Tree	180		180	57	12.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Retain stage 1	
281	Lophostemon confertus	Brush Box	200		200	63	10.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
282	Lophostemon confertus	Brush Box	220		220	69	14.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
283	Lophostemon confertus	Brush Box	150		150	47	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
284	Alphitonia excelsa	Soap Tree	150		150	47	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
285	Lophostemon confertus	Brush Box	430	300, 240, 150	596	187	22.0	12.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
286	Mallotus philippensis	Red Kamala	100		100	31	5.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Remove stage 1	
287	Alphitonia excelsa	Soap Tree	180		180	57	12.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	-	-	Retain stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
288	Acacia disparrima	Hickory Wattle	280	130	309	97	14.0	8.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
289	Alphitonia excelsa	Soap Tree	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
290	Alphitonia excelsa	Soap Tree	130		130	41	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
291	Acacia disparrima	Hickory Wattle	200		200	63	10.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
292	Alphitonia excelsa	Soap Tree	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
293	Acacia disparrima	Hickory Wattle	200		200	63	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
294	Alphitonia excelsa	Soap Tree	200		200	63	8.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
295	Alphitonia excelsa	Soap Tree	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
296	Eucalyptus siderophloia	Grey Ironbark	390		390	123	24.0	14.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
297	Acacia disparrima	Hickory Wattle	300		300	94	10.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
298	Alphitonia excelsa	Soap Tree	120		120	38	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
299	Acacia disparrima	Hickory Wattle	220		220	69	12.0	4.0	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
300	Alphitonia excelsa	Soap Tree	120		120	38	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
301	Acacia disparrima	Hickory Wattle	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
302	Alphitonia excelsa	Soap Tree	120		120	38	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
303	Alphitonia excelsa	Soap Tree	120		120	38	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
304	Eucalyptus siderophloia	Grey Ironbark	290		290	91	20.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
305	Acacia disparrima	Hickory Wattle	180		180	57	14.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
306	Cryptocarya glaucescens	Jackwood	130		130	41	6.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
307	Cryptocarya glaucescens	Jackwood	120		120	38	4.0	2.0	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
308	Mallotus philippensis	Red Kamala	120	70	139	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
309	Mallotus philippensis	Red Kamala	110	110	156	49	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
310	Cryptocarya glaucescens	Jackwood	100		100	31	8.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
311	Eucalyptus siderophloia	Grey Ironbark	480		480	151	28.0	17.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
312	Acacia disparrima	Hickory Wattle	220		220	69	12.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
313	Eucalyptus siderophloia	Grey Ironbark	420	140	443	139	26.0	14.0	5.3	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
314	Grevillea robusta	Silky Oak	170		170	53	16.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
315	Acacia disparrima	Hickory Wattle	230		230	72	12.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
316	Eucalyptus siderophloia	Grey Ironbark	200		200	63	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
317	Eucalyptus siderophloia	Grey Ironbark	180		180	57	12.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
318	Eucalyptus siderophloia	Grey Ironbark	370		370	116	22.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
319	Jagera pseudorhus	Foam Bark	120	90, 80	170	53	8.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
320	Acacia disparrima	Hickory Wattle	180		180	57	6.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
321	Jagera pseudorhus	Foam Bark	250	130	282	89	8.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
322	Eucalyptus siderophloia	Grey Ironbark	280	190	338	106	24.0	8.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
323	Lophostemon confertus	Brush Box	130		130	41	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
324	Lophostemon confertus	Brush Box	130	130	184	58	14.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
325	Acacia disparrima	Hickory Wattle	210		210	66	16.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
326	Lophostemon confertus	Brush Box	380		380	119	20.0	12.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
327	Alphitonia excelsa	Soap Tree	300		300	94	12.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
328	Alphitonia excelsa	Soap Tree	170		170	53	10.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
329	Corymbia torelliana	Cadaghi	170		170	53	12.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP (remediation)		

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
330	Cryptocarya glaucescens	Jackwood	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
331	Acacia disparrima	Hickory Wattle	140		140	44	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
332	Eucalyptus tereticornis	Forest Red Gum	280		280	88	18.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
333	Lophostemon confertus	Brush Box	140		140	44	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	Both	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
334	Lophostemon confertus	Brush Box	150		150	47	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
335	Alphitonia excelsa	Soap Tree	120		120	38	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
336	Lophostemon confertus	Brush Box	370		370	116	22.0	10.0	4.4	2.2	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
337	Lophostemon confertus	Brush Box	230		230	72	20.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
338	Lophostemon confertus	Brush Box	380	330, 260	566	178	22.0	12.0	6.8	2.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
339	Alphitonia excelsa	Soap Tree	100		100	31	8.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
340	Lophostemon confertus	Brush Box	390		390	123	24.0	12.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
341	Polyscias elegans	Celerywood	170		170	53	12.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
342	Syzygium australe	Brush Cherry	480		480	151	14.0	8.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
343	Acacia disparrima	Hickory Wattle	200		200	63	8.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
344	Lophostemon confertus	Brush Box	200		200	63	12.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
345	Alphitonia excelsa	Soap Tree	150	120, 120	226	71	8.0	5.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
346	Commersonia bartramia	Brown Kurrajong	110	110	156	49	8.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
347	Acacia disparrima	Hickory Wattle	250		250	79	6.0	3.0	3.0	1.8	One-sided	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
348	Alphitonia excelsa	Soap Tree	170	130	214	67	8.0	4.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
349	Mallotus philippensis	Red Kamala	140	120, 120	220	69	8.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
350	Lophostemon confertus	Brush Box	370		370	116	18.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
351	Lophostemon confertus	Brush Box	190		190	60	12.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
352	Acacia disparrima	Hickory Wattle	150		150	47	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
353	Lophostemon confertus	Brush Box	130		130	41	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
354	Eucalyptus cloeziana	Gympie Messmate	190		190	60	12.0	2.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
355	Lophostemon confertus	Brush Box	120		120	38	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
356	Jagera pseudorhus	Foam Bark	110	80	136	43	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
357	Lophostemon confertus	Brush Box	250		250	79	12.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
358	Corymbia citriodora	Spotted Gum	270		270	85	24.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
359	Lophostemon confertus	Brush Box	180		180	57	14.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
360	Lophostemon confertus	Brush Box	110		110	35	8.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
361	Corymbia citriodora	Spotted Gum	220		220	69	22.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
362	Lophostemon confertus	Brush Box	130		130	41	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove stage 1		
363	Lophostemon confertus	Brush Box	340		340	107	20.0	10.0	4.1	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
364	Corymbia citriodora	Spotted Gum	400		400	126	28.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
365	Lophostemon confertus	Brush Box	120		120	38	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
366	Lophostemon confertus	Brush Box	120		120	38	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
367	Acacia disparrima	Hickory Wattle	130		130	41	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
368	Lophostemon confertus	Brush Box	330	300	446	140	24.0	12.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
369	Lophostemon suaveolens	Swamp Box	160	100	189	59	10.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
370	Lophostemon confertus	Brush Box	290		290	91	22.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
371	Lophostemon confertus	Brush Box	280		280	88	24.0	10.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
372	<i>Alphitonia excelsa</i>	Soap Tree	210		210	66	8.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
373	<i>Lophostemon confertus</i>	Brush Box	320		320	101	20.0	8.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
374	<i>Eucalyptus siderophloia</i>	Grey Ironbark	250		250	79	20.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
375	<i>Lophostemon confertus</i>	Brush Box	440	430	615	193	22.0	16.0	7.4	2.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
376	<i>Eucalyptus siderophloia</i>	Grey Ironbark	120		120	38	10.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
377	<i>Eucalyptus siderophloia</i>	Grey Ironbark	240	150	283	89	18.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
378	<i>Eucalyptus siderophloia</i>	Grey Ironbark	200		200	63	20.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
379	<i>Eucalyptus siderophloia</i>	Grey Ironbark	230		230	72	20.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
380	<i>Eucalyptus siderophloia</i>	Grey Ironbark	170		170	53	22.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
381	<i>Eucalyptus siderophloia</i>	Grey Ironbark	290		290	91	24.0	12.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
382	<i>Eucalyptus siderophloia</i>	Grey Ironbark	160		160	50	16.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
383	<i>Eucalyptus siderophloia</i>	Grey Ironbark	260		260	82	16.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
384	<i>Acacia disparrima</i>	Hickory Wattle	150	150, 110	239	75	8.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
385	<i>Eucalyptus siderophloia</i>	Grey Ironbark	180		180	57	16.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
386	<i>Acacia disparrima</i>	Hickory Wattle	240		240	75	4.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
387	<i>Eucalyptus siderophloia</i>	Grey Ironbark	370	300	476	150	24.0	12.0	5.7	2.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
388	<i>Eucalyptus siderophloia</i>	Grey Ironbark	270		270	85	18.0	8.0	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
389	<i>Alphitonia excelsa</i>	Soap Tree	160	150	219	69	8.0	4.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
390	<i>Lophostemon confertus</i>	Brush Box	230	140	269	85	8.0	4.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
391	<i>Alphitonia excelsa</i>	Soap Tree	140		140	44	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
392	<i>Pongamia pinnata</i>	long petiole round leaf	160	160	226	71	8.0	6.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
393	<i>Grevillea robusta</i>	Silky Oak	550		550	173	22.0	8.0	6.6	2.6	Regular	-	-	Die-back	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
394	<i>Eucalyptus siderophloia</i>	Grey Ironbark	520		520	163	24.0	14.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
395	<i>Eucalyptus siderophloia</i>	Grey Ironbark	340		340	107	22.0	8.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
396	<i>Eucalyptus siderophloia</i>	Grey Ironbark	320	270	419	132	24.0	8.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
397	<i>Eucalyptus siderophloia</i>	Grey Ironbark	440	230	496	156	24.0	12.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
398	<i>Eucalyptus siderophloia</i>	Grey Ironbark	540		540	170	24.0	14.0	6.5	2.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
399	<i>Alphitonia excelsa</i>	Soap Tree	220		220	69	10.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
400	<i>Casuarina cunninghamiana</i>	River She-oak	350		350	110	14.0	4.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
401	<i>Casuarina cunninghamiana</i>	River She-oak	110		110	35	8.0		2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
402	<i>Casuarina cunninghamiana</i>	River She-oak	150		150	47	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
403	<i>Casuarina cunninghamiana</i>	River She-oak	180		180	57	10.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
404	<i>Acacia disparrima</i>	Hickory Wattle	220		220	69	7.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
405	<i>Eucalyptus tereticornis</i>	Forest Red Gum	120		120	38	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
406	<i>Eucalyptus tereticornis</i>	Forest Red Gum	360		360	113	24.0	10.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
407	<i>Eucalyptus tereticornis</i>	Forest Red Gum	400		400	126	24.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
408	<i>Alphitonia excelsa</i>	Soap Tree	110		110	35	6.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
409	<i>Eucalyptus tereticornis</i>	Forest Red Gum	260		260	82	24.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
410	<i>Eucalyptus tereticornis</i>	Forest Red Gum	170		170	53	14.0	7.0	2.0	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
411	<i>Eucalyptus tereticornis</i>	Forest Red Gum	280		280	88	24.0	10.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
412	<i>Acacia disparrima</i>	Hickory Wattle	200	200	283	89	10.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
413	<i>Eucalyptus tereticornis</i>	Forest Red Gum	130		130	41	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
414	<i>Eucalyptus tereticornis</i>	Forest Red Gum	140		140	44	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
415	<i>Eucalyptus tereticornis</i>	Forest Red Gum	300		300	94	24.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
416	<i>Eucalyptus tereticornis</i>	Forest Red Gum	170		170	53	12.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
417	<i>Eucalyptus tereticornis</i>	Forest Red Gum	260		260	82	14.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
418	<i>Eucalyptus tereticornis</i>	Forest Red Gum	530		530	167	26.0	14.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
419	<i>Eucalyptus tereticornis</i>	Forest Red Gum	300		300	94	22.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
420	<i>Eucalyptus tereticornis</i>	Forest Red Gum	210		210	66	10.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
421	<i>Eucalyptus tereticornis</i>	Forest Red Gum	450		450	141	24.0	14.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
422	<i>Grevillea robusta</i>	Silky Oak	340		340	107	18.0	8.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
423	<i>Leptospermum petersonii</i>	Lemon-scented Tea-tree	110	100	149	47	4.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
424	<i>Araucaria bidwillii</i>	Bunya Pine	370		370	116	14.0	6.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
425	<i>Eucalyptus tereticornis</i>	Forest Red Gum	330		330	104	12.0	5.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
426	<i>Alphitonia excelsa</i>	Soap Tree	180	130	222	70	5.0	3.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
427	<i>Casuarina cunninghamiana</i>	River She-oak	230		230	72	16.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
428	<i>Alphitonia excelsa</i>	Soap Tree	180	150	234	74	5.0	3.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
429	<i>Eucalyptus grandis</i>	Flooded Gum	440		440	138	20.0	8.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
430	<i>Eucalyptus tereticornis</i>	Forest Red Gum	330		330	104	22.0	10.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
431	<i>Eucalyptus tereticornis</i>	Forest Red Gum	250		250	79	18.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
432	<i>Corymbia tessellaris</i>	Moreton Bay Ash	200		200	63	10.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
433	<i>Eucalyptus tereticornis</i>	Forest Red Gum	160		160	50	14.0	3.0	2.0	1.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
434	<i>Eucalyptus tereticornis</i>	Forest Red Gum	380		380	119	28.0	14.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Retain stage 1		
435	<i>Eucalyptus propinqua</i>	Northern Grey Gum	200		200	63	14.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Retain stage 1		
436	<i>Eucalyptus tereticornis</i>	Forest Red Gum	490		490	154	26.0	14.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
437	<i>Eucalyptus robusta</i>	Swamp Mahogany	200		200	63	8.0	4.0	2.4	1.7	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
438	<i>Grevillea robusta</i>	Silky Oak	190		190	60	10.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
439	<i>Eucalyptus tereticornis</i>	Forest Red Gum	470		470	148	22.0	10.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
440	<i>Eucalyptus eugenioides</i>	Thin-leaved Stringybark	280		280	88	20.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
441	<i>Eucalyptus eugenioides</i>	Thin-leaved Stringybark	360		360	113	22.0	10.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
442	<i>Acacia concurrens</i>	Black Wattle	120		120	38	6.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
443	<i>Flindersia australis</i>	Crows Ash	120		120	38	3.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
444	<i>Corymbia citriodora</i>	Spotted Gum	440	330	550	173	24.0	14.0	6.6	2.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
445	<i>Flindersia australis</i>	Crows Ash	120		120	38	5.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
446	<i>Eucalyptus siderophloia</i>	Grey Ironbark	370		370	116	24.0	12.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
447	<i>Eucalyptus siderophloia</i>	Grey Ironbark	530		530	167	24.0	12.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
448	<i>Eucalyptus siderophloia</i>	Grey Ironbark	350	250	430	135	14.0	8.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
449	<i>Acacia disparrima</i>	Hickory Wattle	140		140	44	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
450	<i>Acacia disparrima</i>	Hickory Wattle	200		200	63	7.0	4.0	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
451	<i>Acacia disparrima</i>	Hickory Wattle	180		180	57	8.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
452	<i>Eucalyptus siderophloia</i>	Grey Ironbark	200		200	63	14.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
453	<i>Cupaniopsis anacardioides</i>	Tuckeroo	140	130	191	60	5.0	3.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
454	<i>Eucalyptus siderophloia</i>	Grey Ironbark	260		260	82	20.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
455	<i>Eucalyptus siderophloia</i>	Grey Ironbark	300		300	94	22.0	10.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
456	Acacia disparrima	Hickory Wattle	250		250	79	12.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	Termite nest	-	Remove remediation works		
457	Eucalyptus siderophloia	Grey Ironbark	140		140	44	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
458	Alphitonia excelsa	Soap Tree	110		110	35	10.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
459	Alphitonia excelsa	Soap Tree	130		130	41	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
460	Acacia disparrima	Hickory Wattle	220		220	69	12.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
461	Acacia disparrima	Hickory Wattle	200		200	63	6.0	2.0	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
462	Eucalyptus tereticornis	Forest Red Gum	520		520	163	26.0	14.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
463	Eucalyptus microcorys	Tallowwood	200		200	63	18.0	7.0	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
464	Lophostemon confertus	Brush Box	320		320	101	18.0	8.0	3.8	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
465	Eucalyptus siderophloia	Grey Ironbark	120		120	38	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
466	Acacia disparrima	Hickory Wattle	120	120	170	53	8.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
467	Corymbia torelliana	Cadaghi	140		140	44	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
468	Acacia disparrima	Hickory Wattle	220		220	69	12.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
469	Acacia disparrima	Hickory Wattle	370		370	116	12.0	7.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
470	Casuarina cunninghamiana	River She-oak	150		150	47	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
471	Eucalyptus siderophloia	Grey Ironbark	330		330	104	26.0	14.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
472	Eucalyptus tereticornis	Forest Red Gum	350	260	436	137	26.0	16.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
473	Eucalyptus siderophloia	Grey Ironbark	280	260	382	120	24.0	12.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
474	Acacia disparrima	Hickory Wattle	180	180	255	80	8.0	4.0	3.1	1.9	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
475	Eucalyptus tereticornis	Forest Red Gum	260		260	82	16.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
476	Eucalyptus siderophloia	Grey Ironbark	140		140	44	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
477	Eucalyptus siderophloia	Grey Ironbark	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
478	Corymbia torelliana	Cadaghi	110	110, 100	185	58	8.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
479	Eucalyptus siderophloia	Grey Ironbark	190		190	60	12.0	5.0	2.3	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
480	Acacia disparrima	Hickory Wattle	180		180	57	8.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
481	Eucalyptus siderophloia	Grey Ironbark	260	220	341	107	10.0	6.0	4.1	2.1	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
482	Acacia disparrima	Hickory Wattle	120		120	38	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
483	Eucalyptus tereticornis	Forest Red Gum	180		180	57	12.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
484	Melaleuca linariifolia	Snow In Summer	500		500	157	8.0	6.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
485	Casuarina cunninghamiana	River She-oak	300		300	94	10.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
486	Casuarina cunninghamiana	River She-oak	330		330	104	12.0	5.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
487	Casuarina cunninghamiana	River She-oak	390		390	123	12.0	5.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
488	Archontophoenix cunninghamii	Bangalow Palm	230		230	72	10.0	2.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
489	Casuarina cunninghamiana	River She-oak	260		260	82	12.0	4.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
490	Casuarina cunninghamiana	River She-oak	180		180	57	11.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
491	Casuarina cunninghamiana	River She-oak	310		310	97	11.0	5.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
492	Castanospermum australe	Black Bean	210		210	66	8.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
493	Grevillea robusta	Silky Oak	280		280	88	10.0	4.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
494	Eucalyptus tereticornis	Forest Red Gum	440		440	138	25.0	14.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
495	Corymbia citriodora	Spotted Gum	830		830	261	25.0	16.0	10.0	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
496	Corymbia citriodora	Spotted Gum	380		380	119	23.0	8.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
497	Corymbia torelliana	Cadaghi	680		680	214	21.0	17.0	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
498	Melaleuca bracteata	Black Tea Tree	240	210, 210, 210, 190	475	149	7.0	8.0	5.7	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
499	Melaleuca viminalis	Weeping Bottlebrush	250		250	79	9.0	4.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
500	Alphitonia excelsa	Soap Tree	130		130	41	7.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
501	Acacia concurrens	Black Wattle	260		260	82	8.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
502	Eucalyptus tereticornis	Forest Red Gum	260	230	347	109	12.0	5.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
503	Jagera pseudorhus	Foam Bark	130		130	41	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
504	Eucalyptus siderophloia	Grey Ironbark	510		510	160	25.0	10.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
505	Eucalyptus siderophloia	Grey Ironbark	450		450	141	22.0	10.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
506	Acacia leiocalyx	Early-flowering Black Wattle	180		180	57	6.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
507	Acacia concurrens	Black Wattle	120		120	38	6.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
508	Corymbia torelliana	Cadaghi	100		100	31	5.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
509	Corymbia torelliana	Cadaghi	110		110	35	4.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
510	Acacia leiocalyx	Early-flowering Black Wattle	110		110	35	5.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
511	Corymbia torelliana	Cadaghi	170		170	53	14.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
512	Corymbia torelliana	Cadaghi	210		210	66	15.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
513	Corymbia torelliana	Cadaghi	250		250	79	15.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
514	Corymbia torelliana	Cadaghi	210		210	66	13.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
515	Corymbia torelliana	Cadaghi	200		200	63	12.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
516	Lophostemon confertus	Brush Box	200	140, 140	281	88	11.0	4.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
517	Lophostemon confertus	Brush Box	220	150	266	84	9.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
518	Alphitonia excelsa	Soap Tree	180		180	57	10.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
519	Castanospermum australe	Black Bean	180		180	57	11.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
520	Jagera pseudorhus	Foam Bark	150		150	47	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
521	Acacia concurrens	Black Wattle	200	190, 180	329	103	12.0	5.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
522	Alphitonia excelsa	Soap Tree	170	160, 100, 90	269	85	14.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
523	Acacia disparima	Hickory Wattle	350		350	110	14.0	6.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
524	Corymbia torelliana	Cadaghi	180		180	57	12.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP		
525	Alphitonia excelsa	Soap Tree	140	90	166	52	10.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
526	Alphitonia excelsa	Soap Tree	150	150, 80	227	71	11.0	4.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
527	Alphitonia excelsa	Soap Tree	190		190	60	11.0	3.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
528	Eucalyptus siderophloia	Grey Ironbark	330		330	104	22.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
529	Eucalyptus siderophloia	Grey Ironbark	180		180	57	10.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
530	Eucalyptus siderophloia	Grey Ironbark	300		300	94	24.0	10.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
531	Eucalyptus siderophloia	Grey Ironbark	530		530	167	26.0	10.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
532	Alphitonia excelsa	Soap Tree	110		110	35	8.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
533	Eucalyptus siderophloia	Grey Ironbark	460	410	616	194	28.0	15.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
534	Eucalyptus siderophloia	Grey Ironbark	290		290	91	17.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
535	Eucalyptus siderophloia	Grey Ironbark	350		350	110	19.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
536	Jagera pseudorhus	Foam Bark	170		170	53	11.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
537	Eucalyptus siderophloia	Grey Ironbark	300		300	94	18.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
538	Jagera pseudorhus	Foam Bark	100		100	31	5.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
539	Lophostemon confertus	Brush Box	330		330	104	24.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
540	<i>Eucalyptus siderophloia</i>	Grey Ironbark	200		200	63	15.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
541	<i>Eucalyptus siderophloia</i>	Grey Ironbark	390		390	123	24.0	10.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
542	<i>Eucalyptus siderophloia</i>	Grey Ironbark	280		280	88	15.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
543	<i>Commersonia bartramia</i>	Brown Kurrajong	150	100	180	57	5.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
544	<i>Acacia concurrens</i>	Black Wattle	170		170	53	13.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
545	<i>Acacia concurrens</i>	Black Wattle	210		210	66	16.0	3.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
546	<i>Acacia concurrens</i>	Black Wattle	200		200	63	16.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
547	<i>Acacia concurrens</i>	Black Wattle	180		180	57	14.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
548	<i>Acacia disparrima</i>	Hickory Wattle	180		180	57	14.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
549	<i>Acacia concurrens</i>	Black Wattle	180		180	57	14.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
550	<i>Acacia concurrens</i>	Black Wattle	160		160	50	15.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
551	<i>Acacia disparrima</i>	Hickory Wattle	190		190	60	14.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
552	<i>Acacia disparrima</i>	Hickory Wattle	270	230	355	111	15.0	16.0	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain stage 1	
553	<i>Eucalyptus siderophloia</i>	Grey Ironbark	220		220	69	17.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
554	<i>Eucalyptus siderophloia</i>	Grey Ironbark	390		390	123	26.0	13.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	Termite nest	-	Retain stage 1	
555	<i>Acacia disparrima</i>	Hickory Wattle	290		290	91	16.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
556	<i>Lophostemon confertus</i>	Brush Box	130	110	170	53	10.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
557	<i>Acacia disparrima</i>	Hickory Wattle	170		170	53	14.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
558	<i>Lophostemon confertus</i>	Brush Box	150	120	192	60	14.0	6.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
559	<i>Alphitonia excelsa</i>	Soap Tree	230		230	72	16.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
560	<i>Acacia disparrima</i>	Hickory Wattle	240		240	75	15.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
561	<i>Lophostemon confertus</i>	Brush Box	120		120	38	5.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
562	<i>Alphitonia excelsa</i>	Soap Tree	290		290	91	15.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
563	<i>Lophostemon confertus</i>	Brush Box	440		440	138	15.0	6.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
564	<i>Lophostemon confertus</i>	Brush Box	1030		1030	324	26.0	14.0	12.4	3.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
565	<i>Lophostemon confertus</i>	Brush Box	230		230	72	16.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
566	<i>Acacia disparrima</i>	Hickory Wattle	330		330	104	16.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
567	<i>Commersonia bartramia</i>	Brown Kurrajong	230		230	72	9.0	4.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
568	<i>Cryptocarya glaucescens</i>	Jackwood	150	150	212	67	9.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
569	<i>Alphitonia excelsa</i>	Soap Tree	150		150	47	13.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
570	<i>Jagera pseudorhus</i>	Foam Bark	130	50	139	44	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
571	<i>Flindersia australis</i>	Crows Ash	590		590	185	23.0	15.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
572	<i>Cupaniopsis anacardioides</i>	Tuckeroo	190		190	60	6.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
573	<i>Corymbia torelliana</i>	Cadaghi	110		110	35	8.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
574	<i>Lophostemon confertus</i>	Brush Box	120		120	38	14.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
575	<i>Lophostemon suaveolens</i>	Swamp Box	110		110	35	8.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
576	<i>Lophostemon confertus</i>	Brush Box	150		150	47	14.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
577	<i>Lophostemon confertus</i>	Brush Box	140		140	44	14.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
578	<i>Lophostemon suaveolens</i>	Swamp Box	170		170	53	13.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
579	<i>Lophostemon confertus</i>	Brush Box	230		230	72	15.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
580	<i>Lophostemon confertus</i>	Brush Box	140		140	44	13.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
581	<i>Lophostemon confertus</i>	Brush Box	190		190	60	15.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
582	Lophostemon suaveolens	Swamp Box	170		170	53	12.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
583	Lophostemon confertus	Brush Box	330		330	104	15.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
584	Lophostemon confertus	Brush Box	180		180	57	16.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
585	Lophostemon suaveolens	Swamp Box	330		330	104	12.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
586	Alphitonia excelsa	Soap Tree	110		110	35	8.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
587	Lophostemon confertus	Brush Box	280	230	362	114	17.0	7.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
588	Lophostemon confertus	Brush Box	260		260	82	16.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
589	Lophostemon confertus	Brush Box	240		240	75	16.0	10.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
590	Lophostemon suaveolens	Swamp Box	160		160	50	14.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
591	Lophostemon confertus	Brush Box	350		350	110	19.0	12.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
592	Lophostemon confertus	Brush Box	340		340	107	16.0	12.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
593	Lophostemon confertus	Brush Box	370		370	116	17.0	10.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
594	Lophostemon confertus	Brush Box	380		380	119	16.0	8.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
595	Alphitonia excelsa	Soap Tree	320		320	101	12.0	12.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
596	Alphitonia excelsa	Soap Tree	210		210	66	13.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
597	Lophostemon confertus	Brush Box	540		540	170	16.0	14.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
598	Eucalyptus siderophloia	Grey Ironbark	500	390	634	199	22.0	15.0	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
599	Eucalyptus fibrosa	Broad-leaved Red Ironbark	360		360	113	22.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
600	Eucalyptus siderophloia	Grey Ironbark	250		250	79	18.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
601	Eucalyptus siderophloia	Grey Ironbark	150		150	47	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
602	Eucalyptus siderophloia	Grey Ironbark	210		210	66	18.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
603	Eucalyptus siderophloia	Grey Ironbark	190		190	60	18.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
604	Eucalyptus siderophloia	Grey Ironbark	340	120	361	113	19.0	10.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
605	Eucalyptus siderophloia	Grey Ironbark	200		200	63	16.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
606	Eucalyptus siderophloia	Grey Ironbark	280		280	88	20.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
607	Eucalyptus siderophloia	Grey Ironbark	260		260	82	16.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
608	Eucalyptus siderophloia	Grey Ironbark	470	240	528	166	26.0	12.0	6.3	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
609	Eucalyptus siderophloia	Grey Ironbark	370		370	116	25.0	14.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
610	Eucalyptus siderophloia	Grey Ironbark	590		590	185	26.0	13.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
611	Acacia leiocalyx	Early-flowering Black Wattle	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
612	Acacia disparrima	Hickory Wattle	420	350, 250	601	189	14.0	10.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
613	Acacia disparrima	Hickory Wattle	310	259	404	127	13.0	8.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
614	Eucalyptus siderophloia	Grey Ironbark	430		430	135	20.0	14.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
615	Eucalyptus siderophloia	Grey Ironbark	390	360, 330	625	196	18.0	15.0	7.5	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
616	Eucalyptus siderophloia	Grey Ironbark	610		610	192	24.0	13.0	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
617	Eucalyptus siderophloia	Grey Ironbark	660		660	207	19.0	12.0	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
618	Eucalyptus siderophloia	Grey Ironbark	420	270	499	157	19.0	12.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
619	Acacia disparrima	Hickory Wattle	300		300	94	10.0	12.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
620	Acacia disparrima	Hickory Wattle	260	210	334	105	12.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
621	Casuarina cunninghamiana	River She-oak	150		150	47	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
622	Casuarina cunninghamiana	River She-oak	210		210	66	14.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
623	Casuarina cunninghamiana	River She-oak	210		210	66	16.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
624	Casuarina cunninghamiana	River She-oak	180		180	57	14.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
625	Casuarina cunninghamiana	River She-oak	220		220	69	16.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
626	Melaleuca quinquenervia	Broad-leaf Paperbark	330		330	104	13.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
627	Casuarina cunninghamiana	River She-oak	180		180	57	16.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
628	Acacia disparrima	Hickory Wattle	260	150	300	94	14.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
629	Eucalyptus tereticornis	Forest Red Gum	180		180	57	15.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
630	Acacia disparrima	Hickory Wattle	210	150	258	81	8.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
631	Eucalyptus tereticornis	Forest Red Gum	360		360	113	17.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
632	Eucalyptus tereticornis	Forest Red Gum	390		390	123	19.0	6.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
633	Eucalyptus tereticornis	Forest Red Gum	250		250	79	14.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
634	Eucalyptus tereticornis	Forest Red Gum	120		120	38	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
635	Acacia disparrima	Hickory Wattle	120		120	38	4.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
636	Casuarina cunninghamiana	River She-oak	300		300	94	14.0	4.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
637	Araucaria cunninghamii	Hoop Pine	330		330	104	15.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
638	Eucalyptus moluccana	Gum-topped Box	260		260	82	17.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
639	Eucalyptus tereticornis	Forest Red Gum	190		190	60	14.0	3.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
640	Corymbia citriodora	Spotted Gum	210		210	66	15.0	3.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
641	Eucalyptus tereticornis	Forest Red Gum	540		540	170	16.0	8.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
642	Eucalyptus tereticornis	Forest Red Gum	250		250	79	16.0	2.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
643	Eucalyptus tereticornis	Forest Red Gum	470		470	148	21.0	8.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
644	Eucalyptus tereticornis	Forest Red Gum	360		360	113	24.0	8.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
645	Grevillea robusta	Silky Oak	200		200	63	10.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
646	Eucalyptus eugenioides	Thin-leaved Stringybark	330		330	104	16.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
647	Eucalyptus eugenioides	Thin-leaved Stringybark	430		430	135	15.0	10.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
648	Eucalyptus eugenioides	Thin-leaved Stringybark	250	160	297	93	15.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
649	Eucalyptus tereticornis	Forest Red Gum	190	140	236	74	9.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
650	Eucalyptus tereticornis	Forest Red Gum	290		290	91	24.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
651	Eucalyptus tereticornis	Forest Red Gum	230		230	72	15.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
652	Eucalyptus tereticornis	Forest Red Gum	120		120	38	14.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
653	Eucalyptus tereticornis	Forest Red Gum	390		390	123	25.0	10.0	4.7	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
654	Lophostemon confertus	Brush Box	280		280	88	15.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
655	Eucalyptus siderophloia	Grey Ironbark	540		540	170	25.0	14.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
656	Eucalyptus propinqua	Northern Grey Gum	450	270	525	165	18.0	10.0	6.3	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	New	-	-	-	-	Remove remediation works	
657	Ficus obliqua	Small Leaf Fig	350		350	110	12.0	18.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
658	Eucalyptus melanophloia	Silver-leaved Ironbark	400		400	126	14.0	7.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
659	Eucalyptus propinqua	Northern Grey Gum	240		240	75	15.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Remove remediation works	
660	Ficus benamina	Weeping Fig	400		400	126	14.0	18.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
661	Acacia disparrima	Hickory Wattle	200	170	262	82	14.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
662	Acacia disparrima	Hickory Wattle	180	150	234	74	12.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
663	Eucalyptus siderophloia	Grey Ironbark	120		120	38	13.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
664	Eucalyptus siderophloia	Grey Ironbark	310		310	97	19.0	9.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
665	Eucalyptus siderophloia	Grey Ironbark	230		230	72	17.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
666	Casuarina cunninghamiana	River She-oak	190		190	60	15.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
667	Casuarina cunninghamiana	River She-oak	140		140	44	14.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
668	Acacia disparrima	Hickory Wattle	130		130	41	6.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
669	Acacia disparrima	Hickory Wattle	130	100, 100, 100	217	68	14.0	7.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
670	Acacia disparrima	Hickory Wattle	180	100, 100, 80, 80	255	80	14.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
671	Acacia disparrima	Hickory Wattle	230		230	72	15.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
672	Acacia disparrima	Hickory Wattle	100		100	31	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
673	Acacia disparrima	Hickory Wattle	120		120	38	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
674	Acacia disparrima	Hickory Wattle	140		140	44	11.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
675	Acacia disparrima	Hickory Wattle	250		250	79	15.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
676	Acacia disparrima	Hickory Wattle	160	90	184	58	14.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
677	Acacia disparrima	Hickory Wattle	140		140	44	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
678	Eucalyptus siderophloia	Grey Ironbark	490		490	154	20.0	14.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
679	Eucalyptus tereticornis	Forest Red Gum	340		340	107	21.0	6.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
680	Eucalyptus tereticornis	Forest Red Gum	260		260	82	18.0	4.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
681	Eucalyptus tereticornis	Forest Red Gum	190		190	60	16.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
682	Alphitonia excelsa	Soap Tree	100		100	31	6.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
683	Acacia disparrima	Hickory Wattle	120		120	38	4.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
684	Eucalyptus tereticornis	Forest Red Gum	250		250	79	18.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
685	Eucalyptus tereticornis	Forest Red Gum	250		250	79	15.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
686	Eucalyptus tereticornis	Forest Red Gum	350		350	110	18.0	10.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
687	Eucalyptus tereticornis	Forest Red Gum	170		170	53	16.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
688	Eucalyptus tereticornis	Forest Red Gum	130		130	41	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
689	Acacia disparrima	Hickory Wattle	190		190	60	10.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
690	Corymbia citriodora	Spotted Gum	300		300	94	24.0	12.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
691	Acacia disparrima	Hickory Wattle	190		190	60	12.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
692	Eucalyptus crebra	Grey Ironbark	250	240	347	109	14.0	6.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
693	Jacaranda mimosifolia	Jacaranda	180		180	57	7.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
694	Corymbia citriodora	Spotted Gum	420	270	499	157	22.0	8.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
695	Citharexylum sponosum	Fiddlewood	180	100	206	65	11.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
696	Jacaranda mimosifolia	jacaranda	150	140	205	64	10.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
697	Corymbia citriodora	Spotted Gum	270		270	85	23.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
698	Corymbia citriodora	Spotted Gum	170		170	53	12.0	5.0	2.0	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
699	Jacaranda mimosifolia	Jacaranda	130		130	41	6.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
700	Citharexylum sponosum	Fiddlewood	140	130, 130	231	73	9.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
701	Eucalyptus propinqua	Northern Grey Gum	460		460	145	24.0	9.0	5.5	2.4	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-	Remove stage 1		
702	Lophostemon confertus	Brush Box	410		410	129	14.0	9.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
703	Eucalyptus siderophloia	Grey Ironbark	180		180	57	13.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
704	Eucalyptus carnea	Broad-leaved White Mahogany	280		280	88	18.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
705	Jacaranda mimosifolia	Jacaranda	130	100	164	52	5.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
706	Eucalyptus siderophloia	Grey Ironbark	200		200	63	15.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
707	Eucalyptus microcorys	Tallowwood	280		280	88	19.0	11.0	3.4	1.9	Irregular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
708	<i>Eucalyptus siderophloia</i>	Grey Ironbark	240		240	75	17.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
709	<i>Eucalyptus microcorys</i>	Tallowwood	180		180	57	10.0	5.0	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove stage 1	
710	<i>Eucalyptus microcorys</i>	Tallowwood	270		270	85	20.0	9.0	3.2	1.9	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
711	<i>Corymbia intermedia</i>	Pink Bloodwood	270		270	85	18.0	11.0	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
712	<i>Jacaranda mimosifolia</i>	Jacaranda	140		140	44	5.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
713	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	160		160	50	7.0	4.0	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove remediation works	
714	<i>Corymbia citriodora</i>	Spotted Gum	240		240	75	19.0	7.0	2.9	1.8	One-sided	-	Thinning	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove stage 1	
715	<i>Corymbia citriodora</i>	Spotted Gum	300		300	94	20.0	12.0	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
716	<i>Eucalyptus siderophloia</i>	Grey Ironbark	240		240	75	15.0	5.0	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
717	<i>Lophostemon confertus</i>	Brush Box	100		100	31	5.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
718	<i>Lophostemon confertus</i>	Brush Box	330		330	104	22.0	11.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
719	<i>Lophostemon confertus</i>	Brush Box	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
720	<i>Corymbia citriodora</i>	Spotted Gum	320		320	101	28.0	7.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
721	<i>Lophostemon suaveolens</i>	Swamp Box	100		100	31	11.0	3.0	2.0	1.3	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
722	<i>Corymbia citriodora</i>	Spotted Gum	250		250	79	17.0	8.0	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
723	<i>Lophostemon confertus</i>	Brush Box	140	130	191	60	11.0	5.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
724	<i>Lophostemon confertus</i>	Brush Box	100	100	141	44	7.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
725	<i>Lophostemon confertus</i>	Brush Box	130		130	41	7.0	4.0	2.0	1.4	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
726	<i>Corymbia citriodora</i>	Spotted Gum	470		470	148	34.0	17.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
727	<i>Lophostemon confertus</i>	Brush Box	120	100, 100, 100	211	66	7.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
728	<i>Lophostemon confertus</i>	Brush Box	120	110	163	51	9.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
729	<i>Lophostemon confertus</i>	Brush Box	230		230	72	15.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
730	<i>Lophostemon confertus</i>	Brush Box	110		110	35	10.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
731	<i>Acacia concurrens</i>	Black Wattle	190		190	60	12.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
732	<i>Acacia concurrens</i>	Black Wattle	120		120	38	11.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove stage 1	
733	<i>Acacia concurrens</i>	Black Wattle	180		180	57	13.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
734	<i>Acacia concurrens</i>	Black Wattle	140		140	44	10.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
735	<i>Lophostemon confertus</i>	Brush Box	100		100	31	11.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
736	<i>Lophostemon confertus</i>	Brush Box	100		100	31	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
737	<i>Lophostemon confertus</i>	Brush Box	140		140	44	11.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
738	<i>Corymbia citriodora</i>	Spotted Gum	470		470	148	33.0	18.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
739	<i>Acacia disparrima</i>	Hickory Wattle	180		180	57	10.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
740	<i>Corymbia citriodora</i>	Spotted Gum	120		120	38	13.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
741	<i>Acacia concurrens</i>	Black Wattle	150		150	47	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
742	<i>Acacia concurrens</i>	Black Wattle	280	200	344	108	7.0	9.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
743	<i>Erythrina crista-galli</i>	Cockspur Coral Tree	310	230, 210, 160	468	147	4.0	6.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
744	<i>Erythrina crista-galli</i>	Cockspur Coral Tree	150	150, 130	249	78	4.0	5.0	3.0	1.8	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
745	<i>Eucalyptus siderophloia</i>	Grey Ironbark	380		380	119	18.0	10.0	4.6	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
746	<i>Delonix regia</i>	Poinciana	260		260	82	10.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
747	<i>Eucalyptus siderophloia</i>	Grey Ironbark	480		480	151	27.0	10.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
748	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	110		110	35	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
749	<i>Lophostemon confertus</i>	Brush Box	240	190	306	96	13.0	7.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details											Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value									
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
750	DEAD/STAG		360		360	113	23.0	8.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
751	Jacaranda mimosifolia	Jacaranda	160	150	219	69	12.0	6.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
752	Melia azedarach	White Cedar	270		270	85	14.0	7.0	3.2	1.9	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
753	Acacia concurrens	Black Wattle	230	240	332	104	12.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
754	Acacia leiocalyx	Early-flowering Black Wattle	250	230, 240, 230, 240	532	167	15.0	9.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	old cubby in tree	
755	Schefflera actinophylla	Umbrella Tree	170	130, 120	245	77			2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
756	Cinnamomum camphora	Camphor Laurel	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
757	Lophostemon confertus	Brush Box	130		130	41	13.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
758	Jacaranda mimosifolia	Jacaranda	260		260	82	10.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
759	Lophostemon confertus	Brush Box	190		190	60	15.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
760	Corymbia torelliana	Cadaghi	440		440	138	23.0	12.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
761	Eucalyptus fibrosa	Broad-leaved Red Ironbark	370		370	116	22.0	11.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
762	Acacia leiocalyx	Early-flowering Black Wattle	110		110	35	8.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
763	Eucalyptus fibrosa	Broad-leaved Red Ironbark	370		370	116	30.0	15.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
764	Acacia disparrima	Hickory Wattle	140	140	198	62	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
765	Corymbia citriodora	Spotted Gum	240		240	75	13.0	7.0	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
766	Corymbia trachyphloia	Brown Bloodwood	210		210	66	14.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
767	Eucalyptus fibrosa	Broad-leaved Red Ironbark	140		140	44	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
768	Acacia disparrima	Hickory Wattle	140		140	44	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
769	Corymbia citriodora	Spotted Gum	380		380	119	22.0	10.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
770	Acacia concurrens	Black Wattle	200	180	269	85	12.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
771	Lophostemon confertus	Brush Box	380	250	455	143	11.0	8.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
772	Corymbia citriodora	Spotted Gum	350		350	110	22.0	12.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
773	Eucalyptus siderophloia	Grey Ironbark	280		280	88	23.0	10.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
774	Eucalyptus siderophloia	Grey Ironbark	330		330	104	29.0	11.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
775	Eucalyptus siderophloia	Grey Ironbark	290		290	91	23.0	12.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
776	Eucalyptus siderophloia	Grey Ironbark	340		340	107	28.0	13.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
777	Eucalyptus siderophloia	Grey Ironbark	340		340	107	19.0	11.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
778	Eucalyptus siderophloia	Grey Ironbark	290		290	91	13.0	4.0	3.5	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	Major	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
779	Eucalyptus siderophloia	Grey Ironbark	270		270	85	15.0	7.0	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
780	Eucalyptus siderophloia	Grey Ironbark	190		190	60	14.0	8.0	2.3	1.6	One-sided	-	Thinning	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
781	Eucalyptus siderophloia	Grey Ironbark	330		330	104	27.0	13.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
782	Acacia concurrens	Black Wattle	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
783	Eucalyptus siderophloia	Grey Ironbark	350		350	110	22.0	10.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
784	Corymbia citriodora	Spotted Gum	120		120	38	13.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
785	Eucalyptus siderophloia	Grey Ironbark	340		340	107	19.0	12.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
786	Acacia disparrima	Hickory Wattle	170		170	53	7.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
787	Lophostemon confertus	Brush Box	150	130, 140	243	76	11.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
788	Eucalyptus siderophloia	Grey Ironbark	190		190	60	12.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
789	Melaleuca saligna	Willow Bottlebrush	240	350, 300	520	163	20.0	8.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
790	Melaleuca leucadendra	Weeping Paperbark	700		700	220	22.0	14.0	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
791	Melaleuca leucadendra	Weeping Paperbark	650	700	955	300	14.0	12.0	11.5	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
792	Melaleuca quinquenervia	Broad-leaf Paperbark	200		200	63	12.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
793	Melaleuca saligna	Willow Bottlebrush	320	240	400	126	14.0	6.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
794	Melaleuca saligna	Willow Bottlebrush	460	370	590	185	15.0	10.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
795	Grevillea robusta	Silky Oak	390	380	545	171	25.0	12.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
796	Ficus rubiginosa	Port Jackson Fig	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
797	Acacia disparrima	Hickory Wattle	390		390	123	10.0	8.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation		
798	Allocasuarina littoralis	Black She-oak	180		180	57	12.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
799	Casuarina glauca	Swamp Oak	200		200	63	14.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
800	Casuarina glauca	Swamp Oak	390		390	123	14.0	4.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
801	Casuarina glauca	Swamp Oak	290		290	91	16.0	4.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
802	Corymbia citriodora	Spotted Gum	400		400	126	26.0	10.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
803	Corymbia citriodora	Spotted Gum	630		630	198	25.0	8.0	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
804	Corymbia torelliana	Cadaghi	160		160	50	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
805	Corymbia torelliana	Cadaghi	360		360	113	16.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
806	Corymbia torelliana	Cadaghi	300		300	94	16.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
807	Corymbia torelliana	Cadaghi	150		150	47	14.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
808	Acacia disparrima	Hickory Wattle	330		330	104	12.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
809	Corymbia citriodora	Spotted Gum	130		130	41	6.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
810	Eucalyptus seeana	Narrow-leaved Red Gum	250	200	320	101	16.0	5.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
811	Corymbia torelliana	Cadaghi	240		240	75	15.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
812	Corymbia torelliana	Cadaghi	260		260	82	14.0	4.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
813	Corymbia torelliana	Cadaghi	280		280	88	14.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
814	Acacia disparrima	Hickory Wattle	170		170	53	12.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
815	Acacia disparrima	Hickory Wattle	130		130	41	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works		
816	Eucalyptus tereticornis	Forest Red Gum	390		390	123	24.0	8.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
817	Acacia disparrima	Hickory Wattle	120		120	38	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
818	Eucalyptus tereticornis	Forest Red Gum	200		200	63	16.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
819	Eucalyptus tereticornis	Forest Red Gum	130		130	41	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
820	Eucalyptus tereticornis	Forest Red Gum	100		100	31	12.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
821	Eucalyptus tereticornis	Forest Red Gum	160		160	50	14.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
822	Eucalyptus tereticornis	Forest Red Gum	120		120	38	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
823	Eucalyptus tereticornis	Forest Red Gum	120		120	38	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
824	Acacia disparrima	Hickory Wattle	100		100	31	6.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
825	Eucalyptus crebra	Grey Ironbark	300		300	94	22.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
826	Corymbia citriodora	Spotted Gum	250		250	79	18.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
827	Eucalyptus crebra	Grey Ironbark	120		120	38	15.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
828	Eucalyptus crebra	Grey Ironbark	150		150	47	15.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
829	Eucalyptus crebra	Grey Ironbark	130		130	41	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
830	Corymbia tessellaris	Moreton Bay Ash	100		100	31	6.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
831	Eucalyptus siderophloia	Grey Ironbark	200		200	63	12.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
832	Eucalyptus crebra	Grey Ironbark	110		110	35	12.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
833	Eucalyptus tereticornis	Forest Red Gum	200		200	63	14.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
834	<i>Eucalyptus siderophloia</i>	Grey Ironbark	120		120	38	14.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
835	<i>Eucalyptus tereticornis</i>	Forest Red Gum	220		220	69	15.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
836	<i>Eucalyptus tereticornis</i>	Forest Red Gum	160		160	50	12.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
837	<i>Acacia disparrima</i>	Hickory Wattle	380		380	119	12.0	6.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
838	<i>Acacia disparrima</i>	Hickory Wattle	550		550	173	14.0	8.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
839	<i>Eucalyptus tereticornis</i>	Forest Red Gum	220		220	69	16.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
840	<i>Eucalyptus tereticornis</i>	Forest Red Gum	130		130	41	14.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
841	<i>Eucalyptus siderophloia</i>	Grey Ironbark	150		150	47	15.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
842	<i>Acacia disparrima</i>	Hickory Wattle	100		100	31	10.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
843	<i>Eucalyptus propinqua</i>	Northern Grey Gum	280		280	88	18.0	3.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
844	<i>Acacia disparrima</i>	Hickory Wattle	300		300	94	15.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
845	<i>Acacia disparrima</i>	Hickory Wattle	210		210	66	18.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
846	<i>Acacia disparrima</i>	Hickory Wattle	200		200	63	15.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
847	<i>Acacia disparrima</i>	Hickory Wattle	200		200	63	12.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
848	<i>Acacia disparrima</i>	Hickory Wattle	260		260	82	14.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
849	<i>Native spp</i>		220		220	69	14.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
850	<i>Alphitonia excelsa</i>	Soap Tree	150		150	47	8.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
851	<i>Citharexylum sponosum</i>	Fiddlewood	150		150	47	14.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
852	<i>Citharexylum sponosum</i>	Fiddlewood	150		150	47	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
853	<i>Corymbia citriodora</i>	Spotted Gum	150		150	47	18.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
854	<i>Corymbia citriodora</i>	Spotted Gum	650		650	204	28.0	15.0	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
855	<i>Corymbia citriodora</i>	Spotted Gum	370		370	116	25.0	10.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
856	<i>Corymbia citriodora</i>	Spotted Gum	160		160	50	15.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
857	<i>Corymbia citriodora</i>	Spotted Gum	100		100	31	10.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
858	<i>Corymbia citriodora</i>	Spotted Gum	120		120	38	15.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
859	<i>Corymbia citriodora</i>	Spotted Gum	160	120	200	63	15.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
860	<i>Corymbia citriodora</i>	Spotted Gum	170		170	53	16.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
861	<i>Corymbia citriodora</i>	Spotted Gum	300		300	94	18.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
862	<i>Acacia disparrima</i>	Hickory Wattle	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
863	<i>Eucalyptus crebra</i>	Grey Ironbark	220		220	69	15.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
864	<i>Citharexylum sponosum</i>	Fiddlewood	200		200	63	12.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
865	<i>Eucalyptus crebra</i>	Grey Ironbark	260		260	82	16.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
866	<i>Grevillea robusta</i>	Silky Oak	140		140	44	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
867	<i>Eucalyptus siderophloia</i>	Grey Ironbark	260		260	82	20.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
868	<i>Eucalyptus propinqua</i>	Northern Grey Gum	330		330	104	22.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
869	<i>Eucalyptus propinqua</i>	Northern Grey Gum	200		200	63	15.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
870	<i>Eucalyptus siderophloia</i>	Grey Ironbark	350		350	110	15.0	5.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
871	<i>Flindersia australis</i>	Crows Ash	250	210, 300, 250	509	160	16.0	8.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
872	<i>Lophostemon suaveolens</i>	Swamp Box	200		200	63	10.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
873	<i>Eucalyptus crebra</i>	Grey Ironbark	110		110	35	10.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
874	<i>Alphitonia excelsa</i>	Soap Tree	180		180	57	12.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
875	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	270		270	85	16.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
876	<i>Eucalyptus siderophloia</i>	Grey Ironbark	180		180	57	12.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
877	<i>Eucalyptus microcorys</i>	Tallowwood	420		420	132	24.0	12.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
878	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	200		200	63	10.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
879	<i>Libidibia ferrea</i>	Leopard Tree	270		270	85	12.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
880	<i>Corymbia torelliana</i>	Cadaghi	330		330	104	18.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
881	<i>Corymbia torelliana</i>	Cadaghi	300		300	94	14.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
882	<i>Corymbia citriodora</i>	Spotted Gum	160		160	50	16.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
883	<i>Corymbia citriodora</i>	Spotted Gum	290	150, 120	348	109	25.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
884	<i>Corymbia citriodora</i>	Spotted Gum	580		580	182	30.0	14.0	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
885	<i>Corymbia citriodora</i>	Spotted Gum	110		110	35	10.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
886	<i>Corymbia citriodora</i>	Spotted Gum	700		700	220	33.0	15.0	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-	Remove stage 1	
887	<i>Corymbia citriodora</i>	Spotted Gum	290		290	91	18.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
888	<i>Corymbia citriodora</i>	Spotted Gum	180		180	57	15.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
889	<i>Lophostemon confertus</i>	Brush Box	220		220	69	12.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
890	<i>Corymbia citriodora</i>	Spotted Gum	190		190	60	15.0	2.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
891	<i>Lophostemon confertus</i>	Brush Box	120		120	38	10.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
892	<i>Lophostemon suaveolens</i>	Swamp Box	140		140	44	12.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
893	<i>Corymbia citriodora</i>	Spotted Gum	170		170	53	15.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
894	<i>Eucalyptus siderophloia</i>	Grey Ironbark	540		540	170	30.0	14.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
895	<i>Corymbia citriodora</i>	Spotted Gum	380	190, 110	439	138	22.0	12.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
896	<i>Corymbia citriodora</i>	Spotted Gum	360		360	113	25.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
897	<i>Eucalyptus siderophloia</i>	Grey Ironbark	650		650	204	28.0	16.0	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
898	<i>Corymbia citriodora</i>	Spotted Gum	280		280	88	18.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
899	<i>Lophostemon confertus</i>	Brush Box	250		250	79	12.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
900	<i>Corymbia citriodora</i>	Spotted Gum	160		160	50	18.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
901	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	370		370	116	20.0	6.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
902	<i>Lophostemon confertus</i>	Brush Box	310		310	97	15.0	6.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
903	<i>Eucalyptus siderophloia</i>	Grey Ironbark	420		420	132	25.0	12.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
904	<i>Lophostemon confertus</i>	Brush Box	150		150	47	14.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
905	<i>Corymbia citriodora</i>	Spotted Gum	430		430	135	30.0	12.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
906	<i>Lophostemon confertus</i>	Brush Box	250		250	79	12.0	4.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
907	<i>Lophostemon confertus</i>	Brush Box	360	250, 100	450	141	18.0	6.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
908	<i>Corymbia citriodora</i>	Spotted Gum	800		800	251	34.0	15.0	9.6	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
909	<i>Lophostemon confertus</i>	Brush Box	280		280	88	15.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
910	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	260		260	82	15.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
911	<i>Lophostemon confertus</i>	Brush Box	210		210	66	12.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
912	<i>Acacia disparima</i>	Hickory Wattle	240		240	75	14.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
913	<i>Corymbia citriodora</i>	Spotted Gum	460		460	145	28.0	12.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
914	<i>Lophostemon confertus</i>	Brush Box	200		200	63	8.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
915	<i>Corymbia citriodora</i>	Spotted Gum	900		900	283	32.0	15.0	10.8	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
916	<i>Acacia disparima</i>	Hickory Wattle	200		200	63	10.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
917	<i>Acacia disparima</i>	Hickory Wattle	140		140	44	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
918	Acacia disparrima	Hickory Wattle	140		140	44	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
919	Acacia disparrima	Hickory Wattle	160		160	50	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
920	Acacia disparrima	Hickory Wattle	160		160	50	12.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
921	Acacia disparrima	Hickory Wattle	390	380	545	171	14.0	10.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
922	Lophostemon confertus	Brush Box	280		280	88	12.0	4.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
923	Allocasuarina littoralis	Black She-oak	200		200	63	10.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
924	Allocasuarina littoralis	Black She-oak	220		220	69	12.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
925	Lophostemon confertus	Brush Box	200		200	63	12.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
926	Corymbia torelliana	Cadaghi	120		120	38	8.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
927	Eucalyptus crebra	Grey Ironbark	260		260	82	22.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
928	Corymbia torelliana	Cadaghi	210		210	66	10.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
929	Eucalyptus siderophloia	Grey Ironbark	320		320	101	22.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
930	Eucalyptus siderophloia	Grey Ironbark	370		370	116	25.0	6.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
931	Acacia disparrima	Hickory Wattle	150		150	47	14.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
932	Araucaria cunninghamii	Hoop Pine	200		200	63	15.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
933	Jacaranda mimosifolia	Jacaranda	400	200	447	140	14.0	6.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
934	Corymbia torelliana	Cadaghi	300		300	94	16.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
935	Acacia disparrima	Hickory Wattle	280		280	88	16.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
936	Acacia disparrima	Hickory Wattle	300		300	94	15.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
937	Corymbia trachyphloia	Brown Bloodwood	280		280	88	15.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
938	Ficus rubiginosa	Port Jackson Fig	520		520	163	20.0	14.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
939	Corymbia torelliana	Cadaghi	160		160	50	14.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
940	Corymbia citriodora	Spotted Gum	550		550	173	32.0	15.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
941	Corymbia torelliana	Cadaghi	400		400	126	25.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
942	Corymbia citriodora	Spotted Gum	400		400	126	28.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
943	Corymbia citriodora	Spotted Gum	340		340	107	26.0	10.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
944	Lophostemon confertus	Brush Box	500		500	157	25.0	15.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
945	Corymbia citriodora	Spotted Gum	510		510	160	26.0	14.0	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
946	Angophora leiocarpa	Smooth-barked Apple	470		470	148	25.0	10.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1		
947	Eucalyptus siderophloia	Grey Ironbark	250		250	79	16.0	3.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
948	Corymbia trachyphloia	Brown Bloodwood	200		200	63	15.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
949	Eucalyptus siderophloia	Grey Ironbark	890		890	280	26.0	14.0	10.7	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
950	Acacia disparrima	Hickory Wattle	110		110	35	8.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
951	Acacia disparrima	Hickory Wattle	140		140	44	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
952	Corymbia citriodora	Spotted Gum	330		330	104	22.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
953	Lophostemon confertus	Brush Box	130	100	164	52	10.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
954	Corymbia trachyphloia	Brown Bloodwood	240		240	75	15.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
955	Eucalyptus siderophloia	Grey Ironbark	460		460	145	32.0	14.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
956	Lophostemon confertus	Brush Box	110		110	35	10.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
957	Angophora leiocarpa	Smooth-barked Apple	260		260	82	25.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
958	Corymbia trachyphloia	Brown Bloodwood	190		190	60	14.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		
959	Eucalyptus siderophloia	Grey Ironbark	420		420	132	28.0	14.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
960	<i>Acacia disparrima</i>	Hickory Wattle	190		190	60	10.0	2.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
961	<i>Eucalyptus siderophloia</i>	Grey Ironbark	340		340	107	18.0	5.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
962	<i>Corymbia trachyphloia</i>	Brown Bloodwood	240		240	75	14.0	2.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
963	<i>Corymbia citriodora</i>	Spotted Gum	420		420	132	30.0	14.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
964	<i>Acacia disparrima</i>	Hickory Wattle	150		150	47	14.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
965	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	460		460	145	24.0	12.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
966	<i>Acacia disparrima</i>	Hickory Wattle	180		180	57	12.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
967	<i>Acacia disparrima</i>	Hickory Wattle	290		290	91	14.0	4.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
968	<i>Eucalyptus crebra</i>	Grey Ironbark	120		120	38	8.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
969	<i>Lophostemon confertus</i>	Brush Box	250		250	79	15.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
970	<i>Melaleuca leucadendra</i>	Weeping Paperbark	380	370	530	167	14.0	8.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
971	<i>Melaleuca quinquenervia</i>	Broad-leaf Paperbark	710		710	223	15.0	11.0	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
972	<i>Melaleuca viminalis</i>	Weeping Bottlebrush	240		240	75	11.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain stage 1	
973	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	250		250	79	10.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain stage 1	
974	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	210		210	66	7.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
975	<i>Eucalyptus melanophloia</i>	Silver-leaved Ironbark	290		290	91	14.0	7.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain subject to remediation	
976	<i>Corymbia intermedia</i>	Pink Bloodwood	210		210	66	8.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
977	<i>Corymbia citriodora</i>	Spotted Gum	600		600	188	21.0	12.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
978	<i>Eucalyptus carnea</i>	Broad-leaved White Mahogany	270	170	319	100	10.0	6.0	3.8	2.0	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
979	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	160		160	50	7.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
980	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	200	200	283	89	11.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
981	<i>Eucalyptus tereticornis</i>	Forest Red Gum	350		350	110	24.0	10.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove remediation works	
982	<i>Lophostemon confertus</i>	Brush Box	160		160	50	11.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
983	<i>Corymbia citriodora</i>	Spotted Gum	120		120	38	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
984	<i>Allocasuarina littoralis</i>	Black She-oak	240		240	75	8.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
985	<i>Eucalyptus tereticornis</i>	Forest Red Gum	300		300	94	21.0	9.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
986	<i>Allocasuarina littoralis</i>	Black She-oak	150	130	198	62	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
987	<i>Eucalyptus tereticornis</i>	Forest Red Gum	200		200	63	18.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
988	<i>Eucalyptus tereticornis</i>	Forest Red Gum	330		330	104	17.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
989	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	160	130, 130	244	77	8.0	4.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
990	<i>Eucalyptus tereticornis</i>	Forest Red Gum	290		290	91	20.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
991	<i>Eucalyptus tereticornis</i>	Forest Red Gum	130		130	41	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
992	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	110		110	35	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
993	<i>Acacia leiocalyx</i>	Early-flowering Black Wattle	120		120	38	3.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
994	<i>Eucalyptus tereticornis</i>	Forest Red Gum	150		150	47	13.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
995	<i>Eucalyptus tereticornis</i>	Forest Red Gum	210	170	270	85	19.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
996	<i>Allocasuarina littoralis</i>	Black She-oak	100	100, 100	173	54	5.0	4.0	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
997	<i>Eucalyptus tereticornis</i>	Forest Red Gum	130		130	41	11.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
998	<i>Eucalyptus tereticornis</i>	Forest Red Gum	180		180	57	17.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
999	<i>Eucalyptus tereticornis</i>	Forest Red Gum	200		200	63	18.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1000	<i>Eucalyptus moluccana</i>	Gum-topped Box	250	200, 200, 180	418	131	19.0	8.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1001	<i>Acacia disparima</i>	Hickory Wattle	300		300	94	11.0	7.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
1002	Acacia disparrima	Hickory Wattle	290		290	91	13.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	
1003	Acacia disparrima	Hickory Wattle	280	250	375	118	13.0	8.0	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove stage 1	

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value							
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
1004	<i>Tipuana tipu</i>	Tipuana	240		240	75	13.0	3.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1005	<i>Spathodea companulata</i>	African Tulip	310		310	97	12.0	4.0	3.7	2.0	Regular	-	-	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1006	<i>Jacaranda mimosifolia</i>	Jacaranda	300	130	327	103	14.0	4.0	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1007	<i>Spathodea companulata</i>	African Tulip	680		680	214	16.0	7.0	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1008	<i>Ficus lyrata</i>	Fiddle Leaf Fig	190	200, 210	347	109	6.0	5.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1009	<i>Schinus terebinthifolius</i>	Broad-leaf Pepper	320		320	101	5.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP (remediation)	



Tree Schedule - Job 9216

53 Seventeen Mile Rocks Road, Oxley (The Minister for Economic Development Queensland)

11/08/2020

Specimen Details											Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
1010	<i>Eucalyptus siderophloia</i>	Grey Ironbark	350		350	110	26.0	10.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1011	<i>Eucalyptus siderophloia</i>	Grey Ironbark	380		380	119	27.0	11.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Weed tree - refer RMP	
1012	<i>Macadamia integrifolia</i>	Macadamia Nut	170	130, 100	236	74	10.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1013	<i>Corymbia citriodora</i>	Spotted Gum	350		350	110	21.0	9.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1014	<i>Jacaranda mimosifolia</i>	Jacaranda	210	180, 180, 150, 150	392	123	10.0	7.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1015	<i>Harpullia pendula</i>	Tulipwood	230		230	72	9.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
1016	<i>Ulmus parvifolia</i>	Chinese elm	250	220, 220, 100	411	129	7.0	5.0	4.9	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove remediation works	
