

Vegetation Management Plan

Version D

Stages 2 to 5 (Phase 1 & School Site)

Brisbane Catholic Education

Economic Development
Queensland

CONTENTS


- 8047 E 02 Stage 2 VMP D -- Vegetation Clearing Notes
- 8047 E 03 Stage 2 VMP D -- Key Plan
- 8047 E 04-10 Stage 2 VMP D -- Detail Sheets
- 8047 E 11 Stage 2 VMP D -- Clearing Direction
- Appendix A -- Tree Schedule

AMENDED IN RED

By: Chessa Lao
Date: 20 November 2024



Key Site Contact
Saunders Havill Group
Dr Andrew Davies
Email: andrewdavies@saundershavill.com

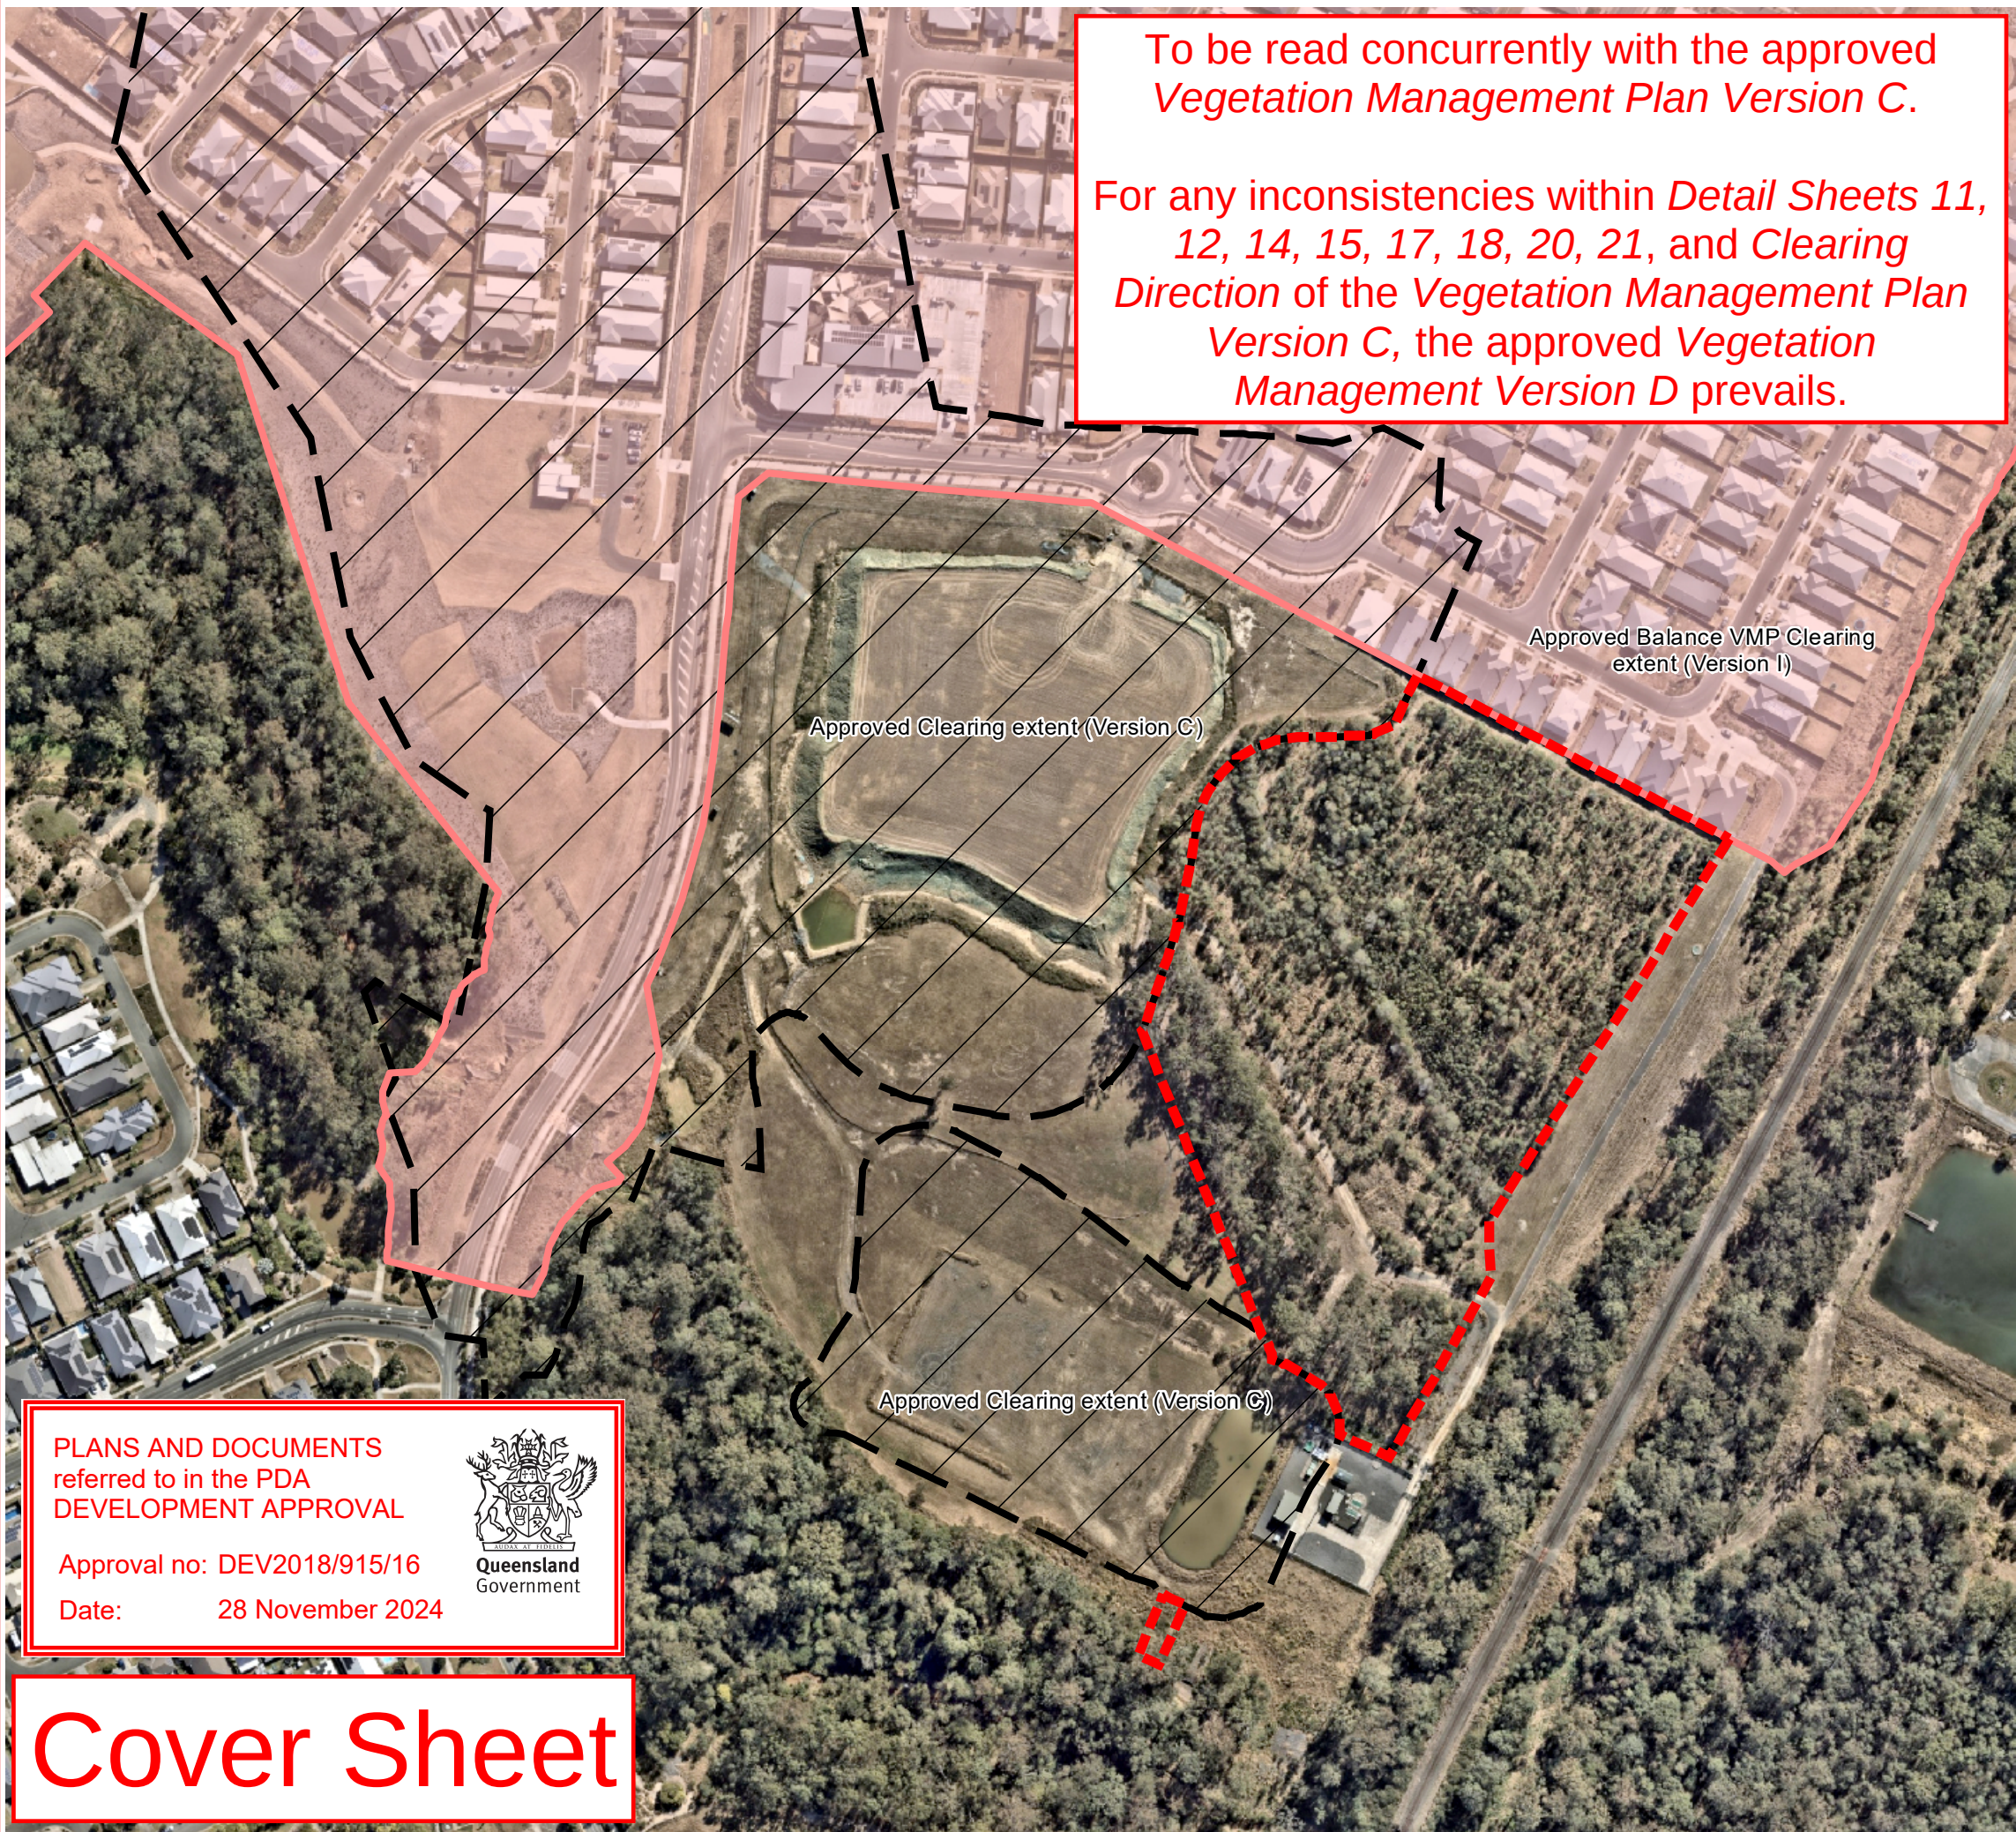

To be read concurrently with the approved
Vegetation Management Plan Version C.

For any inconsistencies within *Detail Sheets 11, 12, 14, 15, 17, 18, 20, 21, and Clearing Direction of the Vegetation Management Plan Version C*, the approved *Vegetation Management Version D* prevails.

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16
Date: 28 November 2024



Cover Sheet

Vegetation Management Plan

Vegetation Clearing - Notes

INTRODUCTION

The *Environmental Management Division* of the **Saunders Havill Group** was engaged by **Brisbane Catholic Education** to prepare a *Vegetation Management Plan (VMP)* for the removal of vegetation for the operational works of the school site in the Flagstone City project.

This VMP was drafted in response to the project's *Natural Environment Site Strategy's (NESS)* requirement for *VMPs*. The *VMP* will manage the vegetation clearing practices during operational work stages. The *VMP* will cover the first phase of clearing of stage 2-5 area of the project and correspond with the lodgement of the planning and civil applications for new roads, school site and space for surplus fill as a result of civil works. The clearing works will follow the general principal for vegetation clearing documented on this sheet.

To assist in the spatial depiction of the phase 1 clearing area and better allocate a tree retention and removal status, ecologists from the **Saunders Havill Group** completed a tree survey using Trimble Antenna based GPS units. The survey collected the following data on trees within and adjoining the phase 1 extent as provided by the project urban designer and engineer:

- Reference Point and Location
- Botanical Name / Common Name
- Trunk DBH

- AS4970-2009 – Tree Protection Zone
- Height and Spread
- Canopy and Trunk Condition Comments
- Fauna and Habitat Values and Details

Particular attention and detail was collected along Sandy Creek interface area to maximise the retention of healthy native habitat trees along the corridor.

CLEARING PHASES AND PROCESS

The following stages are required for clearing to be undertaken on this property and a copy of this *VMP* must be present with the clearing contractor on-site:

PHASE 1 – Demarcation

Tree Protection Fencing to be installed prior to the commencement of any clearing works on the site. Tree protection fencing is to be located at or beyond 12 x diameter at breast height (DBH) unless approved by an appointed Arborist around trees designated for retention or as per the locations shown in this drawing package (refer Fencing Note). Fencing shall clearly demark the extent of works ensuring no additional vegetation will be cleared.

PHASE 2 - Pre-start Meeting

Fencing shall be in place at the time of the official pre-start meeting for inspection by the Environmental Coordinator. A fauna spotter pre-works assessment report must be

carried out prior to the pre-start meeting and provided to the clearing contractor (Refer to *Fauna Management Plan* accompanying this application for details).


PHASE 4 - Undertake Clearing Works

Undertake removal of vegetation once approved for removal by the appointed fauna spotter. Clearing will occur in the direction outlined in *Fauna Management Plan* and managed by the appointed fauna spotter to allow all fauna unimpeded movement away from works areas. The contractor is to follow any tree felling directions of the appointed fauna spotter/arborist, including but not limited to, an excavator vertical tree grab attachment or cherry picker, where the use of bulldozer is not appropriate.

PHASE 5 - Post clearing Works

Cleared vegetation is to be reused on or off premises. Recycling techniques include mulching, tub-grinding, wood chipping and salvage (e.g. custom milling). Trees with identified hollows should have the hollow section preserved and this section should be suitably mounted on nearby or adjacent suitable trees.


Carry out assessment of all retained trees by a qualified arborist along the edge of development once civil works have been completed. Implement any tree management measures if advised by the arborist.

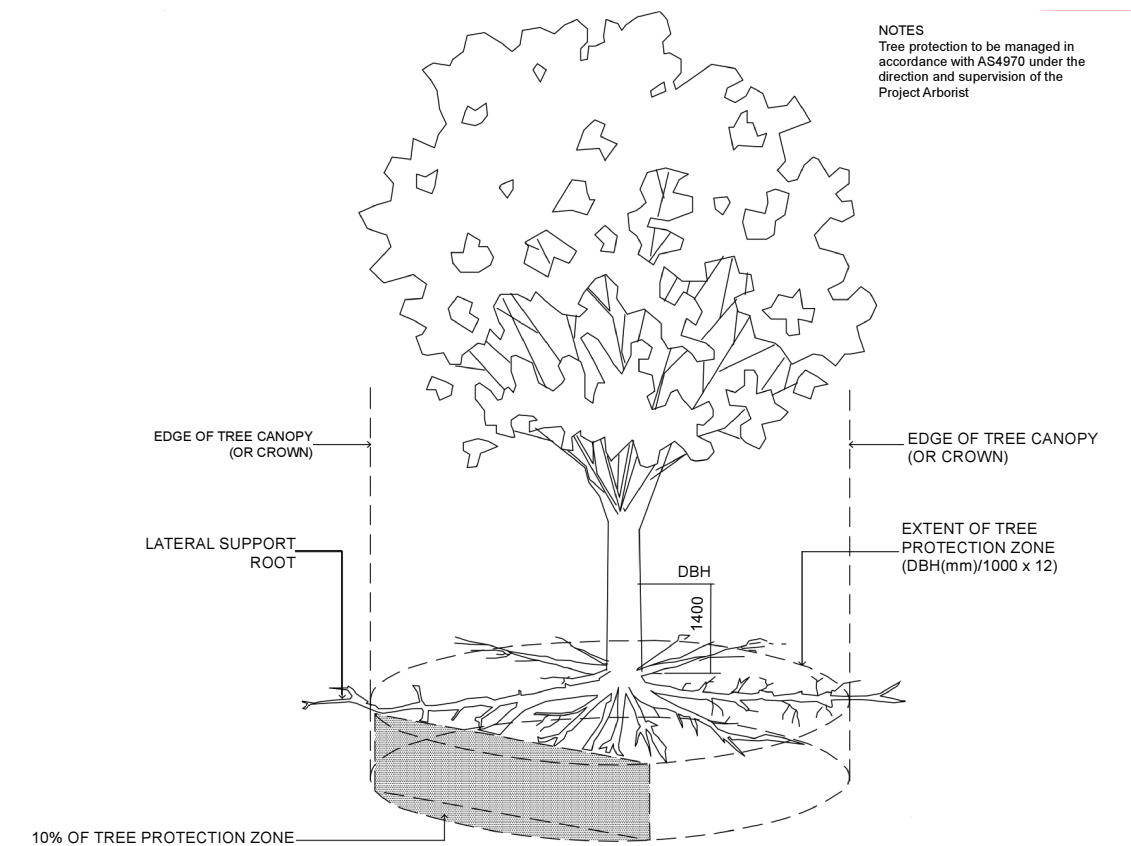

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16

Date: 28 November 2024

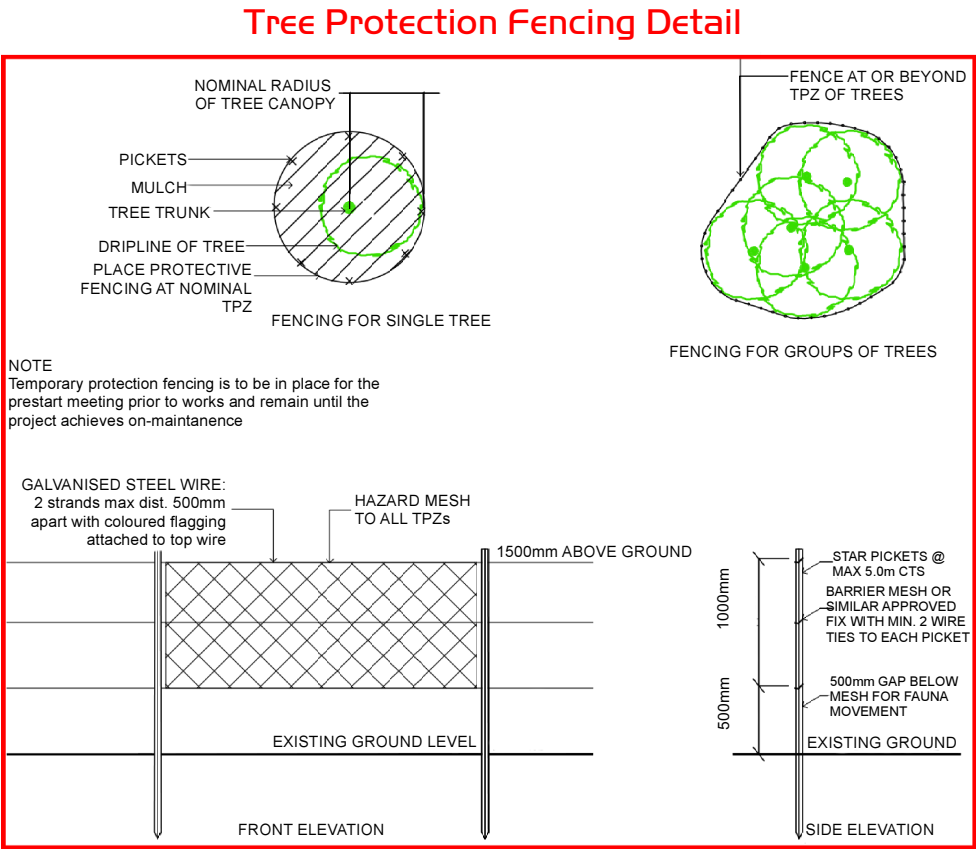

Brisbane Catholic Education

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DERIVED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	5/09/2024	Civil extent amendments	AD

CLIENT:

Brisbane Catholic Education

PROJECT:


Flagstone City - Stage 2-5
Phase 1 works (School Site)



PLAN OF:

Vegetation
Management Plan


DATE: 5/09/2024	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 02 Stage 2 VMP D	

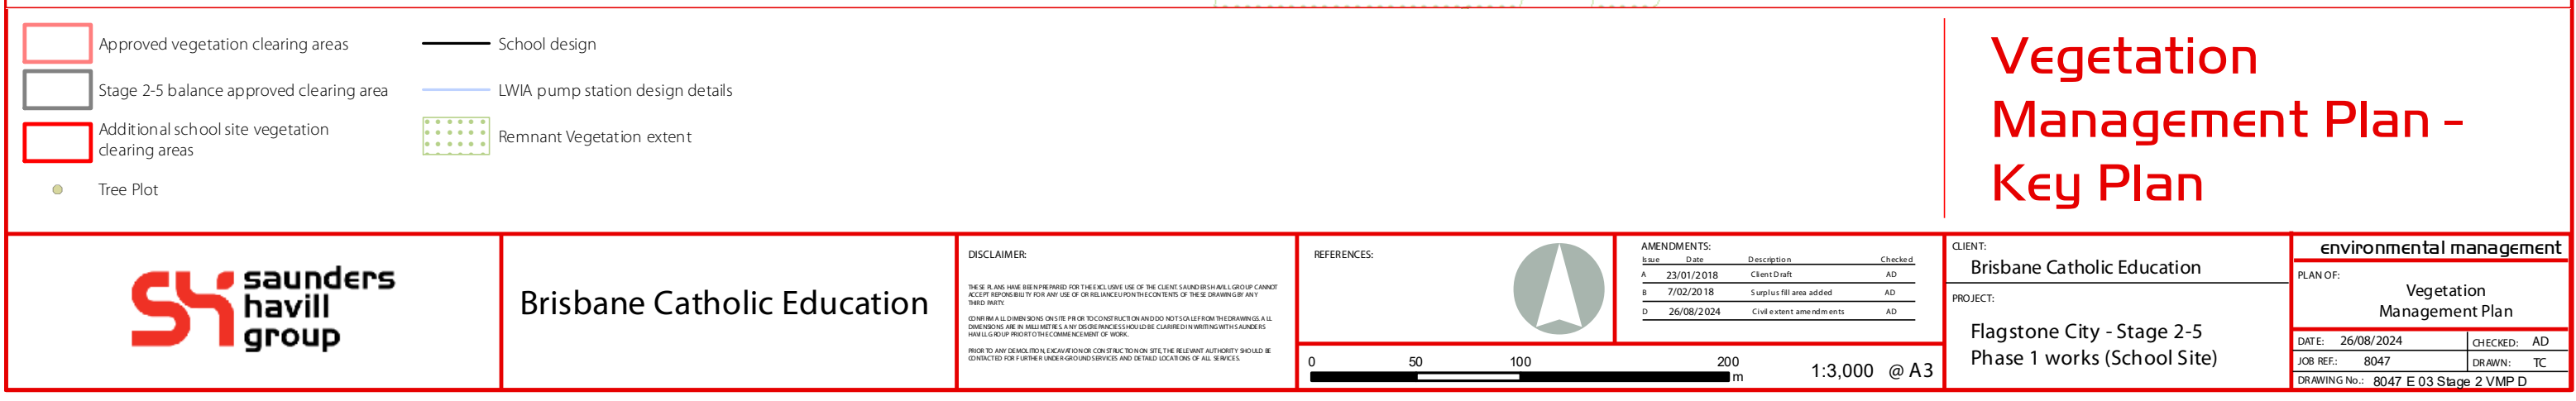

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16

Date: 28 November 2024

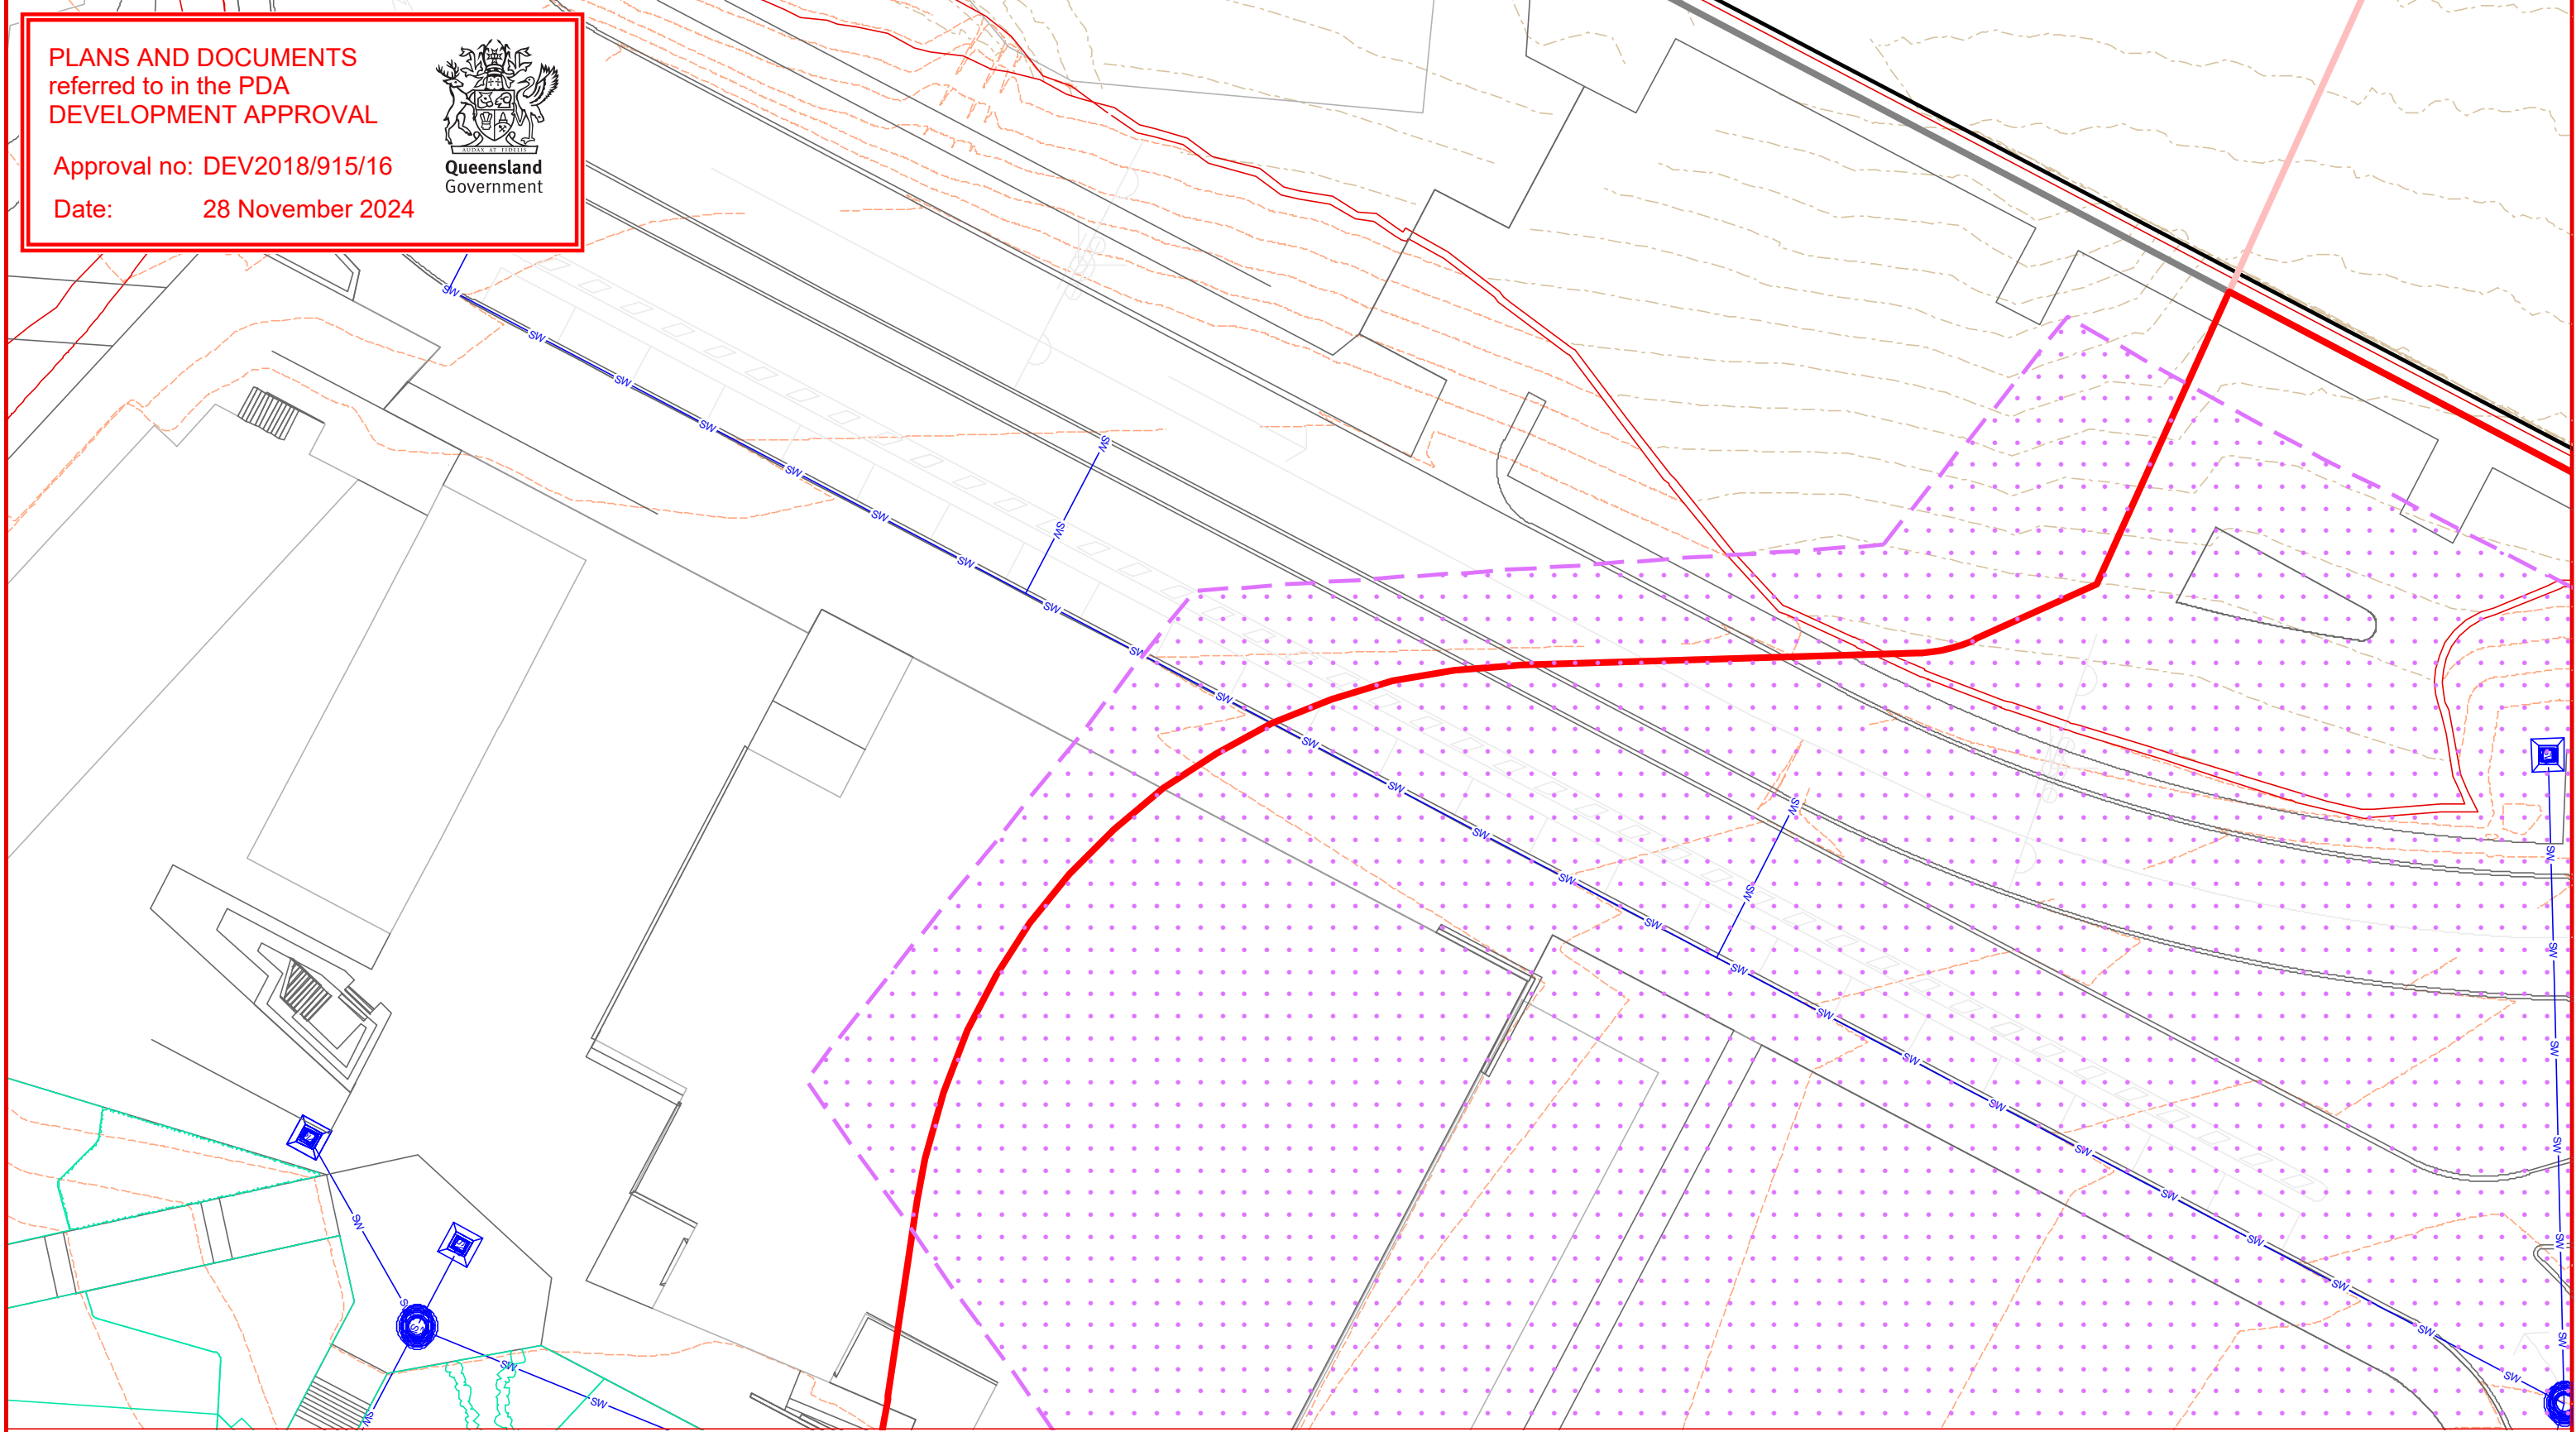

Tree to retain (w/TPZ)

Additional tree to remove (w/TPZ)

Tree approved to remove in previous VMPs (w/TPZ)

Approved vegetation clearing areas

Stage 2-5 balance approved clearing area

Additional school site vegetation clearing areas

Exempt vegetation to be cleared that does not meet the significant definition

School lot boundary

School design (buildings/paths)

Landscape areas

Design contours

Earthwork works batter

Earthworks retaining wall

Road line-markings

Stormwater design

Water design

Existing contours

Stockpile location (indicative)

LWIA pump station design details

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 04

Brisbane Catholic Education

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT SAUNDERS HAVILL GROUP. THE CLIENT ACCEPTS RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFORM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD


CLIENT: Brisbane Catholic Education

PROJECT: Flagstone City - Stage 2-5 Phase 1 works (School Site)

environmental management

PLAN OF: Vegetation Management Plan

DATE: 26/08/2024	CHECKED: AD
JOB REF: 7833	DRAWN: TC
DRAWING No.: 8047 E 04 Stage 2 VMP D	

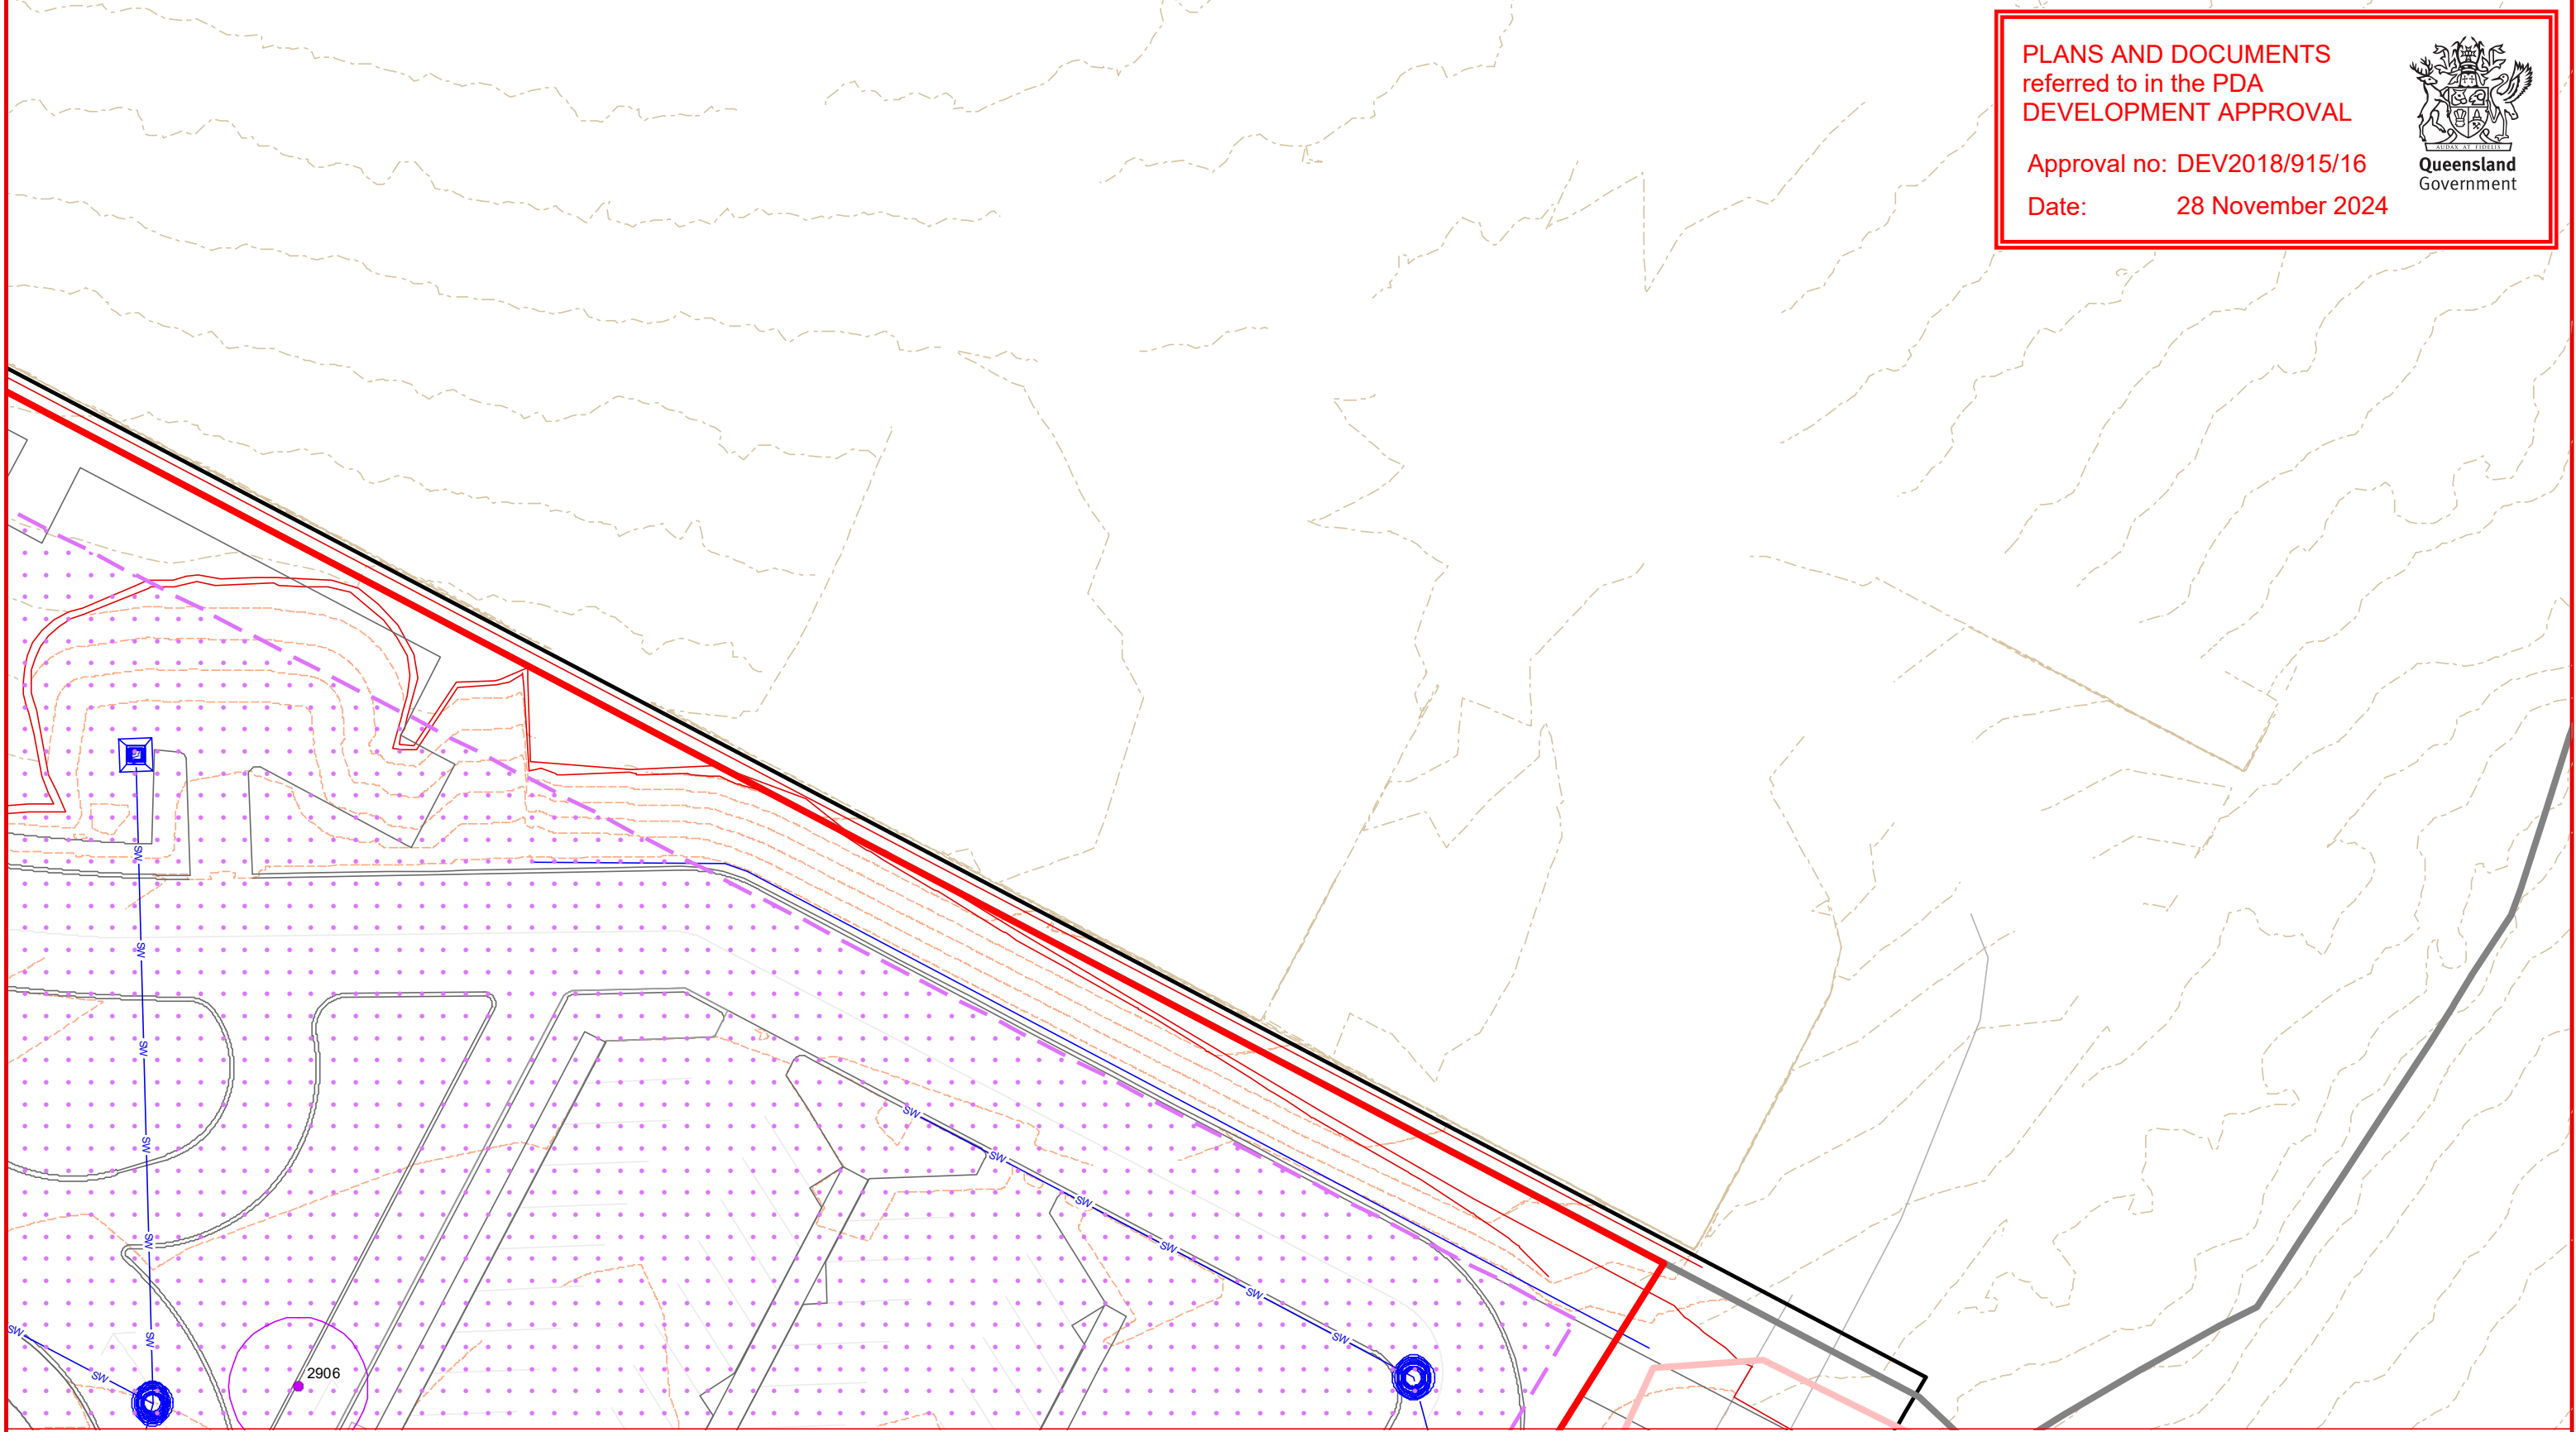

Tree to retain (w/TPZ)

Additional tree to remove (w/TPZ)

Tree approved to remove in previous VMPs (w/TPZ)

Approved vegetation clearing areas

Stage 2-5 balance approved clearing area

Additional school site vegetation clearing areas

Exempt vegetation to be cleared that does not meet the significant definition

School lot boundary

School design (buildings/paths)

Landscape areas

Design contours

Earthwork works batter

Earthworks retaining wall

Road line-markings

Stormwater design

Water design

Existing contours

Stockpile location (indicative)

LWIA pump station design details

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer


Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 05

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16

Date: 28 November 2024

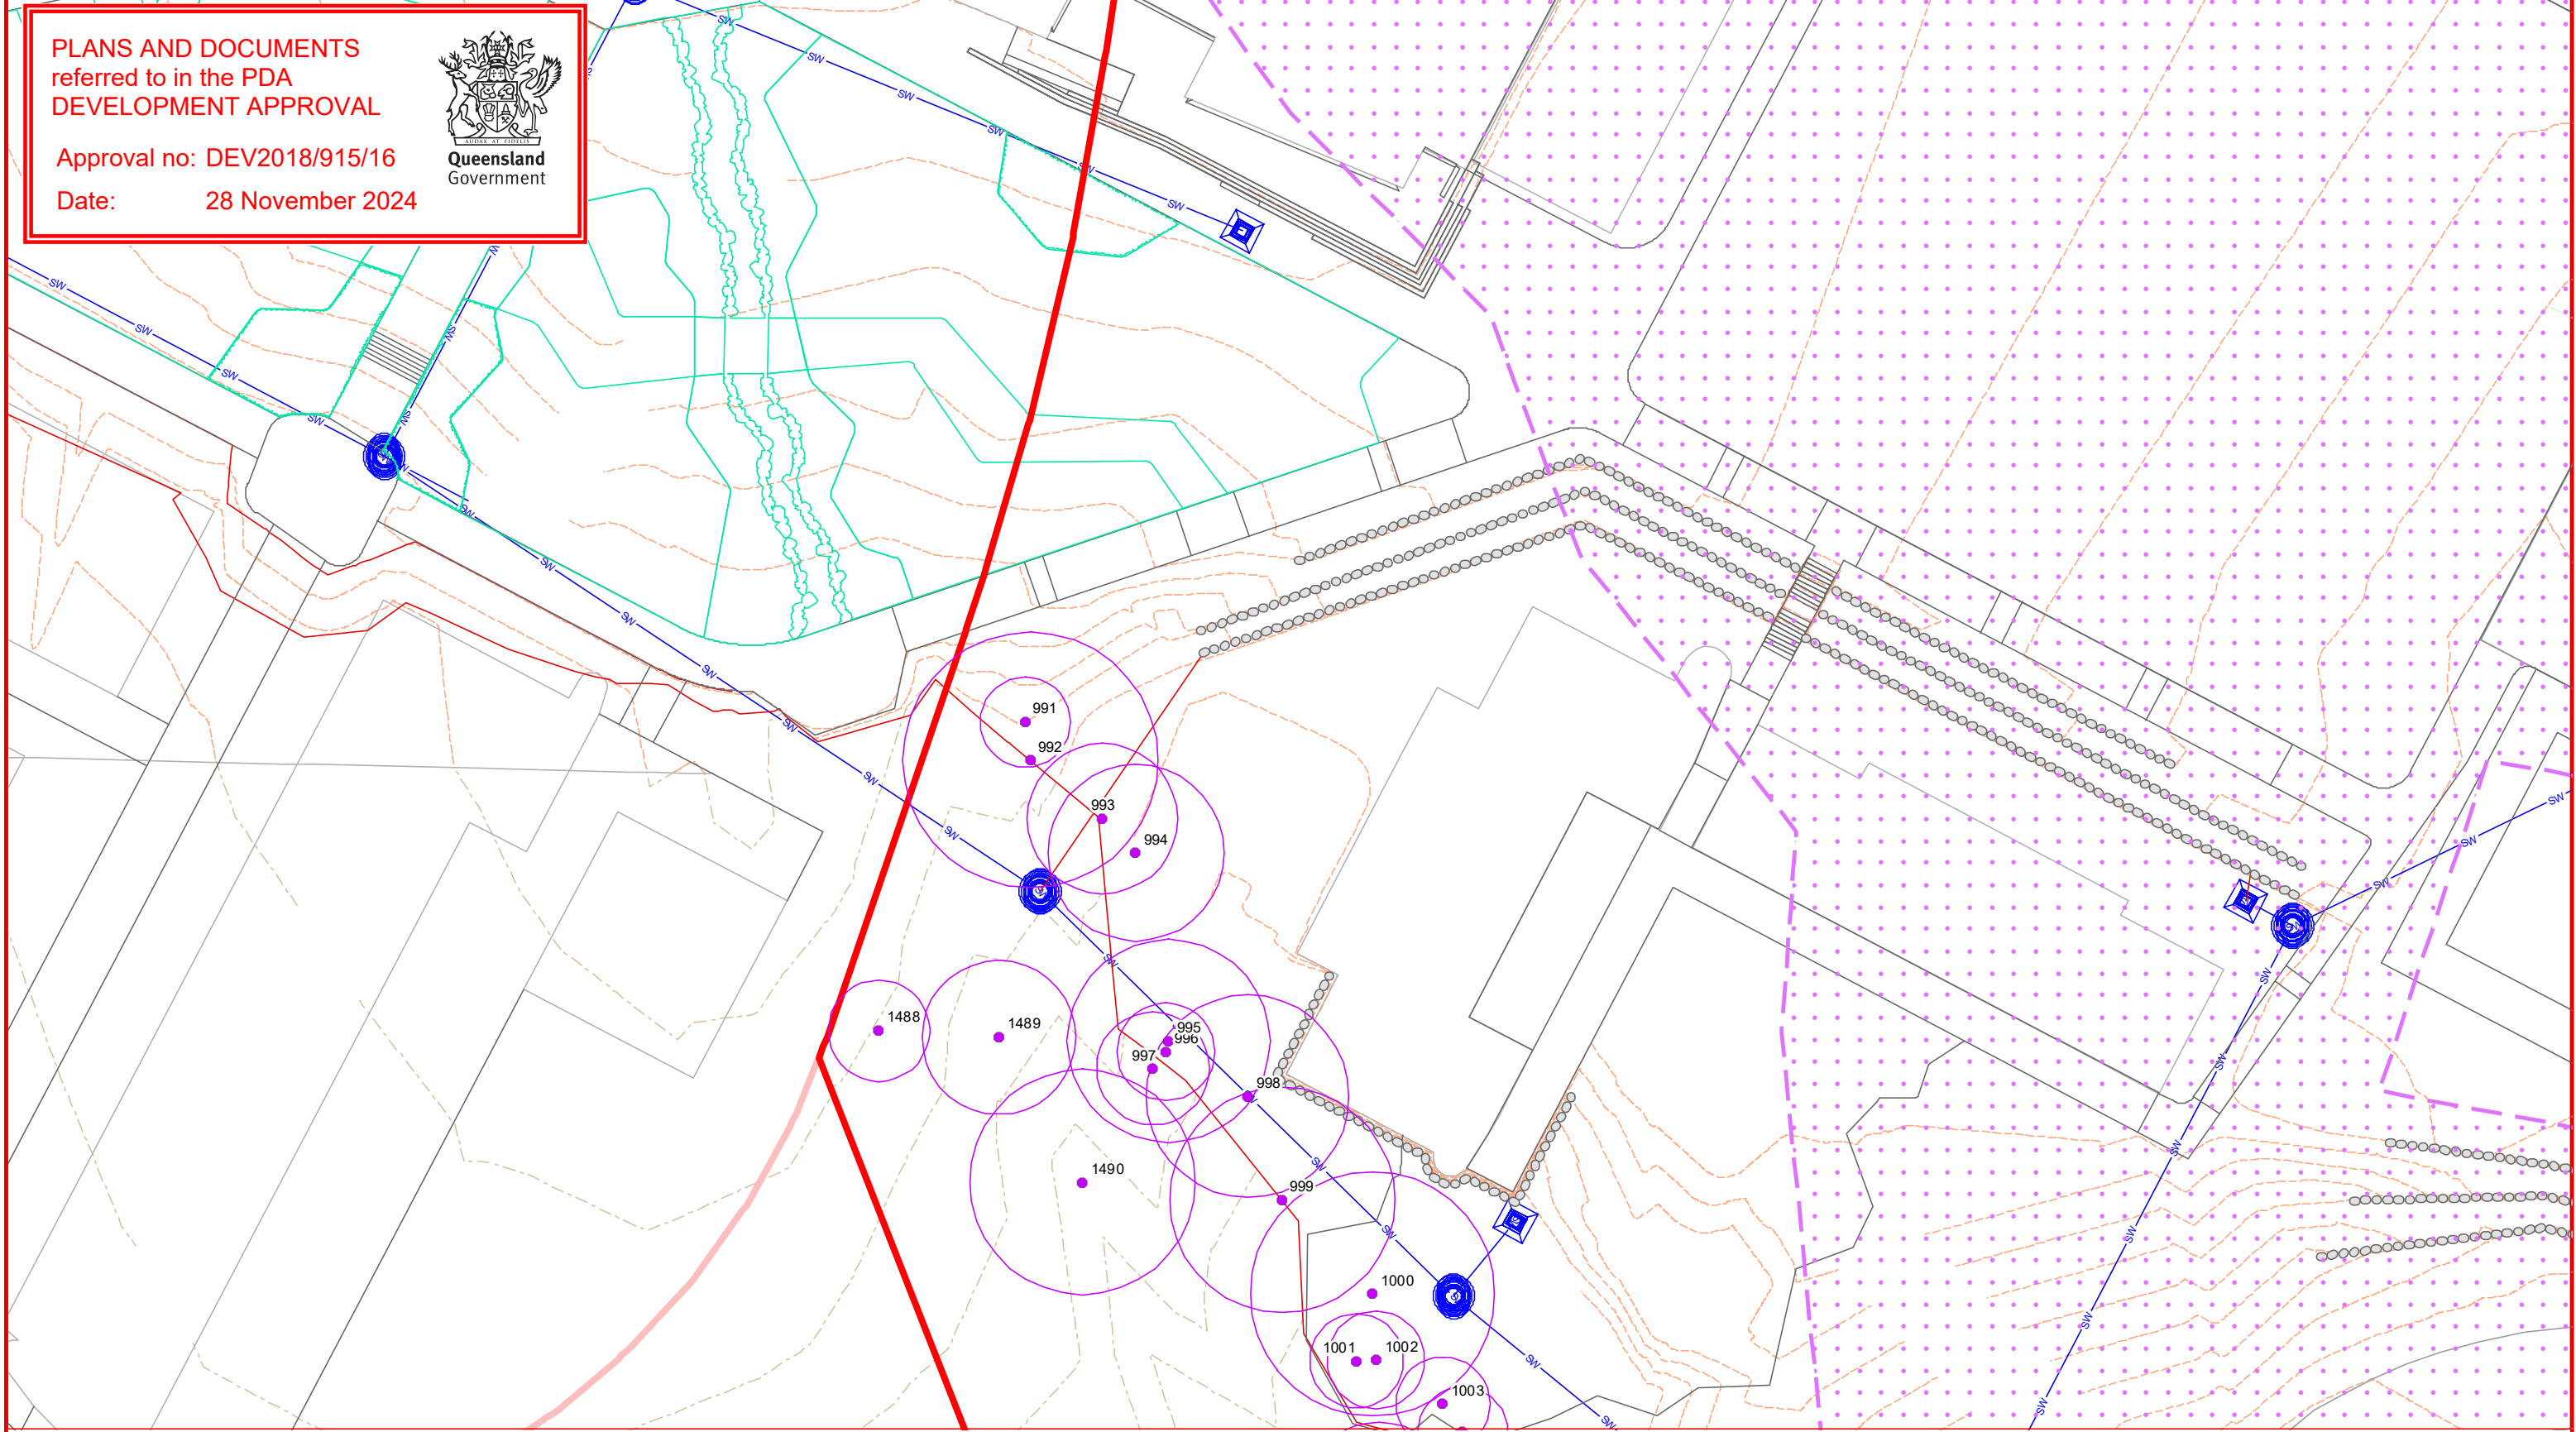

Tree to retain (w/TPZ)

Additional tree to remove (w/TPZ)

Tree approved to remove in
previous VMPs (w/TPZ)

Approved vegetation clearing areas

Stage 2-5 balance approved clearing area

Additional school site vegetation
clearing areas

Exempt vegetation to be cleared that
does not meet the significant definition

School lot boundary

School design (buildings/paths)

Landscape areas

Design contours

Earthwork works batter

Earthworks retaining wall

Road line-markings

Stormwater design

Water design

Existing contours

Stockpile location (indicative)

LWIA pump station design details

Tree protection fencing -
to be fauna friendly design &
subject to minor changes by
Arborist and civil engineer

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 06



Brisbane Catholic Education

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT AND BRISBANE CATHOLIC EDUCATION GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:



0 10 20 m

1:400 @ A3

AMENDMENTS:

Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD

CLIENT:

Brisbane Catholic Education

PROJECT:

Flagstone City - Stage 2-5
Phase 1 works (School Site)

environmental management

PLAN OF:

Vegetation
Management Plan


DATE: 26/08/2024

CHECKED: AD

JOB REF: 7833

DRAWN: TC

DRAWING No.: 8047 E 06 Stage 2 VMP D

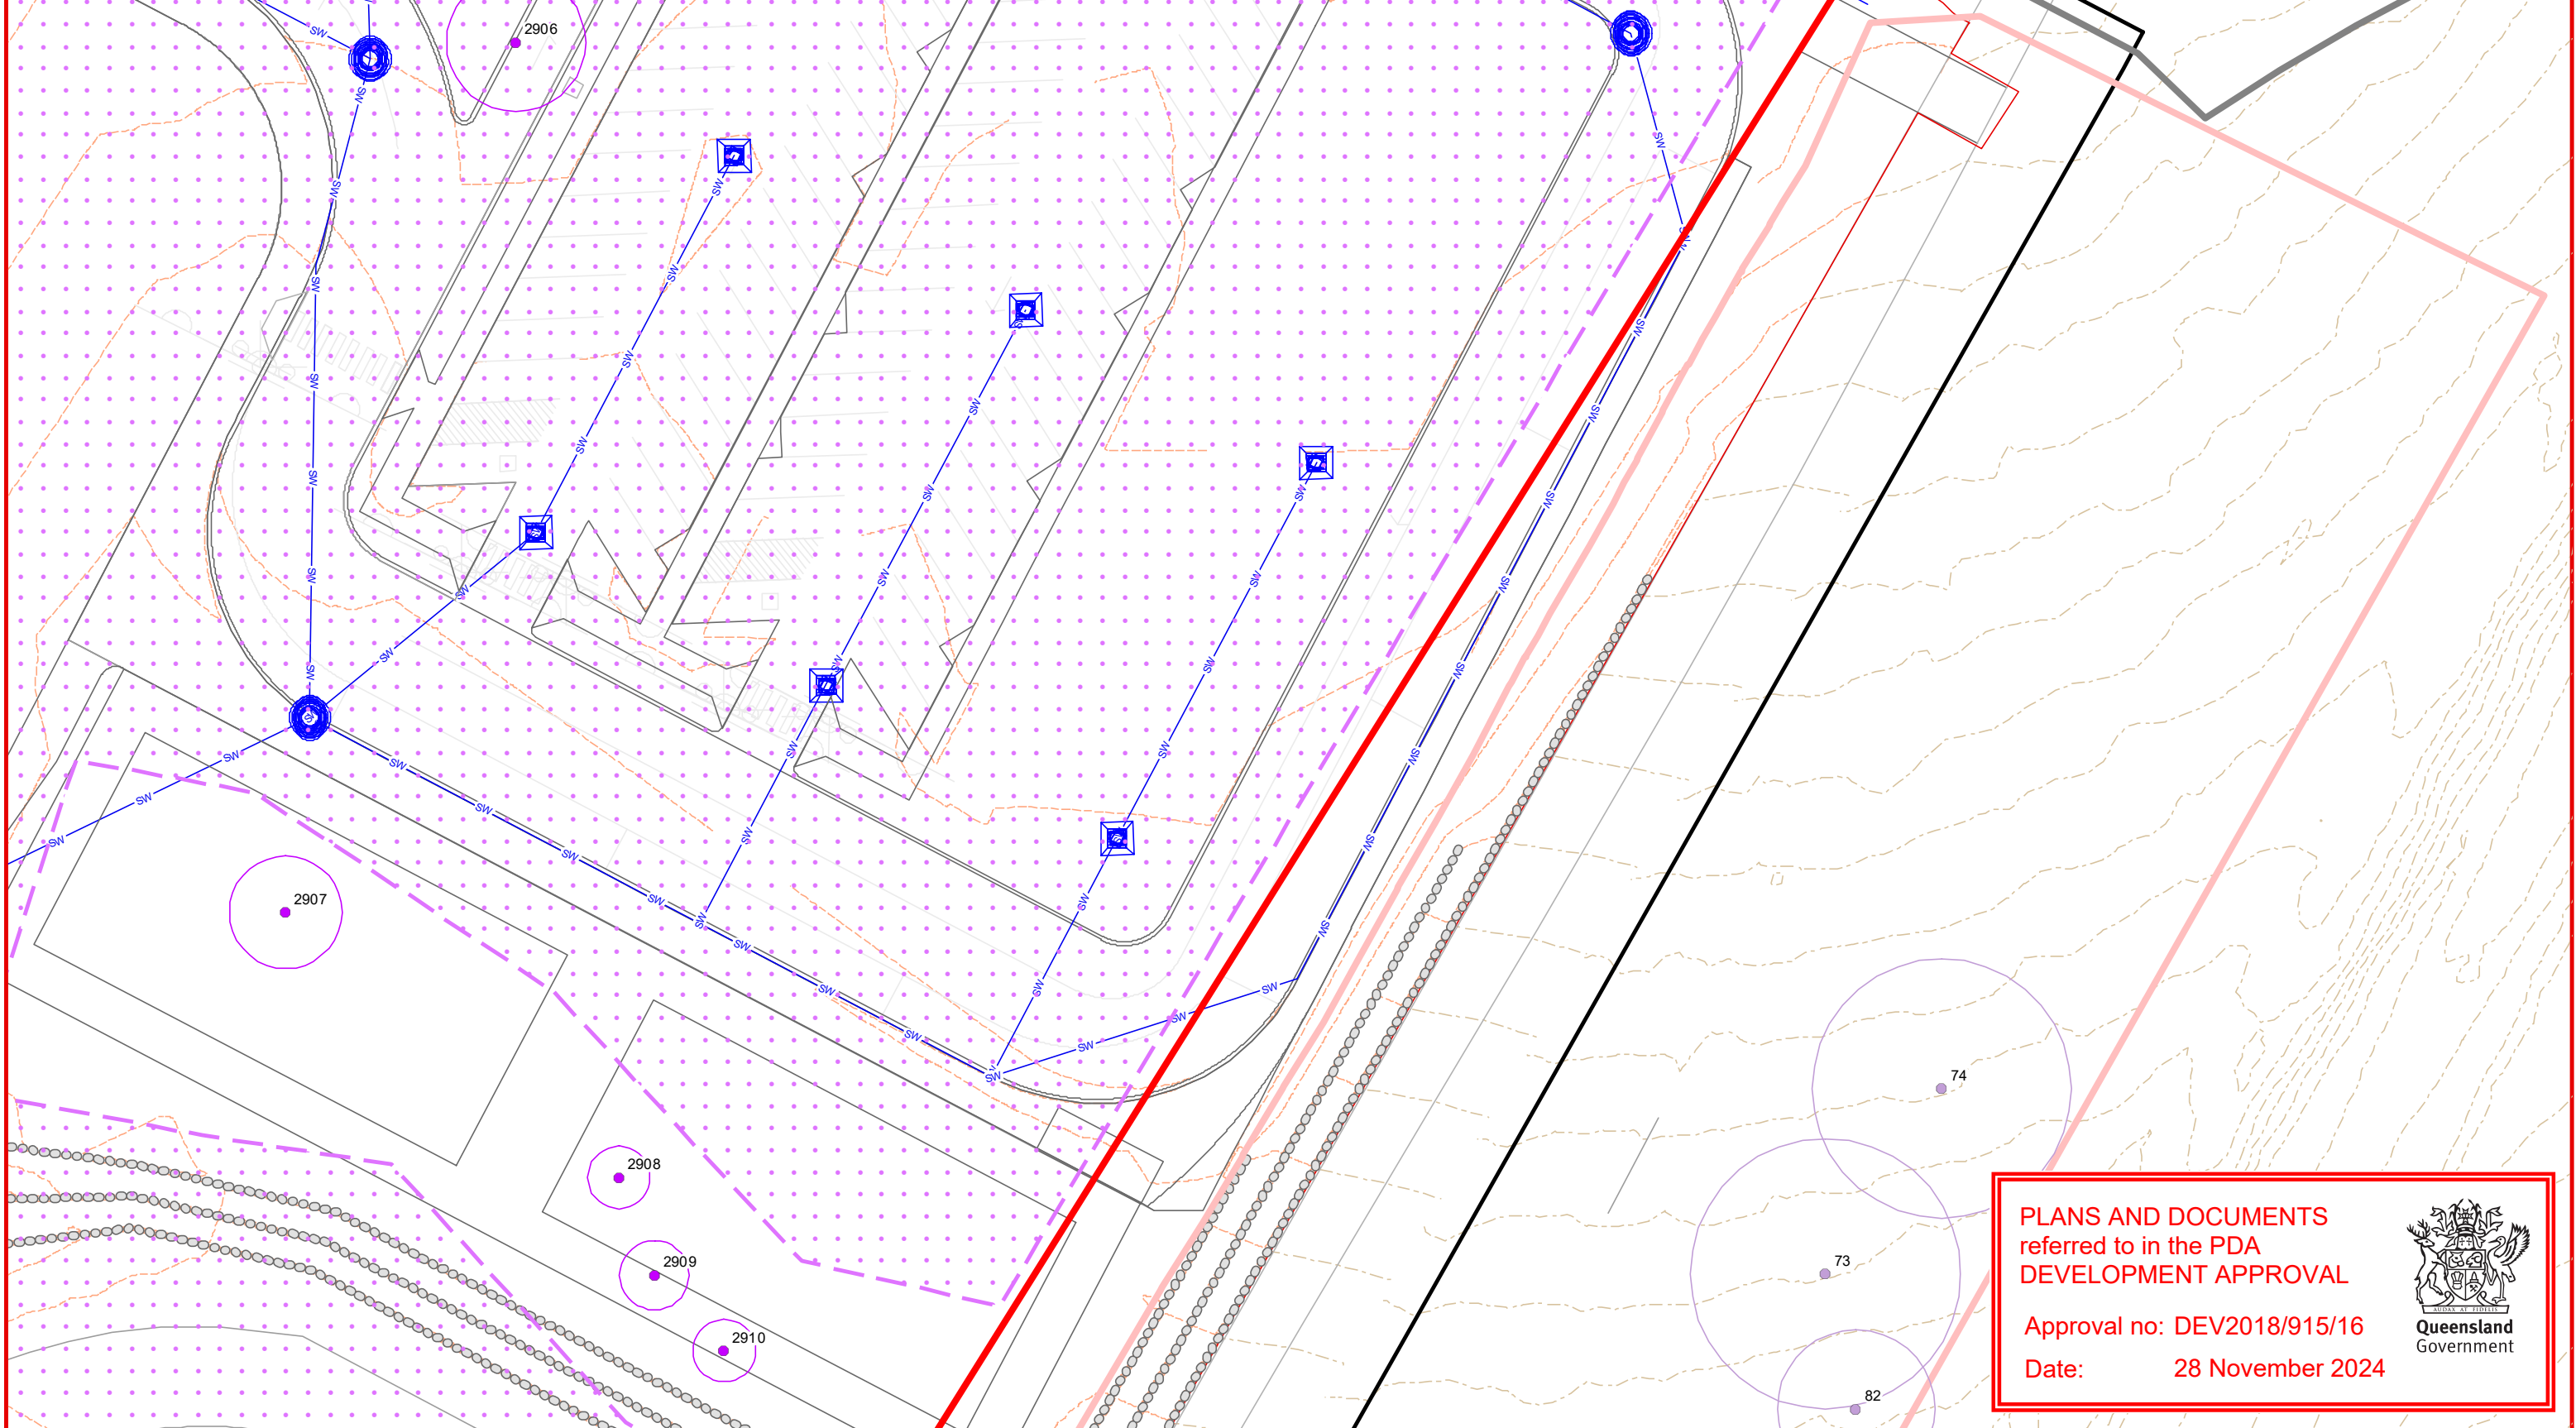

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16
Date: 28 November 2024




- Tree to retain (w/TPZ)
- Additional tree to remove (w/TPZ)
- Tree approved to remove in previous VMPs (w/TPZ)
- Approved vegetation clearing areas
- Stage 2-5 balance approved clearing area
- Additional school site vegetation clearing areas
- Exempt vegetation to be cleared that does not meet the significant definition
- School lot boundary
- School design (buildings/paths)
- Landscape areas
- Design contours
- Earthwork works batter
- Earthworks retaining wall
- Road line-markings
- Stormwater design
- Water design
- Existing contours
- Stockpile location (indicative)
- LWIA pump station design details
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 07



Brisbane Catholic Education

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT SAUNDERS HAVILL GROUP. THE CLIENT ACCEPTS RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFORM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, CONSTRUCTION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.




AMENDMENTS:			
Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD

CLIENT:
Brisbane Catholic Education
PROJECT:
Flagstone City - Stage 2-5
Phase 1 works (School Site)

environmental management

PLAN OF:	
Vegetation Management Plan	
DATE: 26/08/2024	CHECKED: AD
JOB REF: 7833	DRAWN: TC
DRAWING No.: 8047 E 07 Stage 2 VMP D	

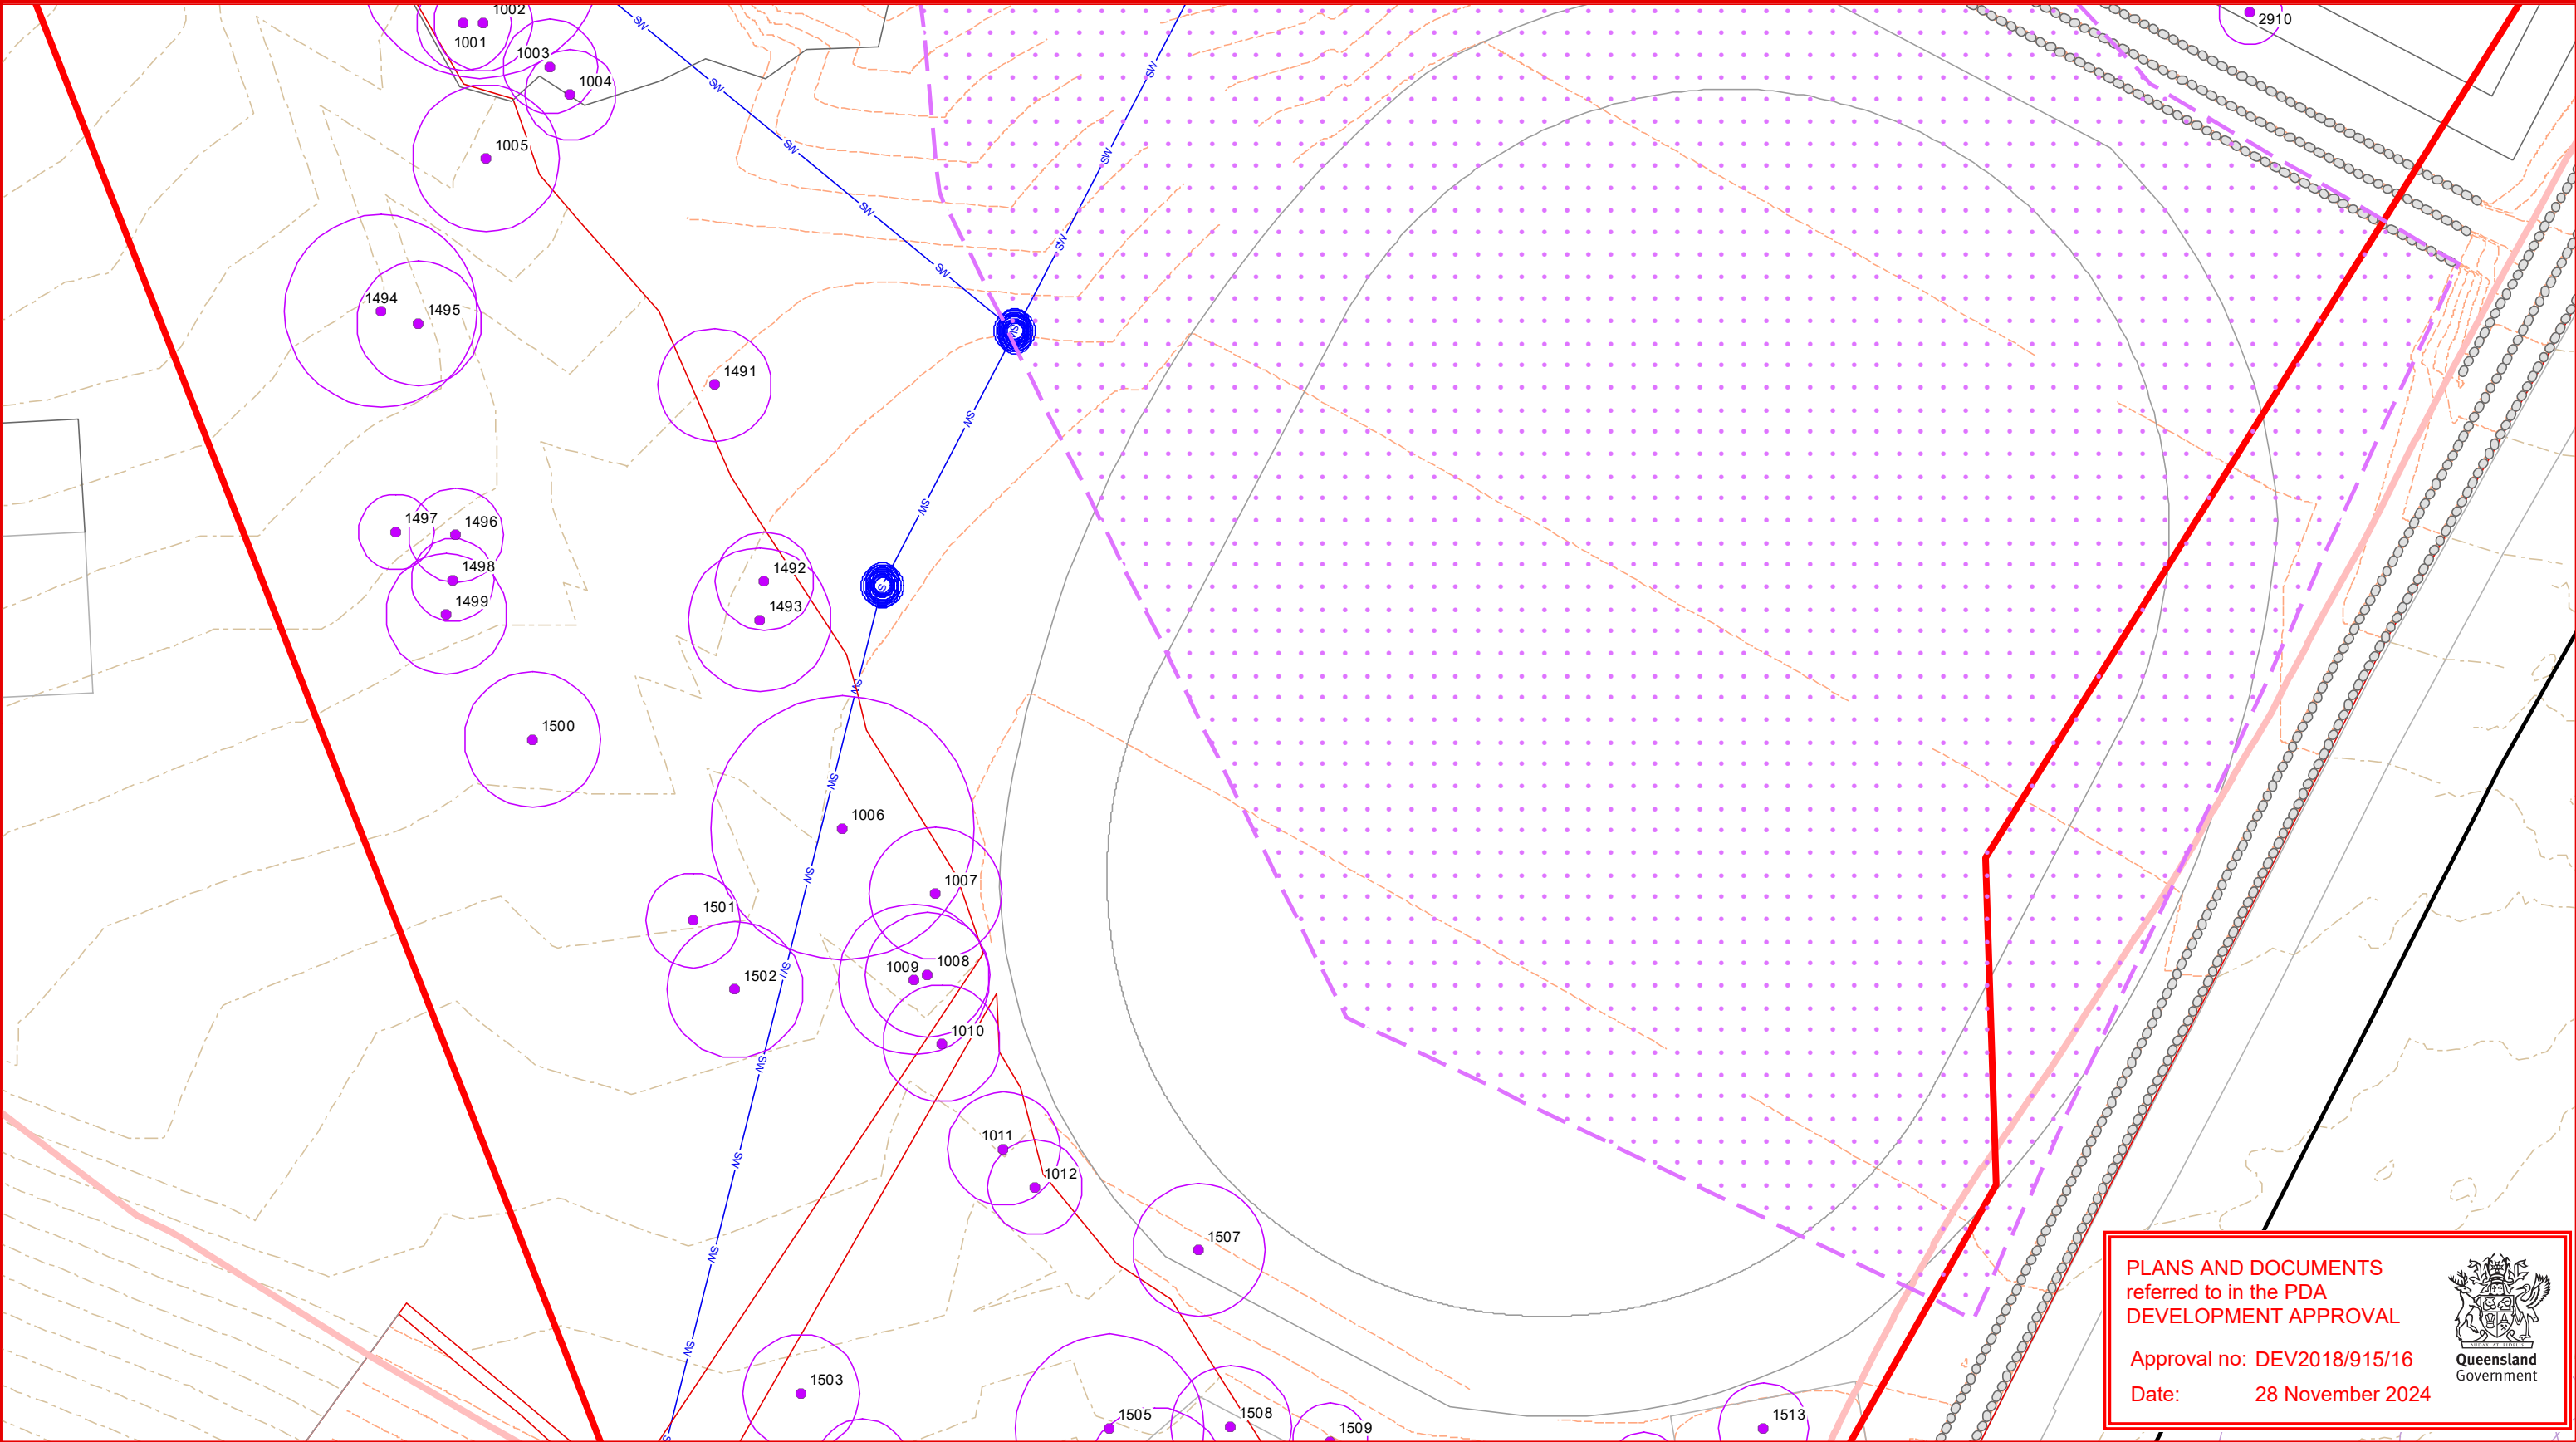

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16

Date: 28 November 2024



Queensland
Government



Tree to retain (w/TPZ)



Additional tree to remove (w/TPZ)



Tree approved to remove in previous VMPs (w/TPZ)



Approved vegetation clearing areas



Stage 2-5 balance approved clearing area



Additional school site vegetation clearing areas



Exempt vegetation to be cleared that does not meet the significant definition



School lot boundary



School design (buildings/paths)



Landscape areas



Design contours



Earthwork works batter



Earthworks retaining wall



Road line-markings



Stormwater design



Water design



Existing contours



Stockpile location (indicative)



LWIA pump station design details



Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer



Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 08



**saunders
havill
group**

Brisbane Catholic Education

DISCLAIMER:


THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT SAUNDERS HAVILL GROUP. THE GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, LANDSCAPE OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:





AMENDMENTS:

Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD


CLIENT:
Brisbane Catholic Education

PROJECT:
Flagstone City - Stage 2-5
Phase 1 works (School Site)

environmental management

PLAN OF:
Vegetation Management Plan

DATE: 26/08/2024	CHECKED: AD
JOB REF: 7833	DRAWN: TC
DRAWING No.: 8047 E 08 Stage 2 VMP D	

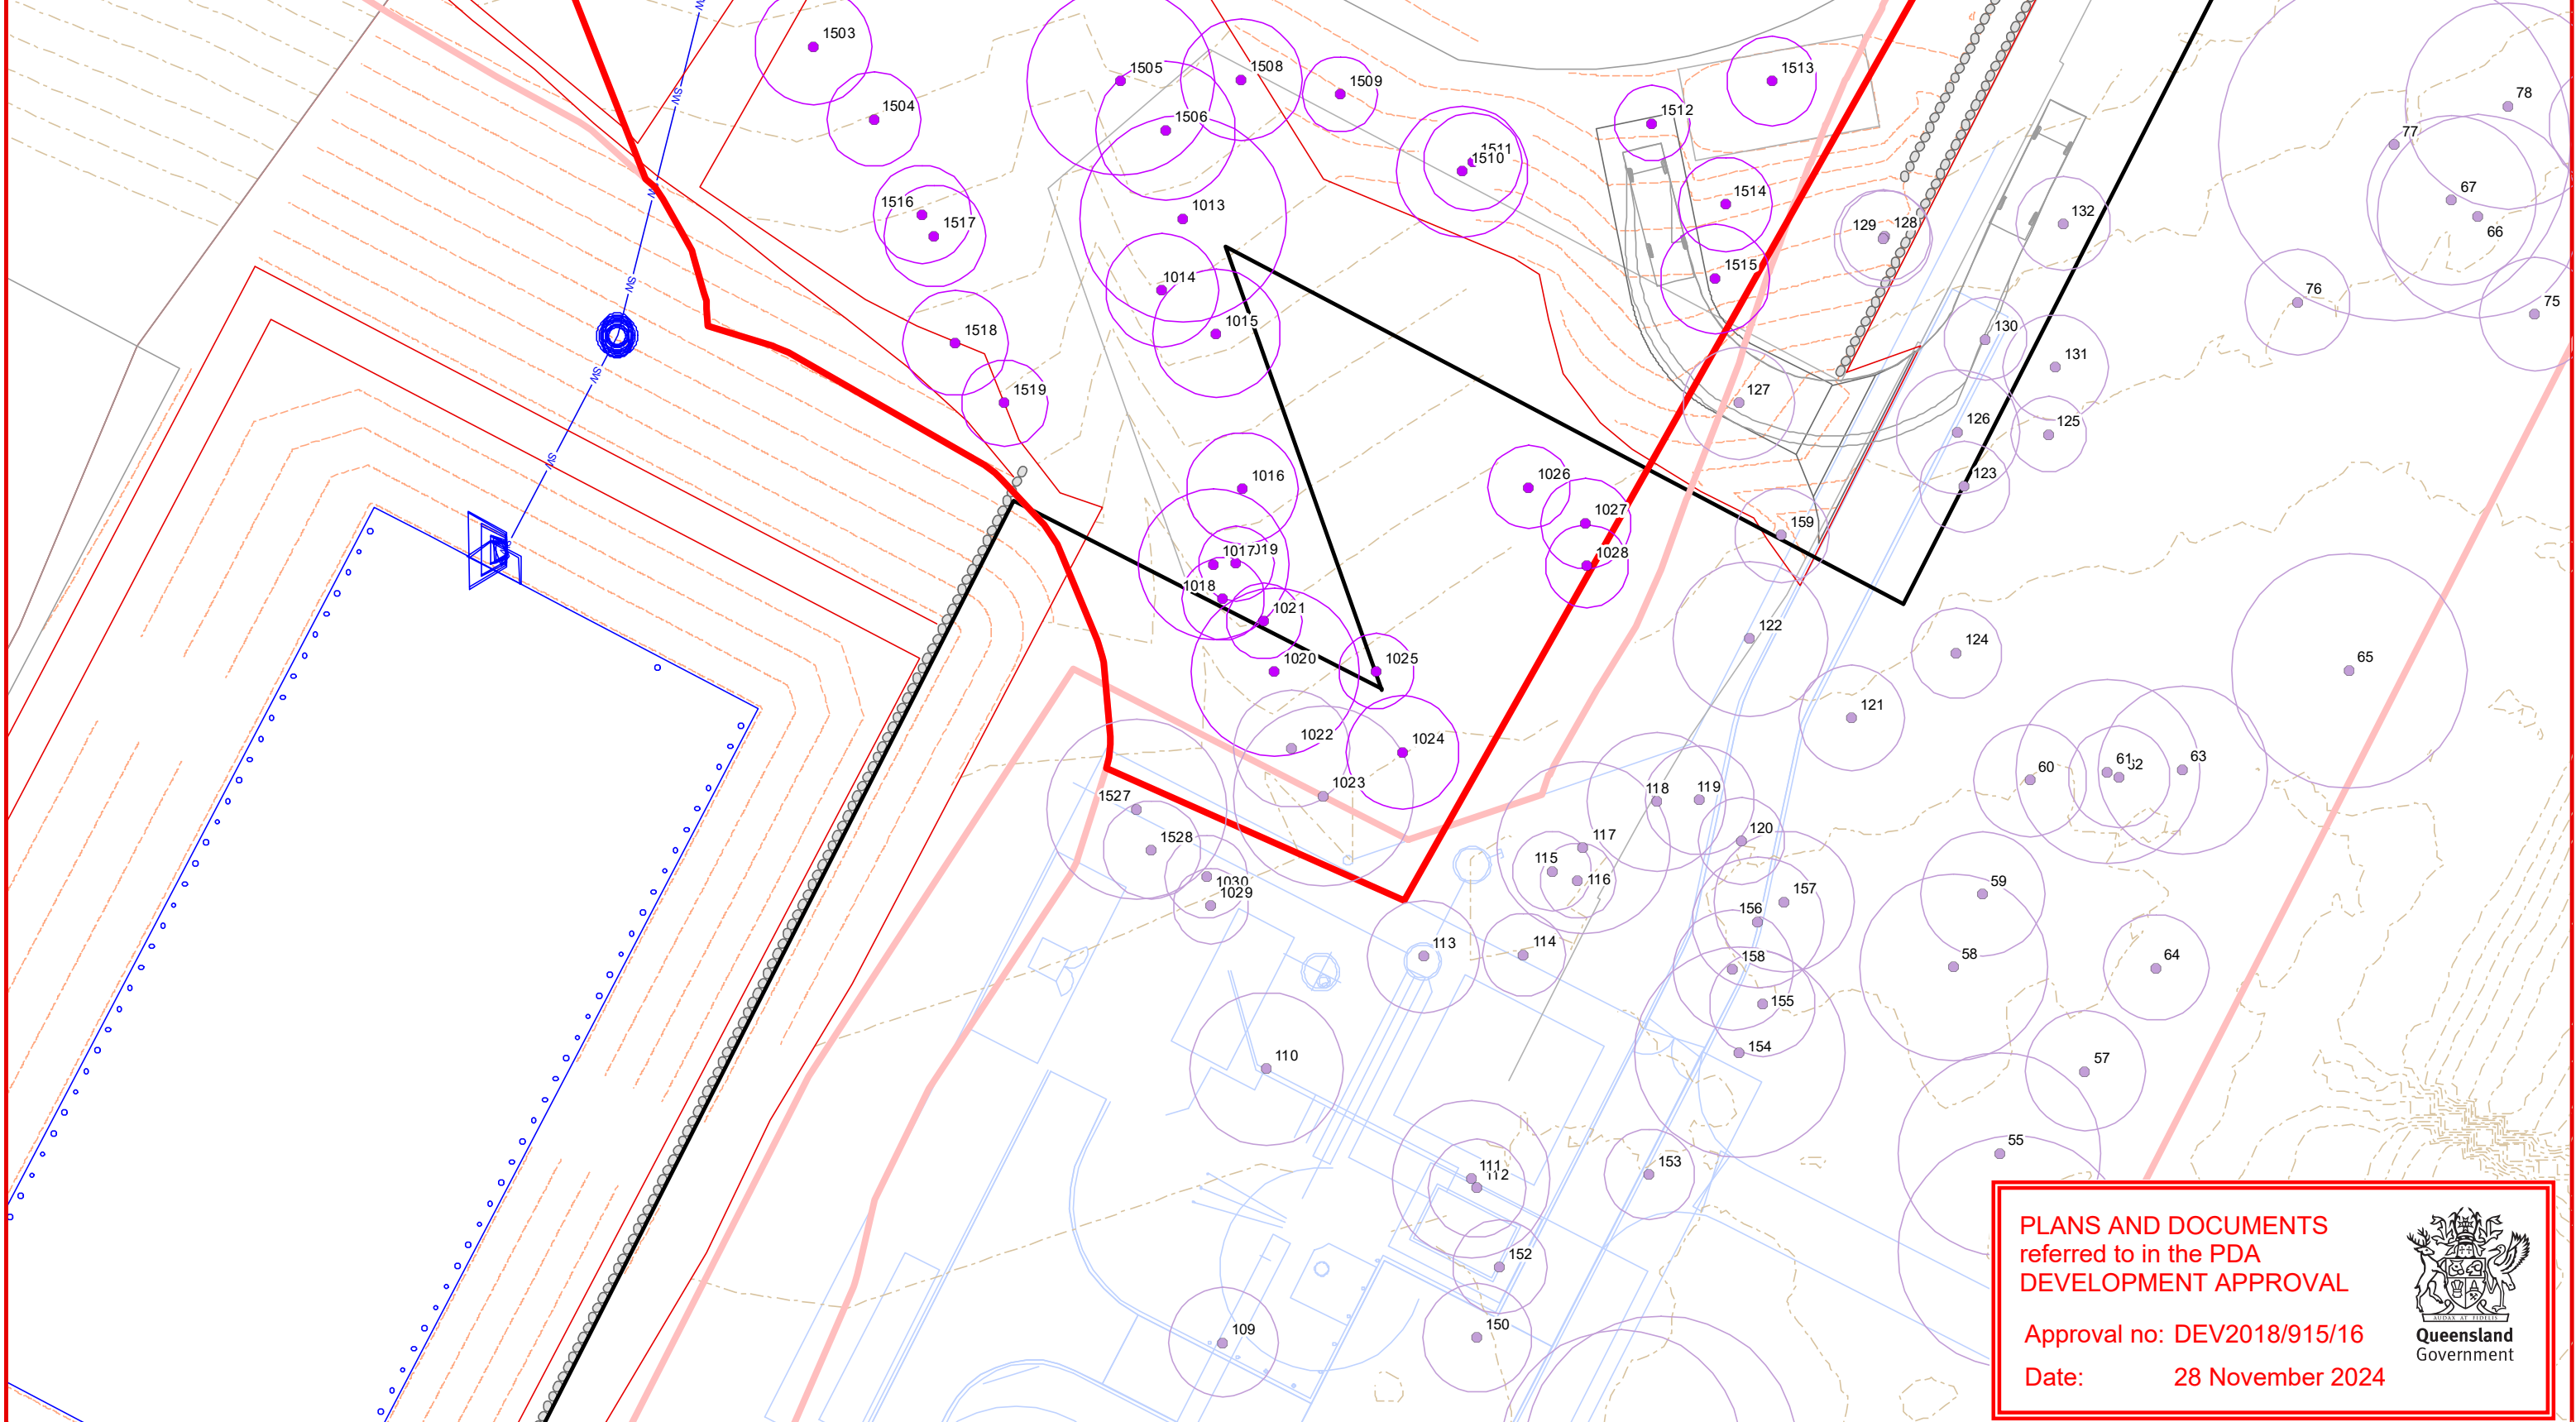

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16
Date: 28 November 2024



- Tree to retain (w/TPZ)

Additional tree to remove (w/TPZ)

Tree approved to remove in previous VMPs (w/TPZ)
- Approved vegetation clearing areas

Stage 2-5 balance approved clearing area

Additional school site vegetation clearing areas

Exempt vegetation to be cleared that does not meet the significant definition

School lot boundary
- School design (buildings/paths)

Landscape areas

Design contours

Earthwork works batter

Earthworks retaining wall
- Road line-markings

Stormwater design

Water design

Existing contours (0.5m)
- Stockpile location (indicative)

LWIA pump station design details
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 09



Brisbane Catholic Education

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT SAUNDERS HAVILL GROUP. THE GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:

1:400 @ A3

AMENDMENTS:			
Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD

CLIENT:
Brisbane Catholic Education

PROJECT:
Flagstone City - Stage 2-5
Phase 1 works (School Site)

environmental management

PLAN OF:


Vegetation
Management Plan

DATE: 26/08/2024	CHECKED: AD
JOB REF: 7833	DRAWN: TC
DRAWING No.: 8047 E 09 Stage 2 VMP D	

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2018/915/16

Date: 28 November 2024

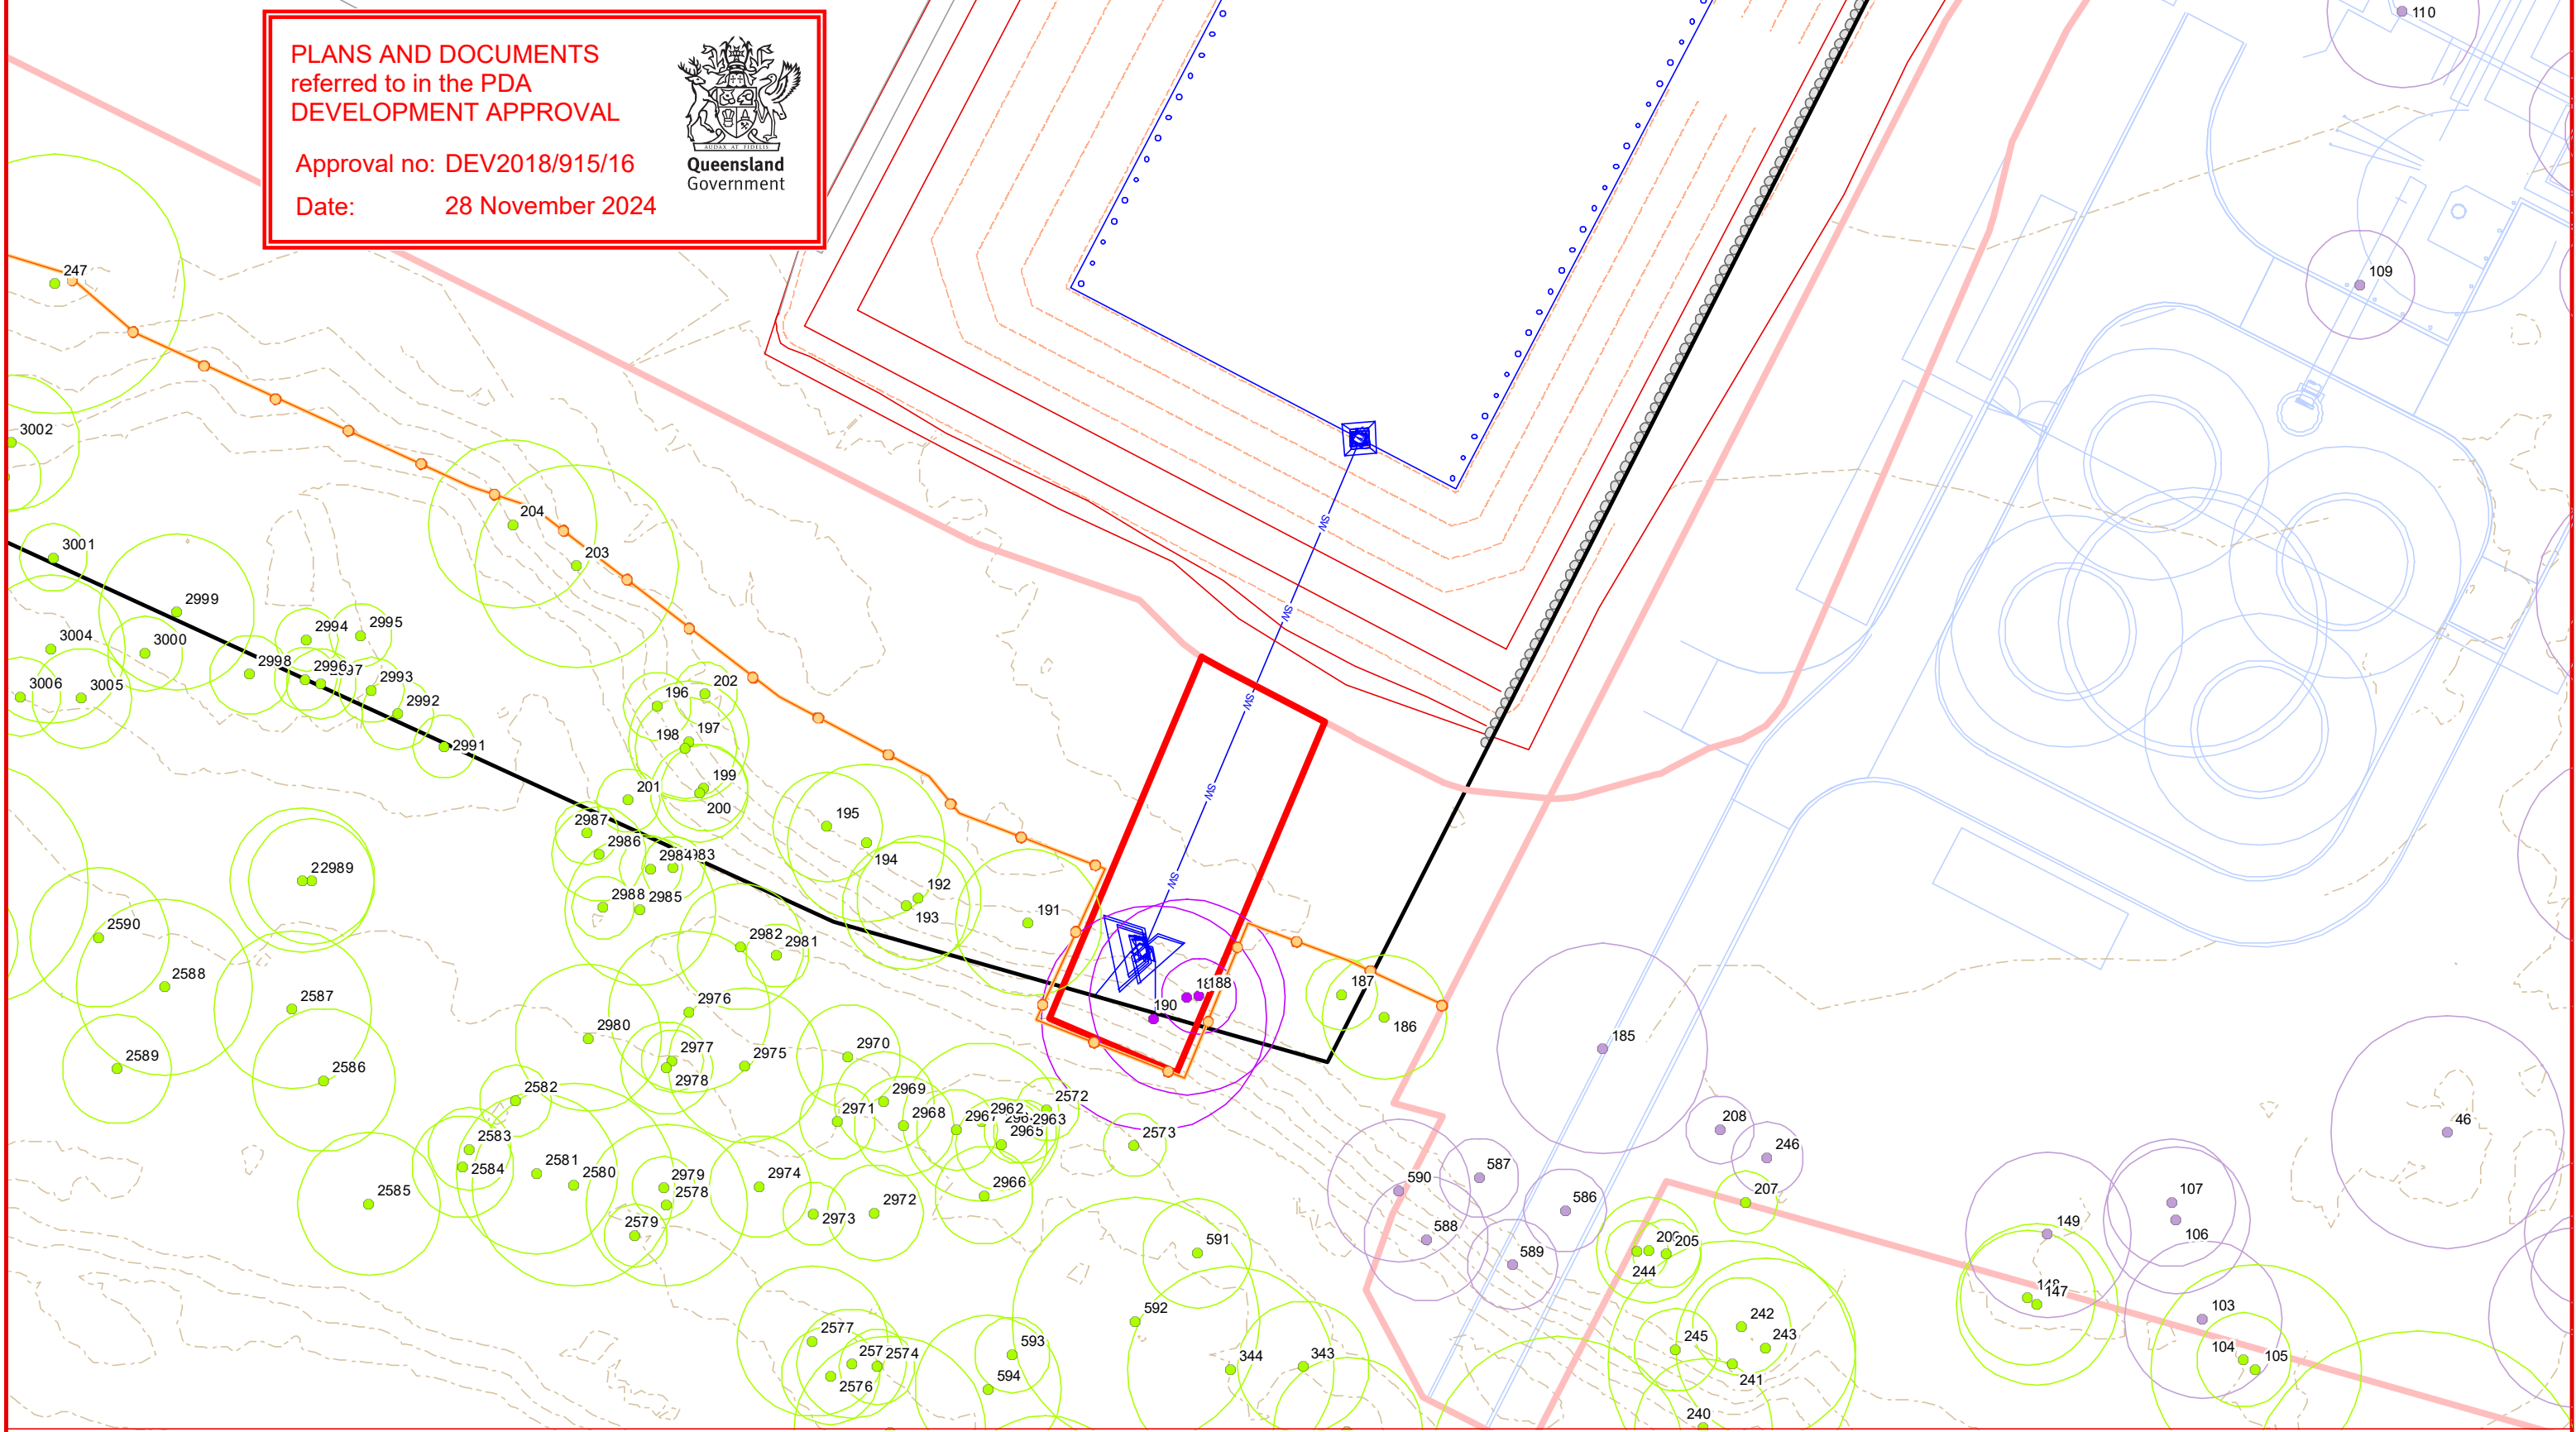

Tree to retain (w/TPZ)

Additional tree to remove (w/TPZ)

Tree approved to remove in
previous VMPs (w/TPZ)

Approved vegetation clearing areas

Stage 2-5 balance approved clearing area

Additional school site vegetation
clearing areas

Exempt vegetation to be cleared that
does not meet the significant definition

School lot boundary

School design (buildings/paths)

Landscape areas

Design contours

Earthwork works batter

Earthworks retaining wall

Road line-markings

Stormwater design

Water design

Existing contours

Stockpile location (indicative)

LWIA pump station design details

Tree protection fencing -
to be fauna friendly design &
subject to minor changes by
Arborist and civil engineer

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet IO



Brisbane Catholic Education

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT SAUNDERS HAVILL GROUP. THE CLIENT ACCEPTS RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, CLEARING OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAIL LOCATIONS OF ALL SERVICES.

REFERENCES:



0 10 20 m

AMENDMENTS:

Issue	Date	Description	Checked
A	23/01/2018	Client Draft	AD
B	7/02/2018	Surplus fill area added	AD
D	26/08/2024	Civil extent amendments	AD

CLIENT:

Brisbane Catholic Education

PROJECT:

Flagstone City - Stage 2-5
Phase 1 works (School Site)

environmental management

PLAN OF:

Vegetation
Management Plan

DATE: 26/08/2024


CHECKED: AD

JOB REF: 7833

DRAWN: TC

DRAWING No.: 8047 E 10 Stage 2 VMP D

1:400 @ A3

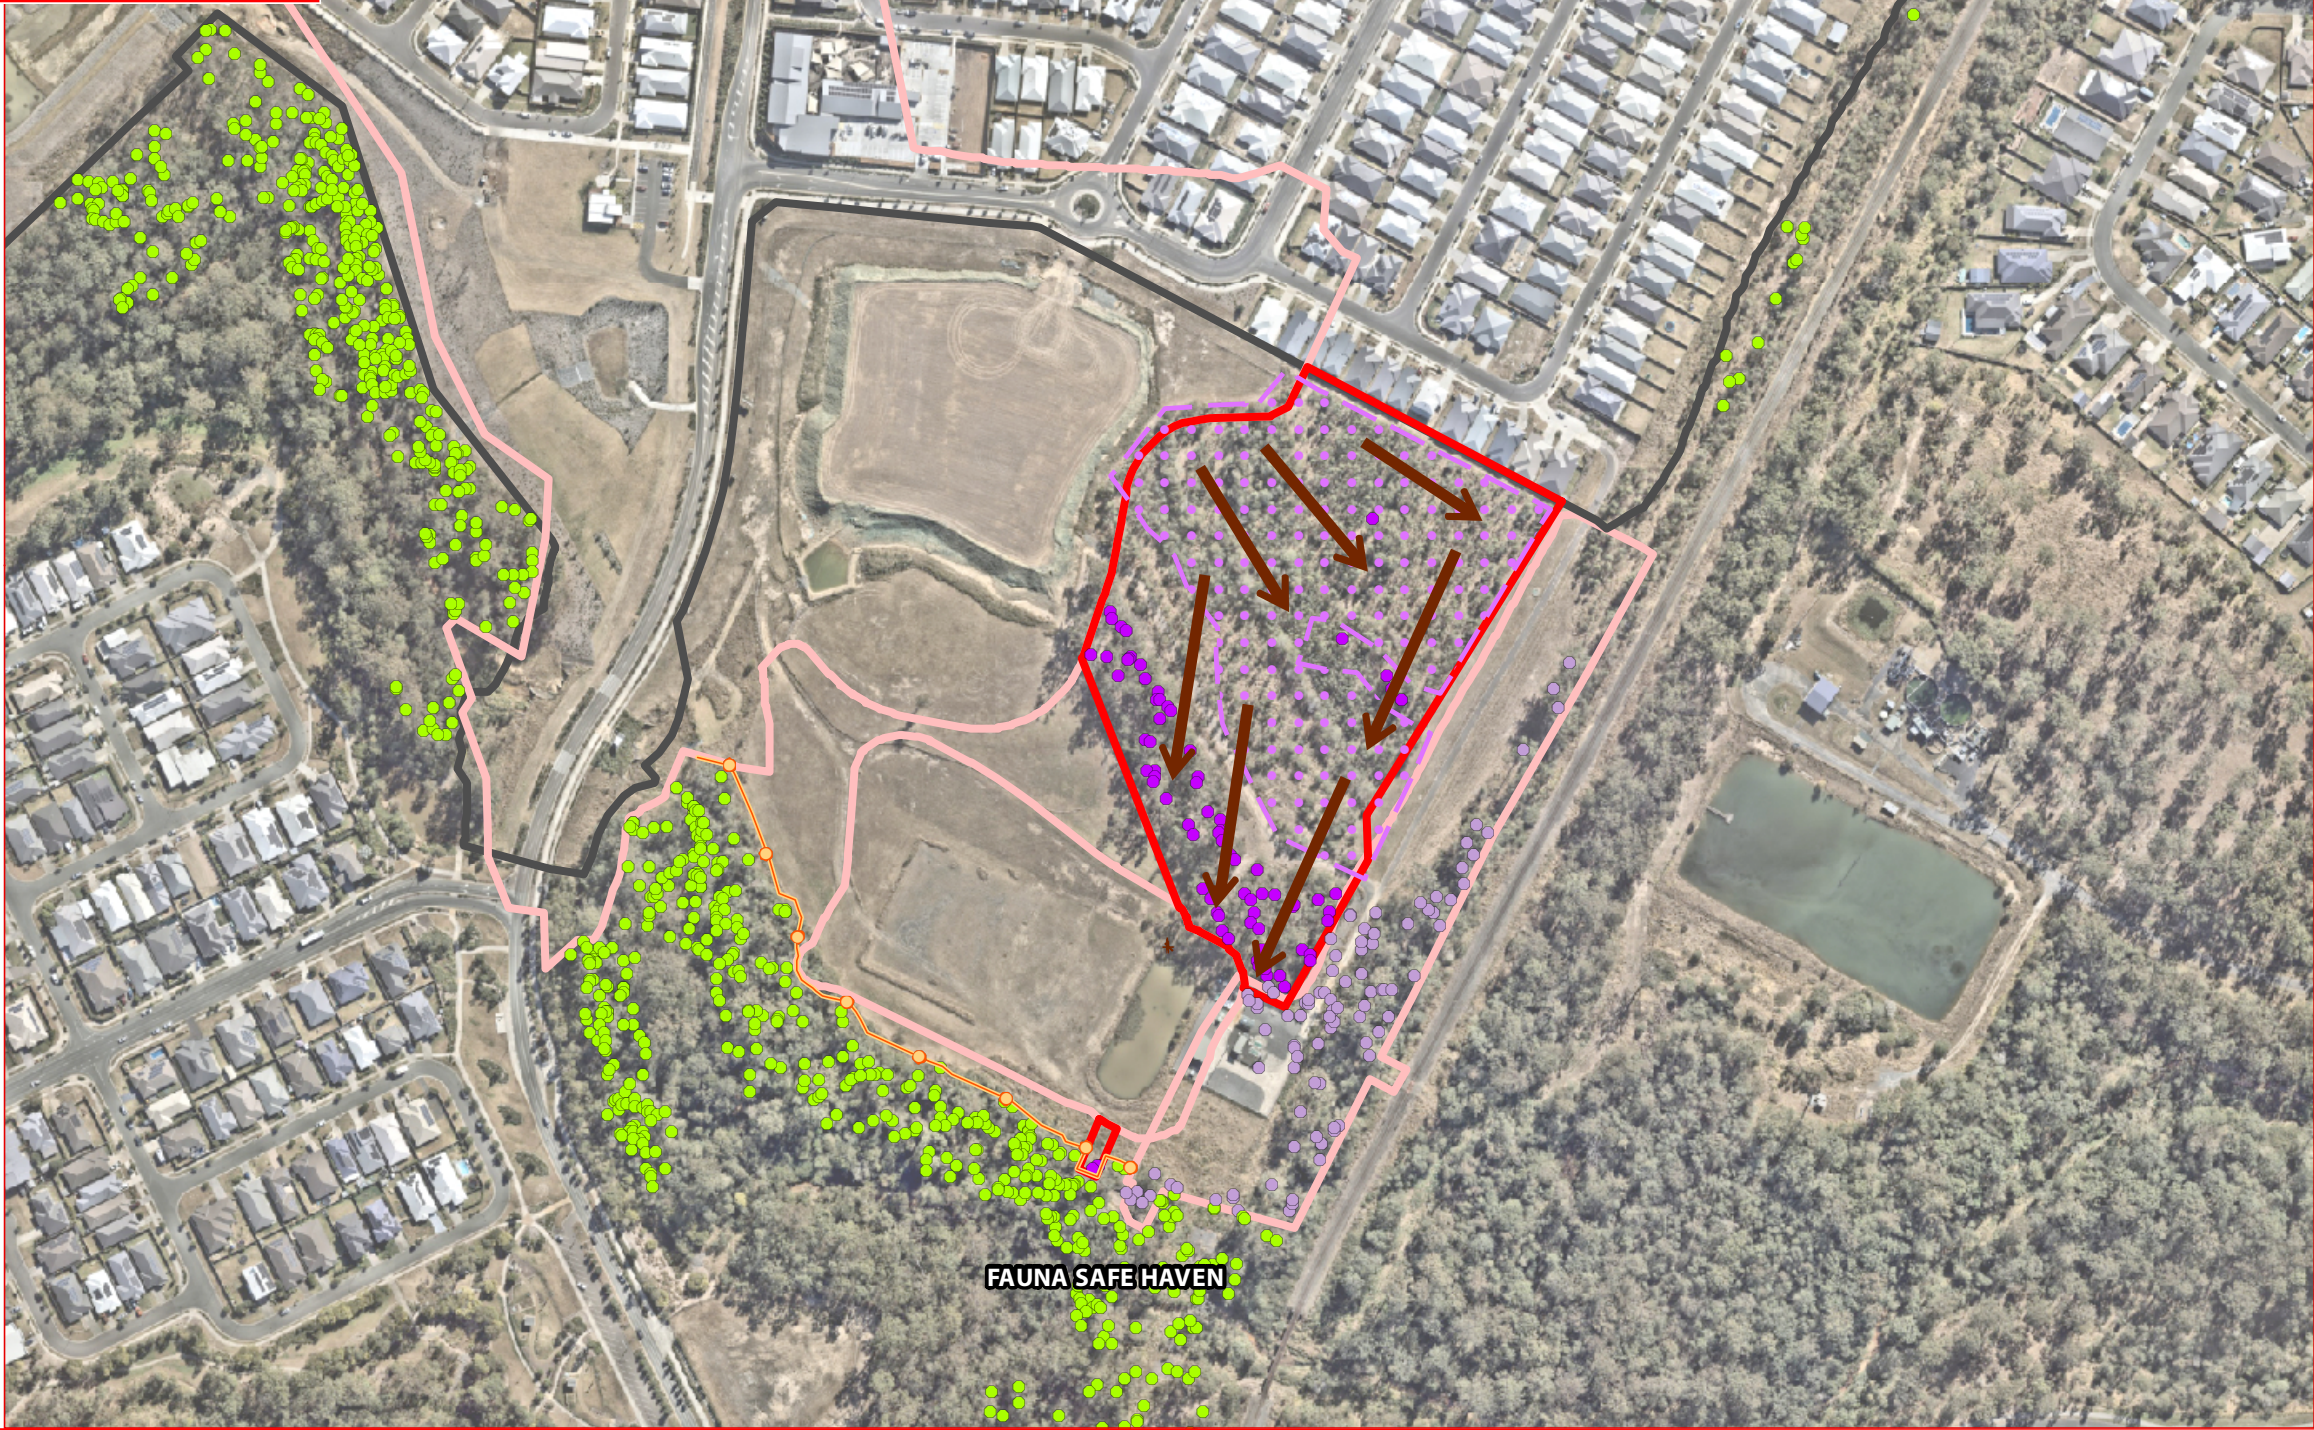

Legend

-  Clearing direction
-  Tree to retain
-  Tree to remove
-  Tree approved to remove in previous VMPs
-  Approved vegetation clearing areas
-  Stage 2-5 balance approved clearing area
-  Additional school site vegetation clearing areas
-  Exempt vegetation to be cleared that does not meet the significant definition
-  Stockpile location (indicative)
-  Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Vegetation Management Plan - Clearing Direction

Specimen Details										Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value									
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
46	<i>Eucalyptus tereticornis</i>	Forest Red Gum	620		620	28.0	11.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
55	<i>Eucalyptus tereticornis</i>	Forest Red Gum	540		540	28.0	7.0	6.5	2.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
56	<i>Eucalyptus tereticornis</i>	Forest Red Gum	620		620	33.0	12.0	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
57	<i>Eucalyptus tereticornis</i>	Forest Red Gum	320		320	23.0	6.0	3.8	2.1	One-sided	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
58	<i>Eucalyptus tereticornis</i>	Forest Red Gum	500		500	28.0	9.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
59	<i>Eucalyptus tereticornis</i>	Forest Red Gum	330		330	26.0	4.0	4.0	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
60	<i>Corymbia tessellaris</i>	Moreton Bay Ash	300		300	19.0	7.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
61	<i>Eucalyptus tereticornis</i>	Forest Red Gum	490		490	29.0	9.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
62	<i>Angophora leiocarpa</i>	Smooth-barked Apple	270		270	17.0	5.0	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
63	DEAD/STAG		450		450	29.0	8.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
64	<i>Eucalyptus tereticornis</i>	Forest Red Gum	280		280	19.0	2.0	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
65	<i>Corymbia citriodora</i>	Spotted Gum	590	210	626	34.0	12.0	7.5	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
66	<i>Eucalyptus tereticornis</i>	Forest Red Gum	540		540	33.0	9.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
67	<i>Corymbia citriodora</i>	Spotted Gum	450		450	32.0	12.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
73	<i>Corymbia citriodora</i>	Spotted Gum	720		720	28.0	12.0	8.6	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
74	<i>Corymbia citriodora</i>	Spotted Gum	690		690	34.0	14.0	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
76	<i>Eucalyptus tereticornis</i>	Forest Red Gum	280		280	13.0	5.0	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
77	<i>Eucalyptus tereticornis</i>	Forest Red Gum	940		940	21.0	7.0	11.3	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
103	<i>Eucalyptus tereticornis</i>	Forest Red Gum	420		420	25.0	7.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
104	<i>Angophora subvelutina</i>	Broad-leaved Apple	250		250	13.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
105	<i>Eucalyptus tereticornis</i>	Forest Red Gum	560		560	27.0	9.0	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
106	<i>Eucalyptus tereticornis</i>	Forest Red Gum	390		390	22.0	8.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
107	<i>Angophora subvelutina</i>	Broad-leaved Apple	340		340	16.0	9.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
109	<i>Corymbia intermedia</i>	Pink Bloodwood	290		290	18.0	7.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
110	<i>Lophostemon suaveolens</i>	Swamp Box	300	200, 190	408	16.0	8.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
111	<i>Eucalyptus tereticornis</i>	Forest Red Gum	420		420	29.0	12.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
112	<i>Eucalyptus tereticornis</i>	Forest Red Gum	260		260	19.0	5.0	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
113	<i>Eucalyptus tereticornis</i>	Forest Red Gum	300		300	18.0	5.0	3.6	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
114	<i>Corymbia tessellaris</i>	Moreton Bay Ash	220		220	18.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
115	<i>Lophostemon suaveolens</i>	Swamp Box	210		210	13.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
116	<i>Lophostemon suaveolens</i>	Swamp Box	200		200	14.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
117	<i>Eucalyptus tereticornis</i>	Forest Red Gum	460		460	27.0	9.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
118	<i>Eucalyptus tereticornis</i>	Forest Red Gum	370		370	23.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
119	<i>Lophostemon suaveolens</i>	Swamp Box	290		290	16.0	7.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
120	<i>Lophostemon suaveolens</i>	Swamp Box	230		230	16.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
121	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	280		280	24.0	6.0	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
122	<i>Acacia disparrima</i>	Hickory Wattle	350	220	413	16.0	9.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
123	<i>Acacia disparrima</i>	Hickory Wattle	240		240	16.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
124	<i>Acacia disparrima</i>	Hickory Wattle	240		240	11.0	9.0	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
125	Corymbia citriodora	Spotted Gum	200		200	17.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
126	Lophostemon suaveolens	Swamp Box	330		330	14.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
127	Acacia disparrima	Hickory Wattle	220	200	297	13.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
128	Eucalyptus moluccana	Gum Topped Box	240		240	18.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
129	Angophora leiocarpa	Smooth-barked Apple	260		260	17.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
130	Corymbia citriodora	Spotted Gum	220		220	18.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
131	Lophostemon suaveolens	Swamp Box	280		280	12.0	4.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
132	Alphitonia excelsa	Soap Tree	250		250	12.0	4.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
147	Eucalyptus tereticornis	Forest Red Gum	430		430	26.0	6.0	5.2	2.3	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
148	Eucalyptus siderophloia	Grey Ironbark	360		360	25.0	9.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
149	Eucalyptus siderophloia	Grey Ironbark	440		440	31.0	12.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Approved to remove		
150	Eucalyptus tereticornis	Forest Red Gum	290		290	24.0	6.0	3.5	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
152	Eucalyptus tereticornis	Forest Red Gum	250		250	16.0	5.0	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
153	Eucalyptus tereticornis	Forest Red Gum	240		240	18.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
154	Eucalyptus tereticornis	Forest Red Gum	560		560	30.0	16.0	6.7	2.6	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
155	Eucalyptus tereticornis	Forest Red Gum	280		280	25.0	5.0	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
156	Eucalyptus tereticornis	Forest Red Gum	350		350	30.0	6.0	4.2	2.1	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
157	Corymbia intermedia	Pink Bloodwood	270	260	375	18.0	5.0	4.5	2.2	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
158	Eucalyptus tereticornis	Forest Red Gum	320		320	28.0	7.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
159	Lophostemon suaveolens	Swamp Box	250		250	10.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
185	Corymbia intermedia	Pink Bloodwood	560		560	26.0	10.0	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
186	Corymbia tessellaris	Moreton Bay Ash	330		330	24.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
187	Alphitonia excelsa	Soap Tree	190		190	11.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
188	Corymbia tessellaris	Moreton Bay Ash	200		200	4.0	2.0	2.4	1.7	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
189	Angophora subvelutina	Broad-leaved Apple	520		520	20.0	11.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
190	Eucalyptus tereticornis	Forest Red Gum	600		600	27.0	12.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
191	Lophostemon suaveolens	Swamp Box	390		390	19.0	6.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
192	Lophostemon suaveolens	Swamp Box	330		330	13.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain		
193	Lophostemon suaveolens	Swamp Box	340		340	14.0	6.0	4.1	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
194	Corymbia tessellaris	Moreton Bay Ash	420		420	24.0	8.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain		
195	Angophora subvelutina	Broad-leaved Apple	290		290	20.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
196	Lophostemon suaveolens	Swamp Box	180		180	11.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
197	Lophostemon suaveolens	Swamp Box	320		320	17.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
198	Lophostemon suaveolens	Swamp Box	270		270	15.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
199	Corymbia tessellaris	Moreton Bay Ash	230		230	20.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
200	Corymbia tessellaris	Moreton Bay Ash	260		260	23.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
201	Acacia disparrima	Hickory Wattle	150		150	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
202	Eucalyptus crebra	Narrow-leaved Ironbark	160		160	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
203	Angophora subvelutina	Broad-leaved Apple	540		540	26.0	12.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
204	Angophora subvelutina	Broad-leaved Apple	450		450	26.0	8.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
205	Lophostemon suaveolens	Swamp Box	180		180	14.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
206	Corymbia tessellaris	Moreton Bay Ash	280		280	20.0	8.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
207	Corymbia tessellaris	Moreton Bay Ash	150		150	20.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
208	Eucalyptus tereticornis	Forest Red Gum	180		180	11.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
241	<i>Corymbia tessellaris</i>	Moreton Bay Ash	660		660	28.0	9.0	7.9	2.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain		
242	<i>Lophostemon suaveolens</i>	Swamp Box	260		260	13.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
243	<i>Corymbia tessellaris</i>	Moreton Bay Ash	480		480	23.0	7.0	5.8	2.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain		
244	<i>Corymbia tessellaris</i>	Moreton Bay Ash	150		150	17.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
245	<i>Lophostemon suaveolens</i>	Swamp Box	220		220	11.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
246	<i>Eucalyptus tereticornis</i>	Forest Red Gum	190		190	15.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
343	<i>Corymbia tessellaris</i>	Moreton Bay Ash	350		350	32.0	16.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
344	<i>Angophora subvelutina</i>	Broad-leaved Apple	550		550	28.0	16.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
586	<i>Acacia concurrens</i>	Black Wattle	220		220	11.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
587	<i>Lophostemon suaveolens</i>	Swamp Box	210		210	16.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
588	<i>Alphitonia excelsa</i>	Soap Tree	330		330	17.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
589	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	240		240	17.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
590	<i>Angophora subvelutina</i>	Broad-leaved Apple	380		380	16.0	7.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
591	<i>Lophostemon suaveolens</i>	Swamp Box	290		290	16.0	5.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
592	<i>Angophora subvelutina</i>	Broad-leaved Apple	660		660	22.0	14.0	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
593	<i>Ficus coronata</i>	Sandpaper Fig	200		200	8.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
965	<i>Corymbia citriodora</i>	Spotted Gum	400		400	22.0	9.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
966	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	220		220	16.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
967	<i>Corymbia citriodora</i>	Spotted Gum	380		380	25.0	10.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
968	<i>Corymbia citriodora</i>	Spotted Gum	340		340	16.0	5.0	4.1	2.1	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
969	<i>Corymbia citriodora</i>	Spotted Gum	300		300	18.0	3.0	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
977	<i>Corymbia citriodora</i>	Spotted Gum	450		450	20.0	8.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-	Approved to remove		
978	<i>Corymbia citriodora</i>	Spotted Gum	680		680	26.0	10.0	8.2	2.8	Regular	-	-	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
979	<i>Corymbia citriodora</i>	Spotted Gum	260		260	18.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
980	<i>Corymbia citriodora</i>	Spotted Gum	200		200	18.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
981	<i>Eucalyptus siderophloia</i>	Grey Ironbark	500		500	23.0	12.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
982	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	280		280	18.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
983	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	100	100	120	14.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
984	<i>Corymbia citriodora</i>	Spotted Gum	420		420	16.0	3.0	5.0	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	Large	-	-	-	Approved to remove		
985	<i>Corymbia citriodora</i>	Spotted Gum	320		320	19.0	10.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
986	<i>Corymbia citriodora</i>	Spotted Gum	410		410	28.0	12.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
987	<i>Corymbia citriodora</i>	Spotted Gum	370		370	16.0	6.0	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
988	<i>Corymbia citriodora</i>	Spotted Gum	470		470	22.0	10.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
989	<i>Corymbia citriodora</i>	Spotted Gum	550		550	27.0	8.0	6.6	2.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
990	<i>Corymbia citriodora</i>	Spotted Gum	470		470	27.0	9.0	5.6	2.4	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
991	<i>Corymbia citriodora</i>	Spotted Gum	240		240	17.0	4.0	2.9	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
992	<i>Corymbia citriodora</i>	Spotted Gum	680		680	28.0	11.0	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
993	<i>Eucalyptus siderophloia</i>	Grey Ironbark	400		400	20.0	10.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
994	<i>Corymbia citriodora</i>	Spotted Gum	470		470	21.0	5.0	5.6	2.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
995	<i>Corymbia intermedia</i>	Pink Bloodwood	540		540	30.0	10.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
996	<i>Corymbia citriodora</i>	Spotted Gum	260		260	21.0	2.0	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
997	<i>Corymbia citriodora</i>	Spotted Gum	300		300	24.0	3.0	3.6	2.0	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
998	<i>Corymbia citriodora</i>	Spotted Gum	540		540	27.0	10.0	6.5	2.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
999	<i>Corymbia citriodora</i>	Spotted Gum	600		600	27.0	14.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	Large	-	-	-	Remove - school design		

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
1000	Corymbia citriodora	Spotted Gum	650		650	30.0	16.0	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-	Remove - school design		
1001	Corymbia citriodora	Spotted Gum	250		250	13.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1002	Eucalyptus tereticornis	Forest Red Gum	260		260	17.0	5.0	3.1	1.9	One-sided	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1003	Corymbia citriodora	Spotted Gum	250		250	17.0	5.0	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1004	Angophora leiocarpa	Smooth-barked Apple	240		240	14.0	4.0	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1005	Corymbia citriodora	Spotted Gum	390		390	17.0	4.0	4.7	2.2	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1006	Eucalyptus tereticornis	Forest Red Gum	700		700	24.0	9.0	8.4	2.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1007	Corymbia citriodora	Spotted Gum	350		350	18.0	6.0	4.2	2.1	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1008	Corymbia citriodora	Spotted Gum	330		330	27.0	10.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1009	Eucalyptus moluccana	Gum Topped Box	400		400	25.0	11.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1010	Eucalyptus moluccana	Gum Topped Box	310		310	24.0	7.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1011	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	17.0	6.0	3.6	2.0	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1012	Eucalyptus moluccana	Gum Topped Box	250		250	17.0	3.0	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1013	Eucalyptus moluccana	Gum Topped Box	550		550	28.0	10.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1014	Eucalyptus moluccana	Gum Topped Box	300		300	18.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1015	Corymbia citriodora	Spotted Gum	340		340	20.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1016	Corymbia intermedia	Pink Bloodwood	220	200	297	18.0	7.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1017	Eucalyptus tereticornis	Forest Red Gum	400		400	25.0	6.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1018	Lophostemon suaveolens	Swamp Box	220		220	16.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1019	Lophostemon suaveolens	Swamp Box	200		200	11.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1020	Eucalyptus tereticornis	Forest Red Gum	330	300	446	27.0	8.0	5.4	2.4	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1021	Lophostemon suaveolens	Swamp Box	200		200	16.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1022	Eucalyptus siderophloia	Grey Ironbark	310		310	26.0	9.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-	Approved to remove		
1023	Eucalyptus tereticornis	Forest Red Gum	480		480	30.0	10.0	5.8	2.4	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1024	Angophora leiocarpa	Smooth-barked Apple	300		300	18.0	7.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1025	Lophostemon suaveolens	Swamp Box	200		200	16.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1026	Angophora leiocarpa	Smooth-barked Apple	220		220	12.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1027	Eucalyptus tereticornis	Forest Red Gum	240		240	17.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1028	Eucalyptus tereticornis	Forest Red Gum	220		220	17.0	4.0	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
1029	Lophostemon suaveolens	Swamp Box	200		200	14.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1030	Lophostemon suaveolens	Swamp Box	220		220	16.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1467	Corymbia citriodora	Spotted Gum	310		310	19.0	12.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1468	Corymbia citriodora	Spotted Gum	270		270	17.0	8.0	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1469	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	16.0	11.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1470	Corymbia citriodora	Spotted Gum	270		270	17.0	9.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1471	Eucalyptus tereticornis	Forest Red Gum	200		200	18.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1472	Corymbia tessellaris	Moreton Bay Ash	220		220	17.0	2.0	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1473	Eucalyptus tereticornis	Forest Red Gum	230		230	15.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1474	Corymbia citriodora	Spotted Gum	200		200	19.0	8.0	2.4	1.7	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1475	Corymbia citriodora	Spotted Gum	330		330	22.0	9.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1476	Eucalyptus tereticornis	Forest Red Gum	480		480	25.0	8.0	5.8	2.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1477	Eucalyptus tereticornis	Forest Red Gum	350		350	26.0	7.0	4.2	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1478	Corymbia citriodora	Spotted Gum	550		550	30.0	15.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1479	Corymbia citriodora	Spotted Gum	420		420	27.0	9.0	5.0	2.3	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		

Specimen Details										Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
1480	Corymbia citriodora	Spotted Gum	300		300	28.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1481	Corymbia citriodora	Spotted Gum	410		410	27.0	8.0	4.9	2.3	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1482	Corymbia citriodora	Spotted Gum	340		340	17.0	9.0	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Approved to remove	
1483	Corymbia citriodora	Spotted Gum	350		350	26.0	14.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1484	Eucalyptus tereticornis	Forest Red Gum	330		330	13.0	4.0	4.0	2.1	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	Major	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Approved to remove	
1485	Corymbia citriodora	Spotted Gum	360		360	25.0	9.0	4.3	2.2	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1486	Eucalyptus tereticornis	Forest Red Gum	530		530	29.0	13.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1487	Corymbia citriodora	Spotted Gum	490		490	27.0	15.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1488	Eucalyptus siderophloia	Grey Ironbark	270		270	17.0	9.0	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1489	Corymbia citriodora	Spotted Gum	410		410	24.0	11.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1490	Corymbia citriodora	Spotted Gum	600		600	31.0	16.0	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1491	Corymbia citriodora	Spotted Gum	300		300	19.0	9.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1492	Angophora leiocarpa	Smooth-barked Apple	260		260	10.0	9.0	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1493	Eucalyptus crebra	Narrow-leaved Ironbark	380		380	21.0	14.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1494	Eucalyptus crebra	Narrow-leaved Ironbark	510		510	24.0	13.0	6.1	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1495	Corymbia citriodora	Spotted Gum	330		330	16.0	14.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1496	Eucalyptus moluccana	Gum Topped Box	250		250	22.0	10.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1497	Eucalyptus moluccana	Gum Topped Box	200		200	12.0	9.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1498	Eucalyptus tereticornis	Forest Red Gum	220		220	18.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1499	Eucalyptus moluccana	Gum Topped Box	320		320	22.0	10.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1500	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	20.0	10.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1501	Corymbia citriodora	Spotted Gum	250		250	19.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove - school design	
1502	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	21.0	9.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-	Remove - school design	
1503	Corymbia citriodora	Spotted Gum	310		310	26.0	12.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1504	Eucalyptus moluccana	Gum Topped Box	250		250	19.0	9.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1505	Eucalyptus moluccana	Gum Topped Box	500		500	30.0	14.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1506	Eucalyptus moluccana	Gum Topped Box	370		370	31.0	9.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1507	Eucalyptus moluccana	Gum Topped Box	350		350	24.0	11.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1508	Eucalyptus moluccana	Gum Topped Box	260	190	322	24.0	10.0	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1509	Angophora leiocarpa	Smooth-barked Apple	200		200	14.0	9.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1510	Eucalyptus moluccana	Gum Topped Box	350		350	23.0	9.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-	Remove - school design	
1511	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	20.0	8.0	3.1	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1512	Alphitonia excelsa	Soap Tree	200		200	12.0	9.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1513	Acacia disparrima	Hickory Wattle	200	130	239	13.0	6.0	2.9	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1514	Corymbia citriodora	Spotted Gum	250		250	21.0	10.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1515	Eucalyptus tereticornis	Forest Red Gum	290		290	23.0	10.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1516	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	19.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-	Remove - school design	
1517	Eucalyptus tereticornis	Forest Red Gum	270		270	23.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1518	Eucalyptus tereticornis	Forest Red Gum	280		280	21.0	10.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1519	Eucalyptus tereticornis	Forest Red Gum	230		230	14.0	5.0	2.8	1.8	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design	
1520	Corymbia citriodora	Spotted Gum	210		210	15.0	7.0	2.5	1.7	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1521	Corymbia intermedia	Pink Bloodwood	210		210	19.0	9.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1522	Eucalyptus tereticornis	Forest Red Gum	250		250	25.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	
1523	Eucalyptus tereticornis	Forest Red Gum	250		250	27.0	9.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove	

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes	
1524	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	360		360	24.0	12.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1525	<i>Lophostemon suaveolens</i>	Swamp Box	230		230	13.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1526	<i>Lophostemon suaveolens</i>	Swamp Box	220	180	284	12.0	9.0	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1527	<i>Eucalyptus tereticornis</i>	Forest Red Gum	480		480	29.0	13.0	5.8	2.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
1528	<i>Corymbia tessellaris</i>	Moreton Bay Ash	260		260	24.0	10.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2388	<i>Corymbia citriodora</i>	Spotted Gum	650		650	34.0	15.0	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2463	<i>Acacia concurrens</i>	Black Wattle	110		110	5.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2572	<i>Alphitonia excelsa</i>	Soap Tree	140		140	11.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2573	<i>Alphitonia excelsa</i>	Soap Tree	120		120	11.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2574	<i>Angophora subvelutina</i>	Broad-leaved Apple	200		200	15.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2575	<i>Angophora subvelutina</i>	Broad-leaved Apple	290		290	16.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2576	<i>Angophora subvelutina</i>	Broad-leaved Apple	260		260	16.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2577	<i>Angophora subvelutina</i>	Broad-leaved Apple	400		400	17.0	9.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2578	<i>Eucalyptus seeana</i>	Narrow-leaved Red Gum	430		430	26.0	16.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2579	<i>Lophostemon suaveolens</i>	Swamp Box	120		120	16.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2580	<i>Aphananthe philippinensis</i>	Native Elm	540		540	20.0	14.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain		
2581	<i>Angophora subvelutina</i>	Broad-leaved Apple	430		430	21.0	11.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2582	<i>Eucalyptus tereticornis</i>	Forest Red Gum	190		190	17.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2583	<i>Lophostemon suaveolens</i>	Swamp Box	220		220	16.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2584	<i>Lophostemon suaveolens</i>	Swamp Box	270		270	16.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2585	<i>Lophostemon suaveolens</i>	Swamp Box	380		380	20.0	10.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Retain		
2586	<i>Corymbia tessellaris</i>	Moreton Bay Ash	380		380	22.0	12.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2587	<i>Corymbia tessellaris</i>	Moreton Bay Ash	420		420	22.0	12.0	5.0	2.3	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2588	<i>Aphananthe philippinensis</i>	Native Elm	470		470	17.0	13.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2589	<i>Lophostemon suaveolens</i>	Swamp Box	290		290	17.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2590	<i>Aphananthe philippinensis</i>	Native Elm	370		370	16.0	10.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain		
2902	<i>Corymbia citriodora</i>	Spotted Gum	290		290	17.0	5.0	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2903	<i>Corymbia citriodora</i>	Spotted Gum	155		155	11.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2904	<i>Corymbia citriodora</i>	Spotted Gum	140		140	10.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2905	<i>Corymbia citriodora</i>	Spotted Gum	170		170	11.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Approved to remove		
2906	<i>Corymbia citriodora</i>	Spotted Gum	370		370	21.0	10.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
2907	<i>Eucalyptus crebra</i>	Narrow-leaved Ironbark	300		300	17.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
2908	<i>Eucalyptus tereticornis</i>	Forest Red Gum	130		130	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
2909	<i>Acacia concurrens</i>	Black Wattle	185		185	7.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
2910	<i>Corymbia citriodora</i>	Spotted Gum	150		150	10.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - school design		
2911	<i>Corymbia citriodora</i>	Spotted Gum	500		500	24.0	12.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Approved to remove		
2962	<i>Angophora subvelutina</i>	Broad-leaved Apple	420		420	21.0	9.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2963	<i>Alphitonia excelsa</i>	Soap Tree	115		115	11.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2964	<i>Alphitonia excelsa</i>	Soap Tree	130		130	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2965	<i>Lophostemon suaveolens</i>	Swamp Box	245		245	12.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2966	<i>Lophostemon suaveolens</i>	Swamp Box	260		260	14.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2967	<i>Acacia disparrima</i>	Hickory Wattle	215		215	13.0	6.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2968	<i>Casuarina cunninghamiana</i>	River Sheoak	265		265	21.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		
2969	<i>Lophostemon suaveolens</i>	Swamp Box	265		265	16.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain		

Specimen Details										Canopy Condition Details						Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention	Additional Notes
2970	<i>Lophostemon suaveolens</i>	Swamp Box	275		275	15.0	6.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2971	<i>Angophora subvelutina</i>	Broad-leaved Apple	200		200	17.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Retain	
2972	<i>Lophostemon suaveolens</i>	Swamp Box	255		255	16.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2973	<i>Lophostemon suaveolens</i>	Swamp Box	130		130	11.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2974	<i>Lophostemon suaveolens</i>	Swamp Box	270		270	16.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Retain	
2975	<i>Aphananthe philippinensis</i>	Native Elm	320	260	412	15.0	8.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2976	<i>Alphitonia excelsa</i>	Soap Tree	430		430	17.0	8.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2977	<i>Lophostemon suaveolens</i>	Swamp Box	155		155	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2978	<i>Lophostemon suaveolens</i>	Swamp Box	245		245	13.0	4.0	2.9	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2979	<i>Ficus coronata</i>	Sandpaper Fig	145	80	166	7.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2980	<i>Corymbia tessellaris</i>	Moreton Bay Ash	390		390	23.0	9.0	4.7	2.2	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2981	<i>Acacia disparrima</i>	Hickory Wattle	125		125	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2982	<i>Eucalyptus tereticornis</i>	Forest Red Gum	335		335	28.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2983	<i>Lophostemon suaveolens</i>	Swamp Box	105		105	8.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2984	<i>Alphitonia excelsa</i>	Soap Tree	130		130	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2985	<i>Eucalyptus tereticornis</i>	Forest Red Gum	400		400	27.0	9.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2986	<i>Lophostemon suaveolens</i>	Swamp Box	250		250	11.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2987	<i>Acacia disparrima</i>	Hickory Wattle	150		150	6.0	5.0	2.0	1.5	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2988	<i>Acacia disparrima</i>	Hickory Wattle	150		150	7.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2989	<i>Lophostemon suaveolens</i>	Swamp Box	250	220	333	14.0	7.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2990	<i>Eucalyptus tereticornis</i>	Forest Red Gum	385		385	26.0	10.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2991	<i>Acacia disparrima</i>	Hickory Wattle	125		125	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2992	<i>Acacia disparrima</i>	Hickory Wattle	190		190	10.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2993	<i>Alphitonia excelsa</i>	Soap Tree	130	115	174	11.0	5.0	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2994	<i>Alphitonia excelsa</i>	Soap Tree	165		165	11.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2995	<i>Alphitonia excelsa</i>	Soap Tree	155		155	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2996	<i>Acacia disparrima</i>	Hickory Wattle	155		155	9.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2997	<i>Alphitonia excelsa</i>	Soap Tree	185		185	11.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2998	<i>Angophora subvelutina</i>	Broad-leaved Apple	210		210	15.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
2999	<i>Acacia disparrima</i>	Hickory Wattle	280	255, 165	413	11.0	7.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
3000	<i>Lophostemon suaveolens</i>	Swamp Box	200		200	12.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain	
