Vegetation Clearing & Fauna Management Plan

New Beith
Southern Entry Bridge

Frasers Property New Beith Pty Ltd

Economic Development
Queensland (EDQ)

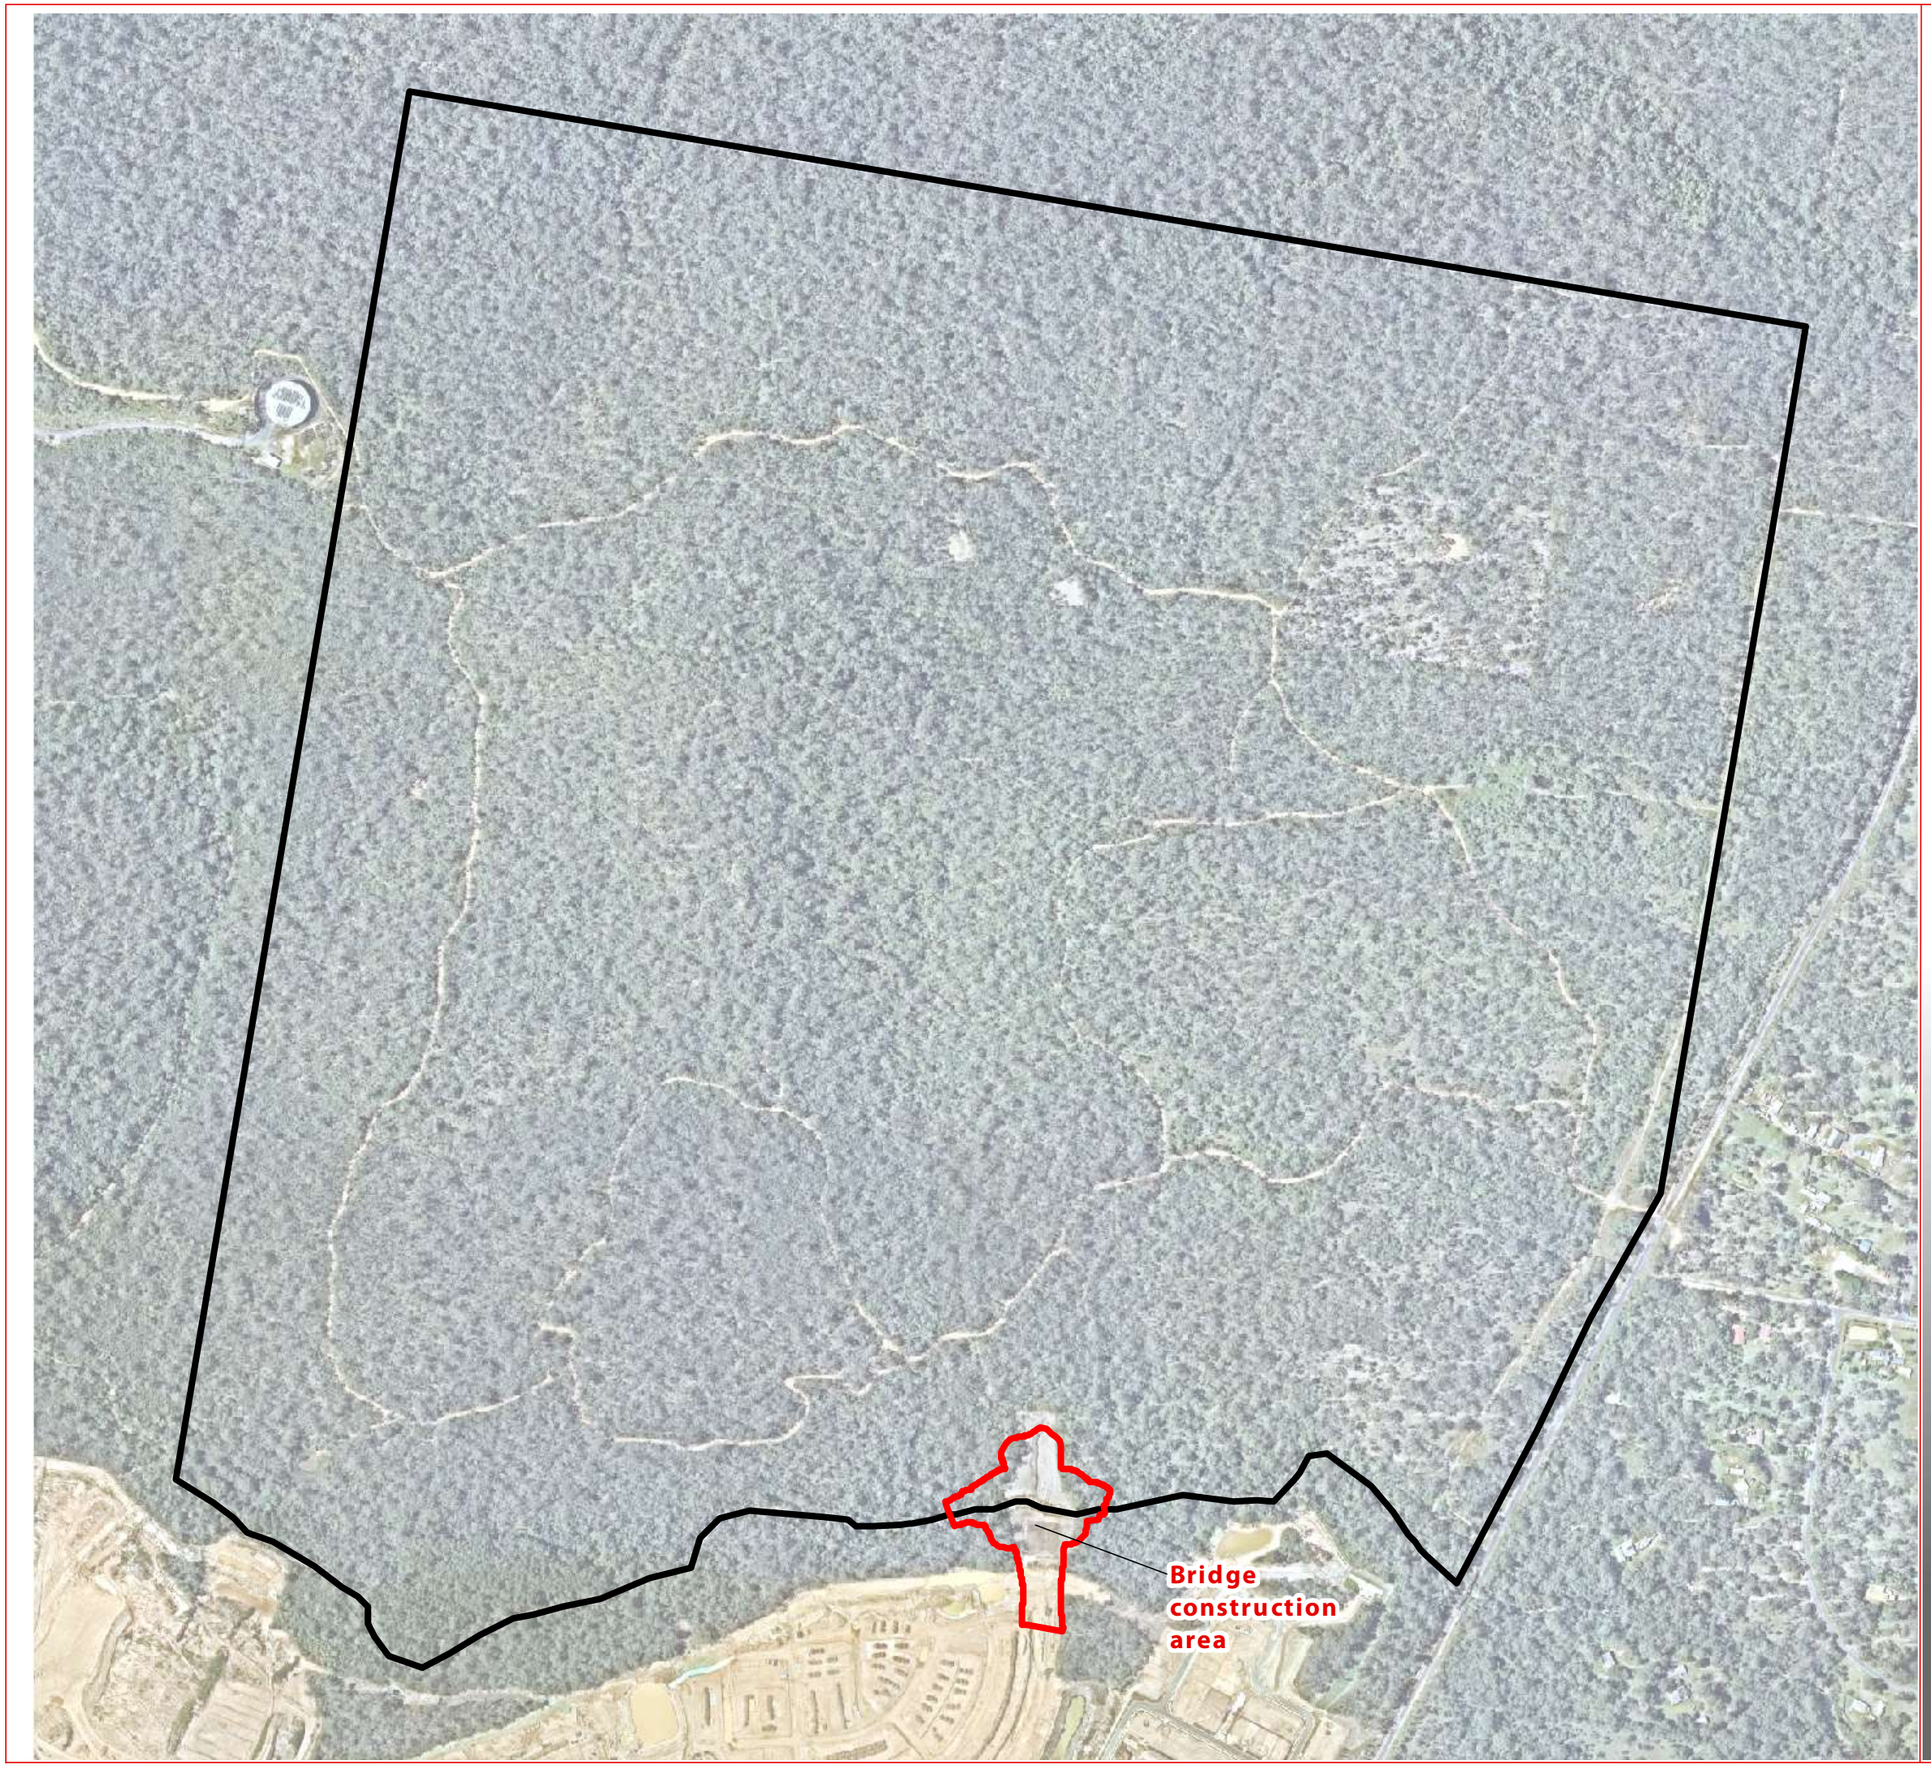

CONTENTS

10941 E 02 S-Bridge VCFMP B -- Vegetation Clearing Notes
10941 E 03 S-Bridge VCFMP B -- Fauna Management Notes
10941 E 04 S-Bridge VCFMP B -- Detail Sheets Context
10941 E 05-09 S-Bridge VCFMP B -- Detail Sheets
10941 E 10 S-Bridge VCFMP B -- Clearing Direction
Appendix A -- Tree Schedule Extract

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

SHG Contact
Dr Andrew Davies
Email: andrewdavies@saundershavill.com

saunders havill group

1:7,000

Vegetation Clearing and Fauna Management Plan - *Notes*

INTRODUCTION

The Environmental Management Division of the **Saunders Havill Group (SHG)** was engaged by **Frasers Property New Beith Pty Ltd** to prepare a Vegetation Clearing & Fauna Management Plan (VCFMP) for the southern entry bridge over Flagstone Creek, including works required to construct the bridge.

This VCFMP is a requirement of the EDQ endorsed Natural Environment Site Strategy for the New Beith project. The purpose of this VCFMP is to manage the vegetation removal process and the protection of fauna species within the clearing area. The plan is required to be approved prior to clearing works commencing. The clearing works will follow general principles for vegetation clearing documented on this sheet, *sheet 4* and all EDQ specific requirements.

This VCFMP has been produced by overlaying the following site datasets to determine impacts and disturbance on existing vegetation in the interface zone between development and Open-space areas:

1. GPS accurate tree data including specimen details & features and site inspection of existing vegetation (SHG, 2024)
2. Bridge detail design (Colliers, 2024)

PROJECT MANAGEMENT

Vegetation management and its processes are an integral part of the construction and operational works phases. The site supervisor is responsible for all onsite works including overseeing vegetation clearing, health and safety of fauna and adhering to both EDQ's conditions and guidelines and Australian Standards - Protection of Trees on Development Sites AS4970-2009 and Pruning of Amenity Trees AS4373-1996.

The site arborist's responsibilities include: prior to the commencement of any earthworks on the site, undertake all appropriate arboricultural measures to ensure the survival and long-term health of existing trees to be retained. These measures may include soil decompaction, soil aeration, fertilising, mulching, watering, root or crown reduction and hazard reduction or as otherwise determined by the arborist. The site arborist is also required to direct and supervise all works within TPZs of trees to be retained and perform arboricultural care requirements where necessary.

SITE CONTACTS

Site and consulting contacts for queries relating to vegetation clearing include:

Client Contact:
Frasers Property New Beith Pty Ltd
Belinda Ryan 07 3249 7462

Environmental Contact:
Saunders Havill Group
Dr Andrew Davies 07 3251 9444

Site Contractor:
To be advised

Site Arborist:
To be advised

Site Fauna spotter-catcher:
To be advised
(Refer to *Fauna Management Plan* document for responsibilities)

Site Bushfire Consultant:
To be advised

CLEARING PHASES AND PROCESS

PHASE 1 - Tree Protection Fencing/Flagging to be installed
Fencing to be installed prior to the commencement of any clearing works on the site. Tree protection fencing to be located at or beyond 12 x diameter at breast height (DBH) (AS4970-2009 Protection of trees on development sites)—unless approved by the appointed arborist.

PHASE 2 - Pre-start Meeting
Fencing/Flagging shall be in place prior to the pre-start meeting for inspection and sign off by the Environmental Coordinator.

PHASE 3 - Fauna Inspections and Management
Undertake necessary fauna management requirements prior to clearing works - as a minimum, this should include the specifications listed on sheet 4, any additional measures proposed by the appointed fauna spotter during their pre-clearance report and acknowledge specific EDQ approval requirements.

PHASE 4 - Undertake Bulk Clearing
Undertake wholesale removal of vegetation once approved for removal by a qualified fauna spotter. Clearing will occur in the direction outlined in *sheet 53* of this VCFMP and managed by the appointed fauna spotter to allow all fauna unimpeded movement north and west towards adjoining remaining bushland. Sequential clearing will occur on the site adhering to the limitations of clearing no more than 4 ha set out in *Section 2, Part 3* of the *Nature Conservation (Koala) Conservation Plan 2017*.

Vegetation clearing techniques:

i. By utilising the most appropriate machinery and equipment during vegetation clearing, the probability of injury or death of wildlife during clearing can be significantly reduced or eliminated while still maintaining an efficient vegetation removal process.
ii. Bulldozers will be used to clear vegetation that has been thoroughly inspected by a fauna spotter-catcher and is found to contain no fauna or potential habitat. When a large tree is suspected of containing fauna or potential habitat, other methods of clearing should be used, when safe to do so. These methods include (a) a vertical tree grab attachment on an excavator (30 tonne) can be used to pull entire trees in size up to 30-40 cm diameter at a height measured at 1.3 metres above ground level and lay them down in a steady controlled fashion, allowing inspection by a fauna spotter-catcher (b) where trees are too large for a vertical tree grab, an elevated work platform or cherry picker, where practical, may be used in conjunction with a chainsaw operator and fauna spotter-catcher to carefully remove a hollow section from the habitat tree and gently lower the section for inspection by the fauna spotter-catcher.

NOTE: Dogs are not permitted onsite at any time during construction. Construction works including clearing must occur between the hours of 6.30am and 6.30pm.

ACCESS AND STOCKPILING

Tree and mulch stockpiling locations are to be designated in an easily accessible area outside of TPZs. Indicative stockpiling locations have been allocated near existing access tracks, allowing for material to be easily delivered and stored. These locations are subject to minor change according to cut/fill activities.

Cleared vegetation free of weeds is to be reused on or off the project site. Recycling techniques include mulching, tub-grinding, wood chipping and salvage (e.g. custom milling). Trees with identified hollows should have the hollow section preserved and should be suitably mounted on nearby or adjacent suitable trees.

MAINTENANCE

After tree clearing works on site, an analysis of the vegetation's health and growth should be undertaken by the project arborist to determine specific maintenance needs. Follow up maintenance works should be carried out on retained vegetation where required.

Tree Protection Zone - Detail (not to scale)

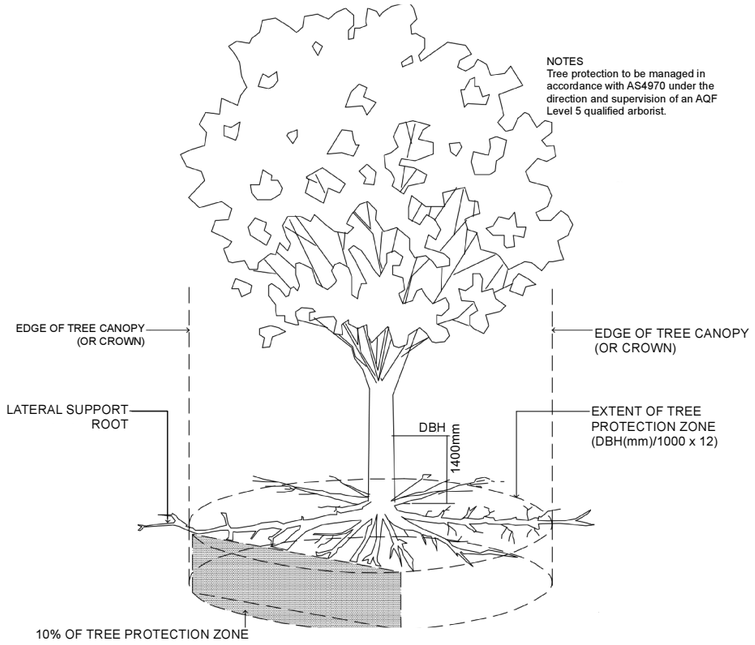

Tree Protection Fencing - Detail (not to scale)

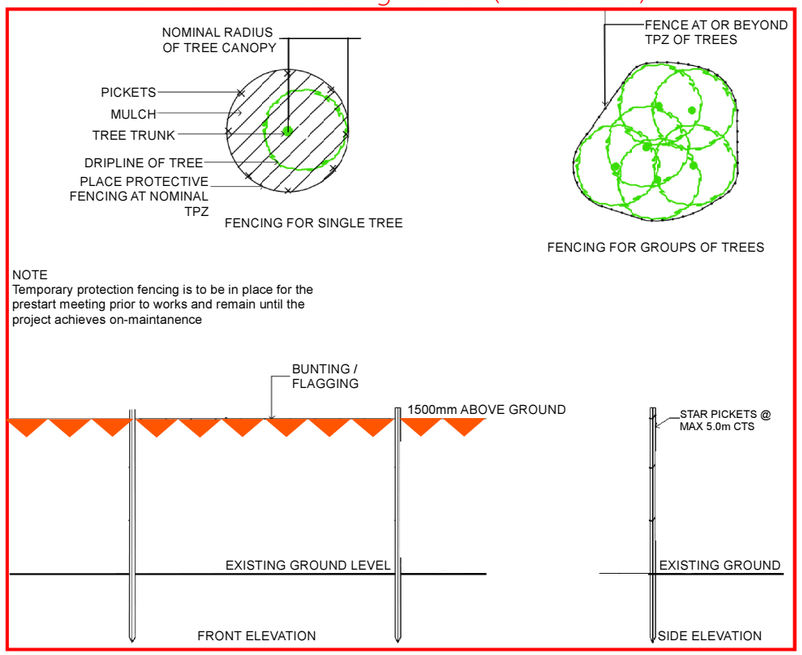

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

saunders havill group

CLIENT:
Frasers Property New Beith Pty Ltd

DISCLAIMER:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAILD LOCATIONS OF ALL SERVICES.

REFERENCES:
AS4970-2009 Protection of trees on development sites
Vegetation clearing techniques (Logan City Council, 2019)

AMENDMENTS:

Issue	Date	Description	Checked
B	8/05/2025	Updated Engineering	AD

PROJECT:
New Beith,
Southern Entry Bridge

environmental management

PLAN OF:
Vegetation Clearing & Fauna Management Plan

DATE:	8/05/2025	CHECKED:	AD
CLIENT REF.:	10941	DRAWN:	TC
DRAWING No.:	10941 E 02 S_Bridge VCFMP B		

Vegetation Clearing and Fauna Management Plan - *Fauna Management Notes*

INTRODUCTION

The Fauna Management specification on this *VCFMP* is designed to protect native animals and control/manage impacts during the vegetation clearing works. The clearing area occurs within the banks of Flagstone Creek, adjacent to existing clearing areas and regrowth bushland. Common species associated with bushland landscapes were spotted at the clearing area during the field assessment. The fauna management specifications and principles incorporated in this *VCFMP* apply generically to all native animals and focus on avoiding conflicts and incorporating measures to minimise disturbance. Compliance with this section of the *VCFMP* is compulsory and incorporates the use of expert consultants including a Fauna Spotter (holding a valid Wildlife Rehabilitation Permit issued by the Department of Environment, Science and Innovation).

FAUNA IMPACTS

Clearing of vegetation provides an obvious source of impact to existing habitat and animal safety. More specifically the existing vegetation provides habitat, movement and protection opportunities for some fauna through both regrowth and canopy trees. These opportunities may be altered during and post vegetation clearing works. Potential impacts include:

Construction Impacts

- Direct removal of site vegetation
- Loss of habitat
- Noise, vibration and dust
- Erosion and sedimentation
- Threats associated with open cuts etc. and fauna entrapment
- Loss of food sources
- Excavation/compaction/changes in ground levels
- Altering hydrological flows
- Fragmentation of habitat

Operational Impacts

- Weed introduction (garden escapees)
- Increased hydrology with increased hardstand
- Altering of run-off chemical and nutrient components (quality)
- Barriers to fauna movement
- Vehicles and pedestrian movement and trespass
- Introduction of domestic and predatory species

FAUNA MANAGEMENT SCHEDULE

Ref:	Management Item	Responsibility	Timing	Reporting
1.0 Pre - Clearing				
1.1	**Temporary Fencing** Prior to the commencement of works and to be inspected by the site Environmental Coordinator and/or Project Arborist—Delineate areas where vegetation is proposed to be retained with exclusion fencing to prevent accidental felling. Clearing is to be undertaken in accordance with AS 4970-2009 Protection of Trees on Development Sites. ▪ Fencing shall be fauna friendly ▪ No clearing, stockpiling, site access, earthworks, storage, etc. is to occur within the temporary protection fencing. ▪ Only approved weed management works to occur within the temporary protection fencing ▪ Fencing to be reinstated immediately if damaged or knocked down, any damage to retained trees to be immediately reported to Project Arborist. ▪ Fencing to remain until the completion of all site works.	Site Supervisor	Prior to the commencement of clearing	Inspected by Environmental coordinator and/or Project Arborist
1.2	**Contractor Education & Awareness** All site contractors and subcontractors will be made aware of their responsibilities to protect native fauna. The Fauna Management notes on this VCFMP are provided as a working document to assist on-site management and protection of native animals. This generally will form part of education and training on a broader work place health and safety but as a minimum will include: ▪ Copy of VCFMP kept on-site (Site Office). ▪ General education and awareness notification of contractors and sub-contractors involved in activities potentially impacting native animals as part of site induction – contractors must know the location of the VCFMP, key phone numbers and who to report to if they breach the VCFMP. ▪ A list of relevant contact phone numbers as listed on these drawings is kept in a visible and accessible location in the site office.	Site Supervisor / The Proponent	Prior to the commencement of clearing and as part of the site induction for new staff and sub-contractors	Site Supervisor
2.0 Vegetation Clearing				
2.1	**Spotter / Relocator** Immediately prior to the commencement of clearing of native vegetation a daily visual inspection of the area must be carried out by a qualified fauna spotter-catcher holding a valid Rehabilitation Permit. Furthermore, the fauna spotter-catcher is to be present on site during all clearing operations to supervise and direct clearing works, and to respond to any situations that may arise in relation to fauna. In the event of an animal being located, a suitable buffer area (as determined by the fauna spotter-catcher) should be established around the animal's location that excludes machinery until it has relocated at its own accord (usually overnight). If an animal requires relocating this must be undertaken by a suitable qualified fauna expert recognized by the Department of Environment, Science and Innovation. For some fauna, specific permit requirements may apply. If vegetation is left stockpiled for more than 24 hours or overnight, the fauna spotter-catcher must inspect the vegetation prior to chipping or removal from site. The Fauna Spotter-catcher will manage the care of any injured or orphaned wildlife (e.g. veterinary attention or delivery to a wildlife carer). Any native fauna listed as a threatened species under the Nature Conservation (Animals) Regulation 2020 that are injured or orphaned by the development process, must be reported to the Department of Environment, Science and Innovation (1300 130 372). Any other injured or orphaned fauna must be reported through the Rehabilitation Permit return process by the Fauna Spotter-catcher. The Site Supervisor is responsible for the safe management of site fauna and implementation of these specific fauna requirements.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher
2.2	**Specific Koala Management Notes** A Koala/Fauna spotter-catcher is a person who holds a valid Rehabilitation Permit from the relevant State Government Agency, and has either a tertiary qualification in Biology or Zoology, or who is demonstrably experienced in the identification and location of Koalas in their natural habitat. For example, a koala keeper employed by a licensed Wildlife exhibitor (i.e. a zoo) may be capable of demonstrating competence in locating Koala's. Prior to the commencement and during felling operations, it is the responsibility of the Koala spotter to be present at the site of felling operations identify any tree at the site within which a Koala is present, as well as any tree that has a crown which is intermeshed or overlapping with such a tree; and advise the person who is authorised to conduct the felling operation, or that persons' representative, of the precise location of each such tree Management Item.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher
2.3	**Clearing Pattern / Fauna Flushing** Clearing occurs once the fauna spotter-catcher gives sign off the site is clear of all native species and all necessary permits are obtained. The intended clearing directions is north away from current works on the Flagstone City project site. Clearing direction is subject to amendment by the fauna spotter-catcher. At the completion of operational works, and prior to the sealing of survey plans for the relevant stage, the fauna spotter-catcher must provide certification to EDQ officers that all works were undertaken in accordance with these fauna management requirements and specific EDQ requirements.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher
2.4	**Specific Habitat Tree Notes** Where possible, clearing of habitat trees is to be avoided during late winter and spring (typically July – October) when many native birds are actively nesting/have young in nests and arboreal mammals have dependent and/or pouch young.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

saunders havill group

Client: Frasers Property New Beith Pty Ltd

Disclaimer:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UP ON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON-SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

References:

AS4970-2009 Protection of trees on development sites

Amendments:

Issue	Date	Description	Checked
B	8/05/2025	Updated Engineering	AD

Project: New Beith, Southern Entry Bridge

environmental management

Plan of: Vegetation Clearing & Fauna Management Plan

Date:	8/05/2025	Checked:	AD
Client Ref:	10941	Drawn:	TC
Drawing No.:	10941 E 03 S_Bridge VCFMP B		

Future Precinct

Precinct B

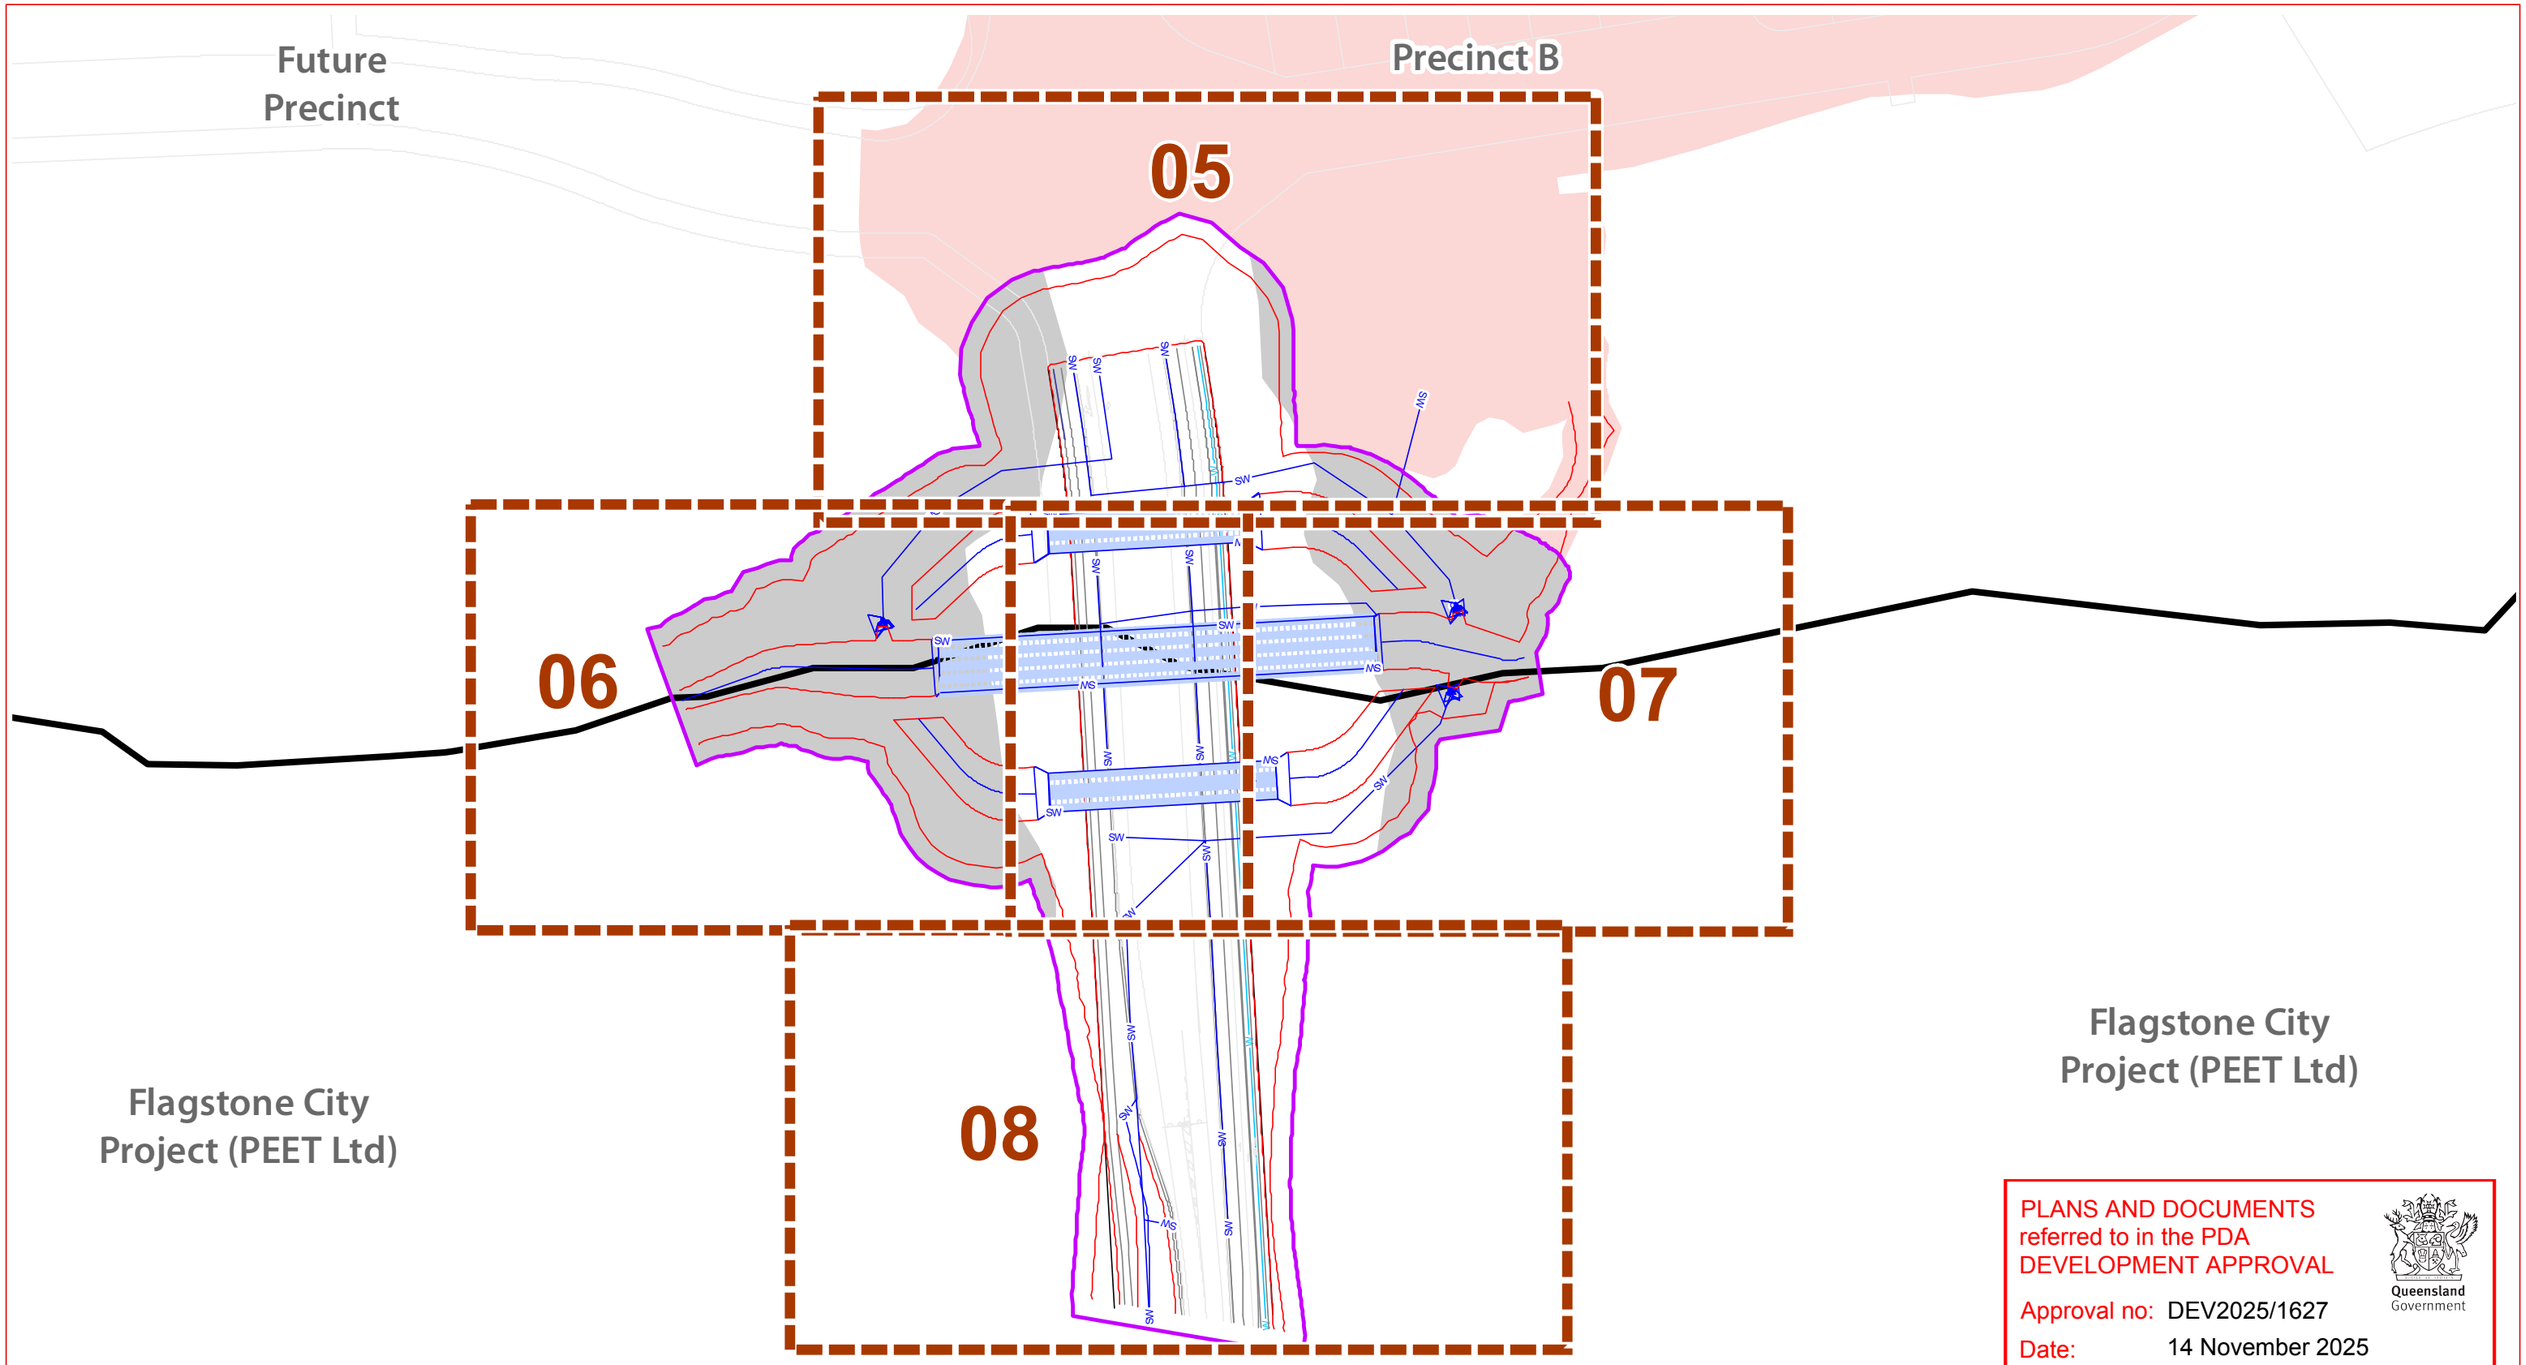

Flagstone City Project (PEET Ltd)

Flagstone City Project (PEET Ltd)

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

Project boundary

Southern bridge earthworks extent

Southern bridge vegetation clearing extent

Road boundary

Road & path pavement design

Stormwater design

Top & toe of batters design

Trunk water design

Culverts

Precinct B works extent/vegetation clearing

Vegetation Clearing & Fauna Management Plan - *Detail sheet context*

saunders havill group

CLIENT:

Frasers Property New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
B	8/05/2025	Updated Engineering	AD

0 20 40 60 80 100

1:1,250 @ A3

PROJECT:

New Beith, Southern Entry Bridge

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE:	8/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 04 S_Bridge VCFMP B		

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

Refer to Precinct B VMP for retention details

Refer to Precinct B VMP for retention details

GPS tree plot (w/TPZ & incl. Survey acc.)

- Tree to retain
- Tree retention subject to future project works
- Tree retention subject to arborist assessment and localised construction impacts
- Tree to remove for bridge construction
- Tree Protection fencing
- Existing contours (0.5m)
- Project boundary
- Southern bridge works extent
- Southern bridge vegetation clearing extent
- Proposed lot boundary
- Road & path pavement design
- Road markings design
- SW Waterflow design
- Culvert design
- Top & toe of batters design
- W Mains water
- Refer Precinct B VMP - works extent/ vegetation clearing
- Indicative stockpile location

Vegetation Clearing & Fauna Management Plan - *Sheet 05*

saunders havill group

CLIENT:

Frasers Property
New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
B	13/05/2025	Engineering updates	AD

0 10 20 30 m 1:400 @ A3

PROJECT:

New Beith,
Southern Entry Bridge

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE:	13/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 05 S_Bridge VCFMP B		

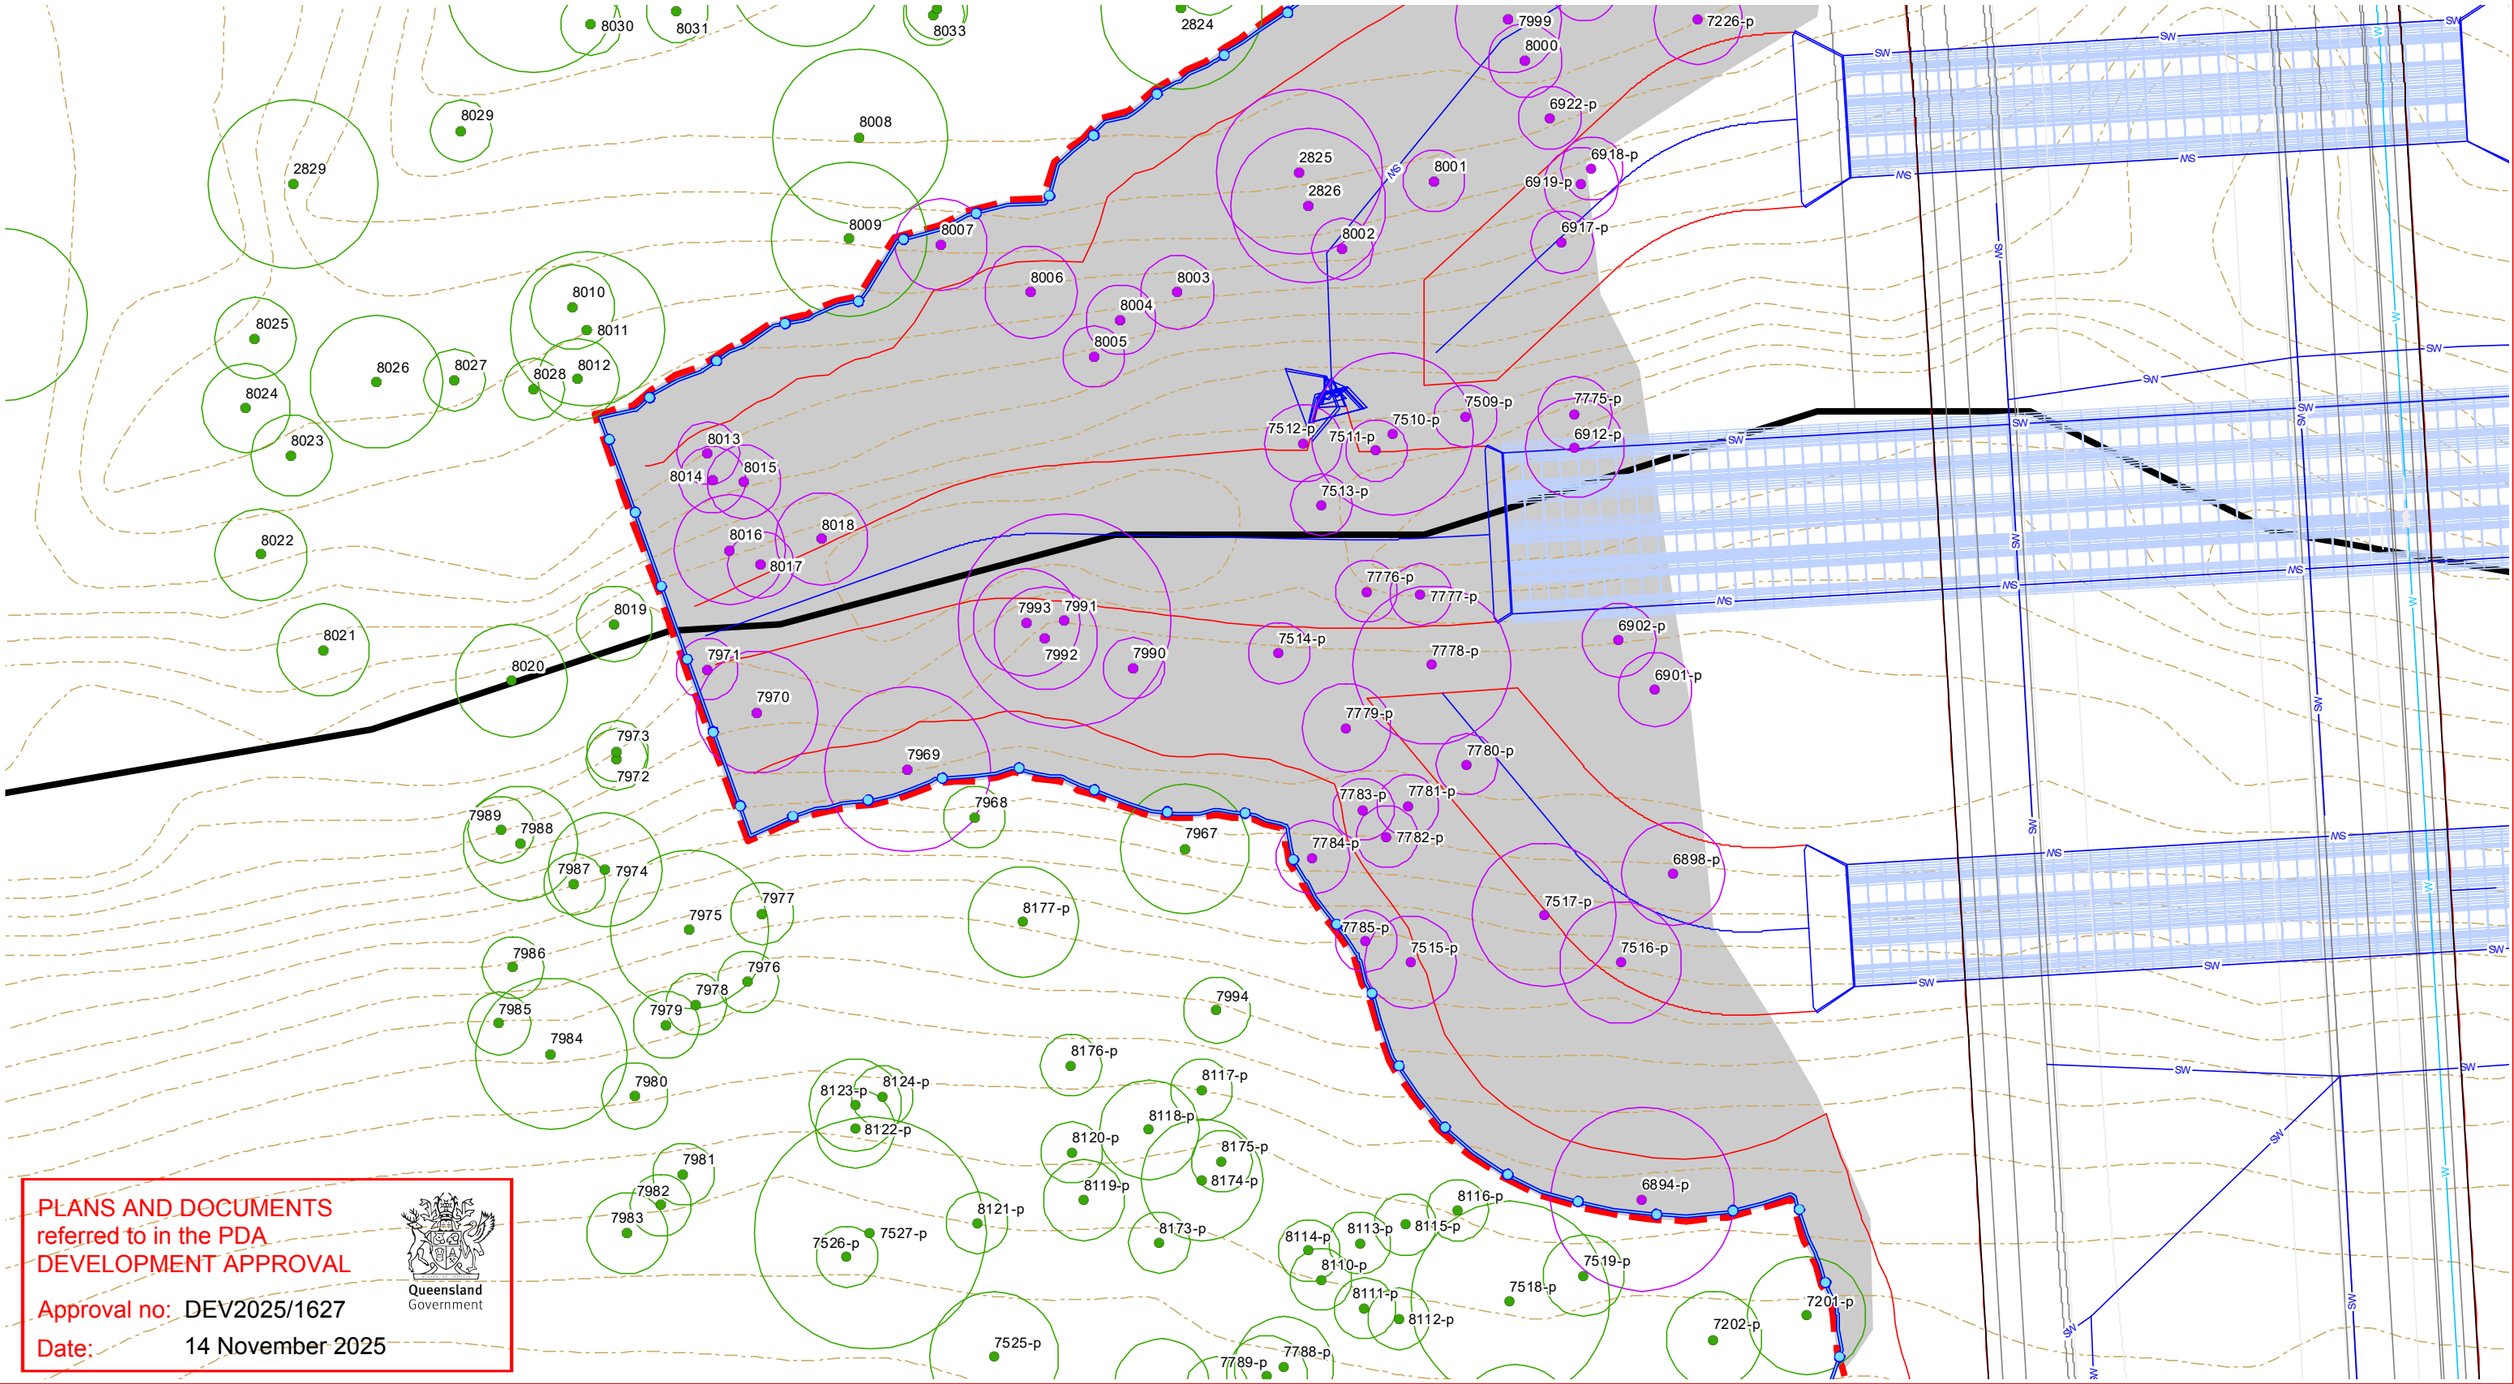

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

GPS tree plot (w/ TPZ & incl. Survey acc.)

- Tree to retain
- Tree retention subject to future project works
- Tree retention subject to arborist assessment and localised construction impacts
- Tree to remove for bridge construction
- Tree Protection fencing
- Existing contours (0.5m)
- Project boundary
- Southern bridge works extent
- Southern bridge vegetation clearing extent
- Proposed lot boundary
- Road & path pavement design
- Road markings design
- SW — Waterflow design
- Culvert design
- Top & toe of batters design
- W — Mains water
- Refer Precinct B VMP - works extent/ vegetation clearing
- Indicative stockpile location

Vegetation Clearing & Fauna Management Plan - *Sheet 06*

saunders havill group

CLIENT:

Frasers Property
New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
B	13/05/2025	Engineering updates	AD

0 10 20 30 m 1:400 @ A3

PROJECT:

New Beith,
Southern Entry Bridge

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE:	13/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 06 S_Bridge VCFMP B		

Refer to Precinct B VMP for retention details

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Approval no: DEV2025/1627

Date: 14 November 2025

Queensland Government

GPS tree plot (w/TPZ & incl. Survey acc.)

- Tree to retain
- Tree retention subject to future project works
- Tree retention subject to arborist assessment and localised construction impacts
- Tree to remove for bridge construction
- Tree Protection fencing
- Existing contours (0.5m)
- Project boundary
- Southern bridge works extent
- Southern bridge vegetation clearing extent
- Proposed lot boundary
- Road & path pavement design
- Road markings design
- Waterflow design
- Culvert design
- Top & toe of batters design
- Mains water
- Refer Precinct B VMP - works extent/ vegetation clearing
- Indicative stockpile location

Vegetation Clearing & Fauna Management Plan - *Sheet 07*

saunders havill group

CLIENT:

Frasers Property New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
B	13/05/2025	Engineering updates	AD

0 10 20 30 m 1:400 @ A3

PROJECT:

New Beith, Southern Entry Bridge

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE:	13/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 07 S_Bridge VCFMP B		

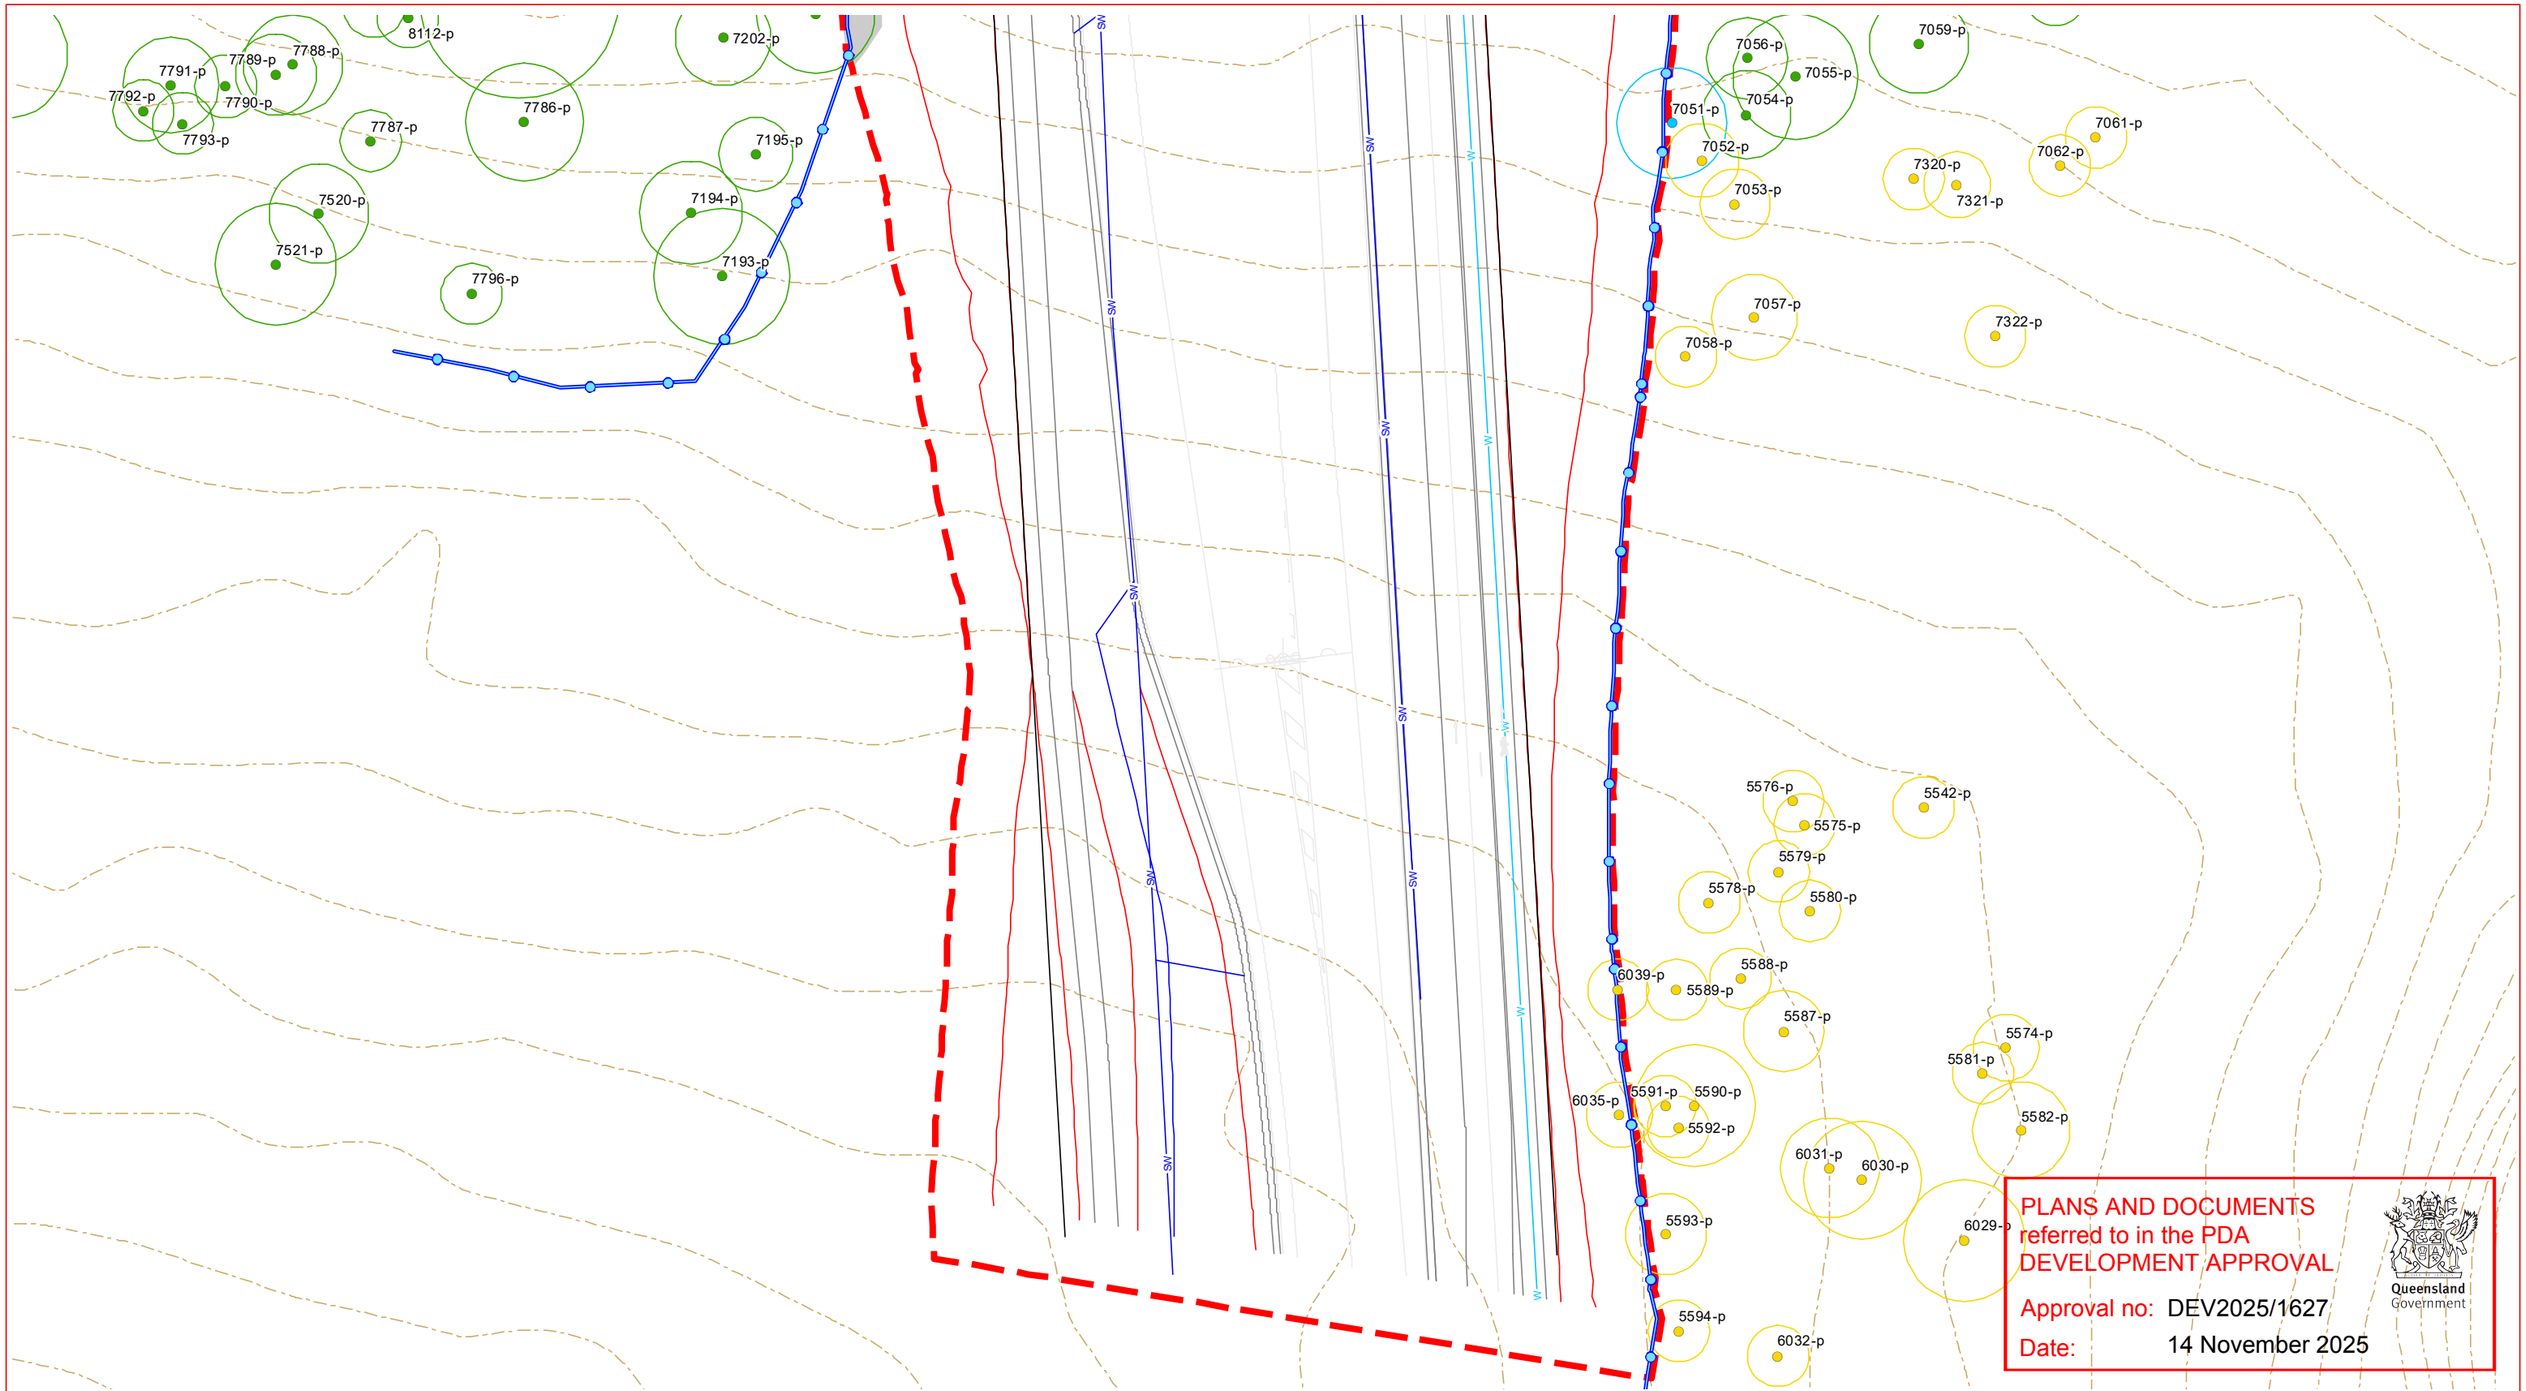

GPS tree plot (w/TPZ & incl. Survey acc.)

- Tree to retain
- Tree retention subject to future project works
- Tree retention subject to arborist assessment and localised construction impacts
- Tree to remove for bridge construction
- Tree Protection fencing
- Existing contours (0.5m)
- Project boundary
- Southern bridge works extent
- Southern bridge vegetation clearing extent
- Proposed lot boundary
- Road & path pavement design
- Road markings design
- Waterflow design
- Culvert design
- Top & toe of batters design
- Mains water
- Refer Precinct B VMP - works extent/ vegetation clearing
- Indicative stockpile location

Vegetation Clearing & Fauna Management Plan - *Sheet 08*

saunders havill group

CLIENT:

Frasers Property
New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
B	13/05/2025	Engineering updates	AD

0 10 20 30 m 1:400 @ A3

PROJECT:

New Beith,
Southern Entry Bridge

environmental management

PLAN OF: Vegetation Clearing & Fauna Management Plan

DATE:	13/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 08 S_Bridge VCFMP B		

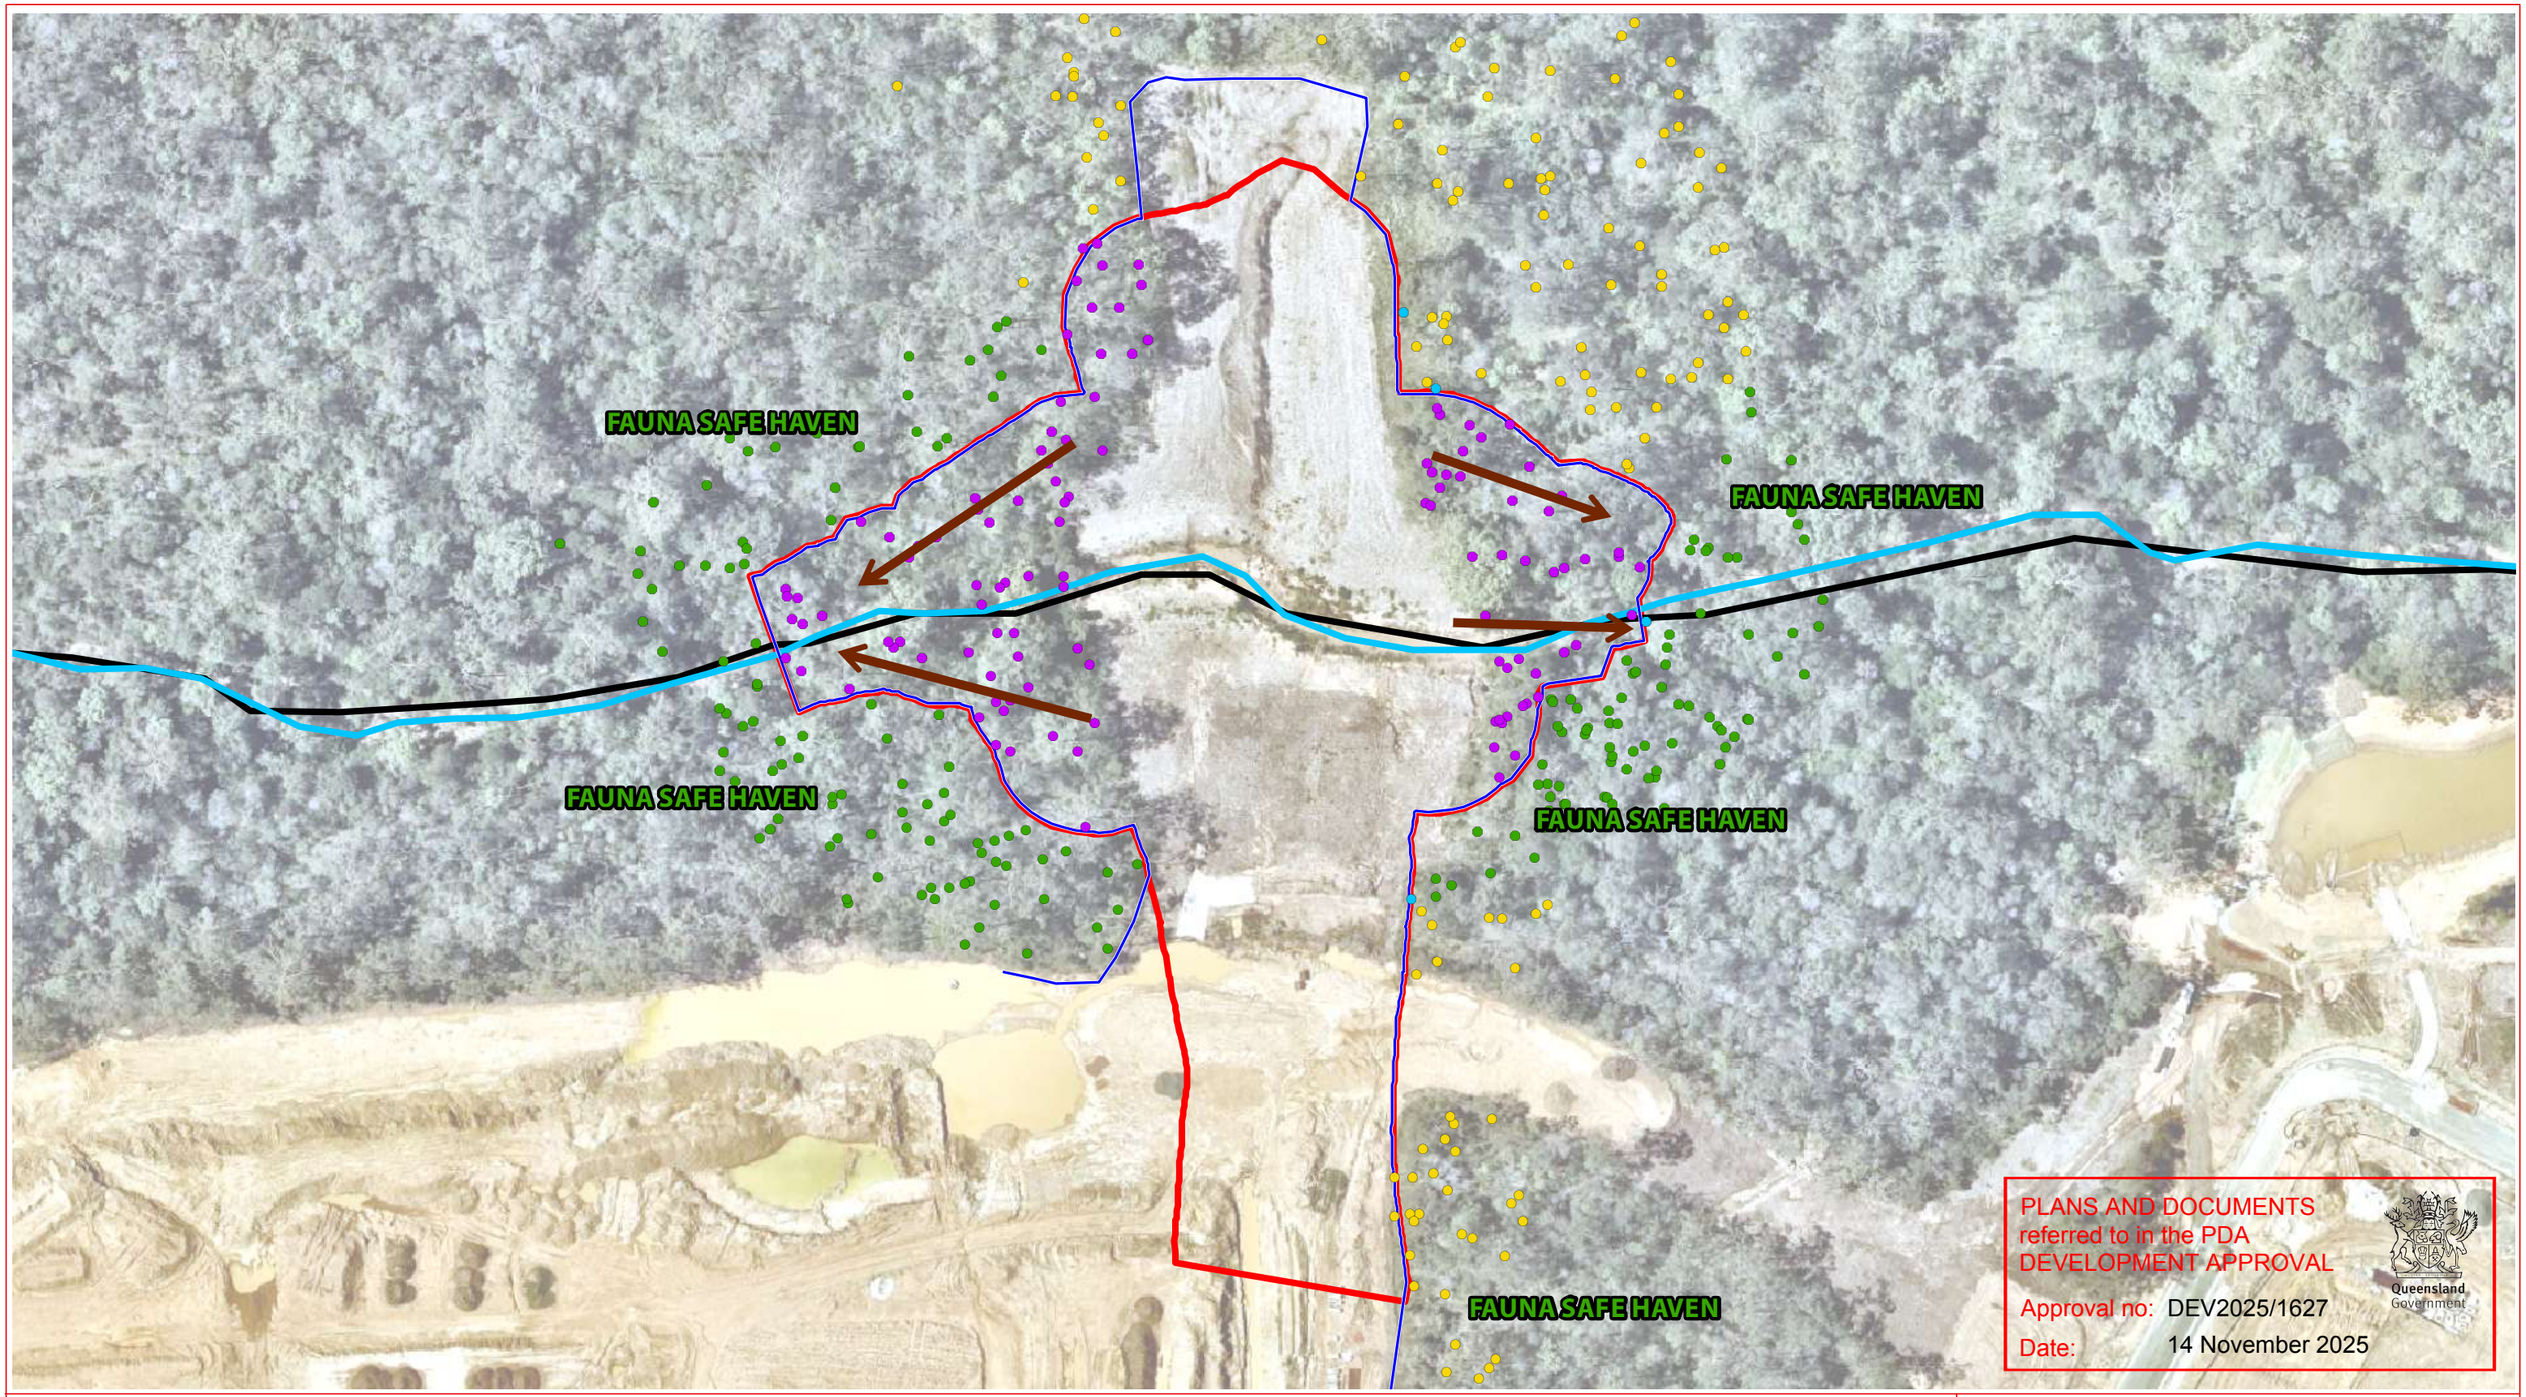

GPS tree plot

- Tree to retain
- Tree retention subject to future project works
- Tree retention subject to arborist assessment and localised construction impacts
- Tree to remove for bridge construction
- Project boundary
- Southern bridge earthworks extent
- Flagstone Creek
- Vegetation clearing direction
- Tree Protection fencing location

Vegetation Clearing & Fauna Management Plan - *Clearing Direction*

saunders havill group

CLIENT:

Frasers Property
New Beith Pty Ltd

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

Layout drawing (RPS, 2025)
Engineering drawing (Colliers, 2025)

AMENDMENTS:

Issue	Date	Description	Checked
A	13/05/2025	Preliminary	AD

0 20 40 60 80 100 m 1:1,250 @ A3

PROJECT:

New Beith,
Southern Entry Bridge

environmental management

PLAN OF:
Vegetation Clearing & Fauna Management Plan

DATE:	13/05/2025	CHECKED:	AD
CLIENT REF:	10941	DRAWN:	TC
DRAWING No.:	10941 E 10 S_Bridge VCFMP B		

PLANS AND DOCUMENTS referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

saunders havill group

Southern Entry Bridge VFCMP B Tree Schedule - 10941
Olsen Road, New Beith (Frasers Property New Beith Pty Ltd)
Date: 2025/05/13

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
319	*Lophostemon suaveolens*	Swamp Box	250		250	79	16.0	9.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
320	*Acacia disparrima*	Hickory Wattle	290		290	91	12.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
323	*Petalostigma pubescens*	Quinine Bush	350		350	110	15.0	10.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
324	*Petalostigma pubescens*	Quinine Bush	360		360	113	15.0	8.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
325	*Petalostigma pubescens*	Quinine Bush	200		200	63	12.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
326	*Corymbia torelliana*	Cadaghi	260		260	82	12.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
327	*Allocasuarina littoralis*	Black She-oak	230		230	72	14.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
328	*Eucalyptus tereticornis*	Forest Red Gum	400		400	126	24.0	7.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
329	*Eucalyptus tereticornis*	Forest Red Gum	490		490	154	24.0	8.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
330	*Corymbia intermedia*	Pink Bloodwood	520		520	163	19.0	9.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
331	*Eucalyptus tereticornis*	Forest Red Gum	500		500	157	24.0	9.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
332	*Acacia disparrima*	Hickory Wattle	230		230	72	10.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
333	*Corymbia intermedia*	Pink Bloodwood	480		480	151	24.0	10.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
334	*Corymbia intermedia*	Pink Bloodwood	550		550	173	24.0	10.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
335	*Lophostemon suaveolens*	Swamp Box	450		450	141	22.0	11.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-	Subject to Future development
663	*Eucalyptus tereticornis*	Forest Red Gum	350		350	110	21.0	13.0	4.2	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
664	*Petalostigma pubescens*	Quinine Bush	285		285	90	9.0	5.0	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
665	*Eucalyptus tereticornis*	Forest Red Gum	385		385	121	26.0	17.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
666	*Acacia disparrima*	Hickory Wattle	220		220	69	11.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Subject to Future development
667	*Petalostigma pubescens*	Quinine Bush	270		270	85	7.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Subject to Future development
668	*Acacia disparrima*	Hickory Wattle	215		215	68	9.0	7.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
669	*Corymbia intermedia*	Pink Bloodwood	515		515	162	18.0	10.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	Fire Dmg.	Typical	-	-	-	-	-	-	Subject to Future development
671	*Eucalyptus tereticornis*	Forest Red Gum	525		525	165	26.0	17.0	6.3	2.5	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Subject to Future development
672	*Corymbia intermedia*	Pink Bloodwood	275		275	86	17.0	10.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
673	*Lophostemon suaveolens*	Swamp Box	195		195	61	10.0	5.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-	Subject to Future development

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
674	*Acacia disparrima*	Hickory Wattle	200		200	63	11.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
675	*Lophostemon suaveolens*	Swamp Box	360		360	113	14.0	8.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
676	*Acacia disparrima*	Hickory Wattle	210		210	66	9.0	7.0	2.5	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
677	*Eucalyptus tereticornis*	Forest Red Gum	275		275	86	16.0	9.0	3.3	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
682	*Eucalyptus tereticornis*	Forest Red Gum	440		440	138	25.0	17.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
784	*Petalostigma pubescens*	Quinine Bush	240		240	75	12.0	8.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Arborist
802	*Acacia disparrima*	Hickory Wattle	290		290	91	13.0	5.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
803	*Eucalyptus crebra*	Narrow-leaved Ironbark	330		330	104	22.0	5.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
804	*Eucalyptus tereticornis*	Forest Red Gum	430		430	135	24.0	8.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
805	*Eucalyptus crebra*	Narrow-leaved Ironbark	260		260	82	17.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
806	*Corymbia intermedia*	Pink Bloodwood	370		370	116	17.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
807	*Lophostemon suaveolens*	Swamp Box	370		370	116	17.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
810	*Eucalyptus tereticornis*	Forest Red Gum	340		340	107	18.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
811	*Eucalyptus tereticornis*	Forest Red Gum	380		380	119	22.0	8.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
812	*Lophostemon suaveolens*	Swamp Box	380		380	119	12.0	7.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
813	*Lophostemon suaveolens*	Swamp Box	250		250	79	14.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
814	*Lophostemon suaveolens*	Swamp Box	280		280	88	16.0	7.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
815	*Lophostemon suaveolens*	Swamp Box	180		180	57	12.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
822	*Corymbia intermedia*	Pink Bloodwood	260		260	82	15.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
823	*Lophostemon suaveolens*	Swamp Box	340		340	107	17.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
824	*Lophostemon suaveolens*	Swamp Box	290		290	91	14.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
825	*Corymbia intermedia*	Pink Bloodwood	250		250	79	15.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
841	*Alphitonia excelsa*	Soap Tree	230		230	72	12.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
842	*Corymbia intermedia*	Pink Bloodwood	330		330	104	20.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)
984	*Acacia disparrima*	Hickory Wattle	230		230	72	6.0	3.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1018	*Eucalyptus tereticornis*	Forest Red Gum	290		290	91	13.0	4.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove (development area)
1019	*Eucalyptus tereticornis*	Forest Red Gum	220		220	69	14.0	3.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove (development area)
1020	*Lophostemon suaveolens*	Swamp Box	280		280	88	11.0	3.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove (development area)

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
1200	*Eucalyptus tereticornis*	Forest Red Gum	550		550	173	24.0	12.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1490	*Acacia disparrima*	Hickory Wattle	140		140	44	8.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1491	*Corymbia intermedia*	Pink Bloodwood	310		310	97	13.0	5.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1492	*Allocasuarina littoralis*	Black She-oak	240		240	75	13.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1493	*Corymbia intermedia*	Pink Bloodwood	240		240	75	12.0	2.0	2.9	1.8	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1494	*Petalostigma pubescens*	Quinine Bush	180		180	57	16.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1495	*Petalostigma pubescens*	Quinine Bush	220		220	69	13.0	9.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1496	*Corymbia intermedia*	Pink Bloodwood	490		490	154	24.0	10.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1497	*Petalostigma pubescens*	Quinine Bush	210		210	66	8.0	9.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1498	*Petalostigma pubescens*	Quinine Bush	280	190	338	106	13.0	12.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1499	*Petalostigma pubescens*	Quinine Bush	310		310	97	13.0	9.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1500	*Petalostigma pubescens*	Quinine Bush	350		350	110	18.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1501	*Corymbia intermedia*	Pink Bloodwood	350		350	110	14.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Arborist
1502	*Corymbia intermedia*	Pink Bloodwood	200		200	63	14.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1503	*Eucalyptus tereticornis*	Forest Red Gum	290		290	91	32.0	8.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1504	*Petalostigma pubescens*	Quinine Bush	330		330	104	9.0	3.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1505	*Petalostigma pubescens*	Quinine Bush	280		280	88	14.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1506	*Petalostigma pubescens*	Quinine Bush	220		220	69	13.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1507	*Petalostigma pubescens*	Quinine Bush	170		170	53	9.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1508	*Corymbia intermedia*	Pink Bloodwood	480	350	594	187	16.0	5.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1509	*Corymbia intermedia*	Pink Bloodwood	260		260	82	16.0	5.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1510	*Grevillea robusta*	Silky Oak	270		270	85	15.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1512	*Acacia disparrima*	Hickory Wattle	160		160	50	12.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1513	*Acacia disparrima*	Hickory Wattle	170		170	53	9.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1705	*Allocasuarina littoralis*	Black She-oak	160		160	50	14.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1706	*Acacia disparrima*	Hickory Wattle	160		160	50	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1707	*Allocasuarina littoralis*	Black She-oak	160		160	50	14.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1713	*Corymbia intermedia*	Pink Bloodwood	270		270	85	17.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
1714	*Allocasuarina littoralis*	Black She-oak	230		230	72	14.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1715	*Lophostemon suaveolens*	Swamp Box	160		160	50	14.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1716	*Allocasuarina littoralis*	Black She-oak	220		220	69	14.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1717	*Petalostigma pubescens*	Quinine Bush	220		220	69	12.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1718	*Eucalyptus tereticornis*	Forest Red Gum	350		350	110	18.0	6.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1719	*Petalostigma pubescens*	Quinine Bush	300		300	94	8.0	9.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1720	*Acacia disparrima*	Hickory Wattle	200		200	63	12.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1721	*Lophostemon suaveolens*	Swamp Box	170		170	53	10.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1722	*Acacia disparrima*	Hickory Wattle	170		170	53	12.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1723	*Corymbia intermedia*	Pink Bloodwood	610		610	192	19.0	11.0	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1724	*Corymbia intermedia*	Pink Bloodwood	310		310	97	16.0	8.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1728	*Lophostemon suaveolens*	Swamp Box	330		330	104	17.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1729	*Alphitonia excelsa*	Soap Tree	290		290	91	18.0	7.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1730	*Corymbia intermedia*	Pink Bloodwood	230		230	72	14.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1731	*Corymbia tessellaris*	Moreton Bay Ash	200		200	63	17.0	4.0	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1732	*Corymbia intermedia*	Pink Bloodwood	160		160	50	16.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1733	*Corymbia intermedia*	Pink Bloodwood	300		300	94	17.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1734	*Lophostemon suaveolens*	Swamp Box	180		180	57	14.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1735	*Lophostemon suaveolens*	Swamp Box	180		180	57	15.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1736	*Corymbia tessellaris*	Moreton Bay Ash	300		300	94	18.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1737	*Corymbia tessellaris*	Moreton Bay Ash	150		150	47	14.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
1738	*Alphitonia excelsa*	Soap Tree	250		250	79	15.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1739	*Lophostemon suaveolens*	Swamp Box	240		240	75	14.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1740	*Acacia disparrima*	Hickory Wattle	160		160	50	13.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1741	*Petalostigma pubescens*	Quinine Bush	290		290	91	14.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1742	*Acacia leiocalyx*	Early-flowering Black Wattle	180		180	57	12.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1743	*Eucalyptus tereticornis*	Forest Red Gum	460		460	145	19.0	9.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1744	*Corymbia intermedia*	Pink Bloodwood	250		250	79	16.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
1745	*Corymbia intermedia*	Pink Bloodwood	220		220	69	16.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1746	*Lophostemon suaveolens*	Swamp Box	300		300	94	16.0	5.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1747	*Grevillea robusta*	Silky Oak	170		170	53	14.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1748	*Alphitonia excelsa*	Soap Tree	170		170	53	14.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1749	*Alphitonia excelsa*	Soap Tree	220		220	69	12.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1750	*Acacia leiocalyx*	Early-flowering Black Wattle	170		170	53	13.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1751	*Acacia disparrima*	Hickory Wattle	180		180	57	14.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
1752	*Alphitonia excelsa*	Soap Tree	170		170	53	14.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
2822	*Eucalyptus tereticornis*	Forest Red Gum	470		470	148	28.0	9.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Subject to Future development
2823	*Eucalyptus siderophloia*	Northern Grey Ironbark	460		460	145	25.0	12.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
2824	*Eucalyptus siderophloia*	Northern Grey Ironbark	440		440	138	26.0	17.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
2825	*Dead/Stag*		450		450	141	19.0	4.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Yes	-		-	Remove - Bridge
2826	*Dead/Stag*		420		420	132	18.0	5.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
2829	*Eucalyptus crebra*	Narrow-leaved Ironbark	460		460	145	32.0	16.0	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
3418	*Corymbia intermedia*	Pink Bloodwood	410		410	129	20.0	10.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
3419	*Petalostigma pubescens*	Quinine Bush	370		370	116	6.0	4.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7902	*Acacia disparrima*	Hickory Wattle	210		210	66	7.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7903	*Corymbia intermedia*	Pink Bloodwood	300		300	94	13.0	4.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7904	*Dead/Stag*		240		240	75	7.0	3.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Yes	-		-	Retain
7905	*Alphitonia excelsa*	Soap Tree	150		150	47	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7906	*Alphitonia excelsa*	Soap Tree	130		130	41	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7907	*Acacia disparrima*	Hickory Wattle	150		150	47	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7908	*Corymbia intermedia*	Pink Bloodwood	590		590	185	16.0	7.0	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7909	*Acacia disparrima*	Hickory Wattle	120		120	38	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7910	*Alphitonia excelsa*	Soap Tree	230		230	72	8.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7911	*Acacia disparrima*	Hickory Wattle	140		140	44	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7912	*Alphitonia excelsa*	Soap Tree	190		190	60	8.0	3.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7913	*Acacia disparrima*	Hickory Wattle	220		220	69	11.0	5.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7914	*Acacia disparrima*	Hickory Wattle	180		180	57	8.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7915	*Dead/Stag*		340		340	107	8.0	4.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Yes	-		-	Retain
7916	*Acacia disparrima*	Hickory Wattle	150		150	47	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7917	*Alphitonia excelsa*	Soap Tree	250		250	79	13.0	4.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7918	*Acacia disparrima*	Hickory Wattle	160		160	50	7.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7919	*Alphitonia excelsa*	Soap Tree	190		190	60	9.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7920	*Alphitonia excelsa*	Soap Tree	290		290	91	9.0	5.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7921	*Erythrina x sykesii*	Coral Tree	120		120	38	6.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7922	*Erythrina x sykesii*	Coral Tree	240		240	75	9.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7923	*Acacia disparrima*	Hickory Wattle	200		200	63	8.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7924	*Alphitonia excelsa*	Soap Tree	140		140	44	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7925	*Petalostigma pubescens*	Quinine Bush	120		120	38	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7926	*Corymbia intermedia*	Pink Bloodwood	170		170	53	7.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7927	*Alphitonia excelsa*	Soap Tree	190		190	60	7.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7928	*Acacia disparrima*	Hickory Wattle	130		130	41	7.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7929	*Alphitonia excelsa*	Soap Tree	160		160	50	11.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7930	*Acacia disparrima*	Hickory Wattle	160		160	50	12.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7931	*Corymbia intermedia*	Pink Bloodwood	140		140	44	11.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7932	*Acacia disparrima*	Hickory Wattle	150		150	47	7.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7933	*Acacia disparrima*	Hickory Wattle	280		280	88	11.0	6.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7934	*Acacia disparrima*	Hickory Wattle	130		130	41	7.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7935	*Acacia disparrima*	Hickory Wattle	210		210	66	11.0	3.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7936	*Corymbia intermedia*	Pink Bloodwood	520		520	163	13.0	6.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7937	*Alphitonia excelsa*	Soap Tree	200		200	63	9.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7938	*Alphitonia excelsa*	Soap Tree	240		240	75	12.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7939	*Grevillea robusta*	Silky Oak	320		320	101	14.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7940	*Ficus coronata*	Sandpaper Fig	280	260	382	120	12.0	5.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7941	*Petalostigma pubescens*	Quinine Bush	290		290	91	8.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7942	*Acacia disparrima*	Hickory Wattle	190		190	60	8.0	4.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7943	*Alphitonia excelsa*	Soap Tree	320		320	101	12.0	4.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7944	*Acacia disparrima*	Hickory Wattle	160		160	50	6.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7945	*Ficus coronata*	Sandpaper Fig	190	130	230	72	7.0	4.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7946	*Acacia disparrima*	Hickory Wattle	100		100	31	7.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7947	*Dead/Stag*		490		490	154	12.0	6.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7948	*Acacia disparrima*	Hickory Wattle	130		130	41	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7949	*Corymbia intermedia*	Pink Bloodwood	540		540	170	14.0	7.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7950	*Lophostemon suaveolens*	Swamp Box	260		260	82	9.0	4.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7951	*Acacia disparrima*	Hickory Wattle	180		180	57	8.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7952	*Corymbia intermedia*	Pink Bloodwood	330		330	104	14.0	6.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7953	*Corymbia tessellaris*	Moreton Bay Ash	300		300	94	16.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7954	*Corymbia intermedia*	Pink Bloodwood	260		260	82	11.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7955	*Callistemon salignus*	White Bottle Brush	150		150	47	5.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-		-	Retain
7956	*Acacia disparrima*	Hickory Wattle	140		140	44	7.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7957	*Lophostemon suaveolens*	Swamp Box	470		470	148	14.0	6.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7958	*Corymbia intermedia*	Pink Bloodwood	130		130	41	9.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7959	*Alphitonia excelsa*	Soap Tree	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7960	*Alphitonia excelsa*	Soap Tree	140		140	44	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7961	*Callistemon salignus*	White Bottle Brush	160	150	219	69	7.0	4.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Subject to Arborist
7962	*Callistemon salignus*	White Bottle Brush	160		160	50	6.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7963	*Corymbia intermedia*	Pink Bloodwood	260		260	82	14.0	4.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7964	*Acacia disparrima*	Hickory Wattle	160		160	50	11.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7965	*Petalostigma pubescens*	Quinine Bush	100		100	31	5.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7966	*Petalostigma pubescens*	Quinine Bush	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7967	*Angophora leiocarpa*	Smooth-barked Apple	350		350	110	21.0	6.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7968	*Lophostemon suaveolens*	Swamp Box	120		120	38	7.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7969	*Eucalyptus tereticornis*	Forest Red Gum	450		450	141	14.0	6.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7970	*Lophostemon suaveolens*	Swamp Box	330		330	104	7.0	4.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7971	*Callistemon salignus*	White Bottle Brush	110		110	35	7.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7972	*Callistemon citrinus*	Crimson Bottlebrush	150		150	47	11.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7973	*Callistemon citrinus*	Crimson Bottlebrush	140		140	44	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7974	*Corymbia torelliana*	Cadaghi	310		310	97	9.0	5.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7975	*Eucalyptus crebra*	Narrow-leaved Ironbark	430		430	135	18.0	7.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7976	*Angophora leiocarpa*	Smooth-barked Apple	120		120	38	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7977	*Allocasuarina littoralis*	Black She-oak	170		170	53	9.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7978	*Eucalyptus tereticornis*	Forest Red Gum	150		150	47	8.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7979	*Eucalyptus tereticornis*	Forest Red Gum	180		180	57	12.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7980	*Angophora leiocarpa*	Smooth-barked Apple	180		180	57	9.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7981	*Angophora leiocarpa*	Smooth-barked Apple	130		130	41	9.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7982	*Corymbia intermedia*	Pink Bloodwood	140		140	44	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7983	*Eucalyptus crebra*	Narrow-leaved Ironbark	220		220	69	13.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7984	*Dead/Stag*		410		410	129	15.0	4.0	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7985	*Allocasuarina littoralis*	Black She-oak	170		170	53	7.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7986	*Lophostemon suaveolens*	Swamp Box	160		160	50	8.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7987	*Lophostemon suaveolens*	Swamp Box	120		120	38	7.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7988	*Lophostemon suaveolens*	Swamp Box	310		310	97	11.0	3.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7989	*Lophostemon suaveolens*	Swamp Box	180		180	57	8.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7990	*Allocasuarina littoralis*	Black She-oak	110		110	35	8.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7991	*Angophora subvelutina*	Broad-leaved Apple	580		580	182	17.0	14.0	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7992	*Lophostemon suaveolens*	Swamp Box	280		280	88	13.0	4.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7993	*Lophostemon suaveolens*	Swamp Box	290		290	91	11.0	5.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7994	*Corymbia intermedia*	Pink Bloodwood	180		180	57	9.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
7995	*Callistemon salignus*	White Bottle Brush	180		180	57	8.0	7.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7996	*Callistemon salignus*	White Bottle Brush	200		200	63	8.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7997	*Alphitonia excelsa*	Soap Tree	150		150	47	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7998	*Lophostemon suaveolens*	Swamp Box	130		130	41	7.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
7999	*Eucalyptus tereticornis*	Forest Red Gum	290		290	91	16.0	7.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8000	*Corymbia intermedia*	Pink Bloodwood	200		200	63	7.0	1.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8001	*Lophostemon suaveolens*	Swamp Box	120		120	38	4.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8002	*Lophostemon suaveolens*	Swamp Box	160		160	50	5.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8003	*Acacia disparrima*	Hickory Wattle	200		200	63	6.0	2.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8004	*Lophostemon suaveolens*	Swamp Box	190		190	60	7.0	3.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8005	*Petalostigma quadriloculare*		110	110	156	49	5.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8006	*Alphitonia excelsa*	Soap Tree	250		250	79	7.0	4.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8007	*Allocasuarina littoralis*	Black She-oak	250		250	79	7.0	3.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8008	*Corymbia intermedia*	Pink Bloodwood	370	300	476	150	18.0	8.0	5.7	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8009	*Dead/Stag*		420		420	132	14.0	6.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Yes	-		-	Retain
8010	*Corymbia intermedia*	Pink Bloodwood	230		230	72	16.0	5.0	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8011	*Corymbia intermedia*	Pink Bloodwood	420		420	132	20.0	12.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8012	*Allocasuarina littoralis*	Black She-oak	220		220	69	6.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8013	*Allocasuarina littoralis*	Black She-oak	170		170	53	7.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8014	*Aphananthe philippinensis*	Native Elm	180		180	57	5.0	3.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8015	*Acacia disparrima*	Hickory Wattle	200		200	63	7.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8016	*Melaleuca viminalis*	Weeping Bottlebrush	300		300	94	8.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8017	*Melaleuca viminalis*	Weeping Bottlebrush	180		180	57	6.0	3.0	2.2	1.6	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8018	*Melaleuca viminalis*	Weeping Bottlebrush	250		250	79	7.0	4.0	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Remove - Bridge
8019	*Melaleuca viminalis*	Weeping Bottlebrush	140	80 80 70 70	205	65	6.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-		-	Retain
8020	*Melaleuca viminalis*	Weeping Bottlebrush	230	200	305	96	6.0	6.0	3.7	2.0	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-		-	Retain
8021	*Grevillea robusta*	Silky Oak	250		250	79	12.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8022	*Aphananthe philippinensis*	Native Elm	200	150	250	79	9.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8023	*Allocasuarina littoralis*	Black She-oak	220		220	69	8.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8024	*Allocasuarina littoralis*	Black She-oak	240		240	75	10.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8025	*Allocasuarina littoralis*	Black She-oak	220		220	69	8.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
8026	*Petalostigma pubescens*	Quinine Bush	360		360	113	7.0	6.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8027	*Allocasuarina littoralis*	Black She-oak	150		150	47	7.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8028	*Allocasuarina littoralis*	Black She-oak	160		160	50	7.0	3.0	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8029	*Lophostemon suaveolens*	Swamp Box	140		140	44	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8030	*Eucalyptus crebra*	Narrow-leaved Ironbark	160		160	50	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8031	*Lophostemon suaveolens*	Swamp Box	140		140	44	6.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8033	*Lophostemon suaveolens*	Swamp Box	120		120	38	7.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8034	*Acacia disparrima*	Hickory Wattle	160		160	50	7.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8035	*Acacia disparrima*	Hickory Wattle	130		130	41	5.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8036	*Lophostemon suaveolens*	Swamp Box	110		110	35	7.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8037	*Acacia concurrens*	Black Wattle	120		120	38	5.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8038	*Corymbia intermedia*	Pink Bloodwood	270		270	85	20.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8039	*Eucalyptus tereticornis*	Forest Red Gum	340		340	107	22.0	10.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8040	*Corymbia intermedia*	Pink Bloodwood	250		250	79	18.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8046	*Eucalyptus siderophloia*	Northern Grey Ironbark	240		240	75	18.0	7.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
526-p	*Corymbia intermedia*	Pink Bloodwood	210		210	66	19.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
527-p	*Eucalyptus acmenoides*	White Mahogany	330	300	446	140	18.0	10.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
531-p	*Corymbia intermedia*	Pink Bloodwood	240		240	75	18.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
532-p	*Eucalyptus tereticornis*	Forest Red Gum	270		270	85	18.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
533-p	*Eucalyptus acmenoides*	White Mahogany	250	200	320	101	17.0	6.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
534-p	*Eucalyptus acmenoides*	White Mahogany	200	230	305	96	18.0	8.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
535-p	*Eucalyptus acmenoides*	White Mahogany	230	210	311	98	16.0	7.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
536-p	*Eucalyptus tereticornis*	Forest Red Gum	260		260	82	18.0	5.0	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
537-p	*Eucalyptus tereticornis*	Forest Red Gum	230		230	72	19.0	4.0	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
538-p	*Eucalyptus acmenoides*	White Mahogany	230		230	72	16.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
539-p	*Eucalyptus acmenoides*	White Mahogany	270	200	336	106	17.0	8.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
540-p	*Eucalyptus tereticornis*	Forest Red Gum	250		250	79	20.0	6.0	3.0	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
541-p	*Eucalyptus acmenoides*	White Mahogany	200		200	63	16.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
542-p	*Eucalyptus tereticornis*	Forest Red Gum	290		290	91	20.0	6.0	3.5	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
543-p	*Corymbia intermedia*	Pink Bloodwood	280		280	88	18.0	5.0	3.4	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
544-p	*Eucalyptus acmenoides*	White Mahogany	320		320	100	16.0	8.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
547-p	*Corymbia intermedia*	Pink Bloodwood	240	170	294	92	17.0	6.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
551-p	*Eucalyptus acmenoides*	White Mahogany	230		230	72	17.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
552-p	*Corymbia intermedia*	Pink Bloodwood	200		200	63	16.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
553-p	*Eucalyptus acmenoides*	White Mahogany	200		200	63	16.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
853-p	*Eucalyptus tereticornis*	Forest Red Gum	200		200	63	15.0	4.0	2.4	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
854-p	*Angophora leiocarpa*	Smooth-barked Apple	210		210	66	13.0	4.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
855-p	*Eucalyptus acmenoides*	White Mahogany	420		420	132	16.0	6.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1343-p	*Eucalyptus acmenoides*	White Mahogany	220		220	69	17.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
1344-p	*Eucalyptus tereticornis*	Forest Red Gum	580		580	182	28.0	12.0	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
5542-p	*Acacia disparrima*	Hickory Wattle	120		120	38	7.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5574-p	*Acacia leiocalyx*	Early-flowering Black Wattle	180		180	57	9.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5575-p	*Angophora leiocarpa*	Smooth-barked Apple	110		110	35	7.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5576-p	*Angophora leiocarpa*	Smooth-barked Apple	100		100	31	6.0	1.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5578-p	*Angophora leiocarpa*	Smooth-barked Apple	130		130	41	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5579-p	*Acacia disparrima*	Hickory Wattle	100		100	31	5.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5580-p	*Acacia disparrima*	Hickory Wattle	140		140	44	9.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5581-p	*Alphitonia excelsa*	Soap Tree	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5582-p	*Acacia disparrima*	Hickory Wattle	200	100, 140	264	83	7.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5587-p	*Acacia leiocalyx*	Early-flowering Black Wattle	220		220	69	8.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5588-p	*Acacia leiocalyx*	Early-flowering Black Wattle	150		150	47	8.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5589-p	*Acacia disparrima*	Hickory Wattle	100		100	31	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5590-p	*Corymbia intermedia*	Pink Bloodwood	330		330	104	20.0	11.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5591-p	*Acacia disparrima*	Hickory Wattle	160		160	50	9.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5592-p	*Acacia disparrima*	Hickory Wattle	140		140	44	7.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
5593-p	*Petalostigma pubescens*	Quinine Bush	220		220	69	7.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
5594-p	*Acacia leiocalyx*	Early-flowering Black Wattle	100		100	31	7.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6029-p	*Corymbia intermedia*	Pink Bloodwood	330		330	104	18.0	4.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6030-p	*Corymbia intermedia*	Pink Bloodwood	320		320	100	20.0	5.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6031-p	*Lophostemon suaveolens*	Swamp Box	270		270	85	18.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6032-p	*Acacia leiocalyx*	Early-flowering Black Wattle	120		120	38	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6035-p	*Acacia disparrima*	Hickory Wattle	160	80	179	56	8.0	2.0	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6039-p	*Acacia disparrima*	Hickory Wattle	140		140	44	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
6894-p	*Eucalyptus tereticornis*	Forest Red Gum	500		500	157	27.0	14.0	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6898-p	*Eucalyptus tereticornis*	Forest Red Gum	280		280	88	20.0	5.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6901-p	*Acacia disparrima*	Hickory Wattle	200		200	63	11.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6902-p	*Alphitonia excelsa*	Soap Tree	200		200	63	11.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6912-p	*Melaleuca viminalis*	Weeping Bottlebrush	200	180	269	84	9.0	3.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6917-p	*Acacia concurrens*	Black Wattle	170		170	53	12.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6918-p	*Acacia disparrima*	Hickory Wattle	170		170	53	10.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6919-p	*Acacia disparrima*	Hickory Wattle	150	100, 90	201	63	10.0	4.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6922-p	*Lophostemon suaveolens*	Swamp Box	170		170	53	13.0	2.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
6923-p	*Corymbia intermedia*	Pink Bloodwood	350		350	110	18.0	5.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7051-p	*Corymbia citriodora*	Spotted Gum	300		300	94	21.0	6.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Arborist
7052-p	*Petalostigma pubescens*	Quinine Bush	200		200	63	9.0	3.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7053-p	*Acacia disparrima*	Hickory Wattle	190		190	60	11.0	3.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7054-p	*Alphitonia excelsa*	Soap Tree	240		240	75	11.0	4.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7055-p	*Corymbia intermedia*	Pink Bloodwood	340		340	107	18.0	7.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7056-p	*Corymbia citriodora*	Spotted Gum	220		220	69	19.0	4.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7057-p	*Acacia leiocalyx*	Early-flowering Black Wattle	160	170	233	73	9.0	5.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7058-p	*Corymbia citriodora*	Spotted Gum	140		140	44	17.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7059-p	*Corymbia citriodora*	Spotted Gum	270		270	85	17.0	5.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7060-p	*Acacia disparrima*	Hickory Wattle	130		130	41	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7061-p	*Alphitonia excelsa*	Soap Tree	140		140	44	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7062-p	*Acacia disparrima*	Hickory Wattle	160		160	50	10.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7193-p	*Corymbia citriodora*	Spotted Gum	370		370	116	25.0	8.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7194-p	*Eucalyptus tereticornis*	Forest Red Gum	280		280	88	20.0	7.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7195-p	*Corymbia intermedia*	Pink Bloodwood	200		200	63	15.0	6.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7201-p	*Petalostigma pubescens*	Quinine Bush	180	150, 150, 160	321	101	8.0	5.0	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7202-p	*Corymbia intermedia*	Pink Bloodwood	260		260	82	22.0	6.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7226-p	*Allocasuarina littoralis*	Black She-oak	240		240	75	15.0	5.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7227-p	*Corymbia intermedia*	Pink Bloodwood	180		180	57	15.0	4.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7228-p	*Acacia leiocalyx*	Early-flowering Black Wattle	150		150	47	15.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7230-p	*Eucalyptus tereticornis*	Forest Red Gum	330		330	104	23.0	4.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7231-p	*Eucalyptus tereticornis*	Forest Red Gum	350		350	110	24.0	7.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7320-p	*Acacia disparrima*	Hickory Wattle	150		150	47	8.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7321-p	*Acacia disparrima*	Hickory Wattle	180		180	57	9.0	2.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7322-p	*Acacia disparrima*	Hickory Wattle	150		150	47	10.0	2.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Subject to Future development
7775-p	*Melaleuca viminalis*	Weeping Bottlebrush	200		200	63	16.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7454-p	*Corymbia intermedia*	Pink Bloodwood	600		600	188	26.0	12.0	7.2	2.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7455-p	*Corymbia intermedia*	Pink Bloodwood	240		240	75	22.0	14.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7456-p	*Corymbia intermedia*	Pink Bloodwood	230		230	72	22.0	10.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7457-p	*Alphitonia excelsa*	Red Ash	180		180	57	10.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7458-p	*Acacia disparrima*	Hickory Wattle	150		150	47	8.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7459-p	*Petalostigma pubescens*	Quinine Bush	170		170	53	10.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7460-p	*Corymbia citriodora*	Spotted Gum	290		290	91	26.0	12.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7461-p	*Acacia disparrima*	Hickory Wattle	260		260	82	12.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7462-p	*Alphitonia excelsa*	Red Ash	120		120	38	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7463-p	*Eucalyptus tereticornis*	Forest Red Gum	210		210	66	22.0	12.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7464-p	*Lophostemon suaveolens*	Swamp Box	190		190	60	14.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7509-p	*Melaleuca viminalis*	Weeping Bottlebrush	170		170	53	8.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7510-p	*Ficus benjamina*	Weeping Fig	440		440	138	18.0	12.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7511-p	*Grevillea robusta*	Silky Oak	110		110	35	12.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7512-p	*Casuarina cunninghamiana*	River Sheoak	210		210	66	20.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7513-p	*Acacia disparrima*	Hickory Wattle	150		150	47	14.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7514-p	*Alphitonia excelsa*	Red Ash	140		140	44	16.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7515-p	*Petalostigma pubescens*	Quinine Bush	250		250	79	8.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7516-p	*Alphitonia excelsa*	Red Ash	330		330	104	14.0	12.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7517-p	*Eucalyptus siderophloia*	Grey Ironbark	390		390	122	26.0	14.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Remove - Bridge
7518-p	*DEAD/STAG*		540		540	170	12.0	4.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-	Retain
7519-p	*Eucalyptus tereticornis*	Forest Red Gum	220		220	69	20.0	10.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7520-p	*Corymbia intermedia*	Pink Bloodwood	270		270	85	20.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7521-p	*Corymbia citriodora*	Spotted Gum	330		330	104	26.0	12.0	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7523-p	*Alphitonia excelsa*	Red Ash	230		230	72	12.0	10.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7524-p	*Corymbia citriodora*	Spotted Gum	240		240	75	24.0	10.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7525-p	*Corymbia citriodora*	Spotted Gum	350		350	110	24.0	14.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7526-p	*Corymbia citriodora*	Spotted Gum	150		150	47	18.0	6.0	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7527-p	*Eucalyptus siderophloia*	Grey Ironbark	630		630	198	24.0	12.0	7.6	2.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-	Retain
7722-p	*Corymbia citriodora*	Spotted Gum	200		200	63	20.0	13.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7723-p	*Petalostigma pubescens*	Quinine Bush	160	160	226	71	4.0	11.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7776-p	*Alphitonia excelsa*	Red Ash	150		150	47	15.0	10.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7777-p	*Alphitonia excelsa*	Red Ash	150		150	47	13.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7778-p	*Eucalyptus tereticornis*	Forest Red Gum	430		430	135	22.0	16.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7779-p	*Lophostemon suaveolens*	Swamp Box	240		240	75	16.0	8.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7780-p	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	38	15.0	9.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7781-p	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	35	16.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7782-p	*Allocasuarina littoralis*	Black Sheoak	150		150	47	16.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7783-p	*Allocasuarina littoralis*	Black Sheoak	100	70, 70	141	44	13.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7784-p	*Eucalyptus siderophloia*	Grey Ironbark	200		200	63	20.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge
7785-p	*Allocasuarina littoralis*	Black Sheoak	120		120	38	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Remove - Bridge

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
7786-p	*Corymbia citriodora*	Spotted Gum	320		320	100	22.0	14.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7787-p	*Acacia disparrima*	Hickory Wattle	100	100, 80	162	51	4.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7788-p	*Corymbia citriodora*	Spotted Gum	270		270	85	20.0	13.0	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7789-p	*Alphitonia excelsa*	Red Ash	220		220	69	14.0	13.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7790-p	*Petalostigma pubescens*	Quinine Bush	170		170	53	3.0	2.0	2.0	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7791-p	*Eucalyptus siderophloia*	Grey Ironbark	260		260	82	20.0	13.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7792-p	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	31	12.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7793-p	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	35	13.0	7.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
7796-p	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	44	15.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	Retain
8110-p	*Corymbia citriodora*	Spotted Gum	110		110	35	13.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8111-p	*Acacia disparrima*	Hickory Wattle	110	90	142	45	9.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-		-	Retain
8112-p	*Acacia disparrima*	Hickory Wattle	160		160	50	8.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8113-p	*Acacia disparrima*	Hickory Wattle	165		165	52	9.0	3.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8114-p	*Corymbia citriodora*	Spotted Gum	110		110	35	13.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8115-p	*Alphitonia excelsa*	Soap Tree	100		100	31	9.0	2.0	2.0	1.3	Regular	-	-	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-		-	Retain
8116-p	*Corymbia citriodora*	Spotted Gum	110		110	35	13.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8117-p	*Corymbia intermedia*	Pink Bloodwood	140		140	44	13.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	Fire Dmg.	Typical	-	-	-	-		-	Retain
8118-p	*Dead/Stag*		270		270	85	8.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8119-p	*Alphitonia excelsa*	Soap Tree	220		220	69	9.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-		-	Retain
8120-p	*Allocasuarina littoralis*	Black She-oak	105		105	33	7.0	2.0	2.0	1.3	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8121-p	*Dead/Stag*		140		140	44	5.0	1.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8122-p	*Dead/Stag*		215		215	68	14.0	6.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8123-p	*Dead/Stag*		250		250	79	15.0	5.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8124-p	*Dead/Stag*		120		120	38	8.0	2.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8173-p	*Corymbia intermedia*	Pink Bloodwood	140		140	44	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8174-p	*Corymbia intermedia*	Pink Bloodwood	330		330	104	14.0	10.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8175-p	*Corymbia citriodora*	Spotted Gum	140		140	44	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
8176-p	*Allocasuarina littoralis*	Black She-oak	140		140	44	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain

PLANS AND DOCUMENTS
referred to in the PDA
DEVELOPMENT APPROVAL
Approval no: DEV2025/1627
Date: 14 November 2025
Queensland Government

Specimen Details											Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value						Additional Details
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Trunk Circumference (cm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Retention
8177-p	*Eucalyptus crebra*	Narrow-leaved Ironbark	300		300	94	15.0	8.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-		-	Retain
