Vegetation Management Plan

Stages 2 to 5 (Phase 2)

Flagstone

by PEET Ltd

Economic Development Queensland

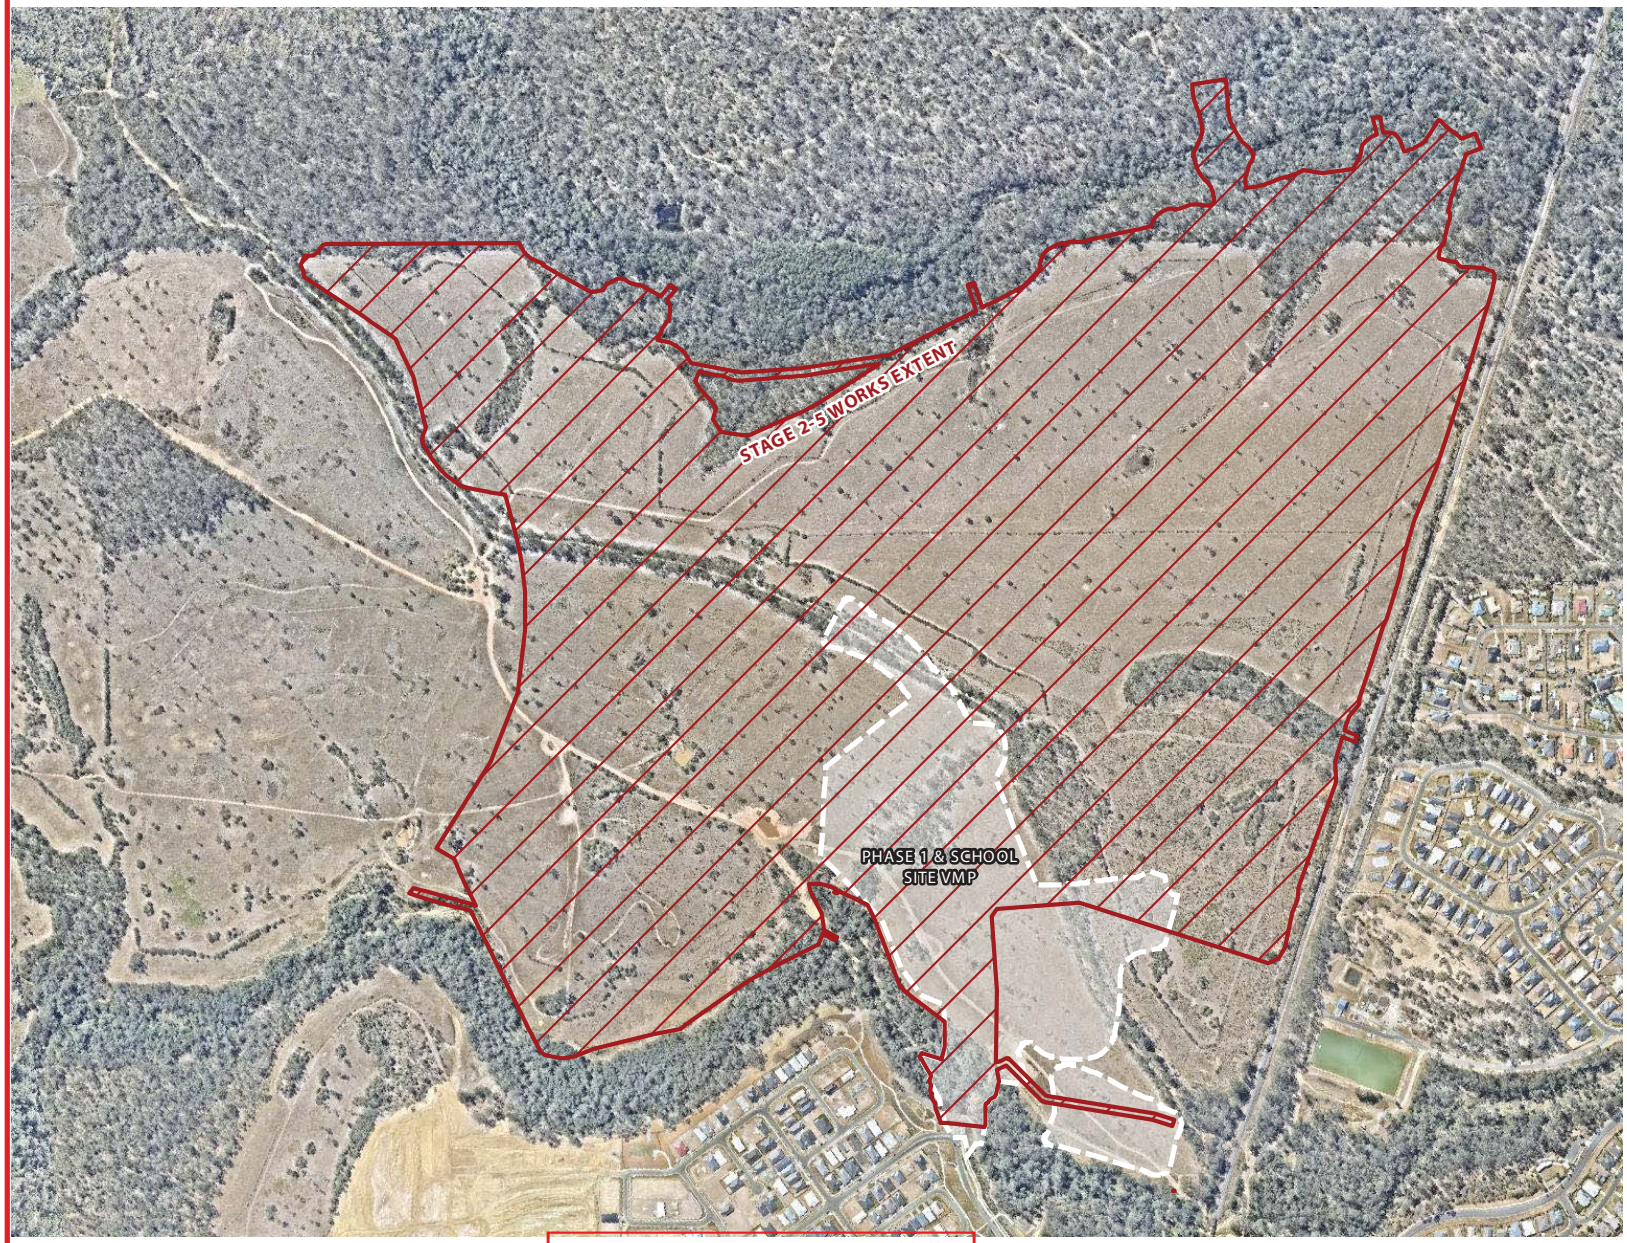

PLANS AND DOCUMENTS referred to in the PDA DEVELOPMENT APPROVAL

Queensland Government

Approval no: DEV2012/403

Date: 19 August 2019

CONTENTS

8047 E 02 BAL Stage 2 VMP E -- Vegetation Clearing Notes
8047 E 03 BAL Stage 2 VMP E -- Key Plan
8047 E 04-78 BAL Stage 2 VMP E -- Detail Sheets
8047 E 78 BAL Stage 2 VMP E -- Clearing Direction
Appendix A -- Stage 2-5 Tree Schedule (Master Schedule)

Key Site Contacts

Saunders Havill Group
Dr Andrew Davies
Phone: (07) 3251 9444
Email: andrewdavies@saundershavill.com

saunders havill group

PEET

Vegetation Management Plan
Vegetation Clearing - Notes

INTRODUCTION

The *Environmental Management Division* of the **Saunders Havill Group** was engaged by **PEET Flagstone City** to prepare a *Vegetation Management Plan* (*VMP*) for the removal of vegetation for the second phase of operational works in stages 2 to 5 of the Flagstone City project.

This VMP was drafted in response to the project's *Natural Environment Site Strategy's* (*NESS)* requirement for *VMPs.* The *VMP* will manage the vegetation clearing practices during operational work stages. The *VMP* will cover the second phase of clearing in the Stage 2-5 area and correspond with the lodgement of the planning and civil applications for the proposed development, including basins and road locations. The clearing works will follow the general principal for vegetation clearing documented on this sheet and be read in conjunction with the *Fauna Management Plan* document.

To assist in the spatial depiction of the phase 2 clearing area and better allocate a tree retention and removal status, ecologists from the **Saunders Havill Group** completed a tree survey using Trimble GNSS based GPS units. The survey collected the following features of trees within and adjoining the phase 2 works extent as provided by the project engineer (**Meinhardt**):

- Reference number and point location
- Botanical Name / Common Name
- Trunk DBH
- AS4970-2009 – Tree Protection Zone
- Height and Spread
- Canopy and Trunk Condition
- Fauna and Habitat Values Details

Particular attention and detail was collected along Sandy Creek & Flagstone Creek interface areas to maximise the retention of healthy native habitat trees along the corridor.

CLEARING PHASES AND PROCESS

The following stages are required for clearing to be undertaken on this property and a copy of this *VMP* must be present with the clearing contractor on-site:

PHASE 1 – Demarcation

Tree Protection Fencing to be installed prior to the commencement of any clearing works on the site. Tree protection fencing is to be located at or beyond 12 x diameter at breast height (DBH) unless approved by an appointed Arborist around trees designated for retention or as per the locations shown in this drawing package (refer Fencing Note). Fencing shall clearly demark the extent of works ensuring no additional vegetation will be cleared.

PHASE 2 - Pre-start Meeting

Fencing shall be in place at the time of the official pre-start meeting for inspection by the Environmental Coordinator. A fauna spotter pre-works assessment report must be carried out prior to the pre-start meeting and provided to the clearing contractor (Refer to *Fauna Management Plan* accompanying this application for details).

PHASE 4 - Undertake Clearing Works

Undertake removal of vegetation once approved for removal by the appointed fauna spotter. Clearing will occur in the direction outlined in *Fauna Management Plan* and managed by the appointed fauna spotter to allow all fauna unimpeded movement away from works areas. The contractor is to follow any tree felling directions of the appointed fauna spotter/arborist, including but not limited to, an excavator vertical tree grab attachment or cherry picker, where the use of bulldozer is not appropriate.

PHASE 5 - Post clearing Works

Cleared vegetation is to be reused on or off premises. Recycling techniques include mulching, tub-grinding, wood chipping and salvage (e.g. custom milling). Trees with identified hollows should have the hollow section preserved and this section should be suitably mounted on nearby or adjacent suitable trees.

Carry out assessment of all retained trees by a qualified arborist along the edge of development once civil works have been completed. Implement any tree management measures if advised by the arborist.

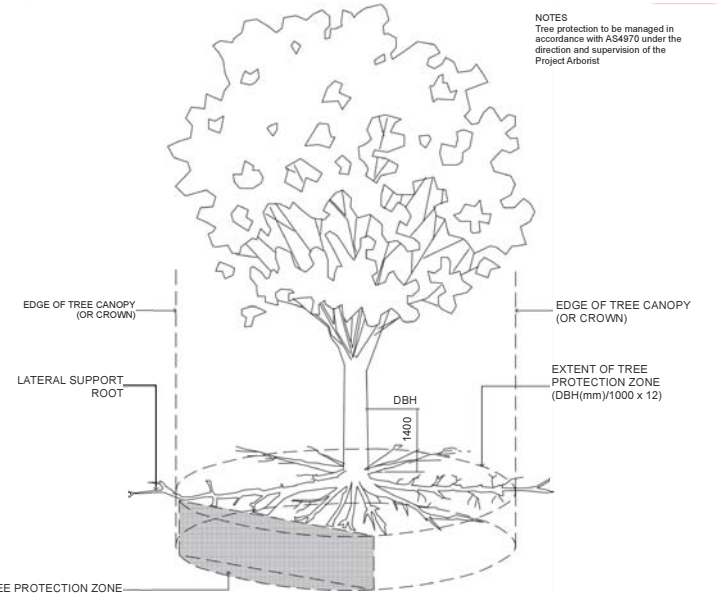

Tree Protection Fencing Detail

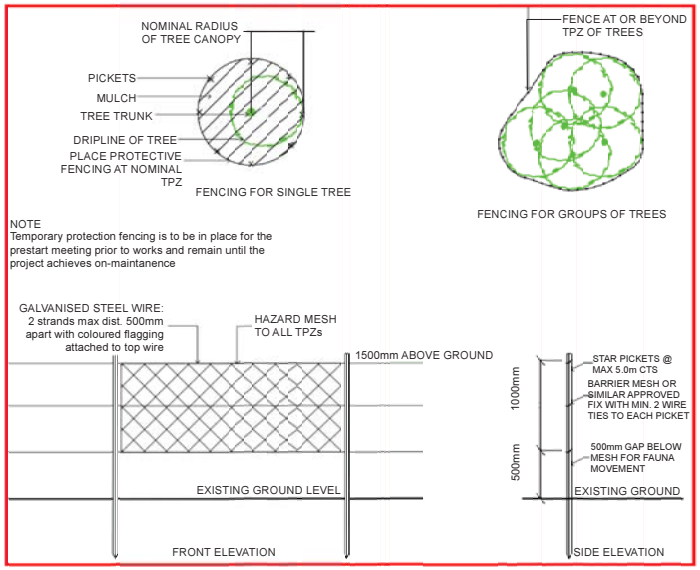

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWING BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDER-GROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	22/02/2019	RFI	AD

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 22/02/2019 CHECKED: AD

JOB REF: 8047 DRAWN: TC

DRAWING No.: 8047 E 02 BAL Stage 2 VMP E

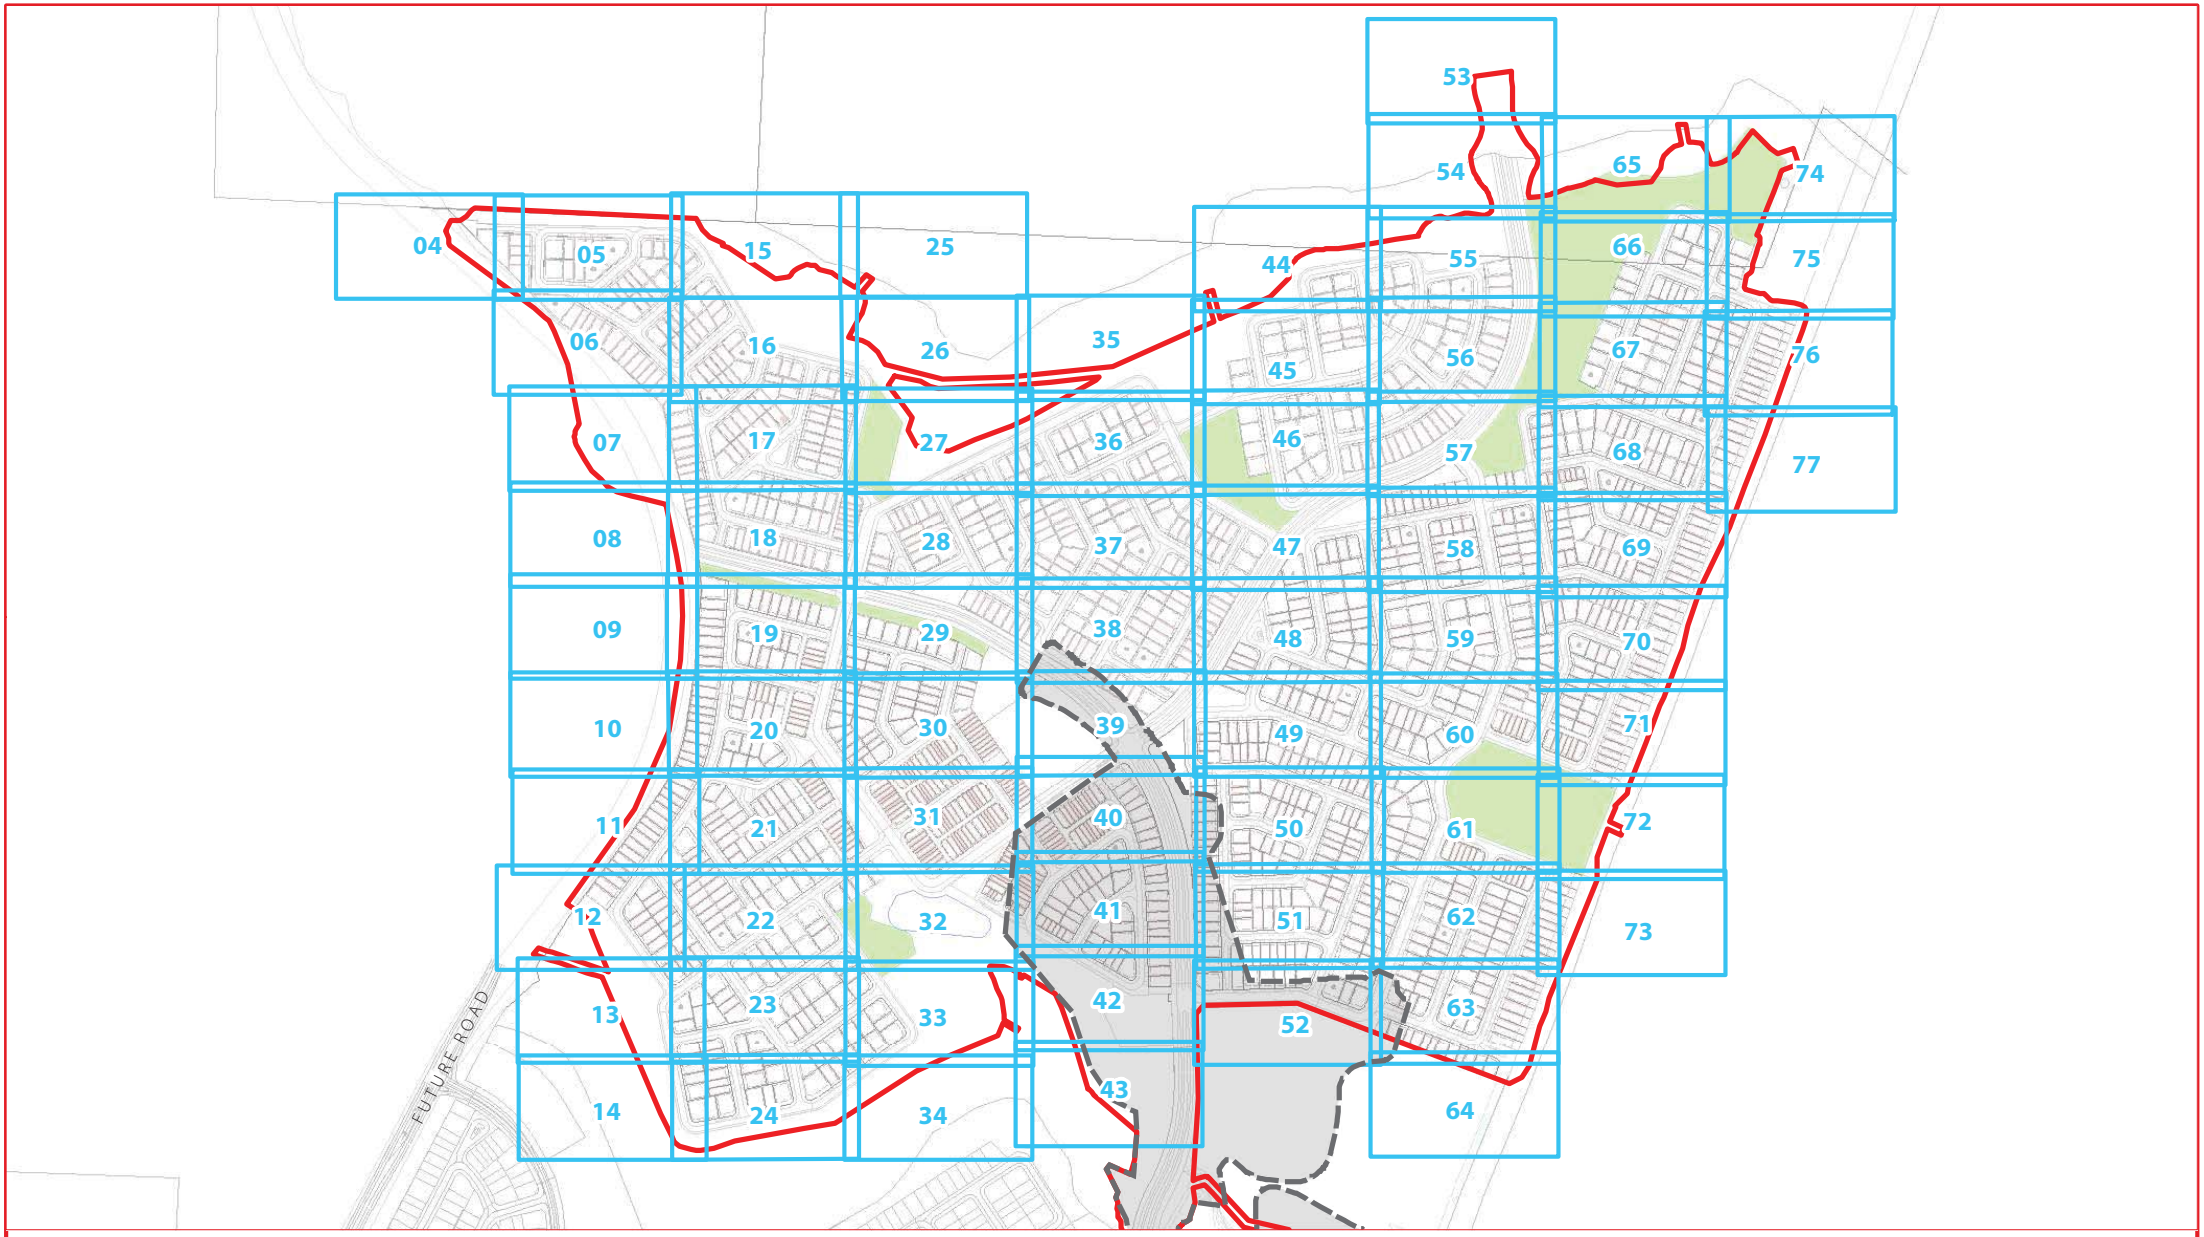

Legend

- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access)
- Stage 2-5 Layout design (RPS)
- Trunk sewer
- Phase 1 & School site VMP area

Vegetation Management Plan - *Detail Sheets Key Plan*

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THESE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ONSITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 50 100 200 300 400 500 m

1:7,000 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 03 BAL Stage 2 VMP E

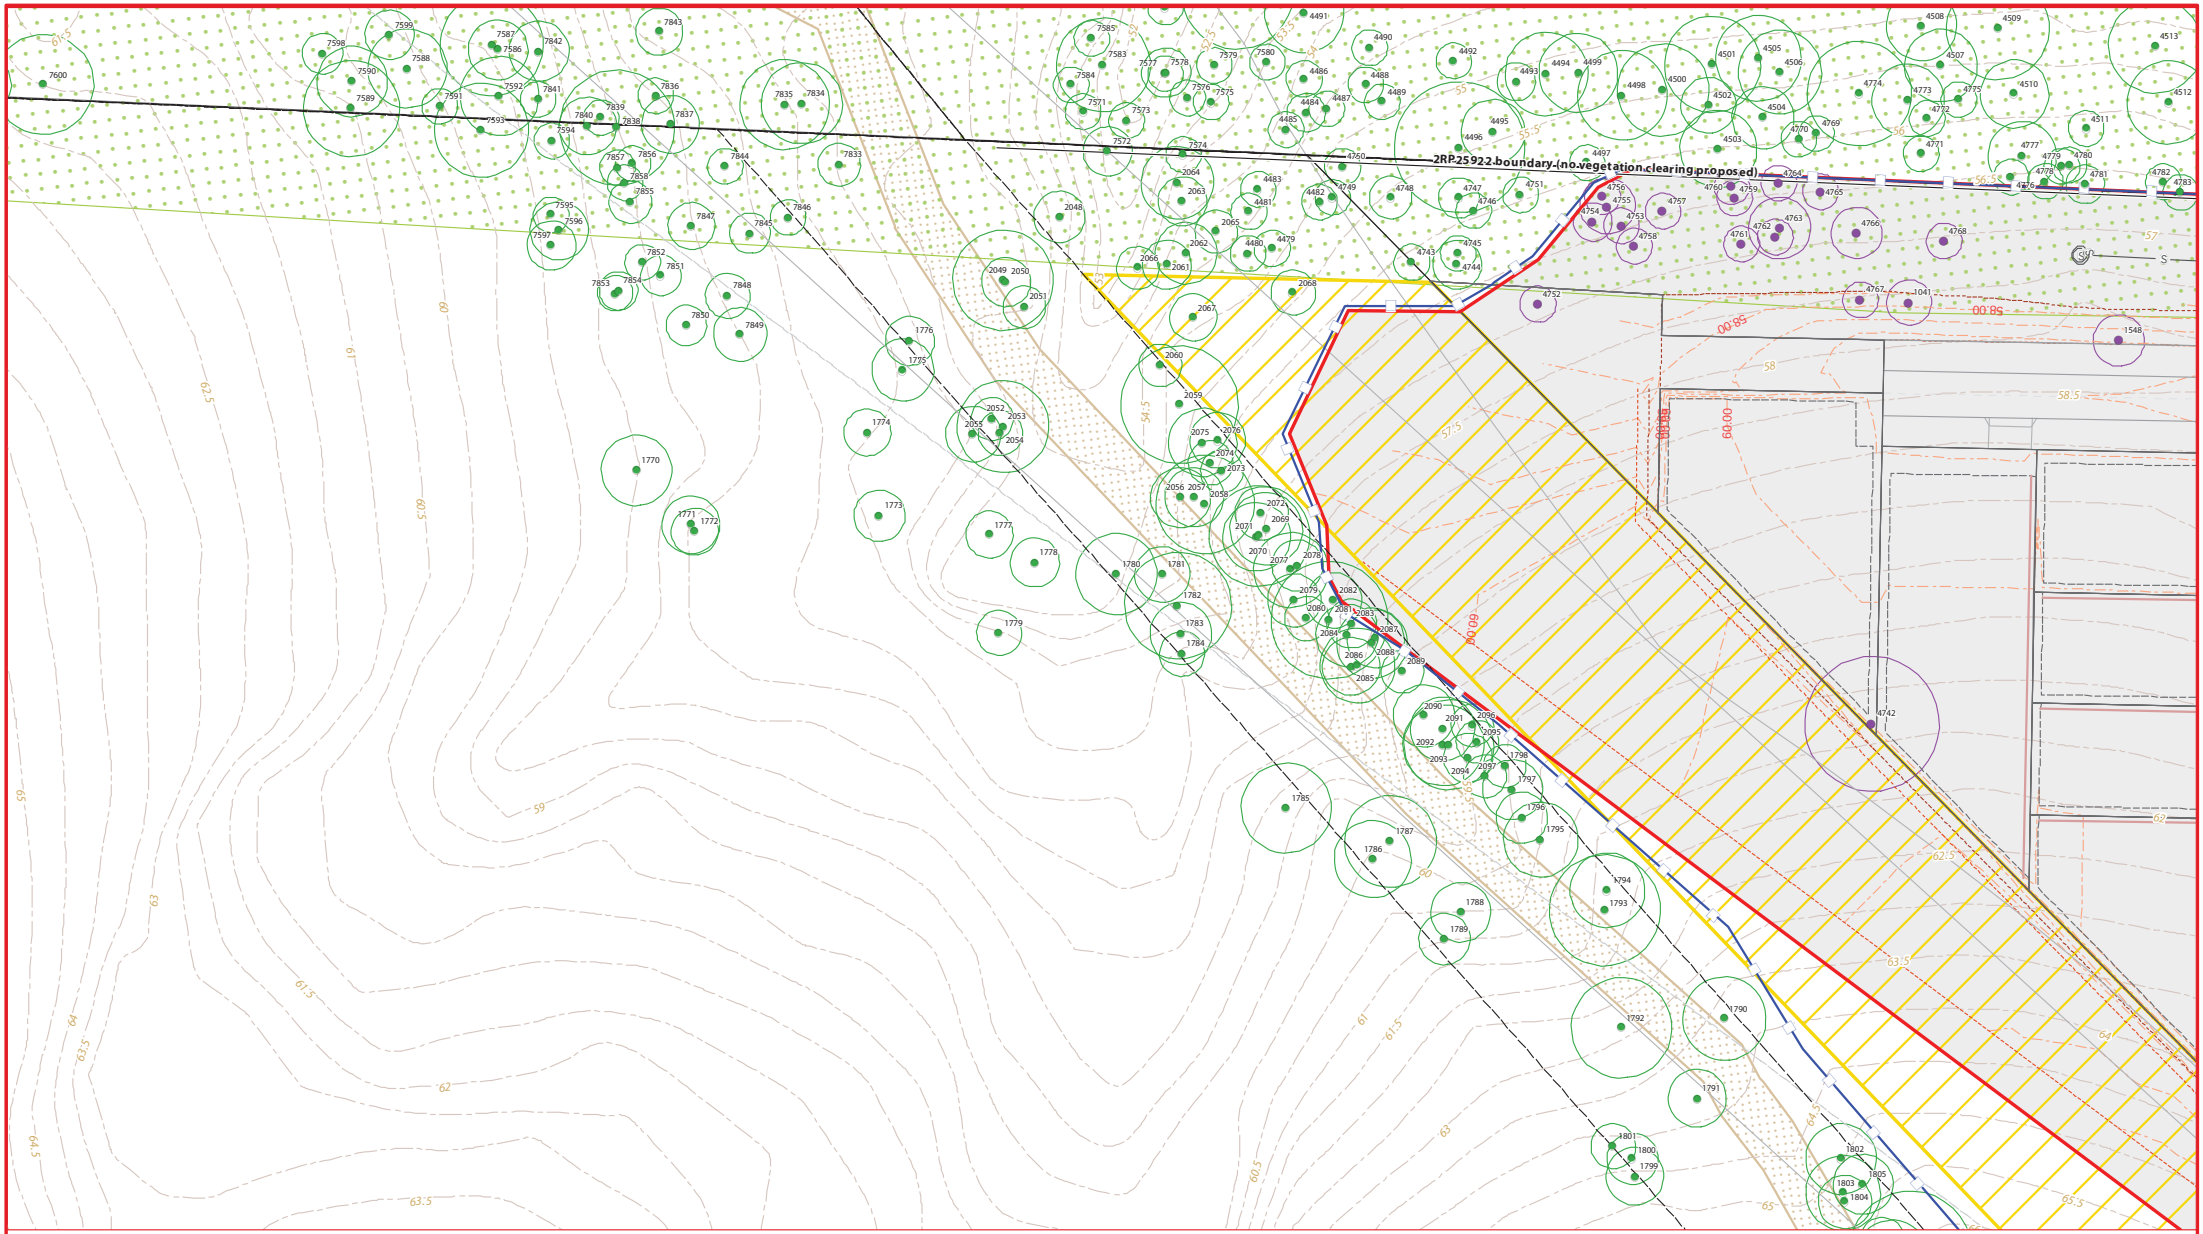

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 04

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 04 BAL Stage 2 VMP E	

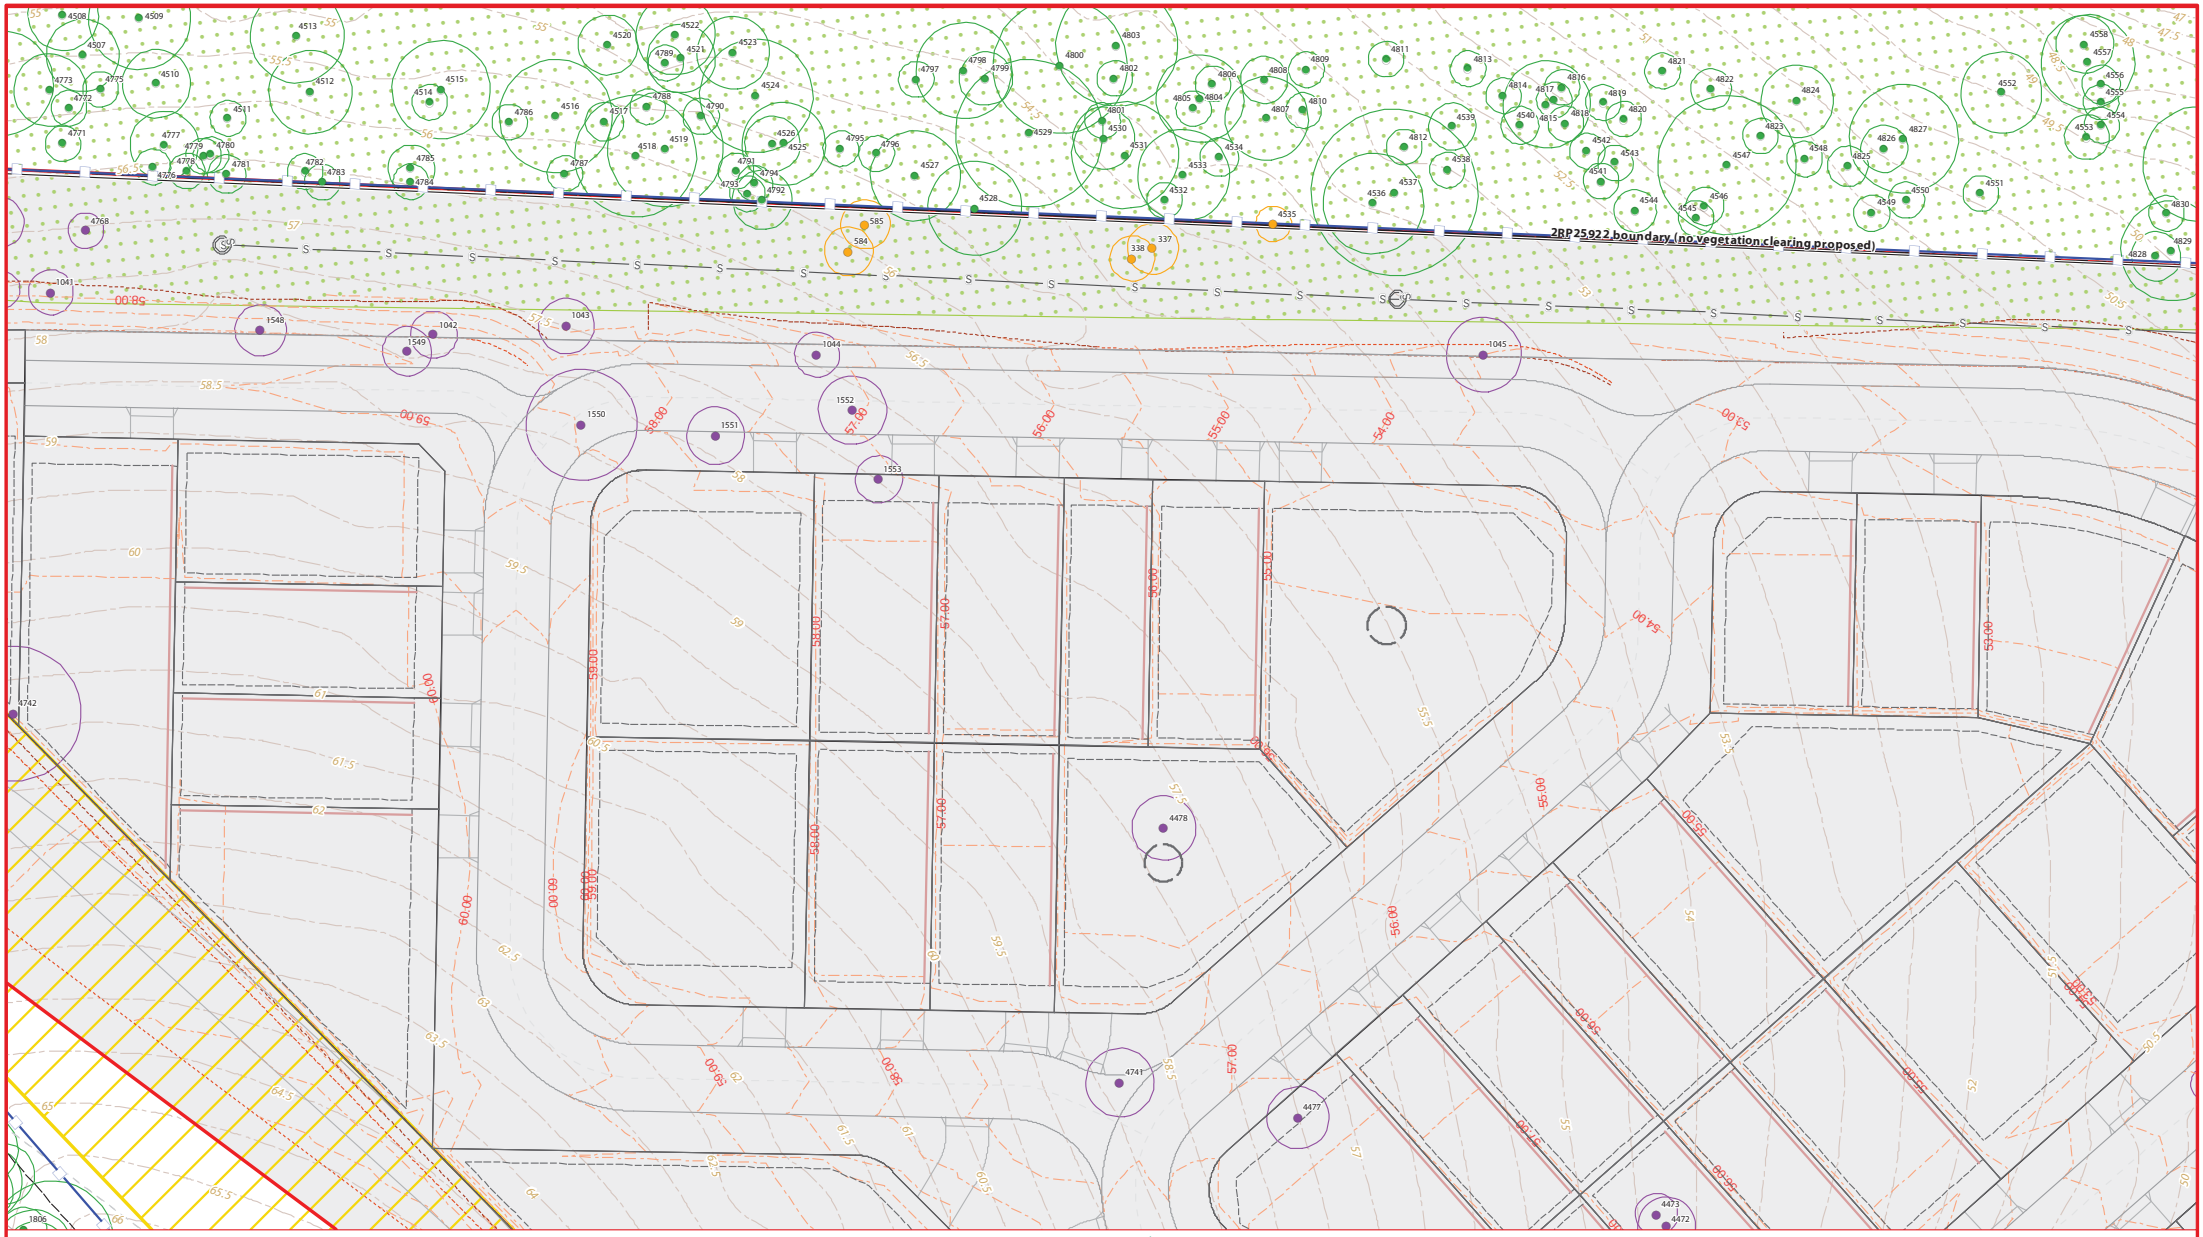

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 05

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 05 BAL Stage 2 VMP E

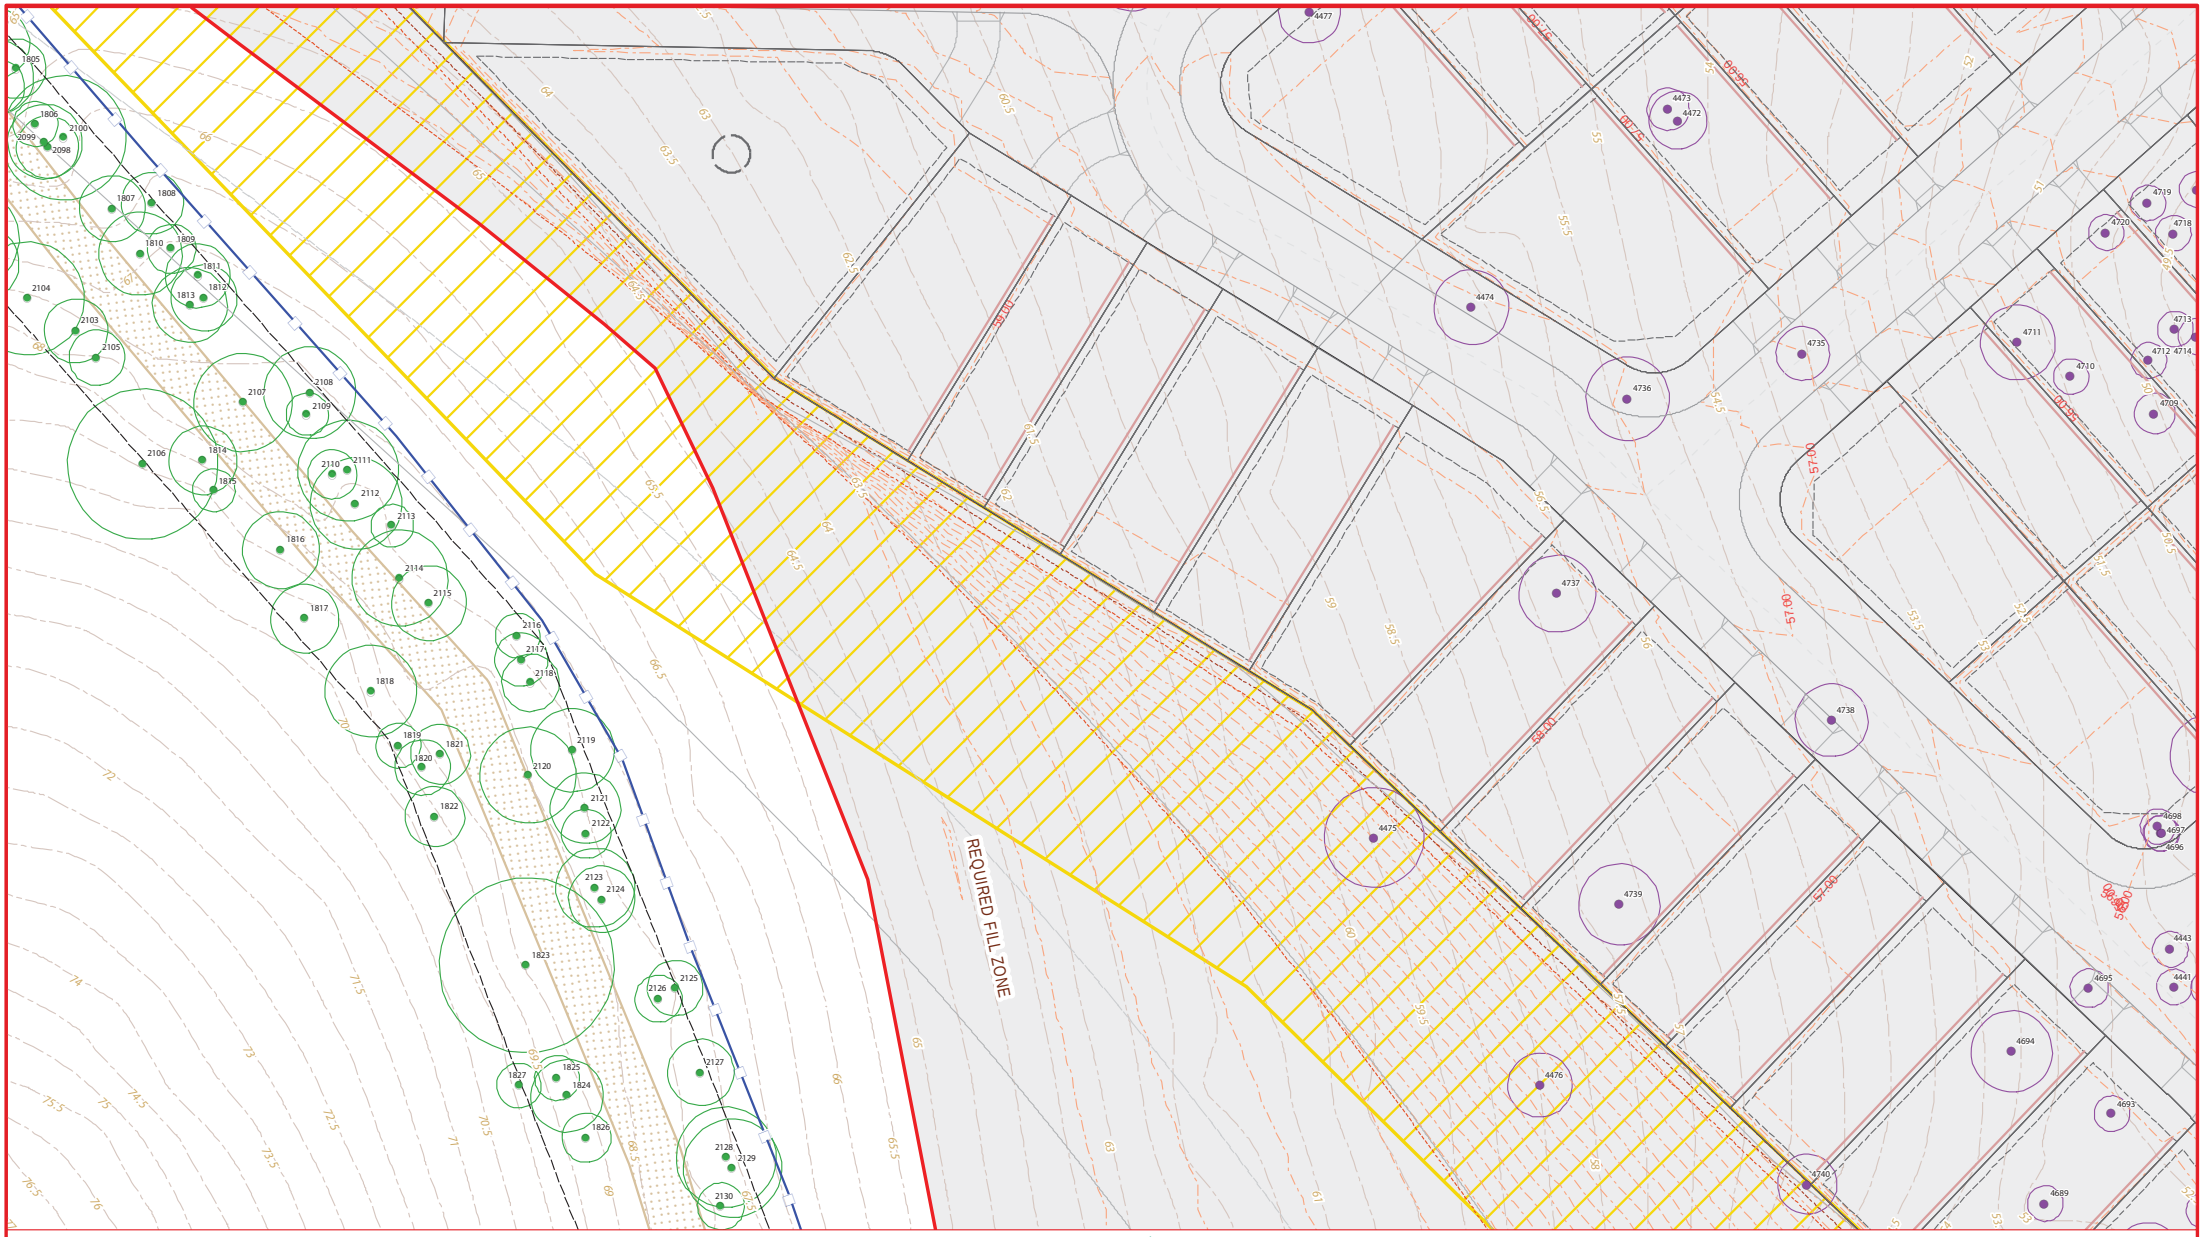

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 06

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 06 BAL Stage 2 VMP E	

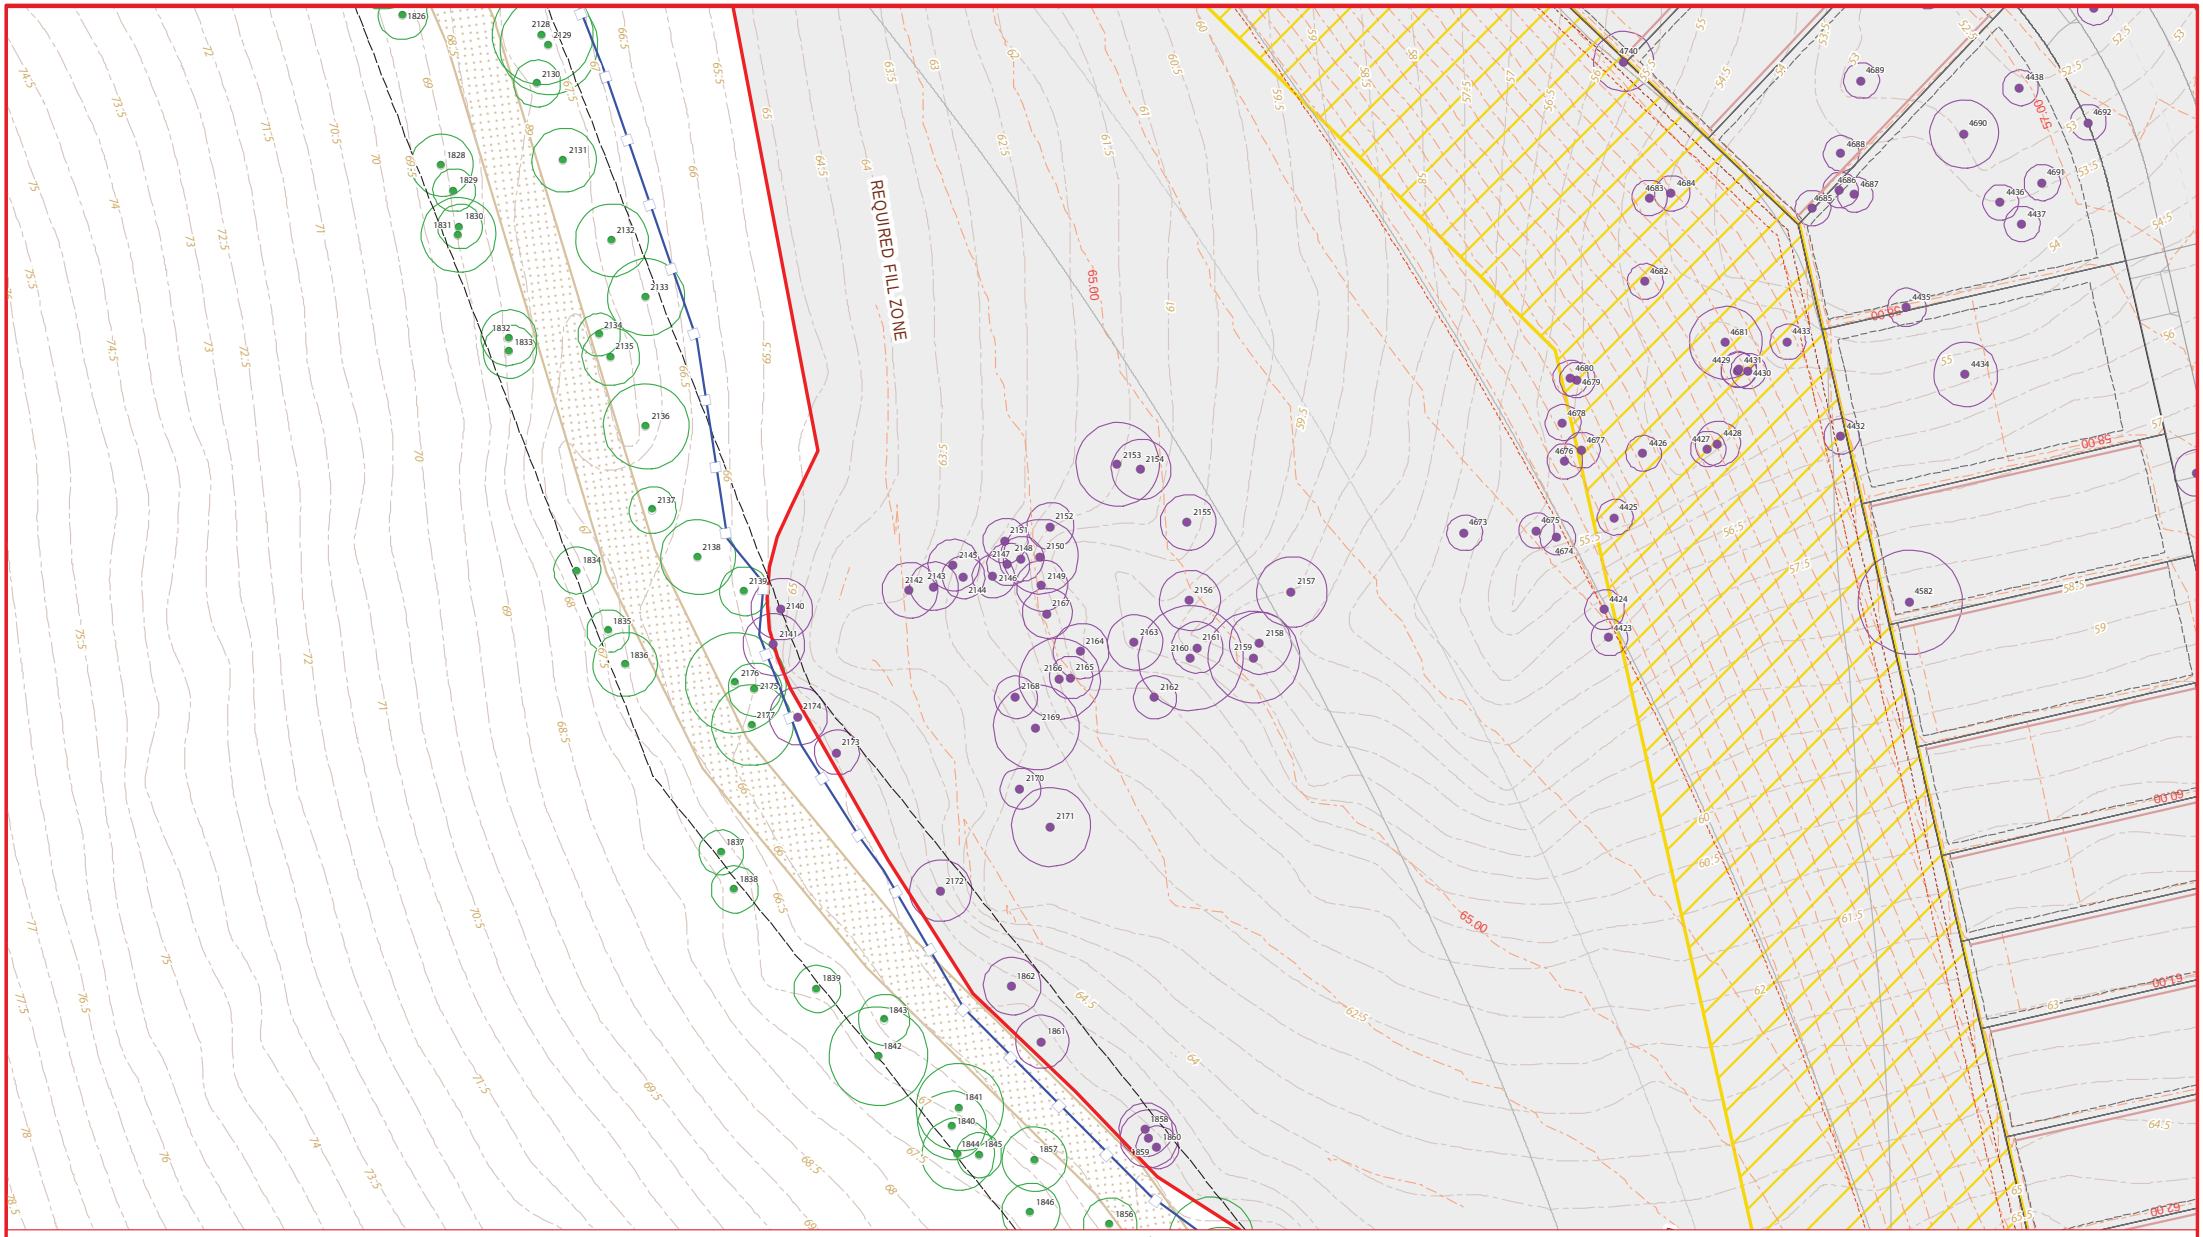

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 07

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 07 BAL Stage 2 VMP E

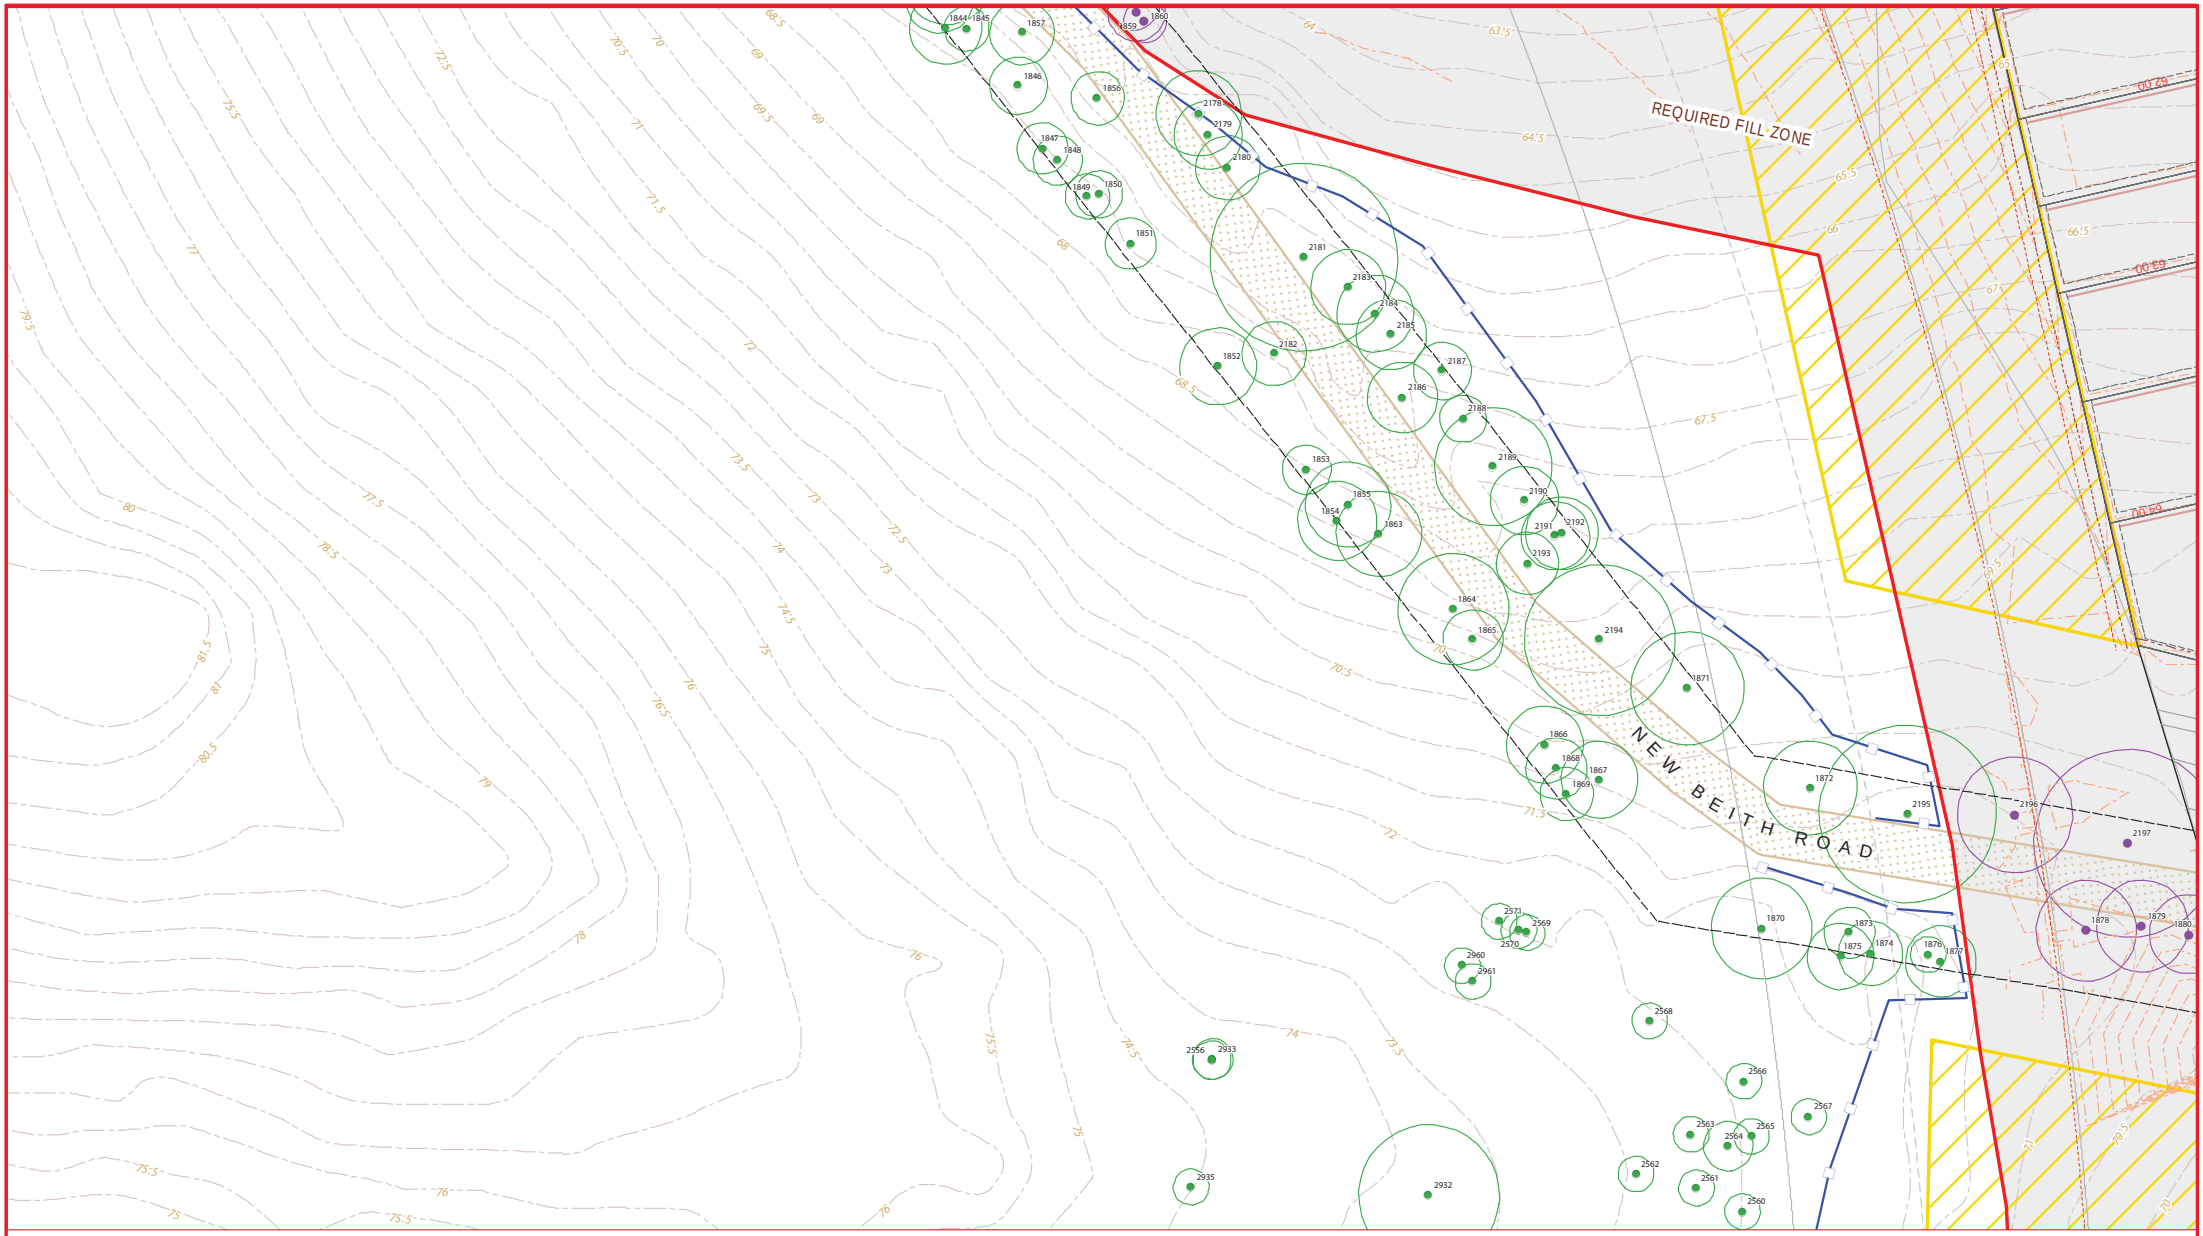

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 08

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC
DRAWING No.:	8047 E 08 BAL Stage 2 VMP E		

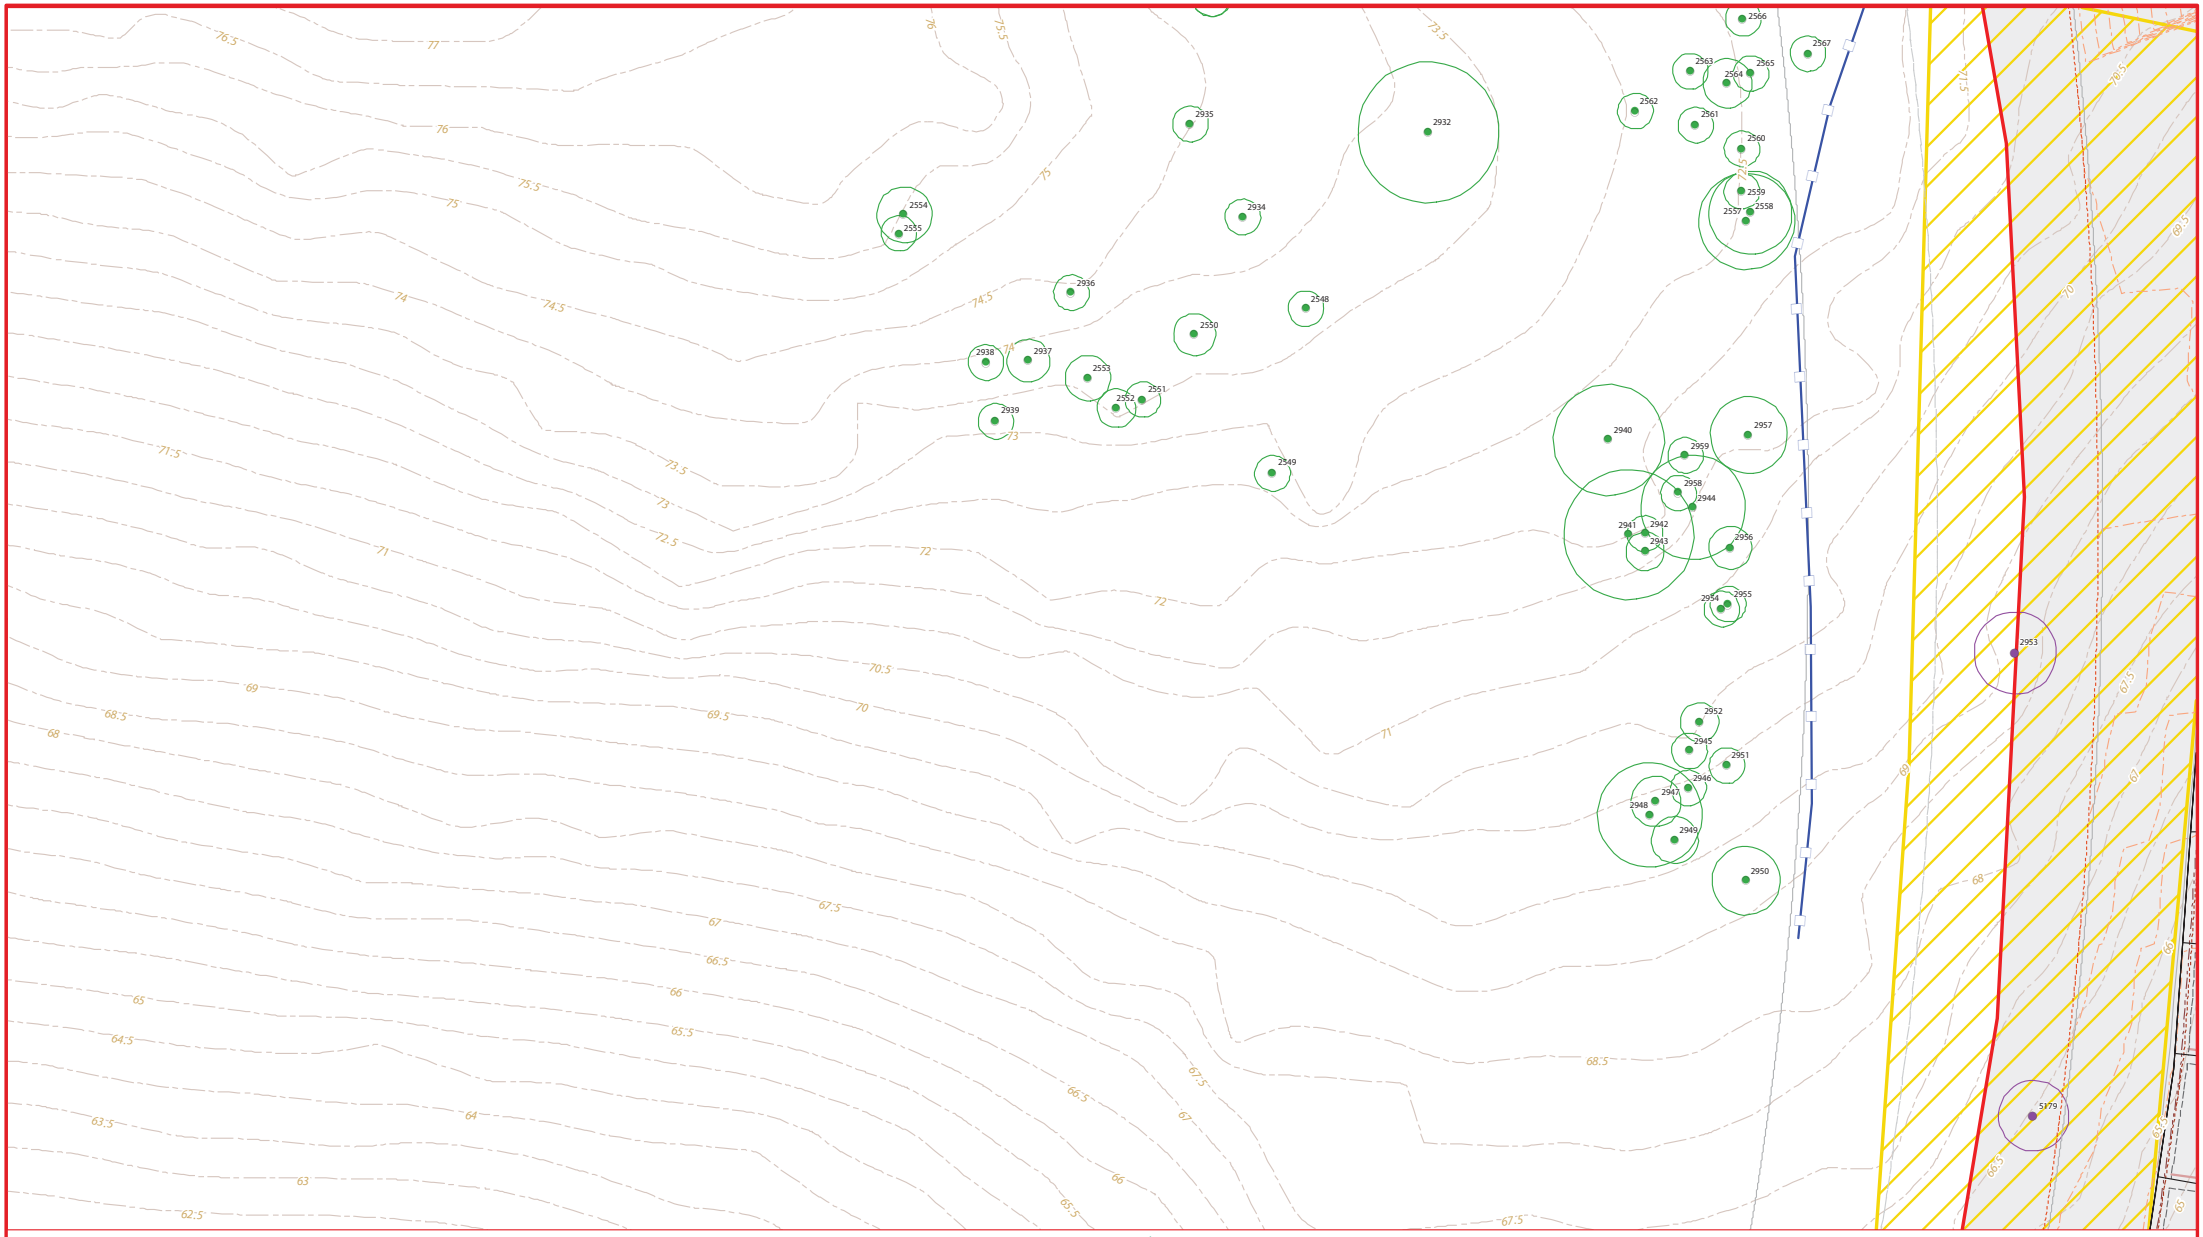

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 09

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC
DRAWING No.:	8047 E 09 BAL Stage 2 VMP E		

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 10

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 10 BAL Stage 2 VMP E

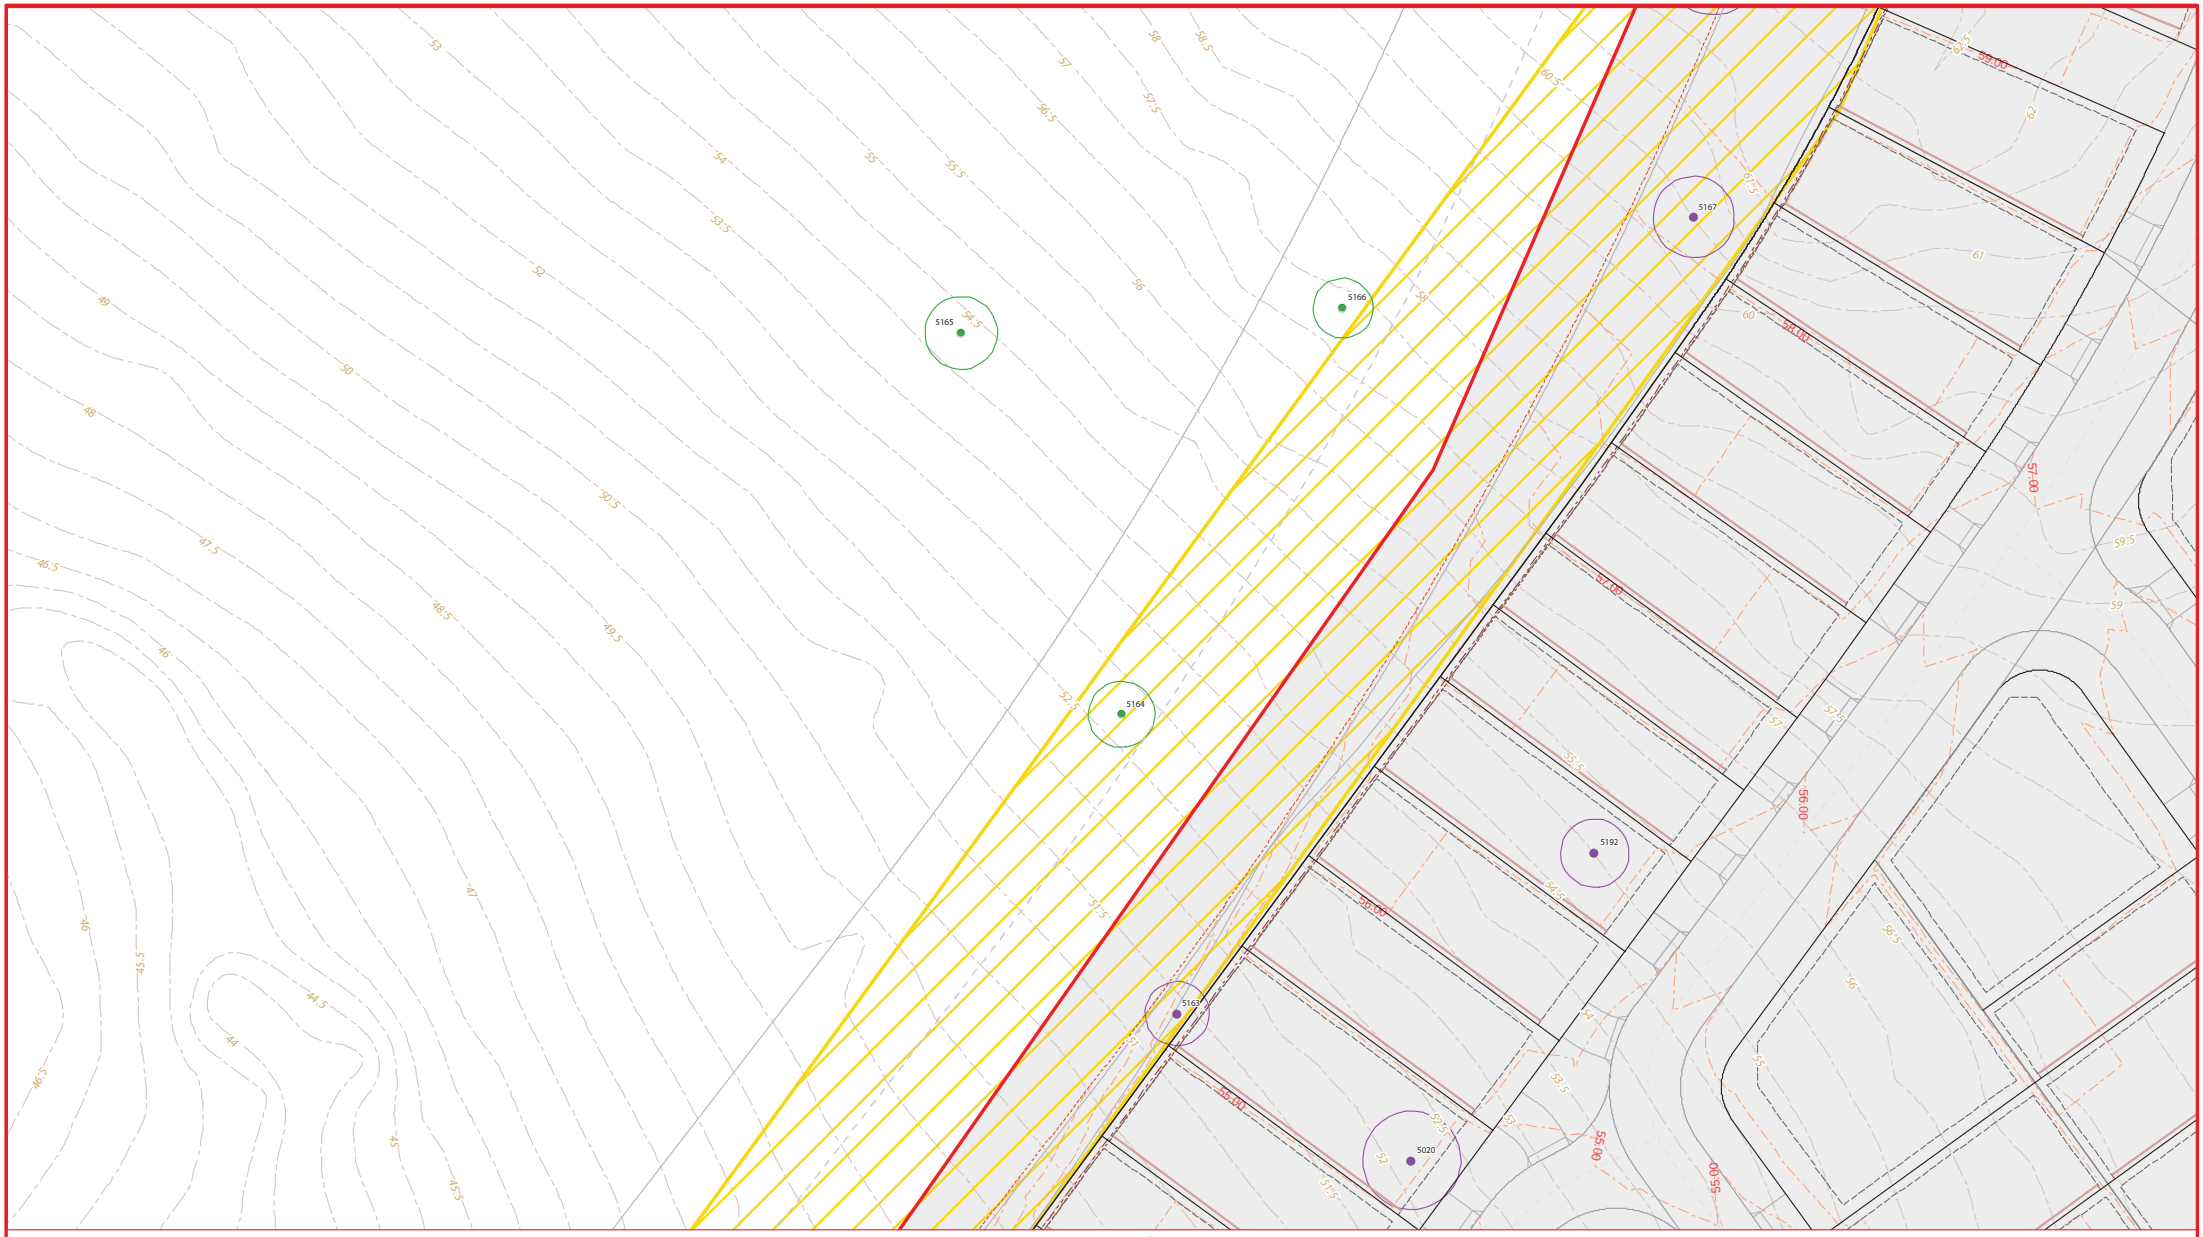

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 11

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 11 BAL Stage 2 VMP E

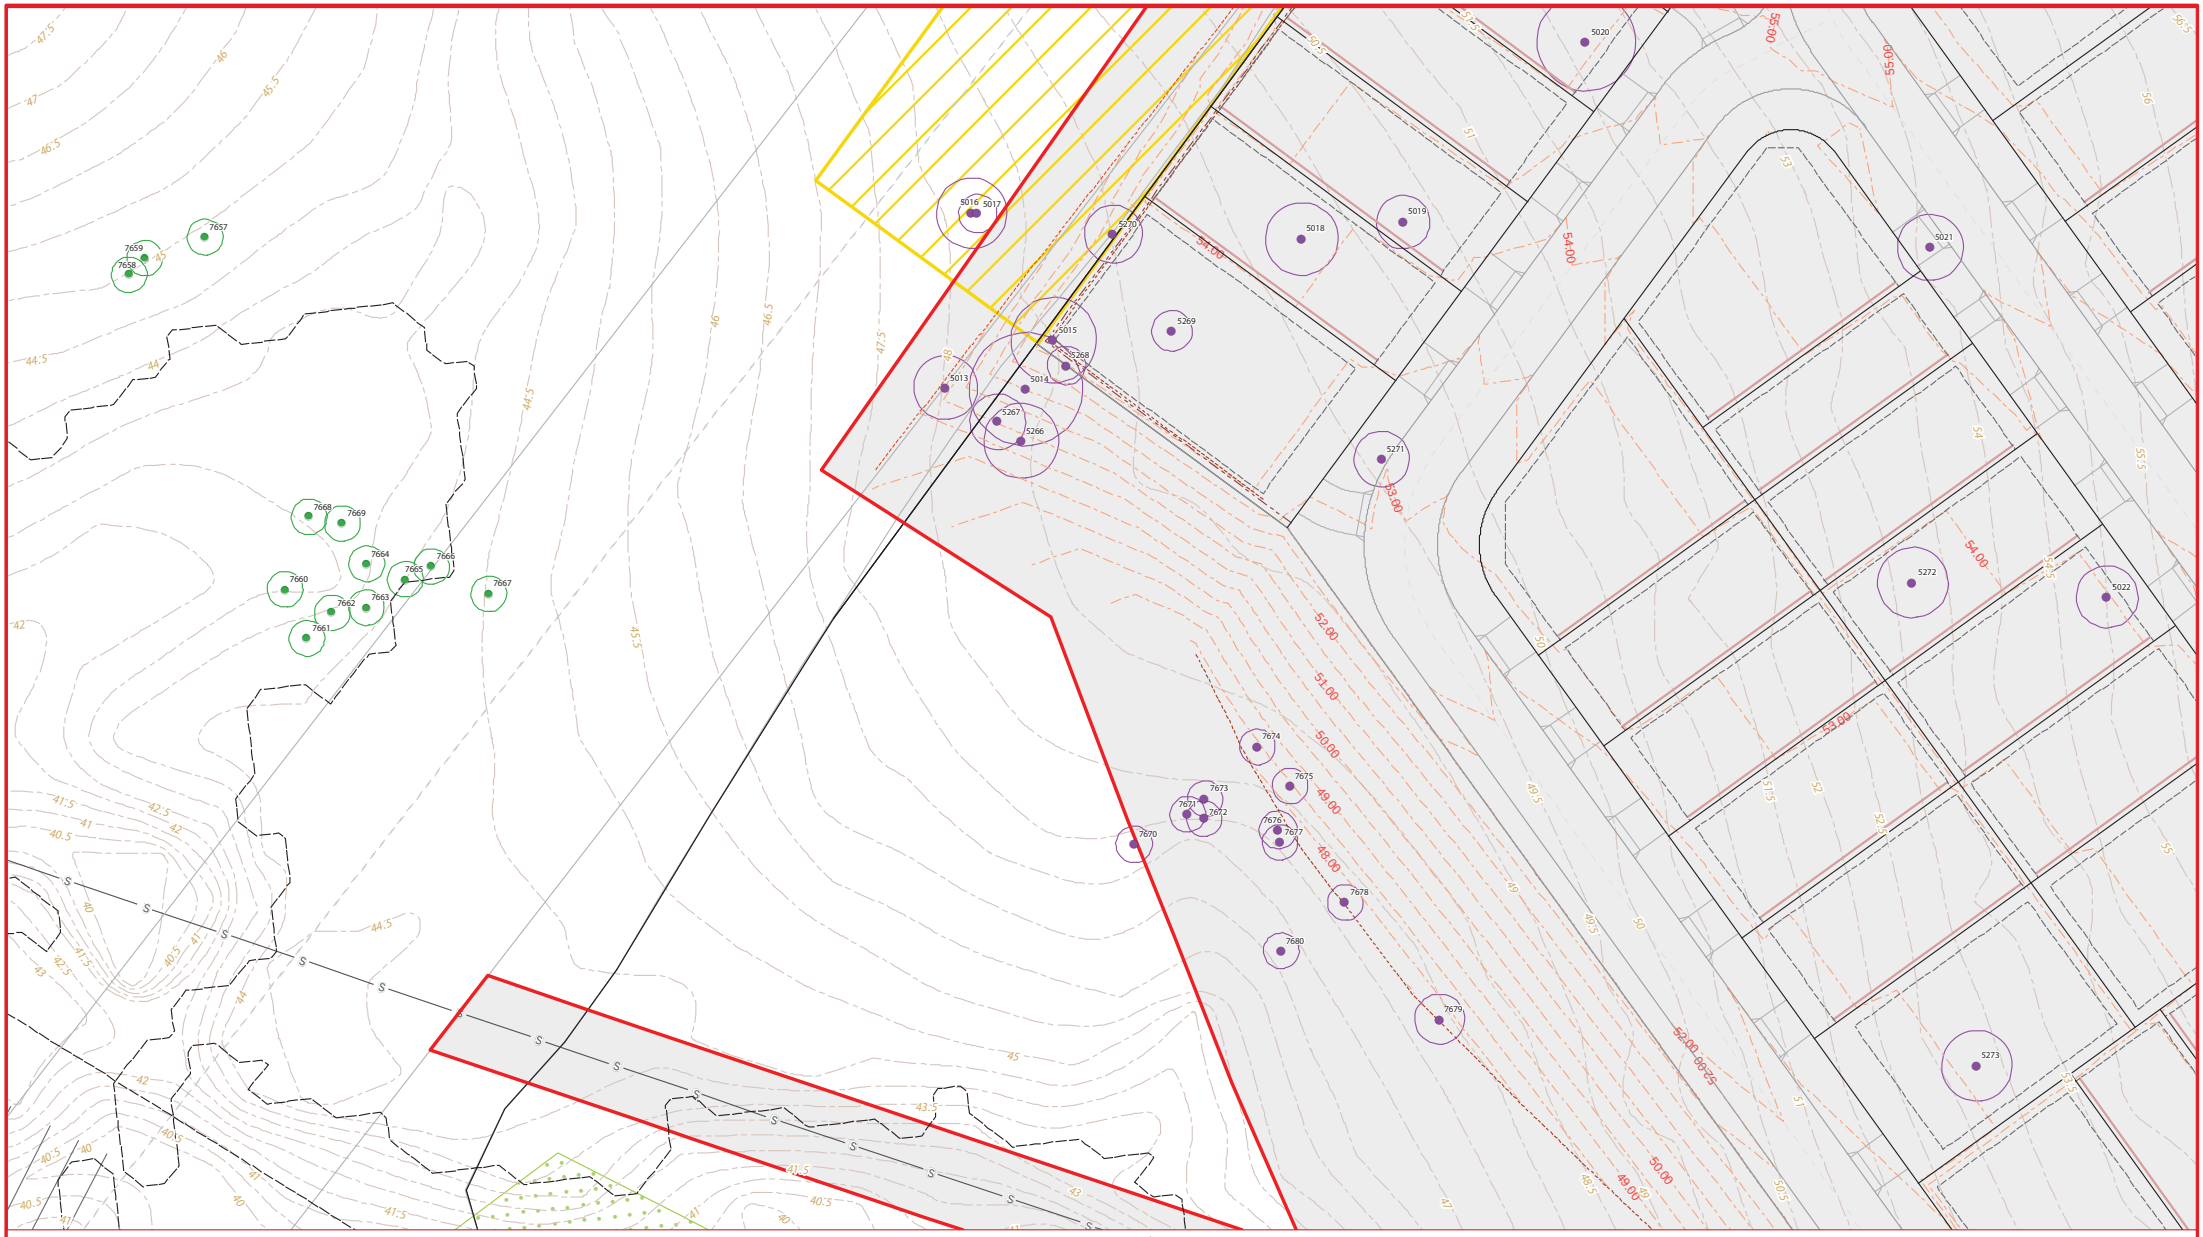

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 12

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 12 BAL Stage 2 VMP E	

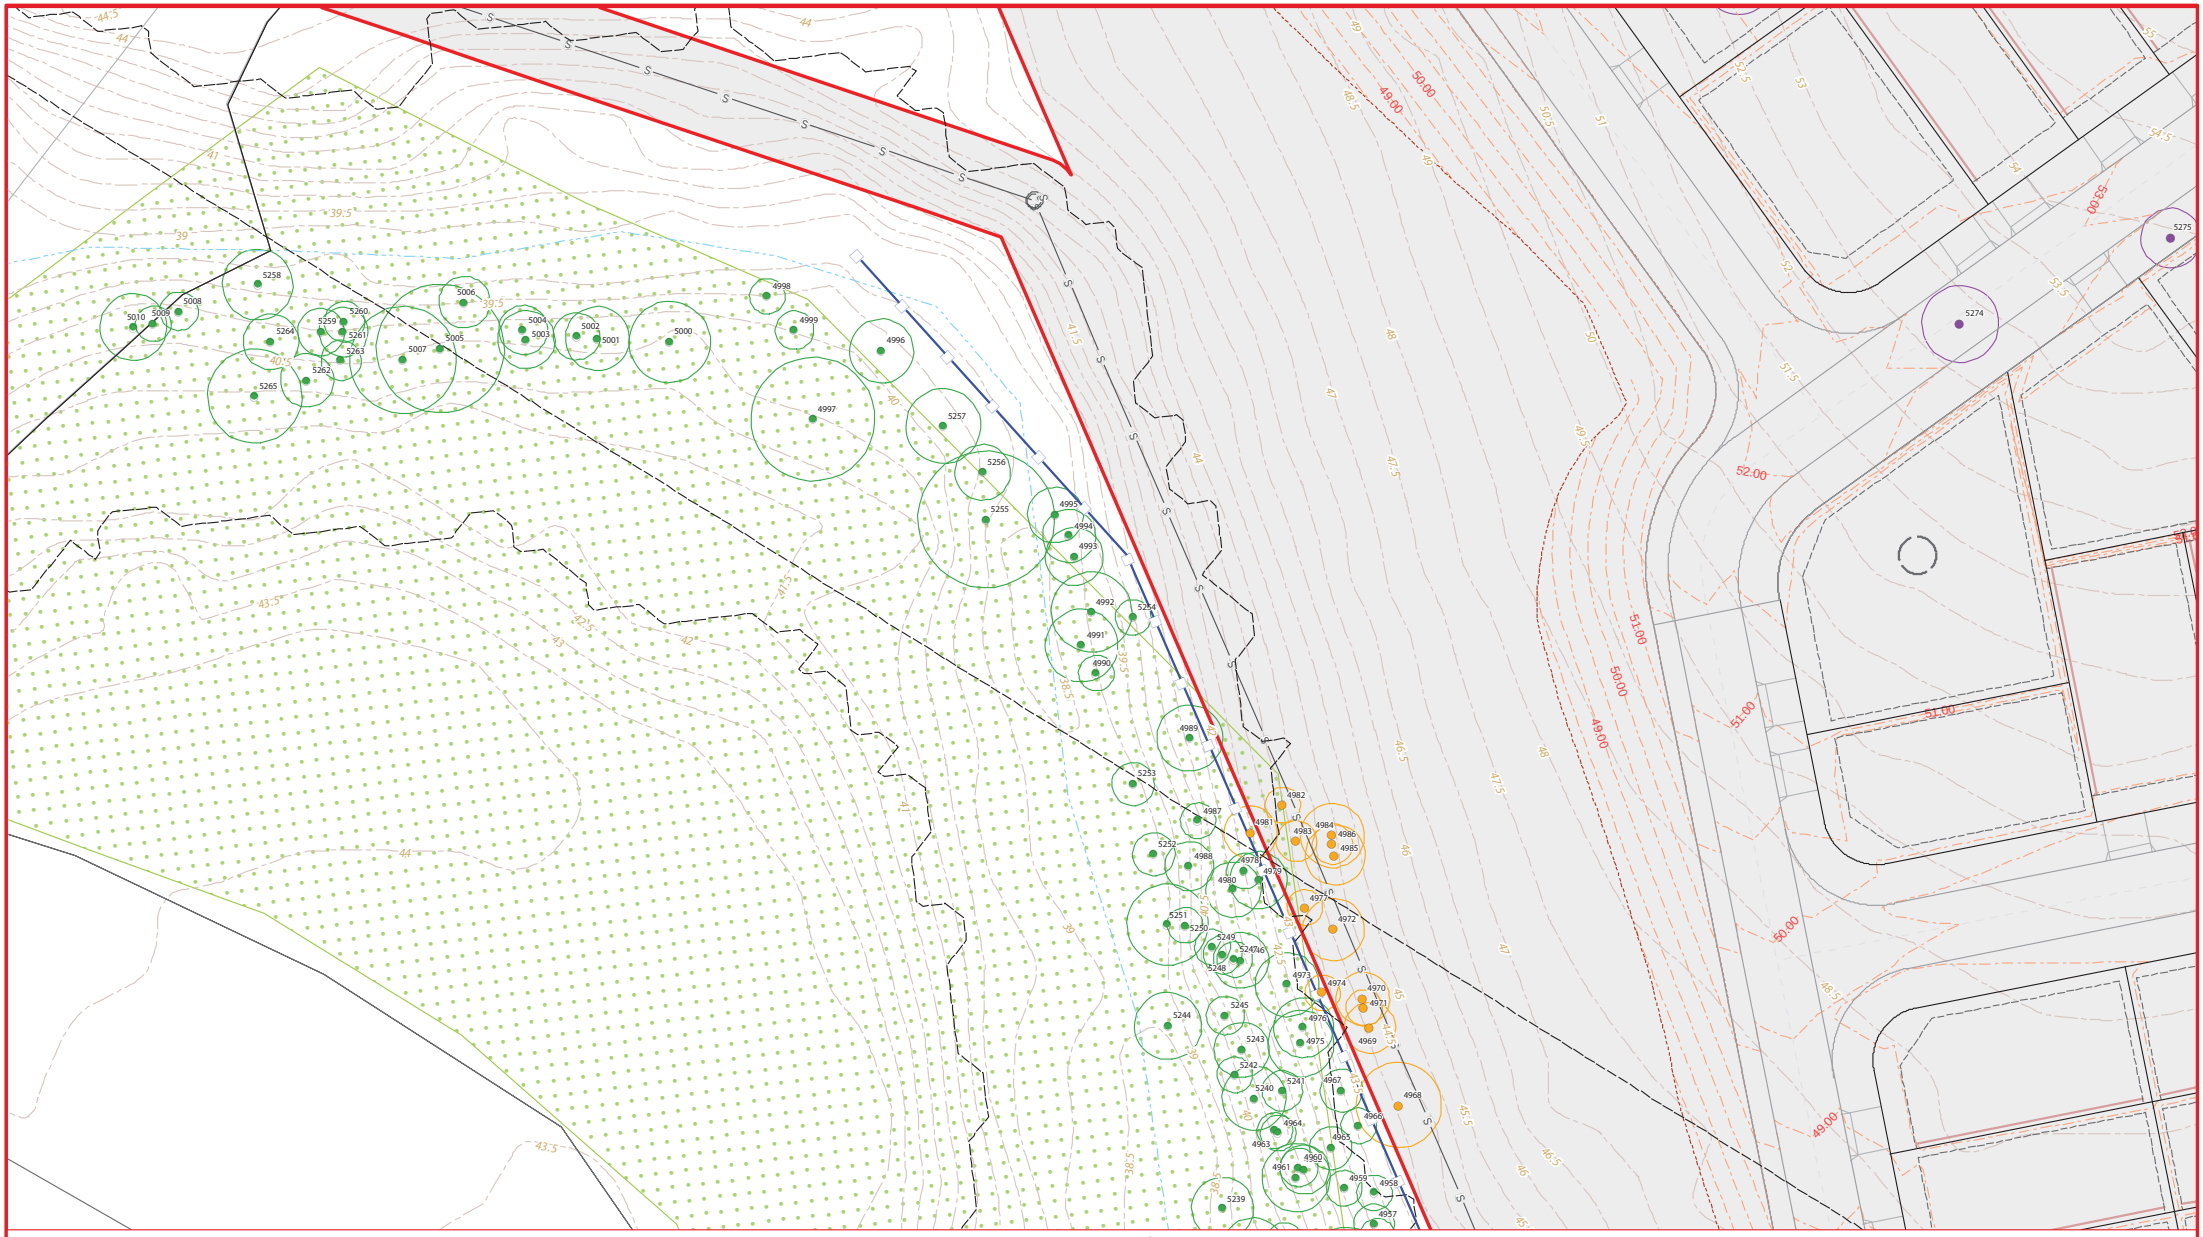

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 13

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 13 BAL Stage 2 VMP E	

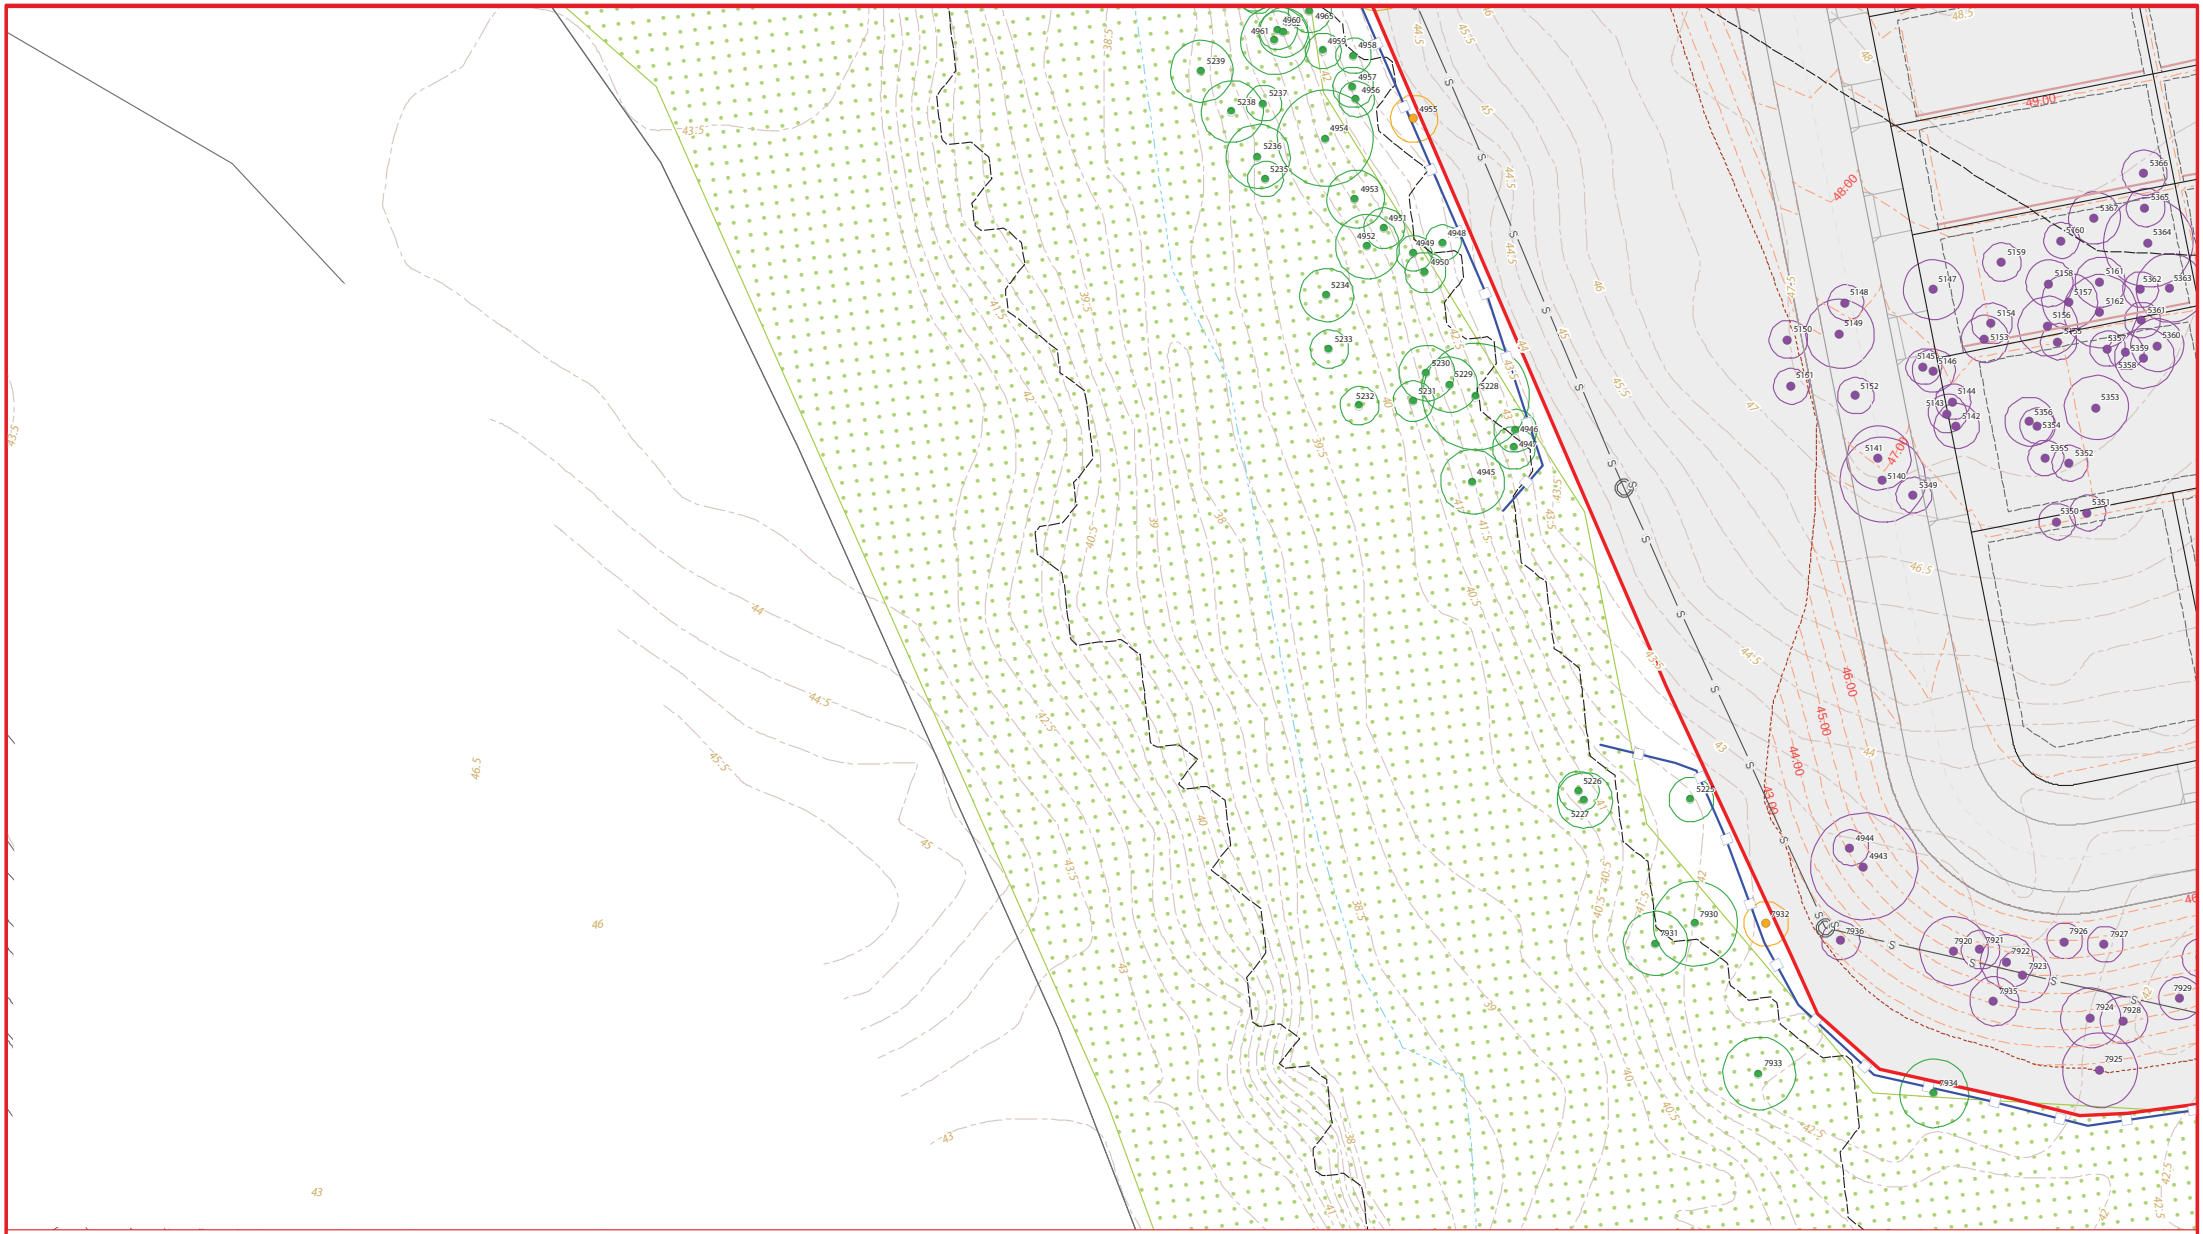

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 14

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 14 BAL Stage 2 VMP E	

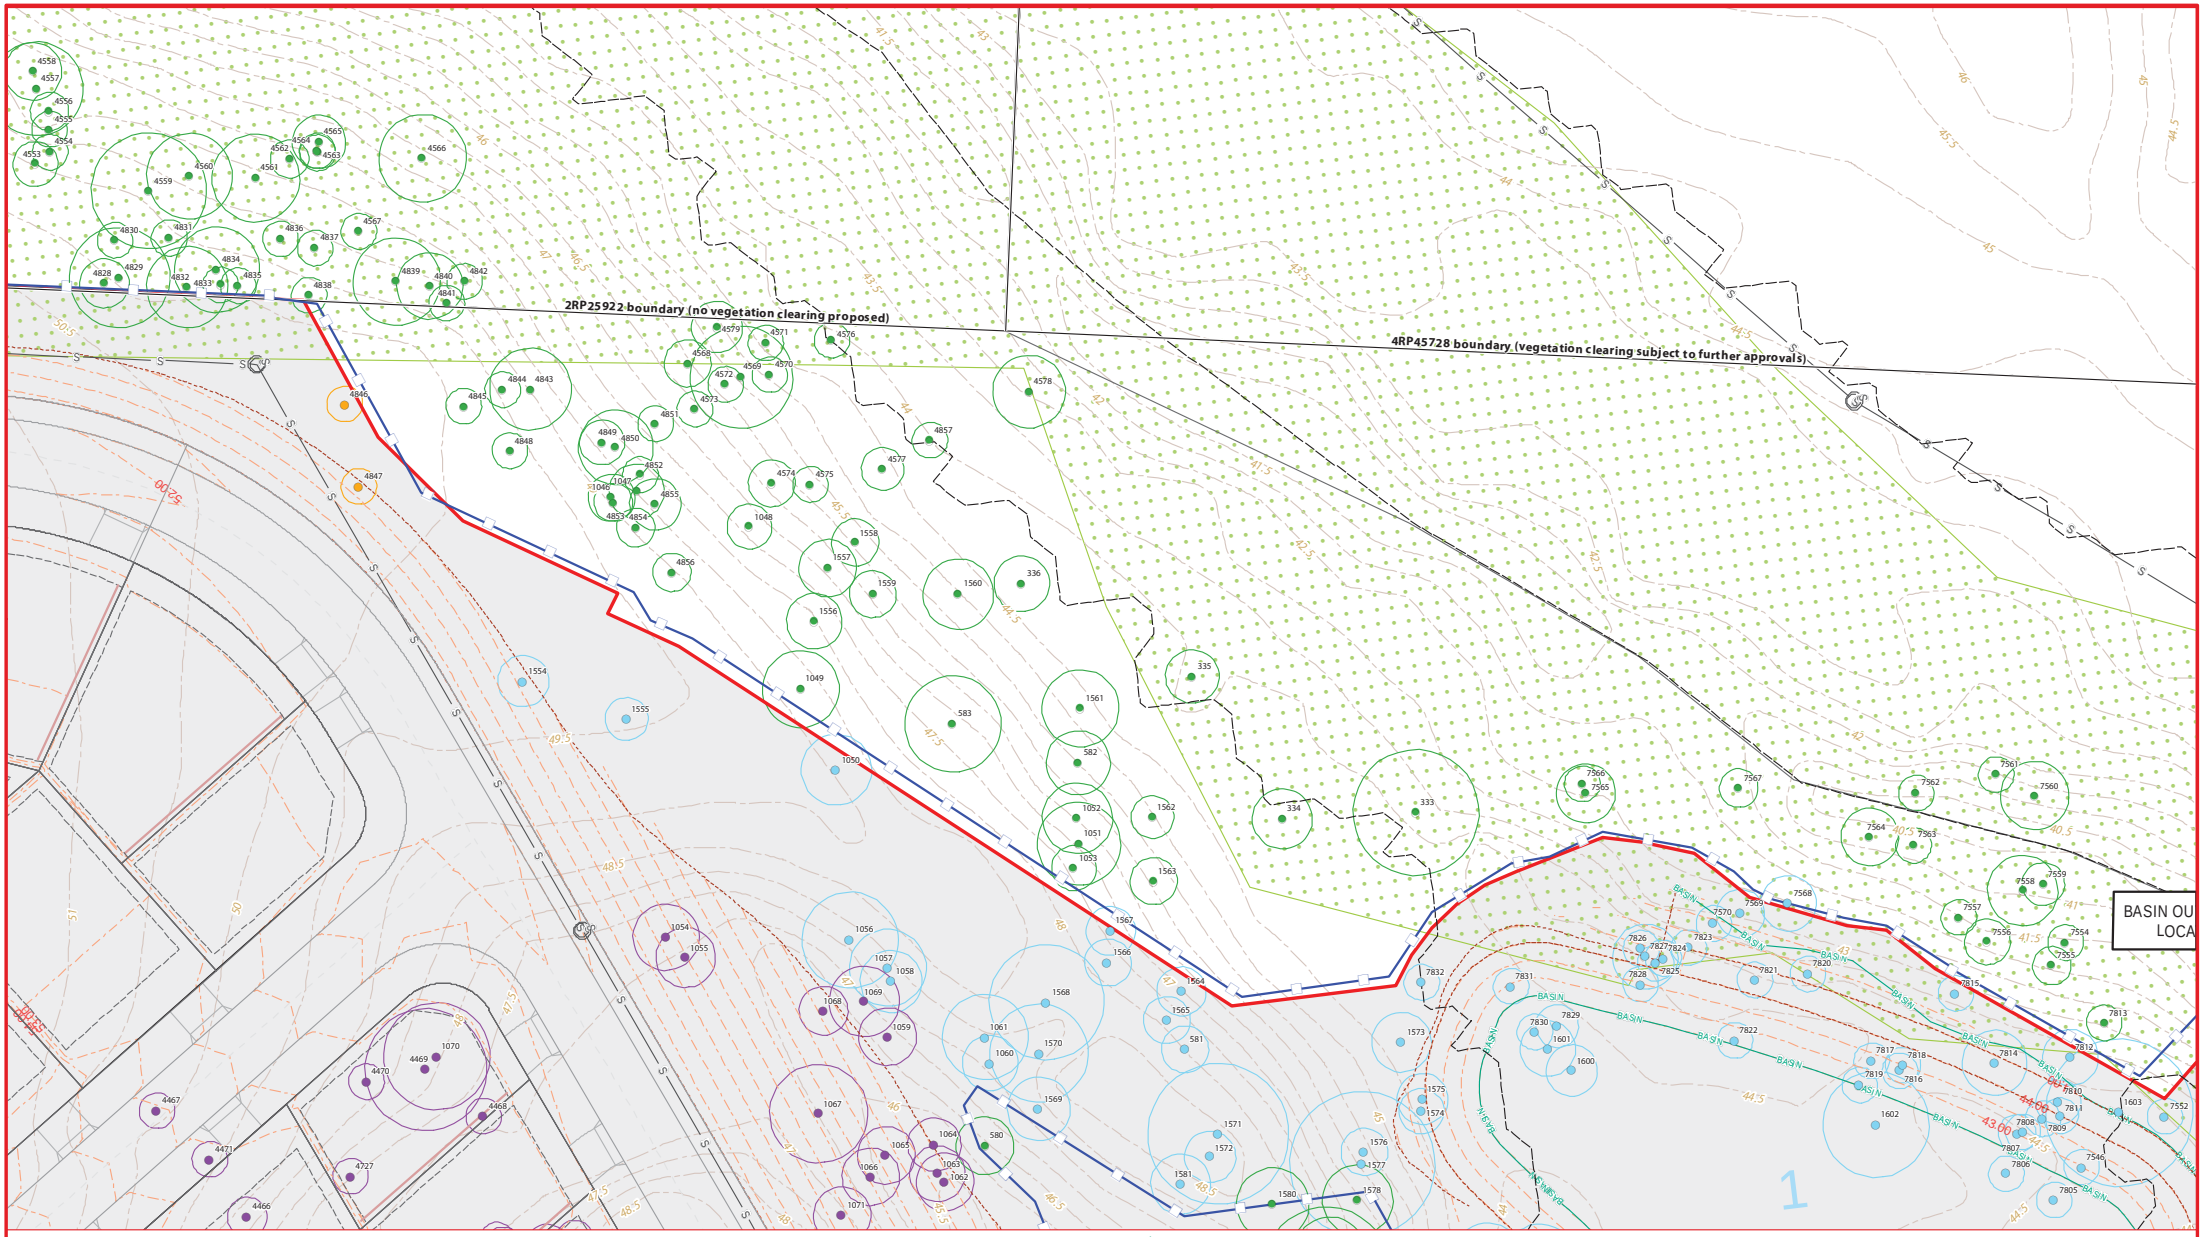

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 15

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE S. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 15 BAL Stage 2 VMP E	

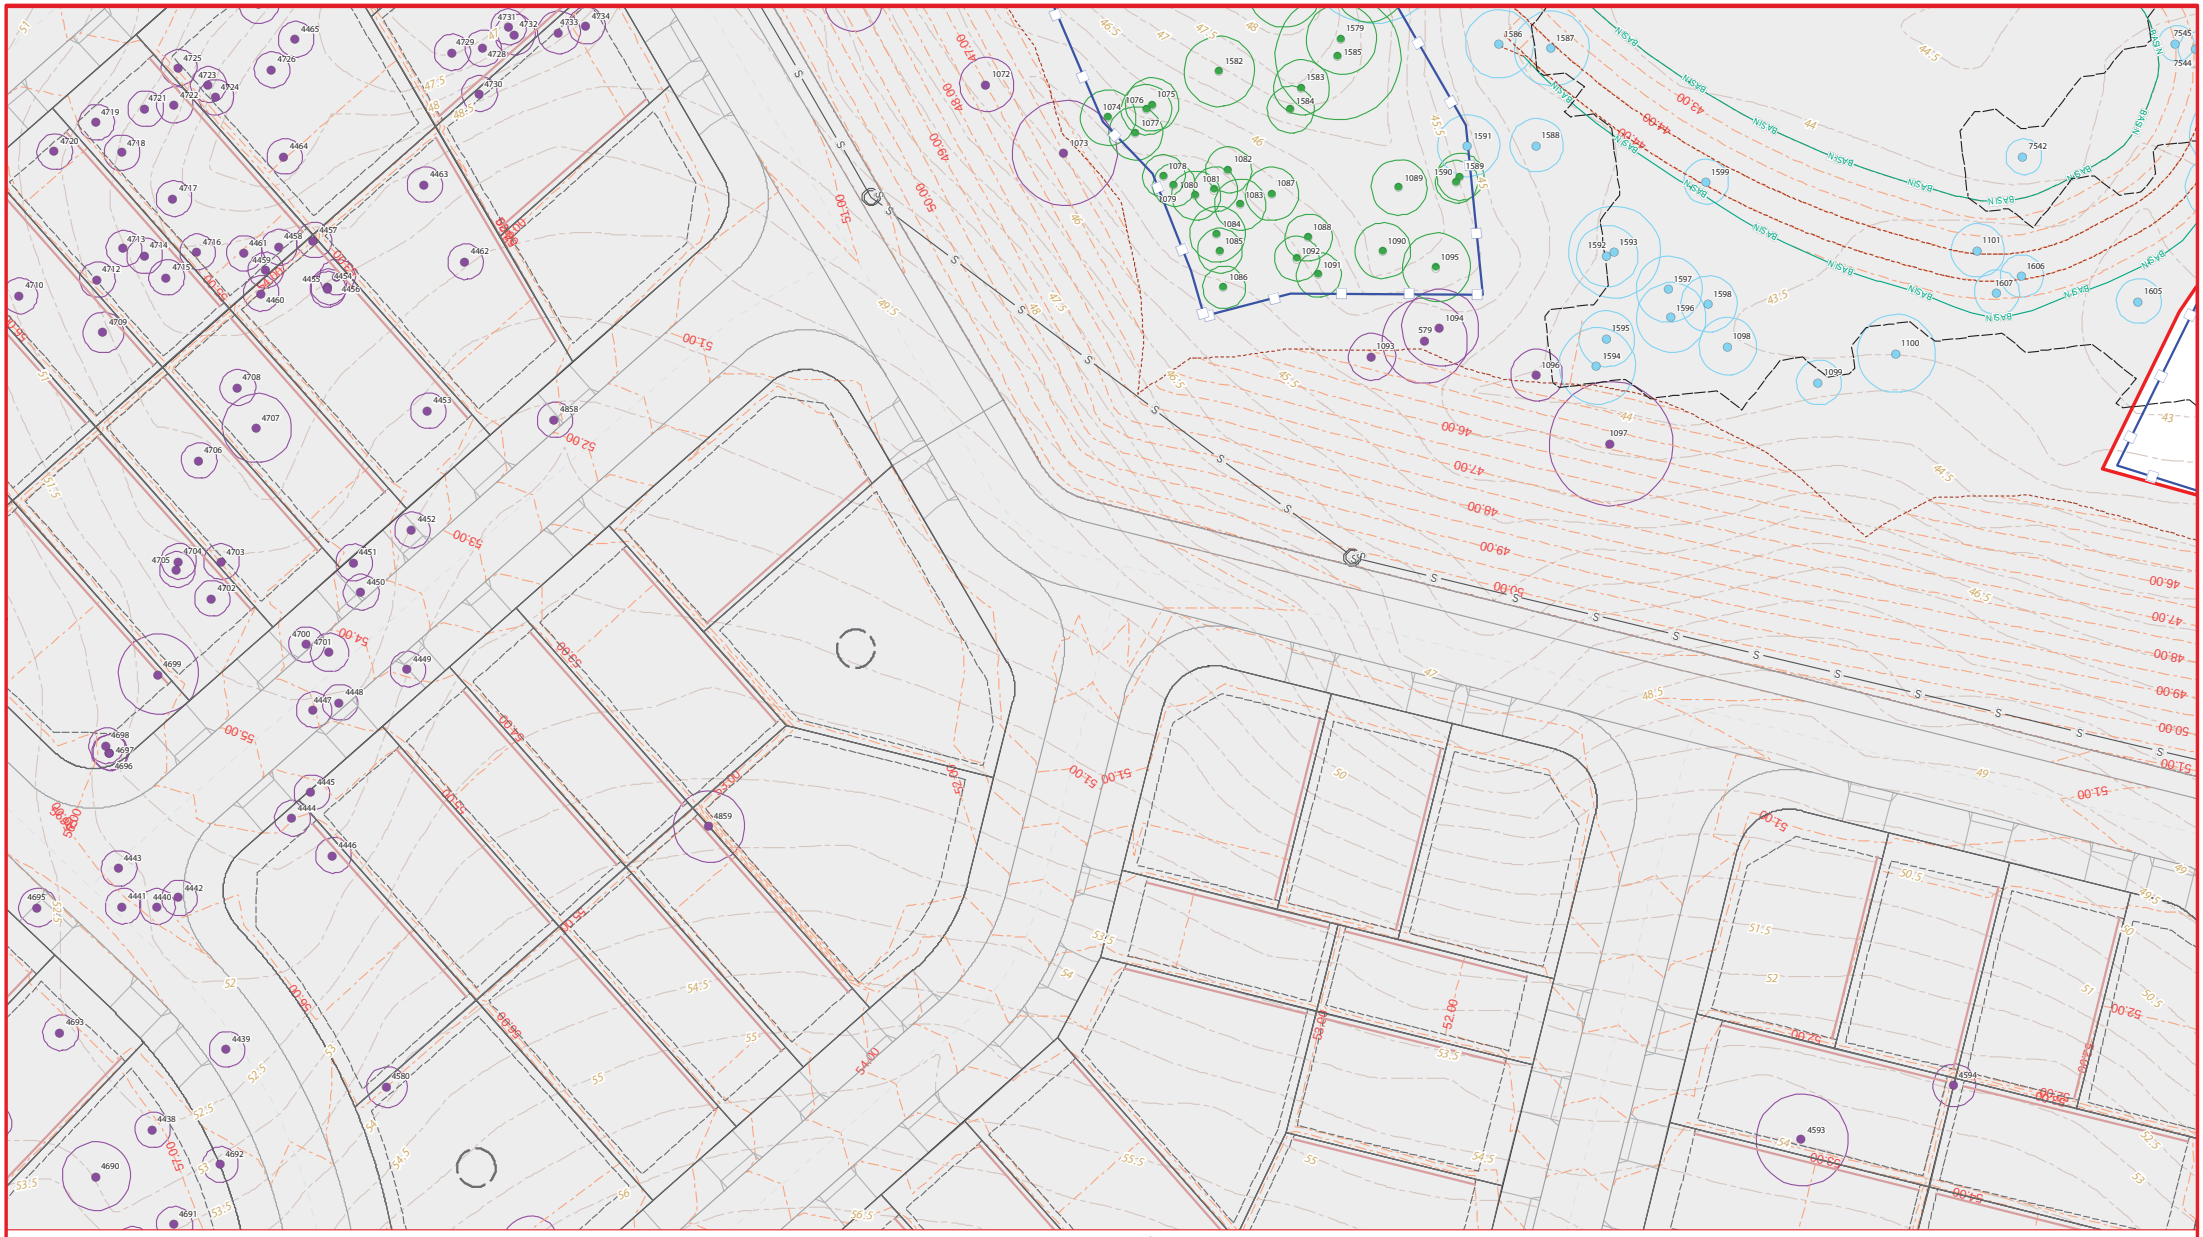

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 16

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 16 BAL Stage 2 VMP E	

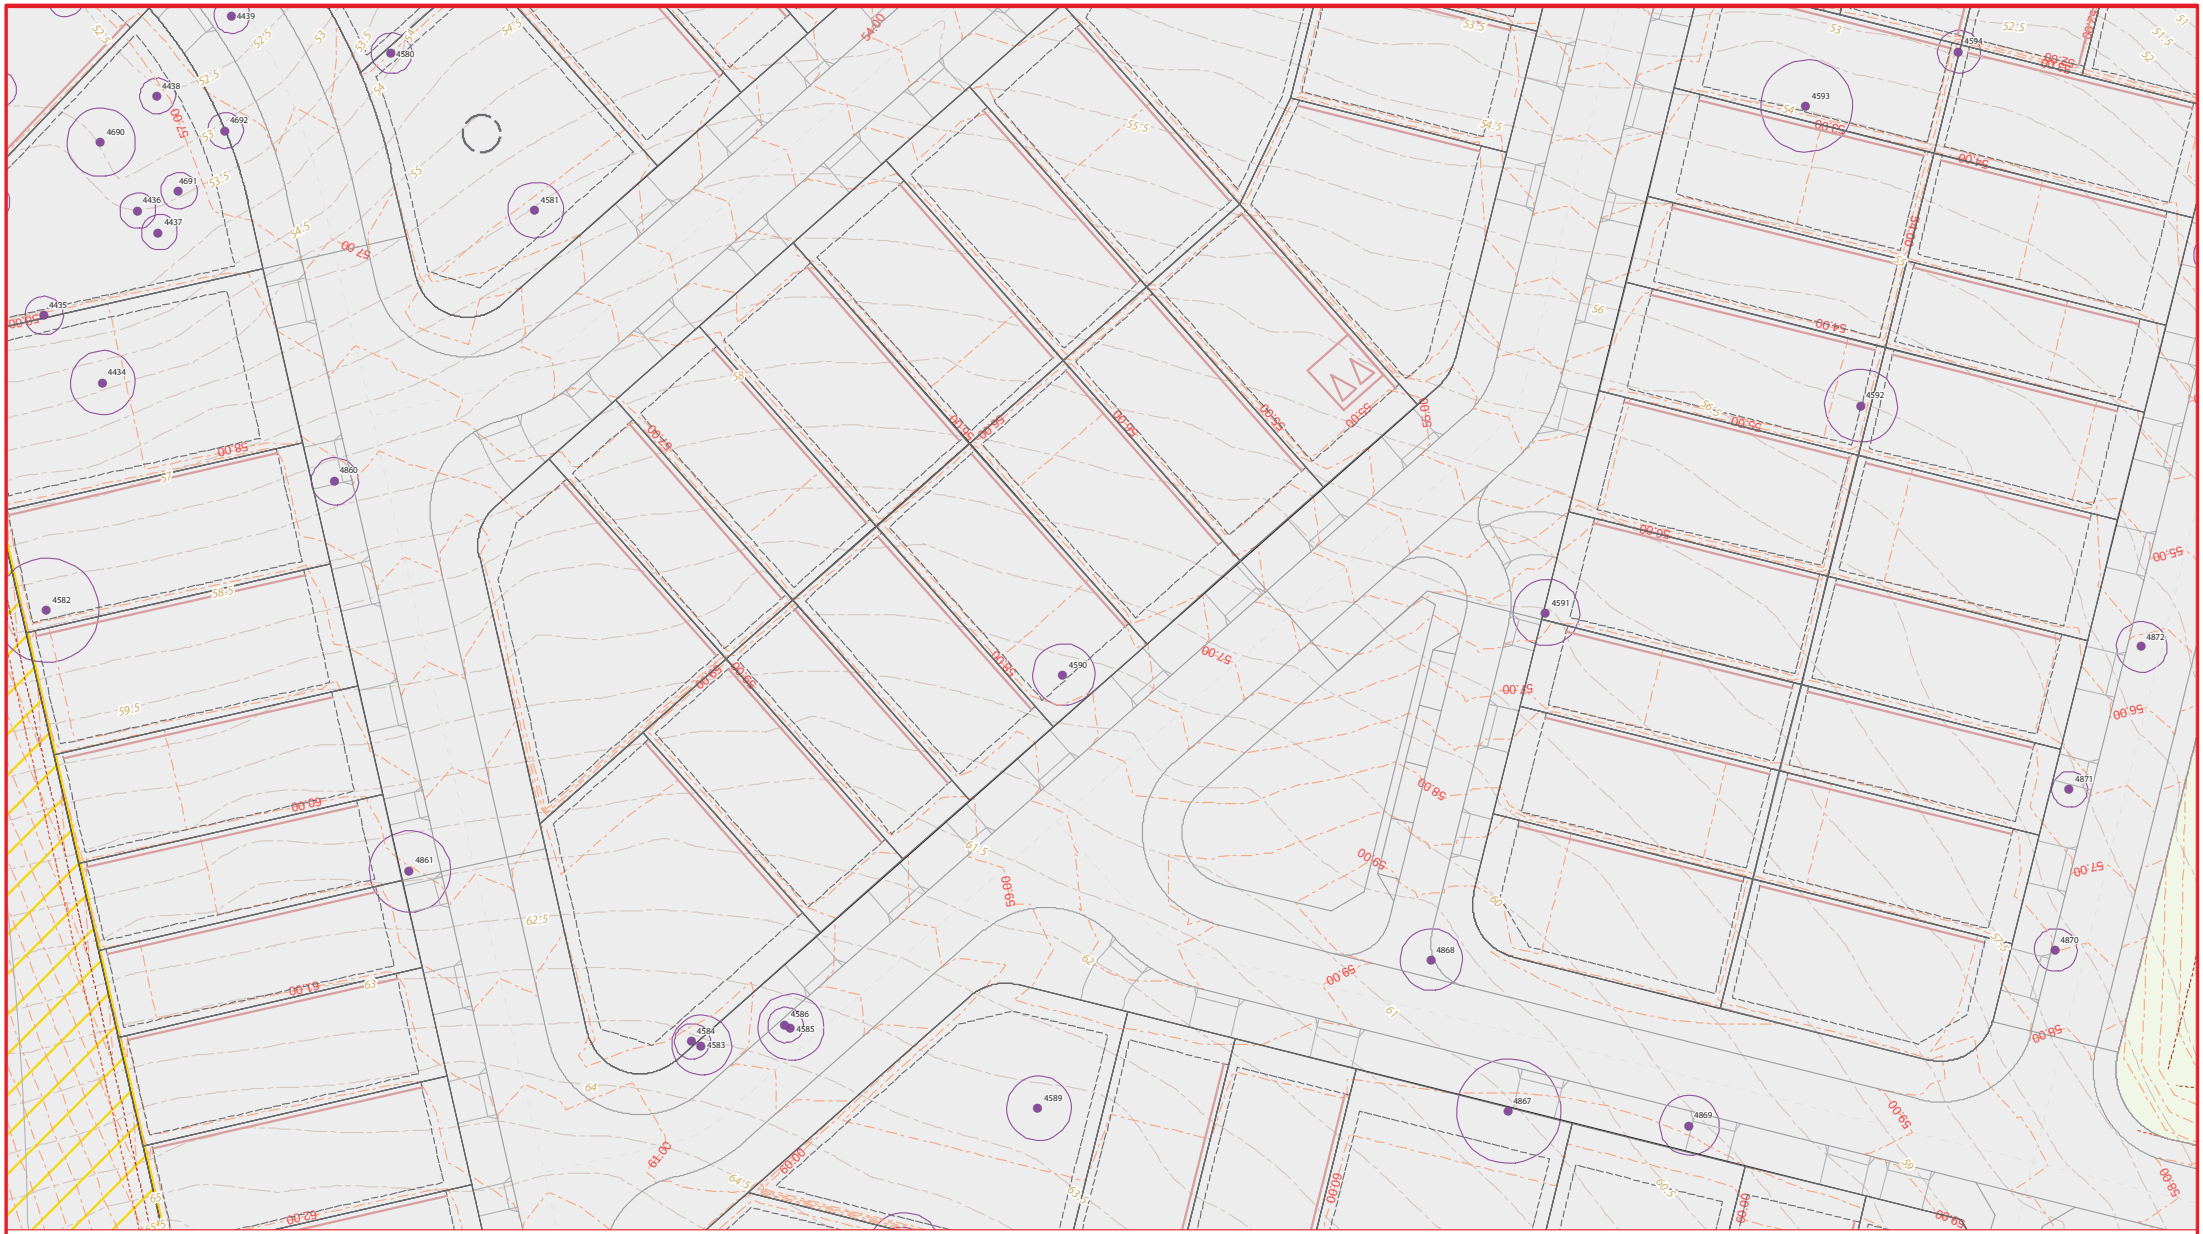

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 17

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 17 BAL Stage 2 VMP E	

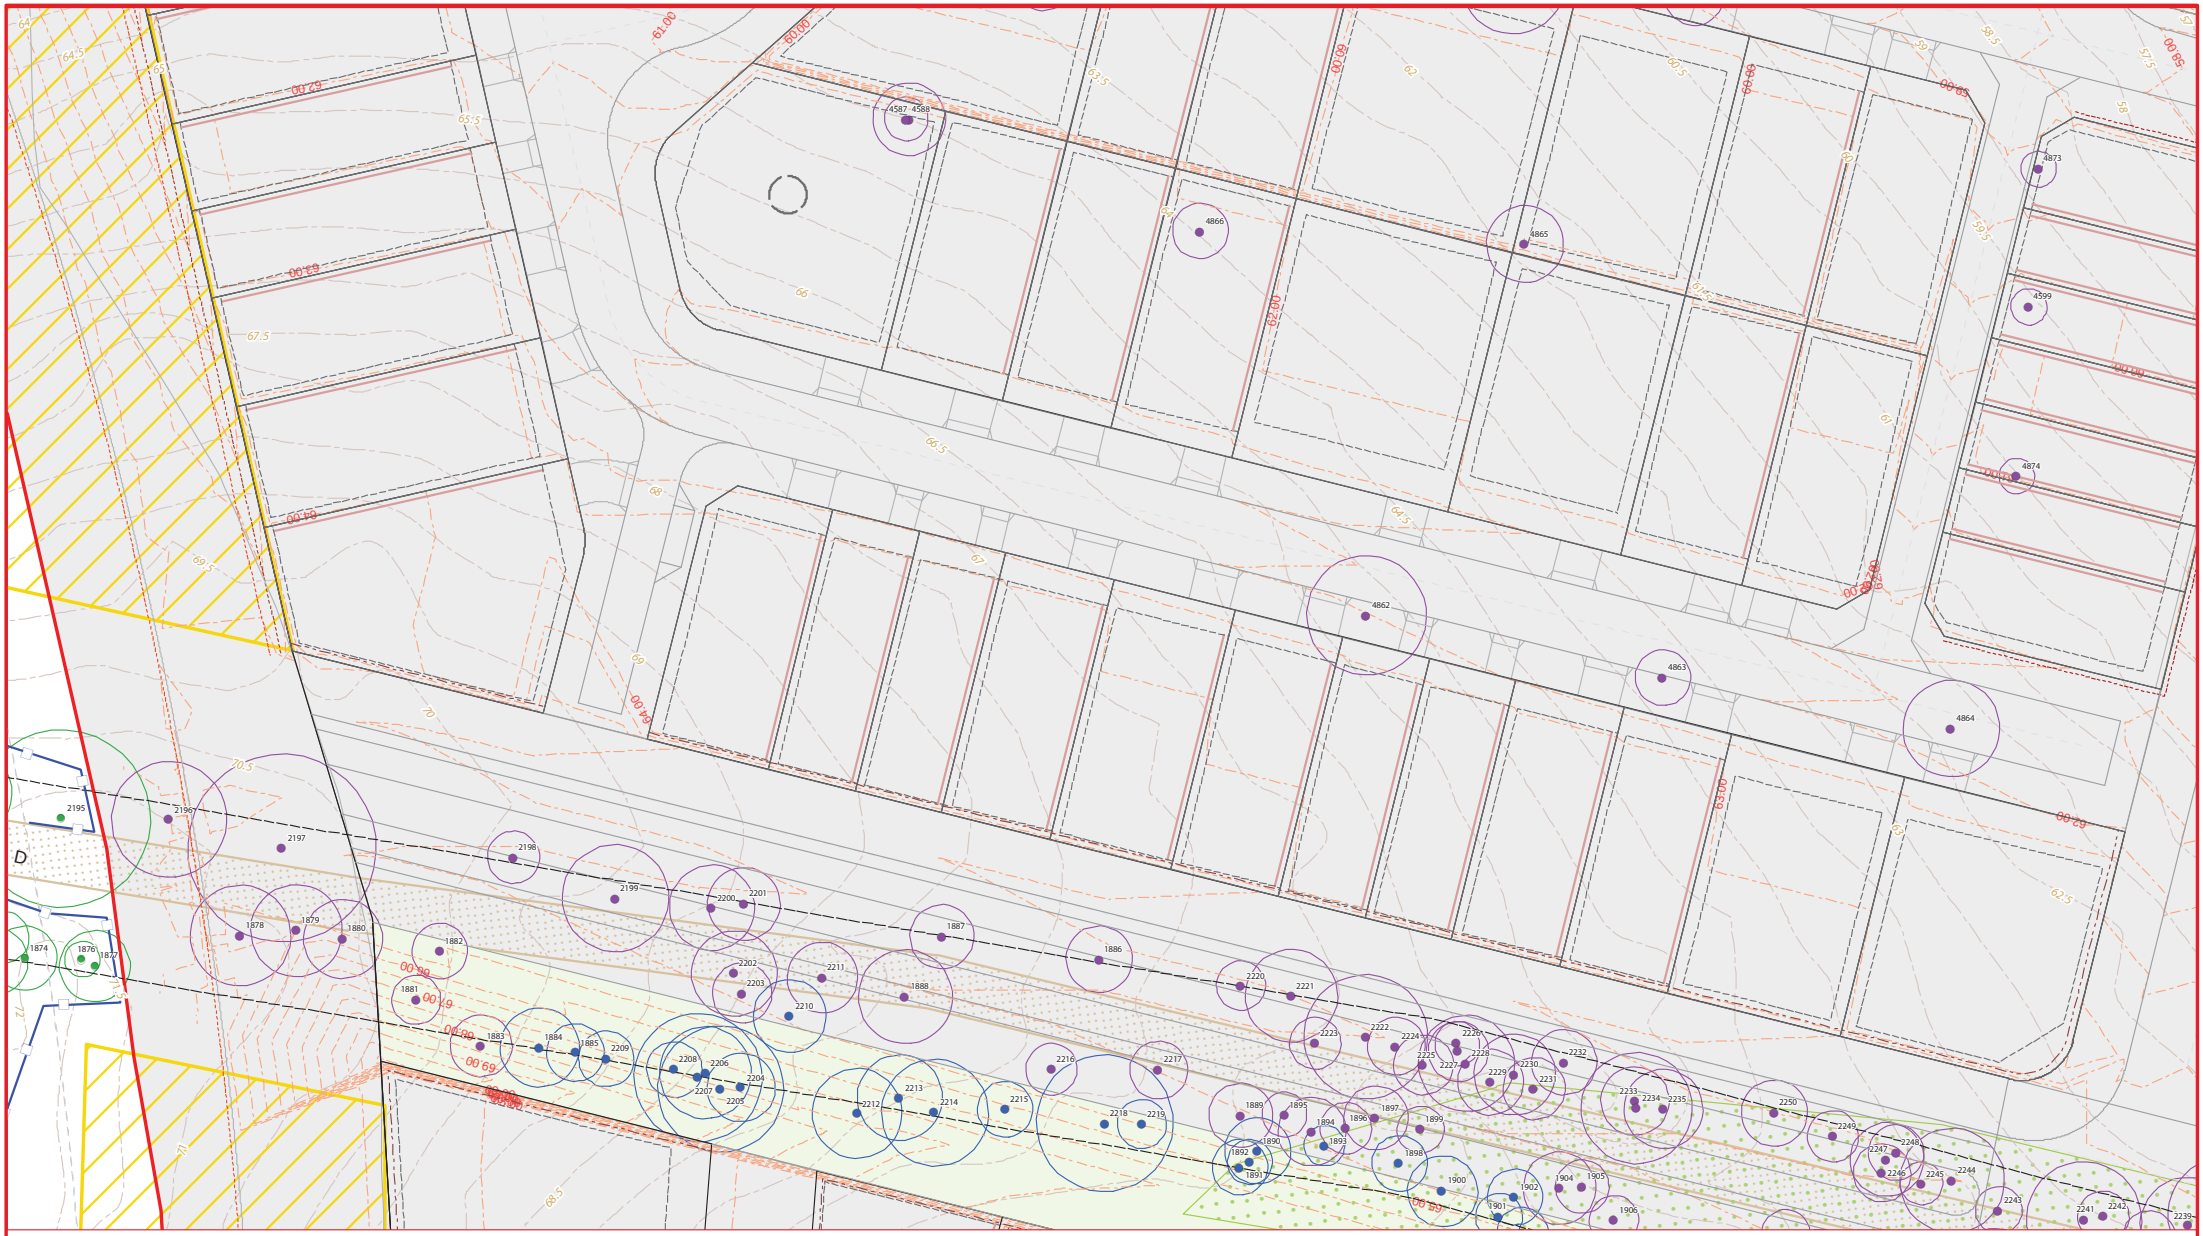

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 18

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 18 BAL Stage 2 VMP E	

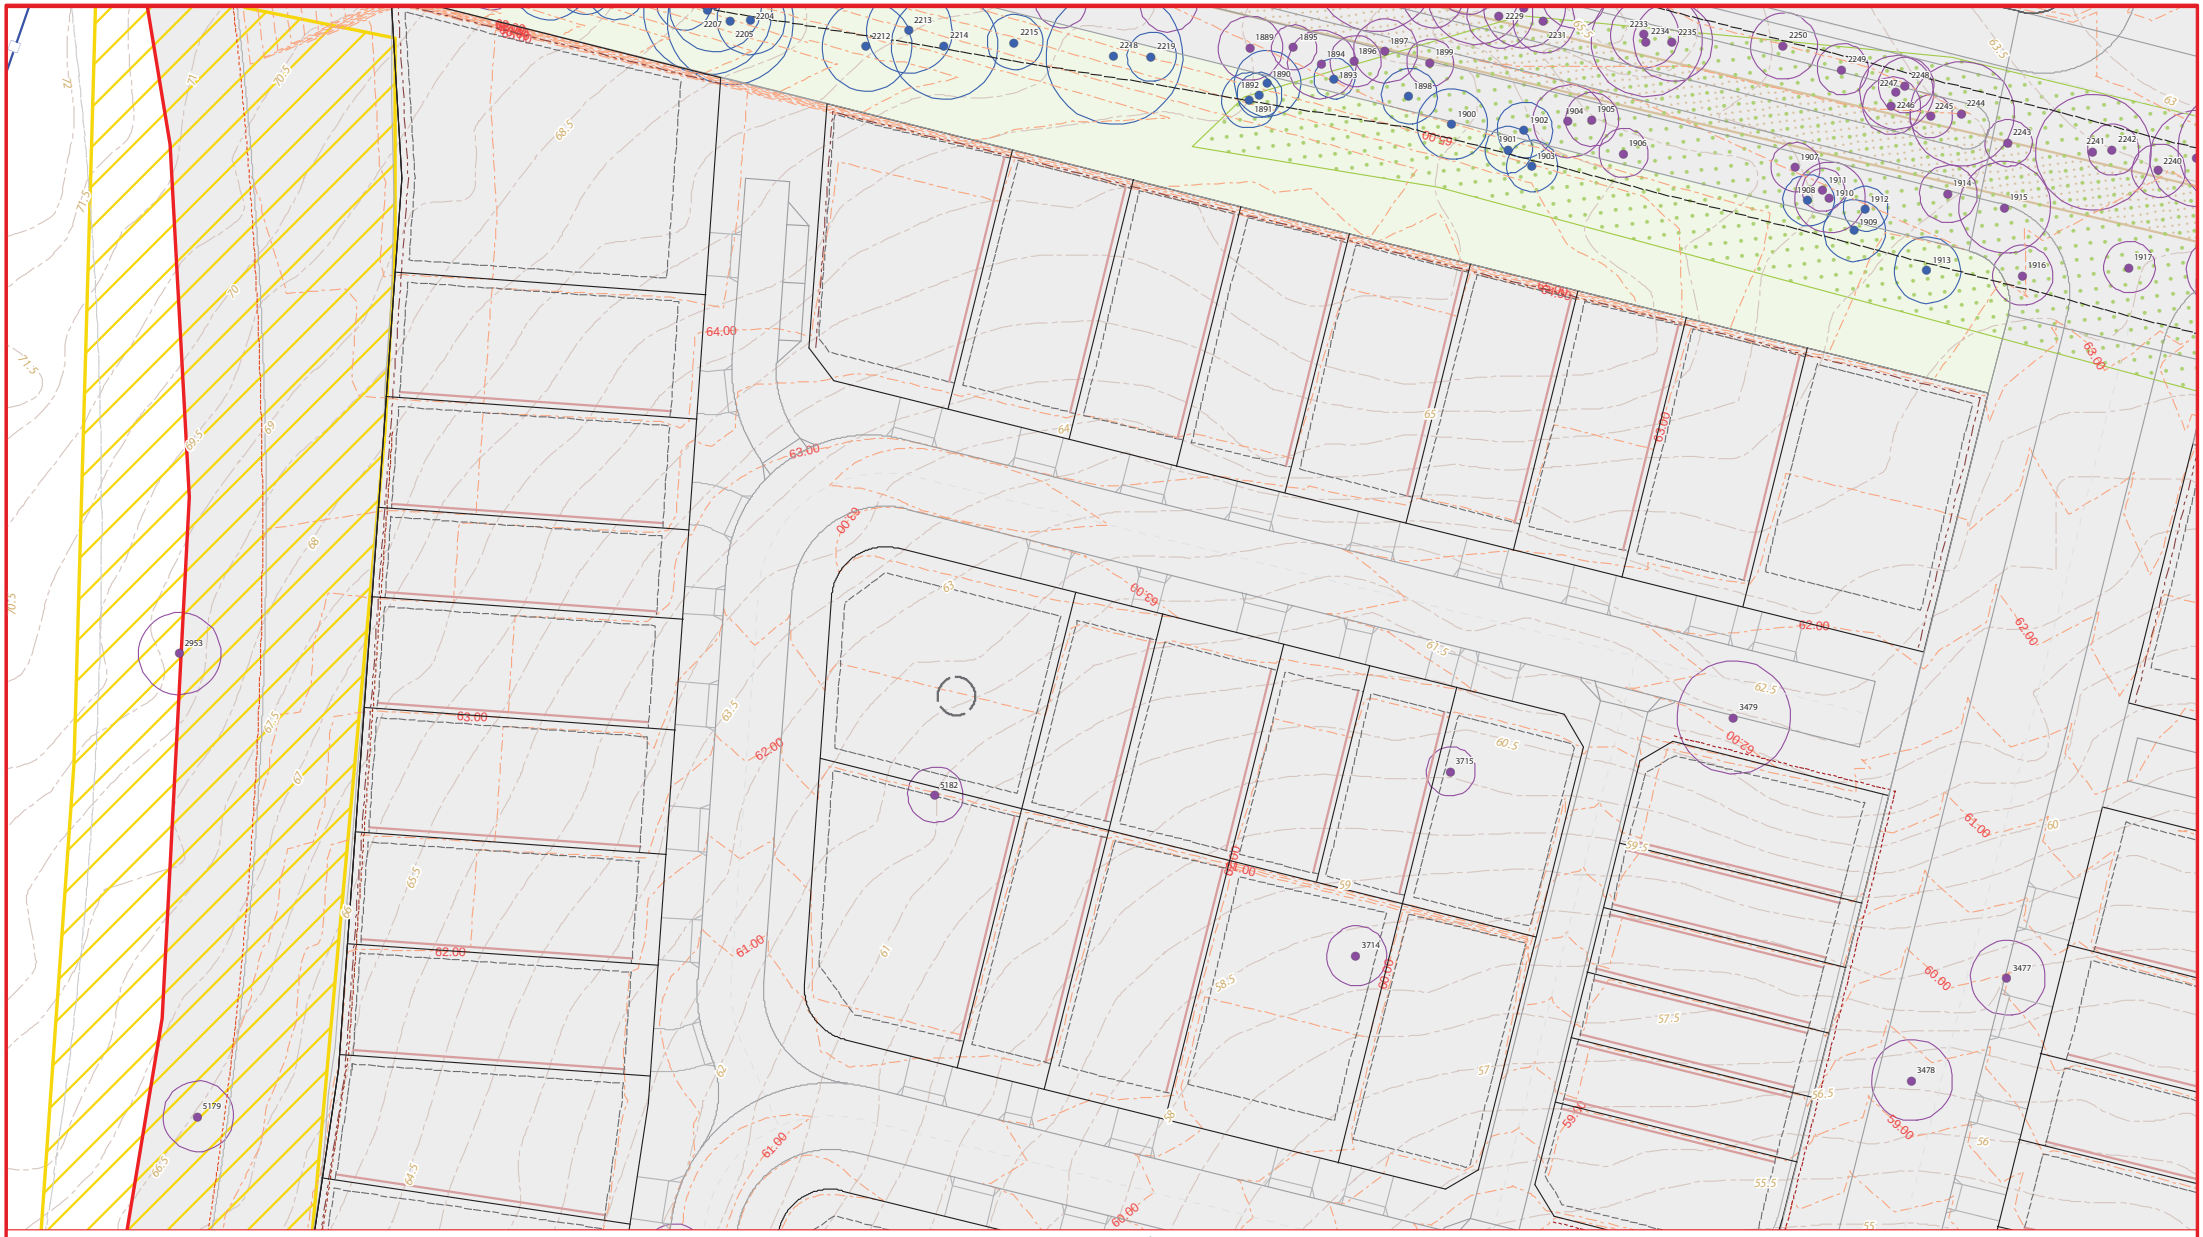

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 19

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC
DRAWING No.:	8047 E 19 BAL Stage 2 VMP E		

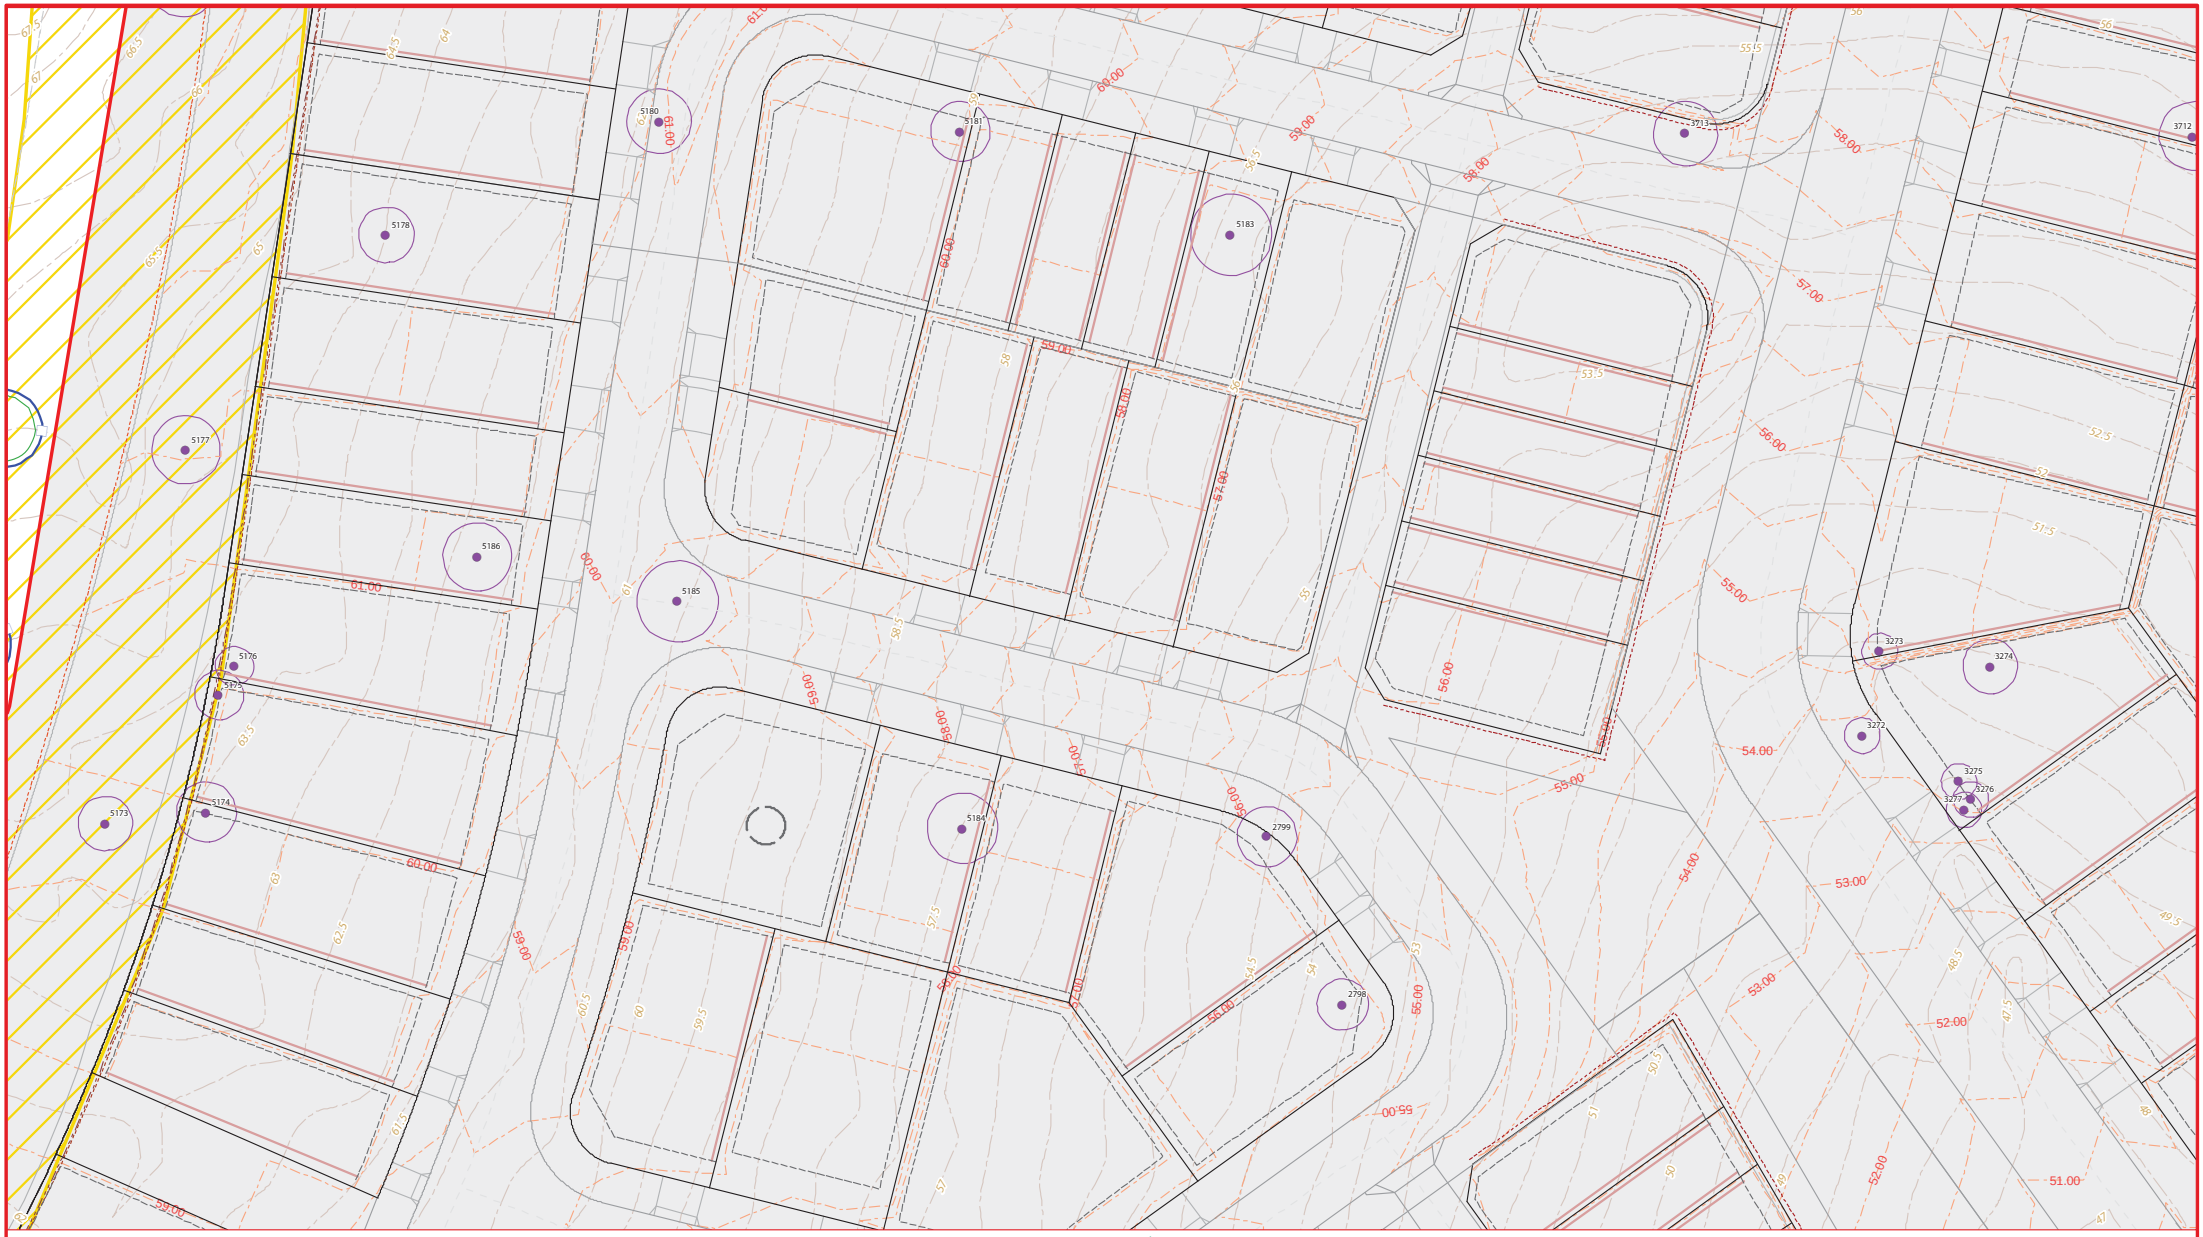

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 20

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 20 BAL Stage 2 VMP E	

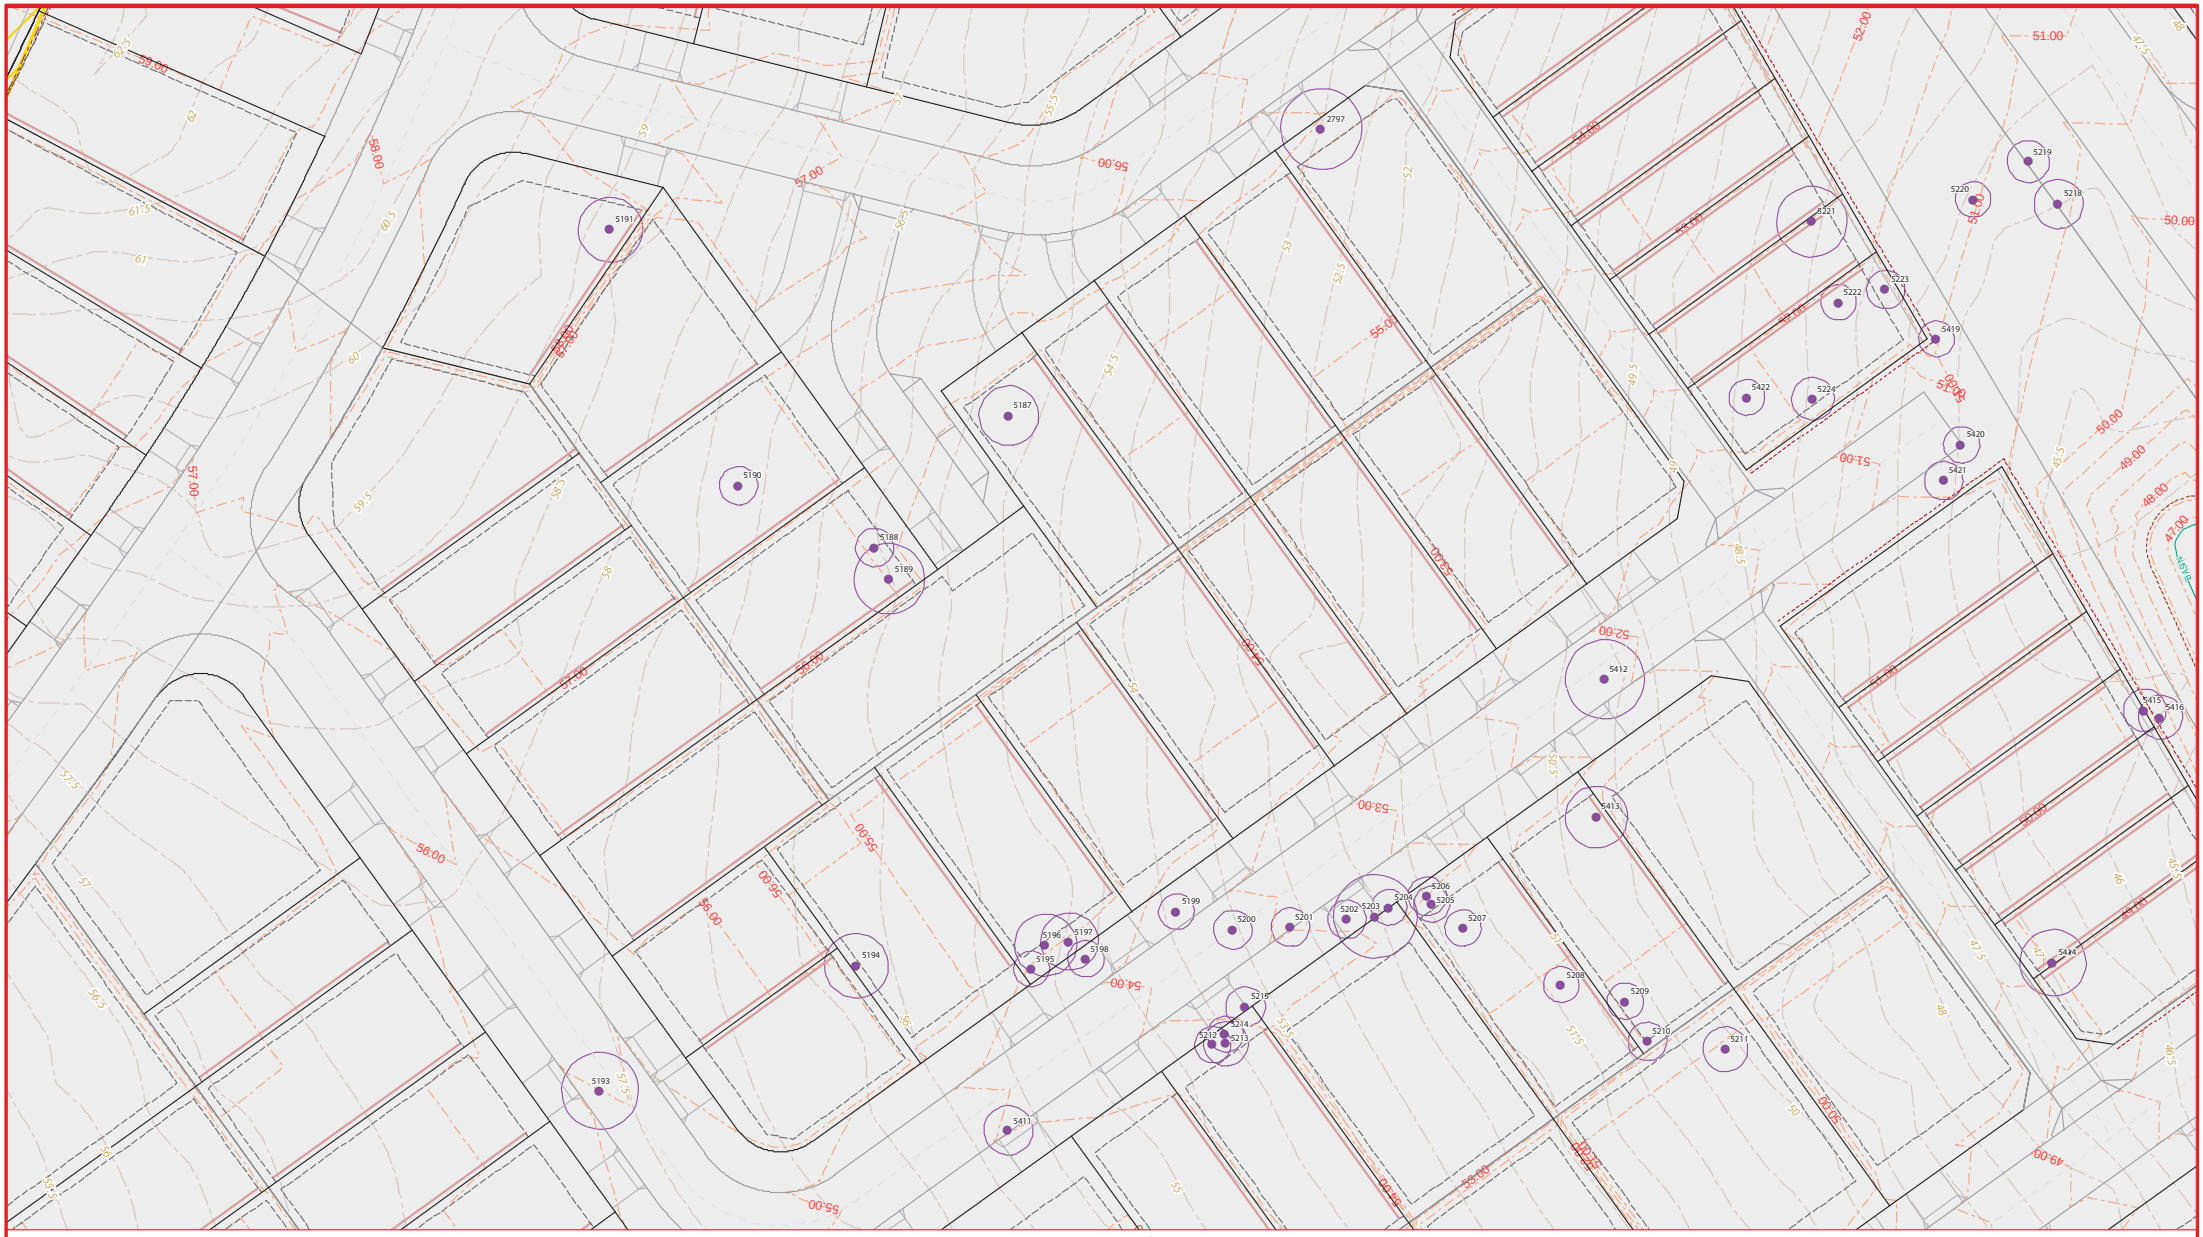

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 21

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 21 BAL Stage 2 VMP E	

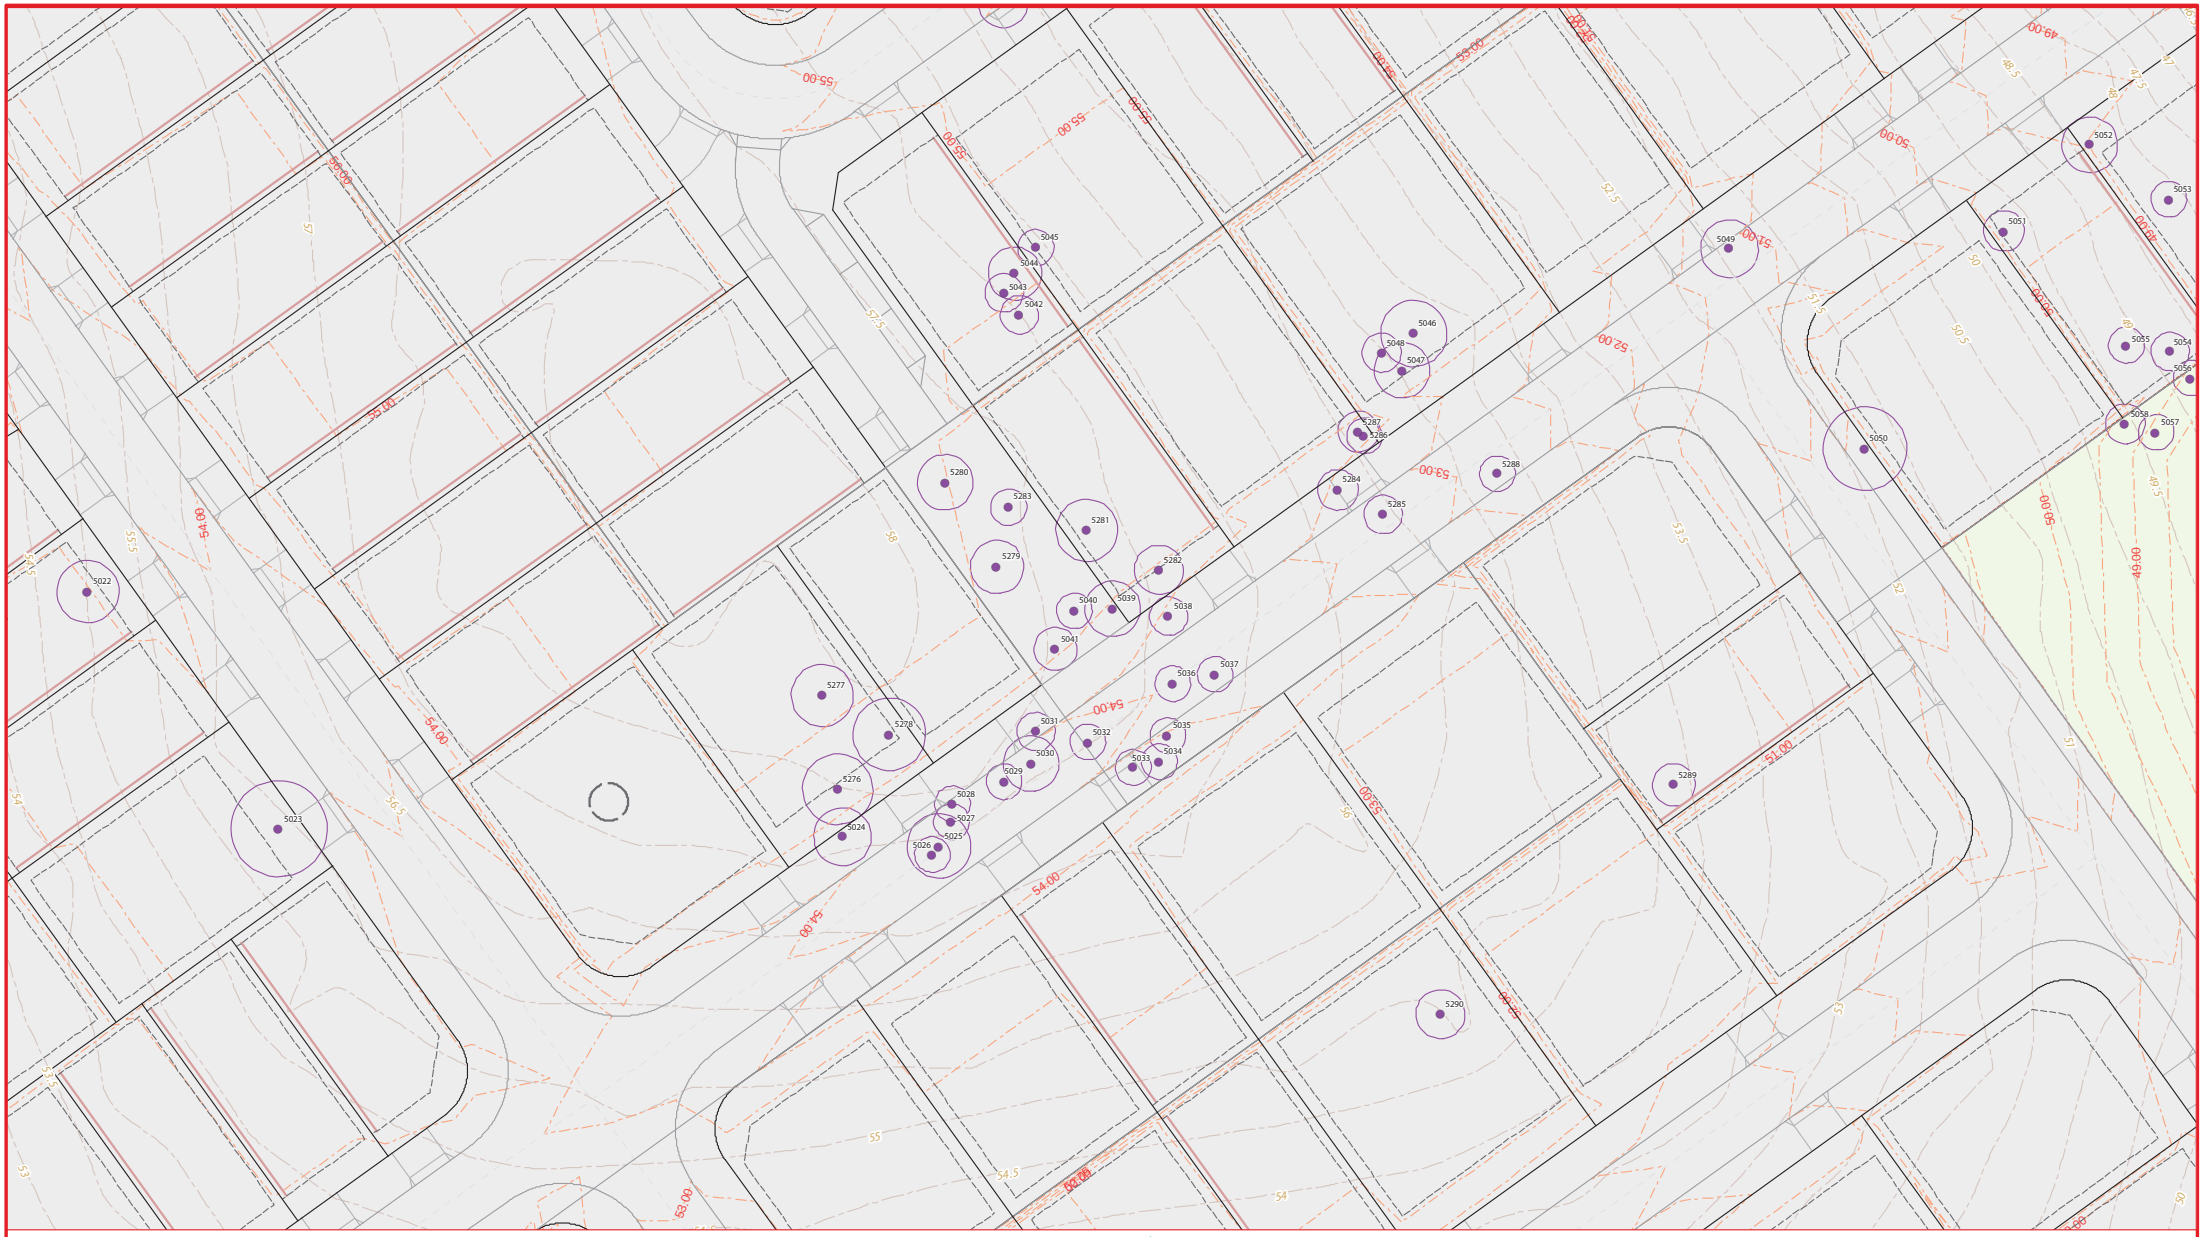

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 22

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 22 BAL Stage 2 VMP E

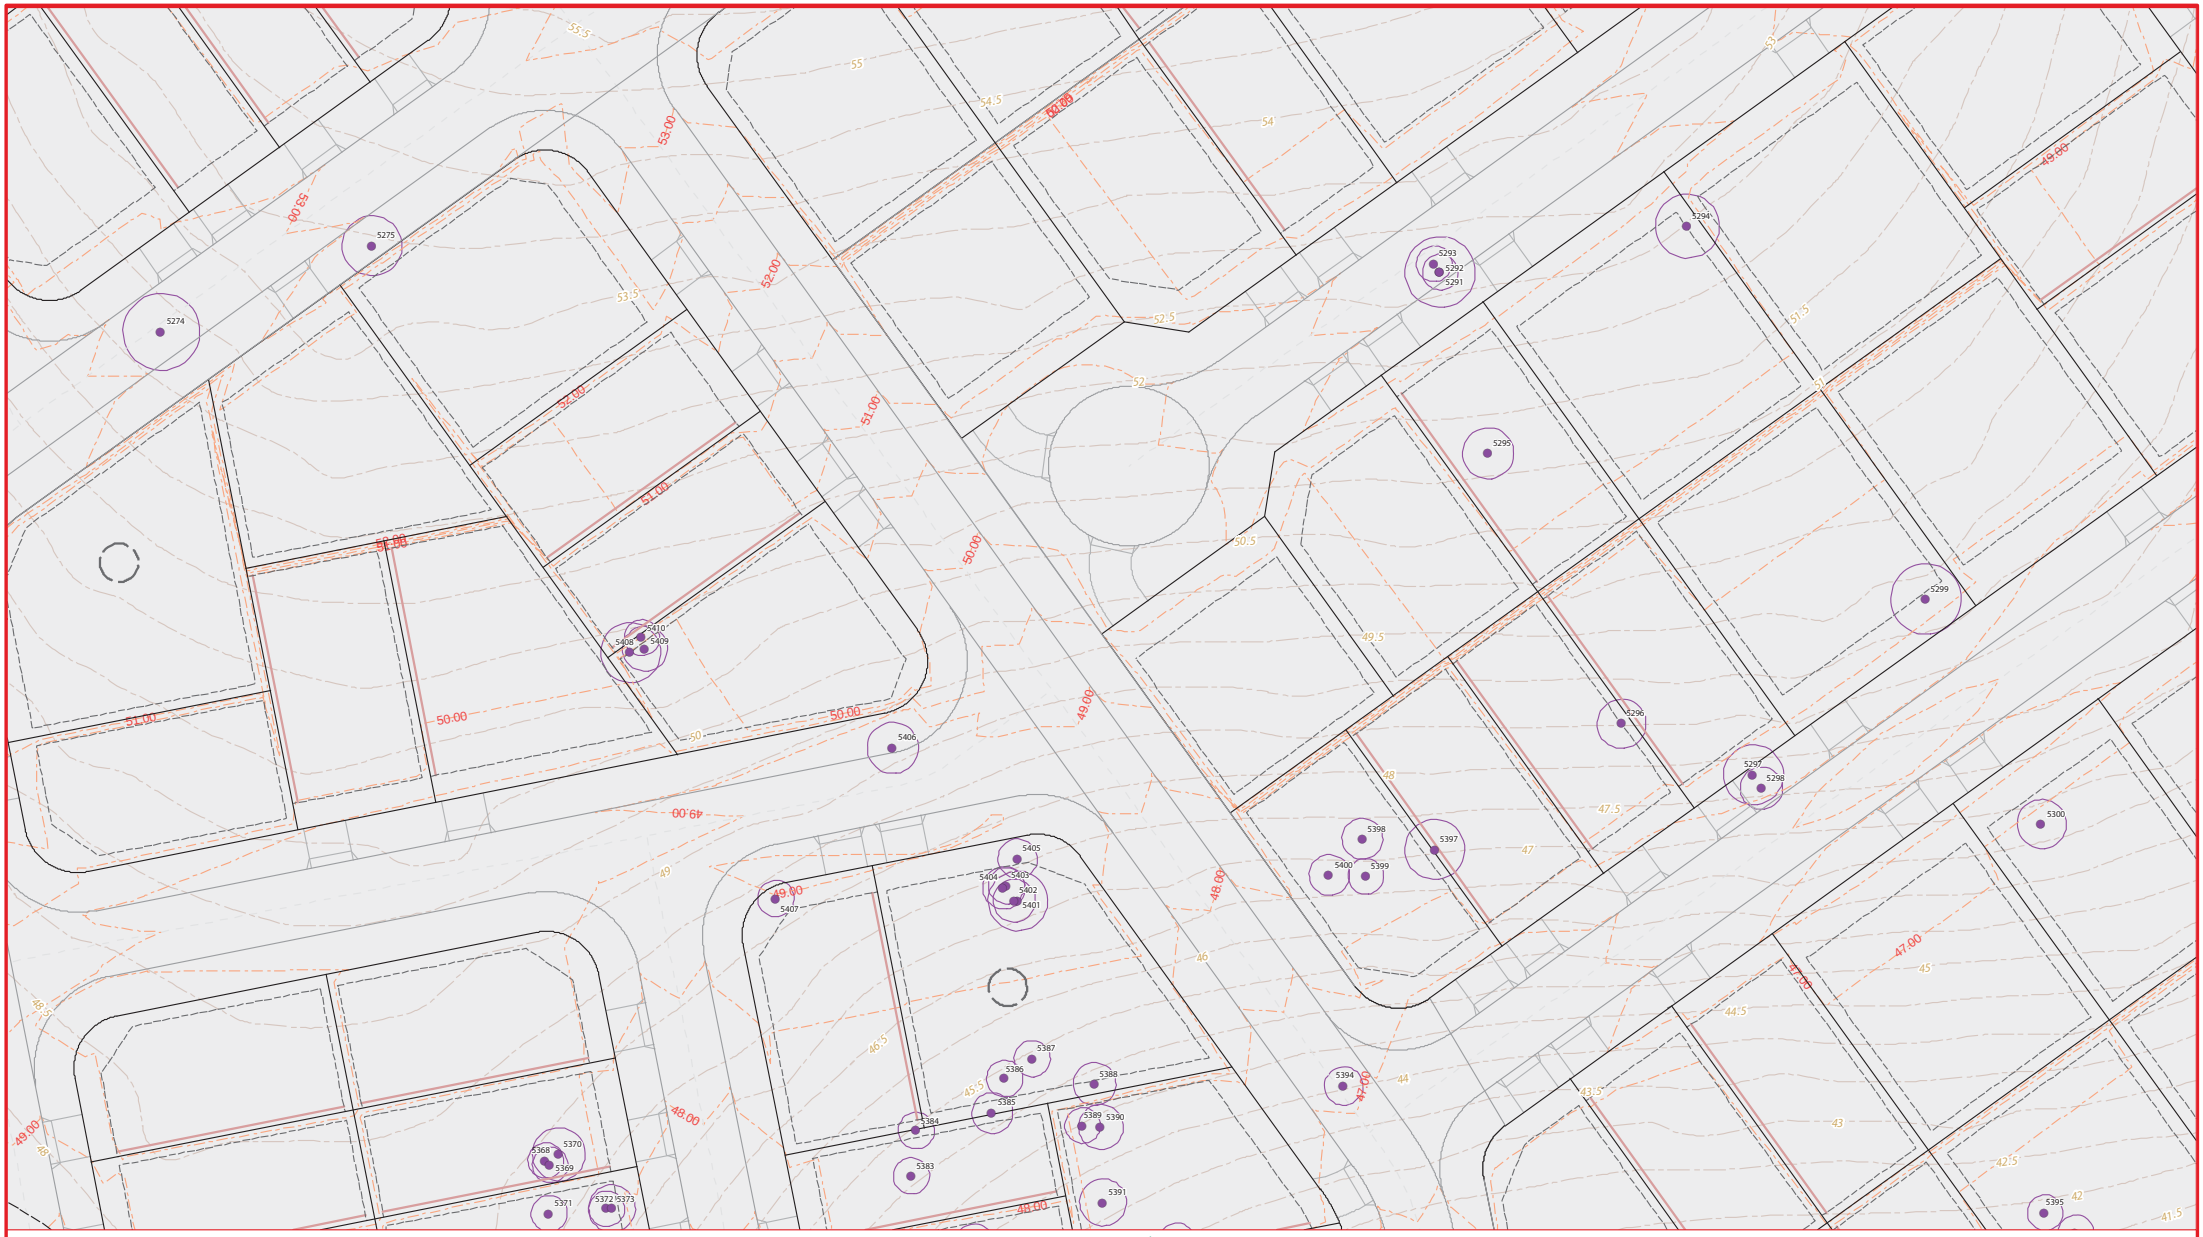

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 23

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 23 BAL Stage 2 VMP E

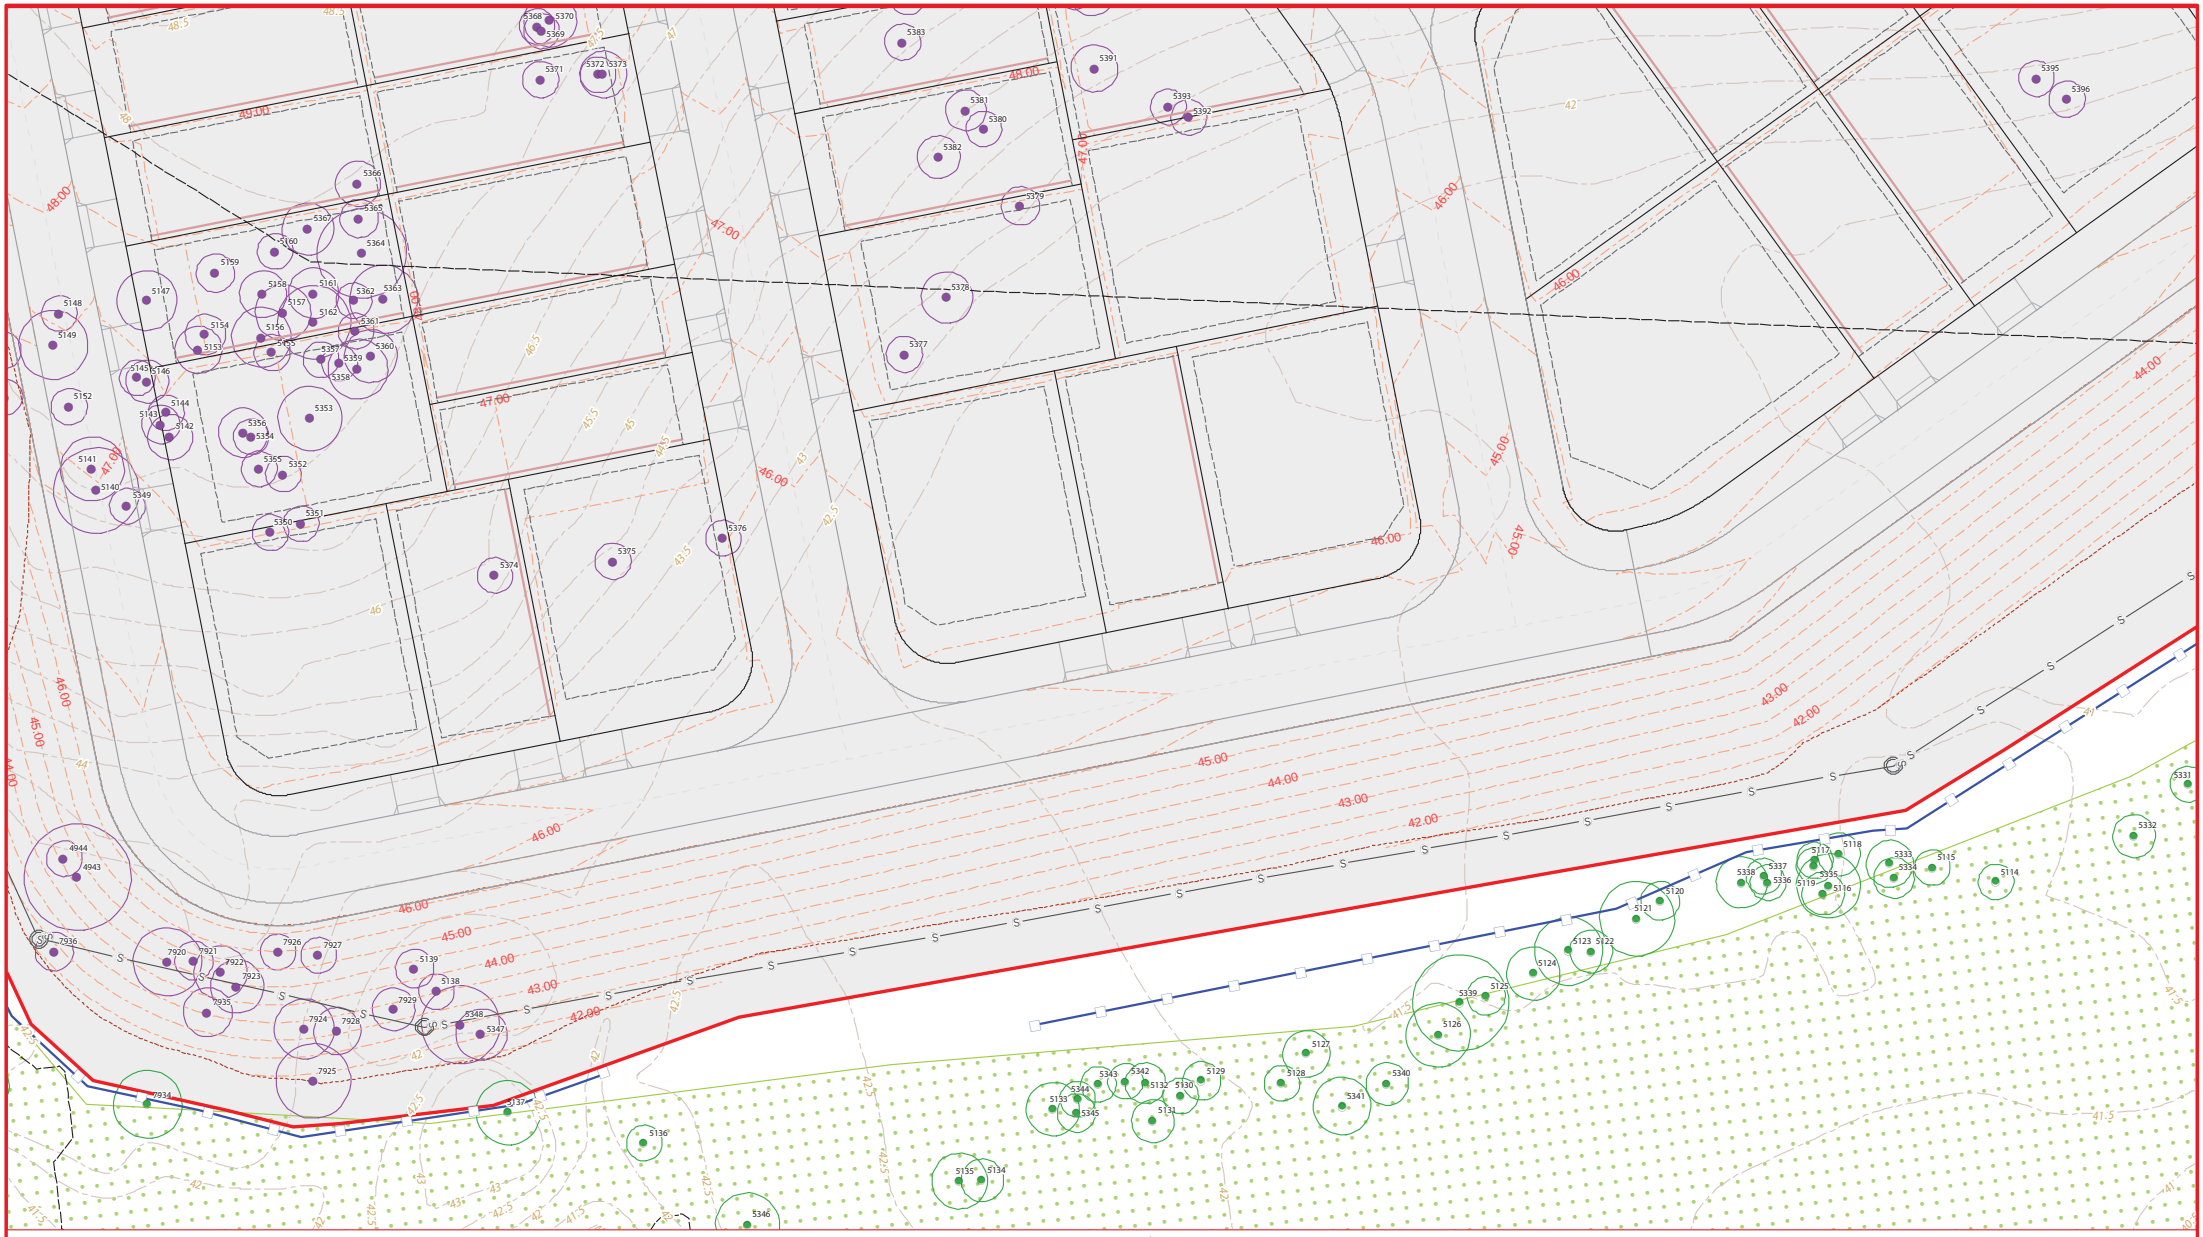

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 24

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE'S. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 24 BAL Stage 2 VMP E	

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 25

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 25 BAL Stage 2 VMP E

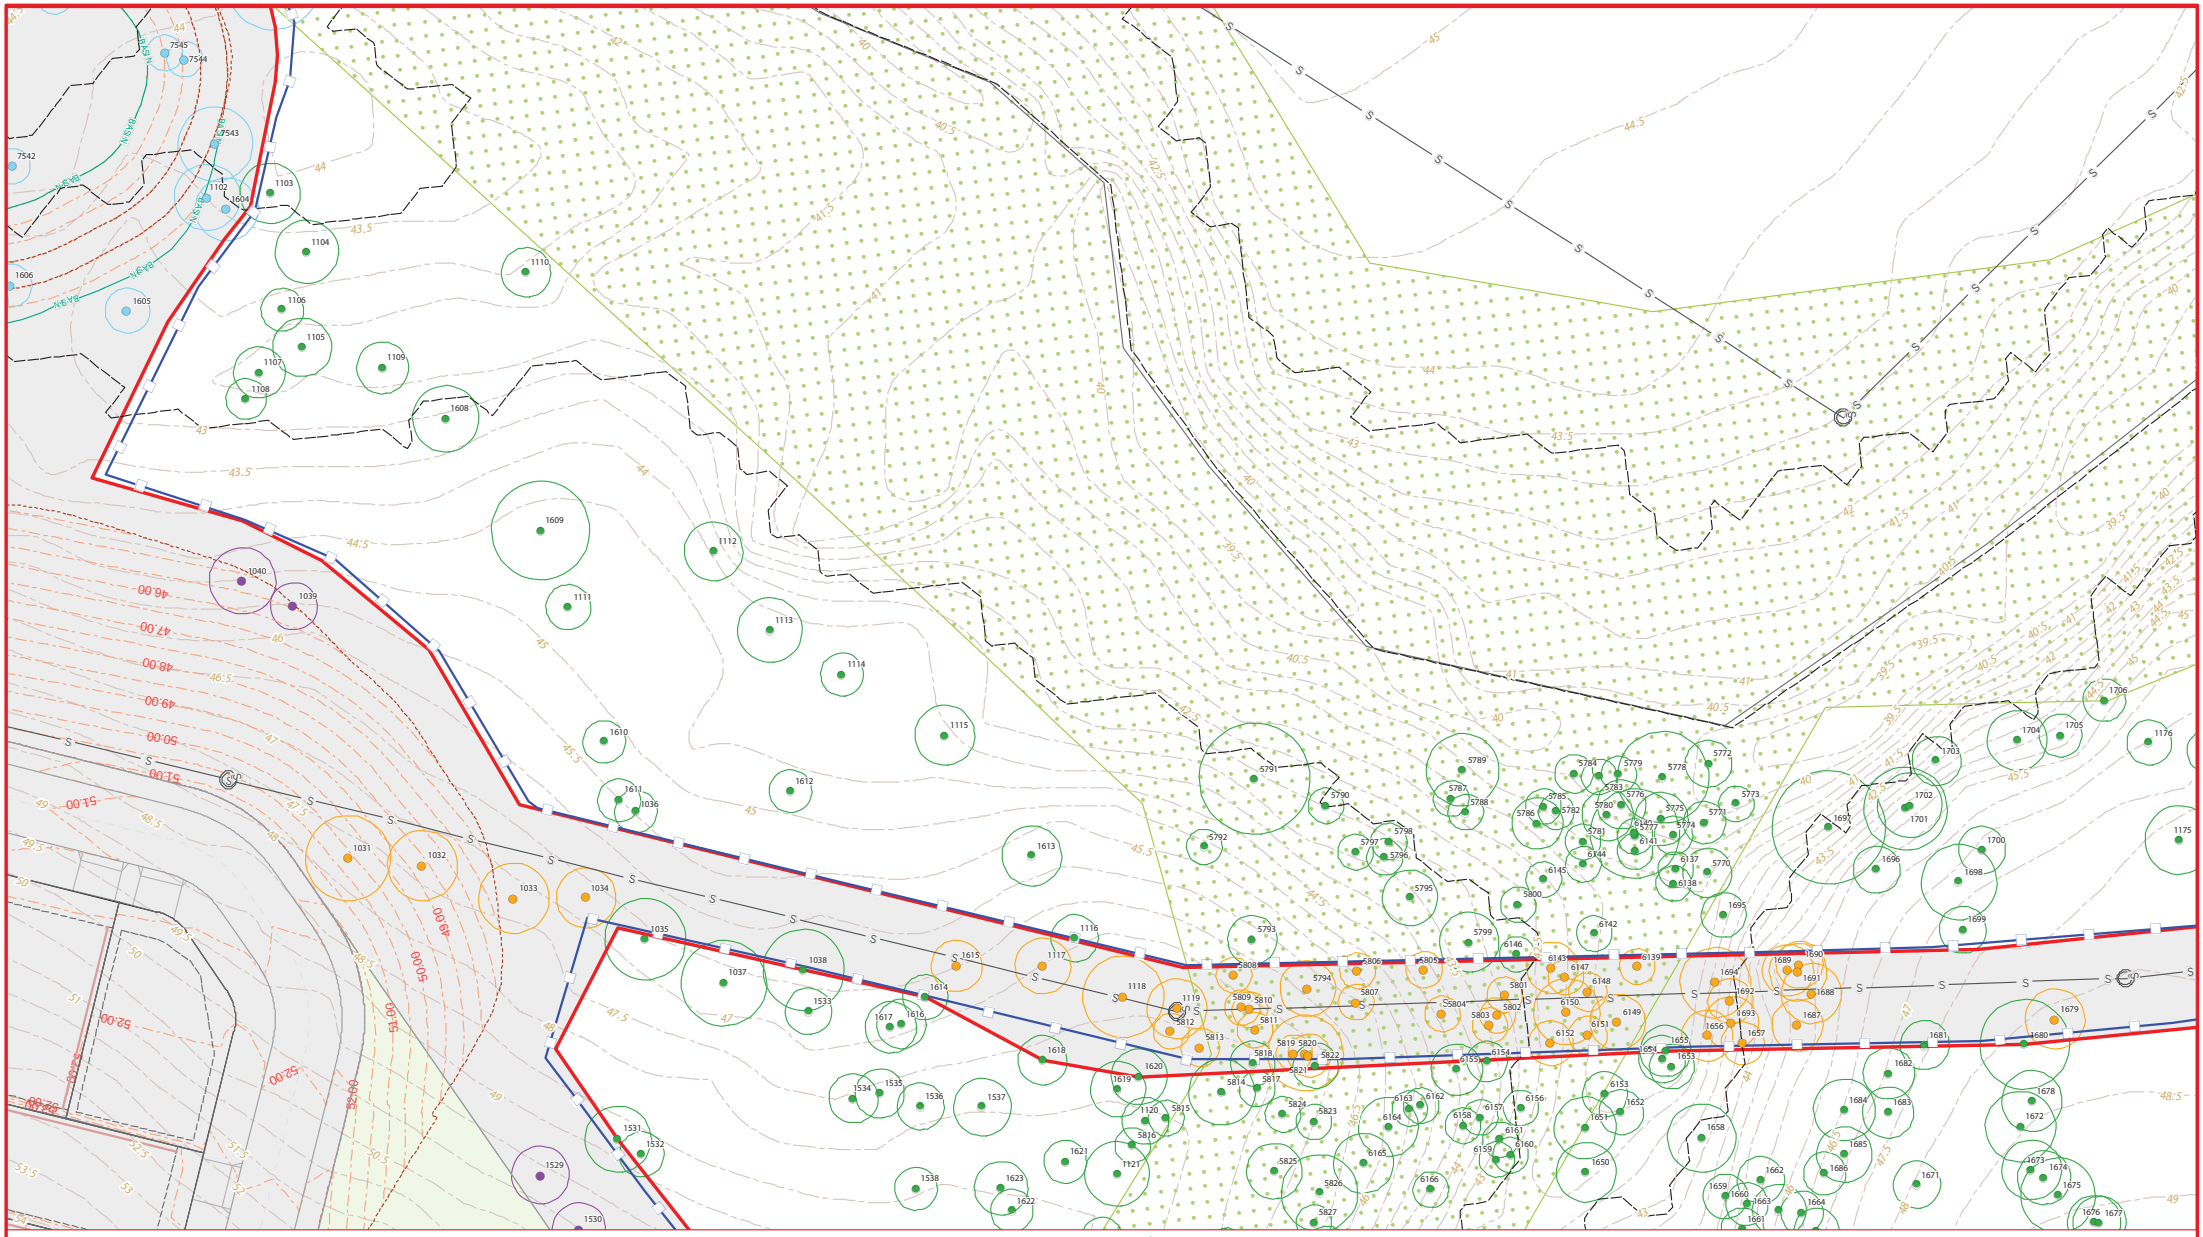

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 26

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 26 BAL Stage 2 VMP E	

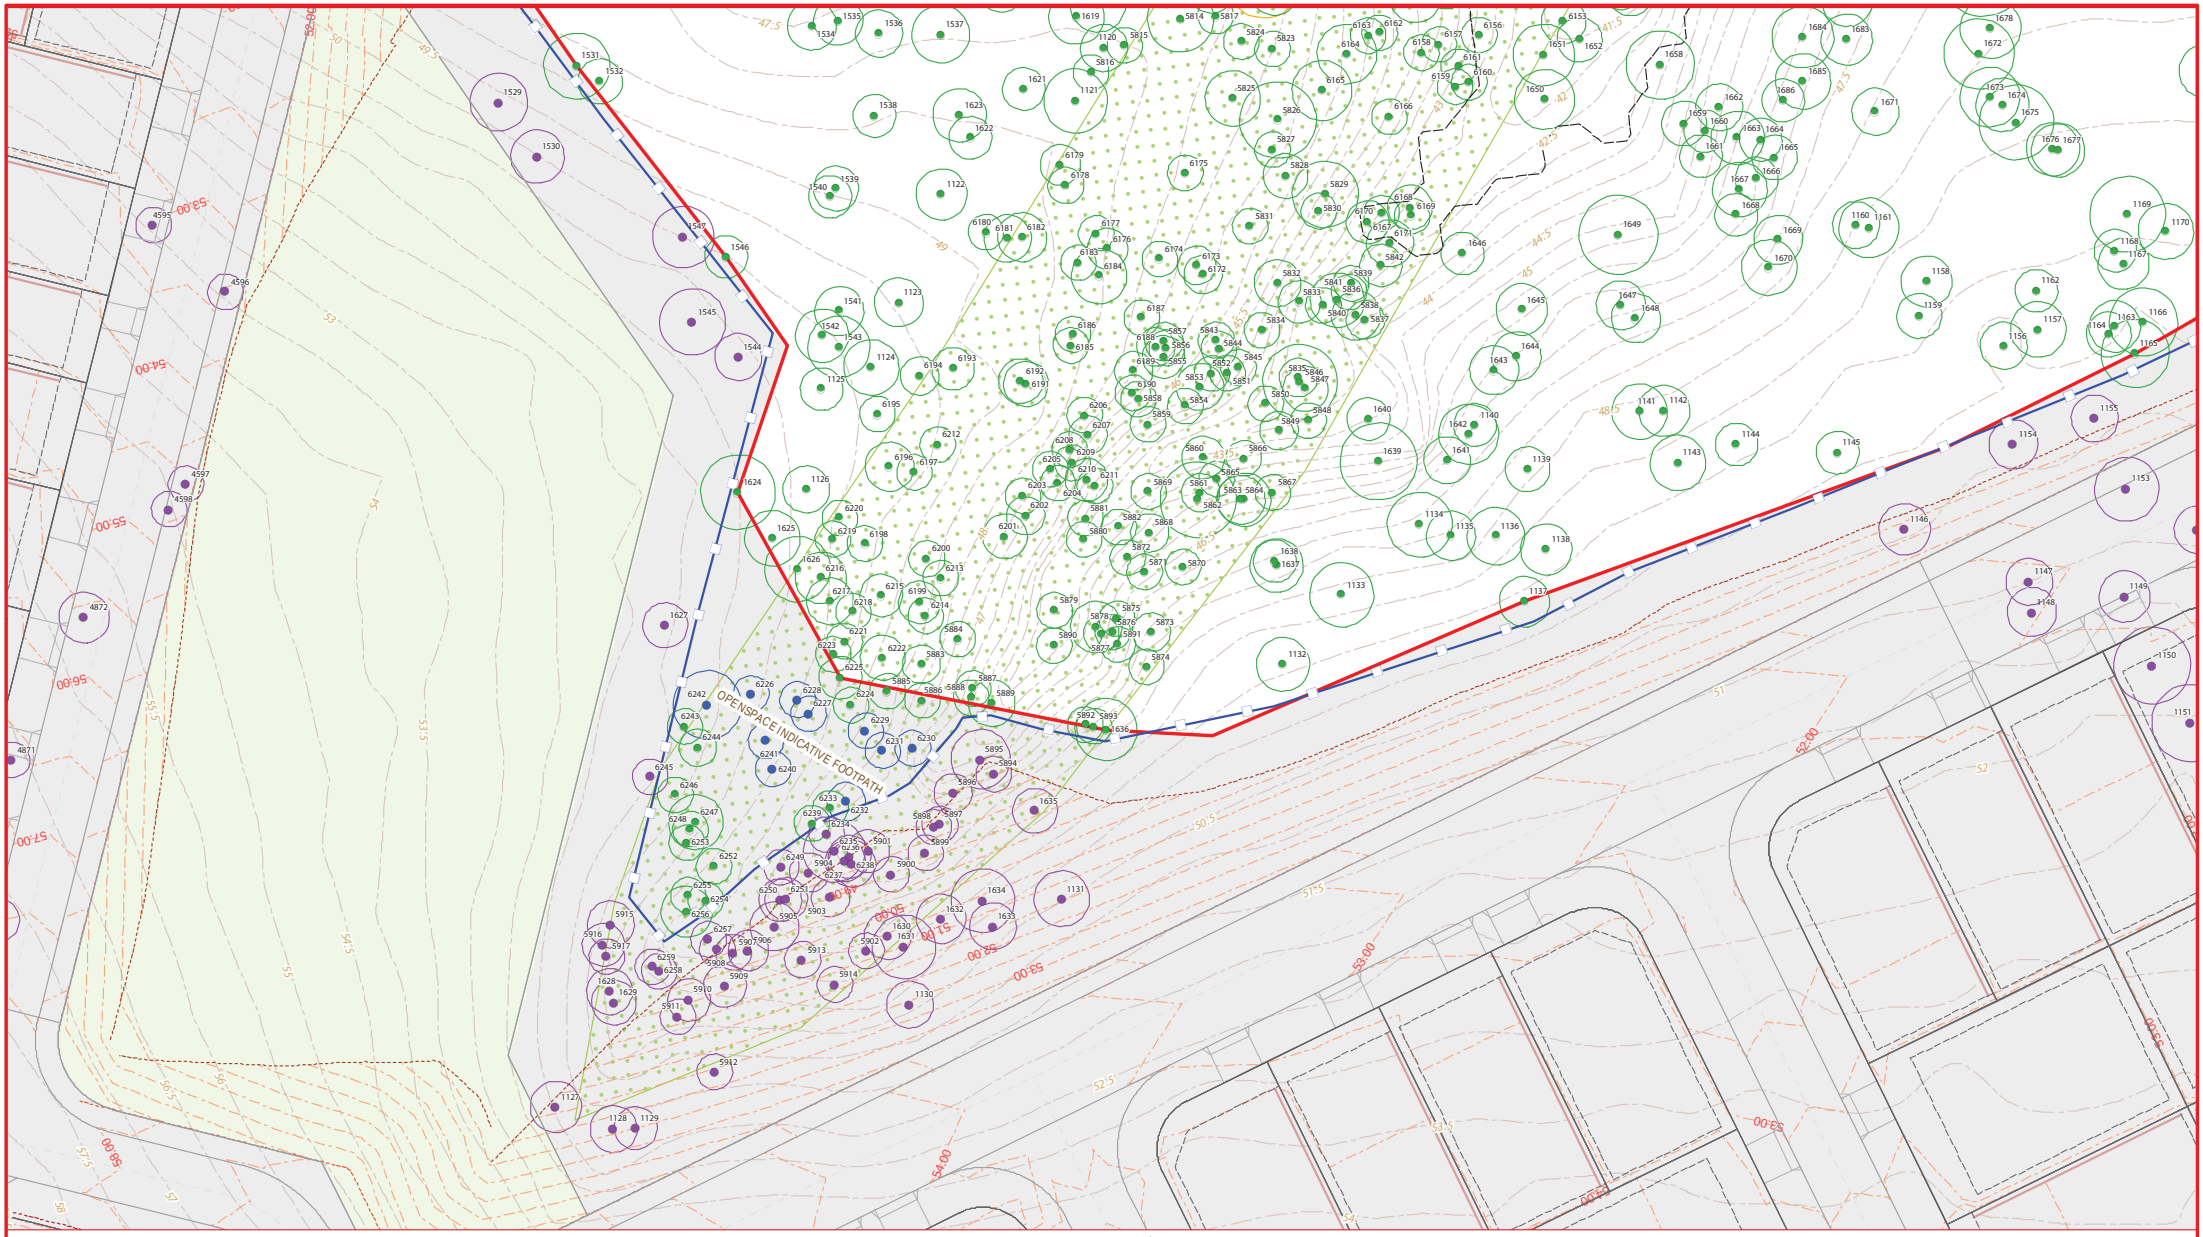

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 27

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE & ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 27 BAL Stage 2 VMP E	

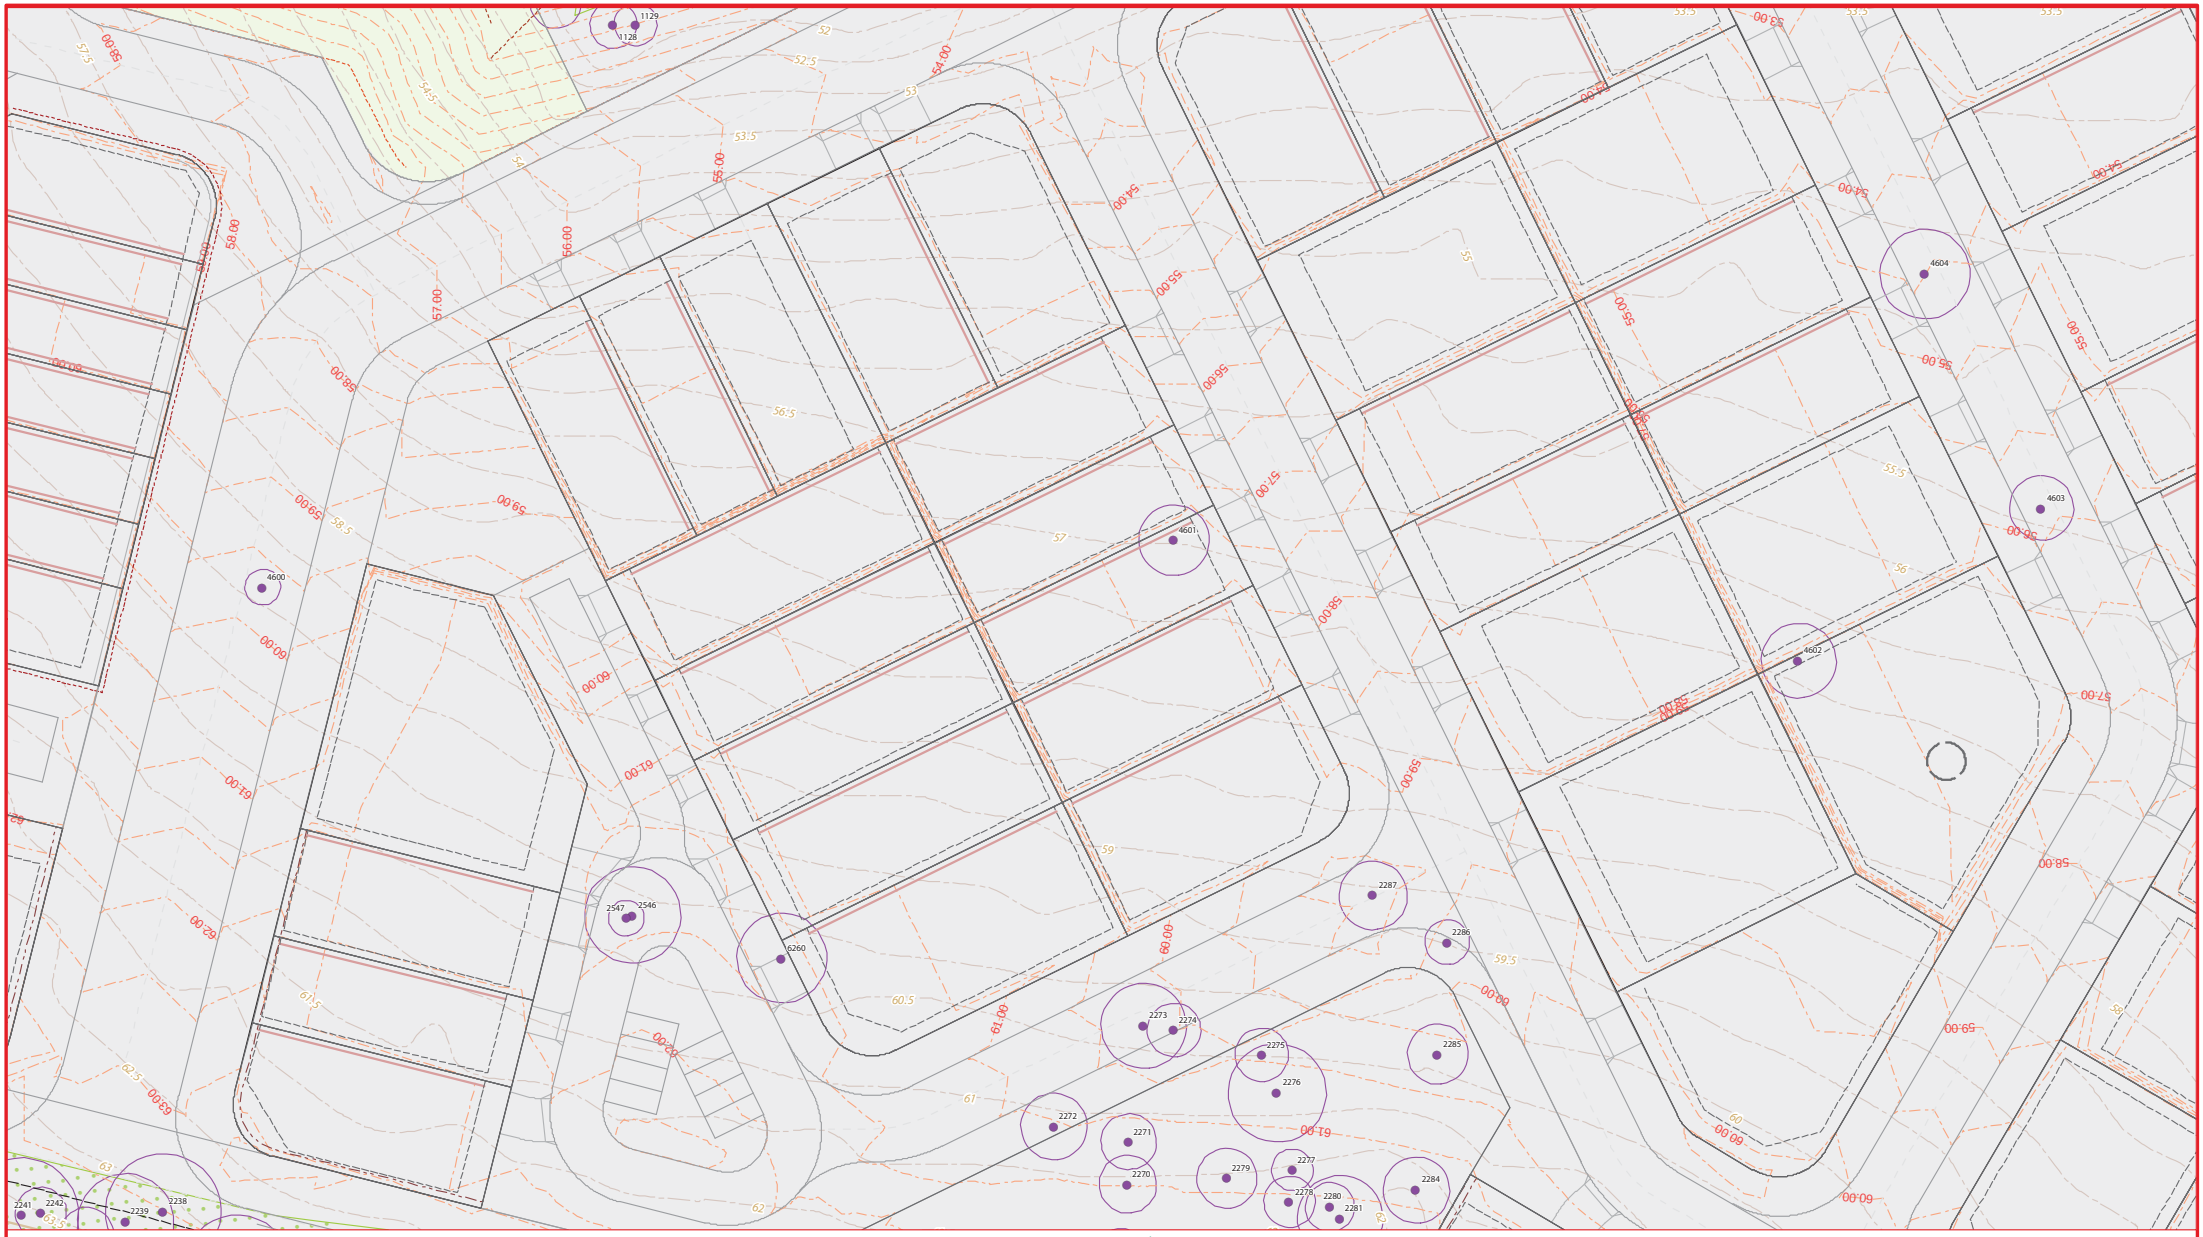

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 28

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 28 BAL Stage 2 VMP E	

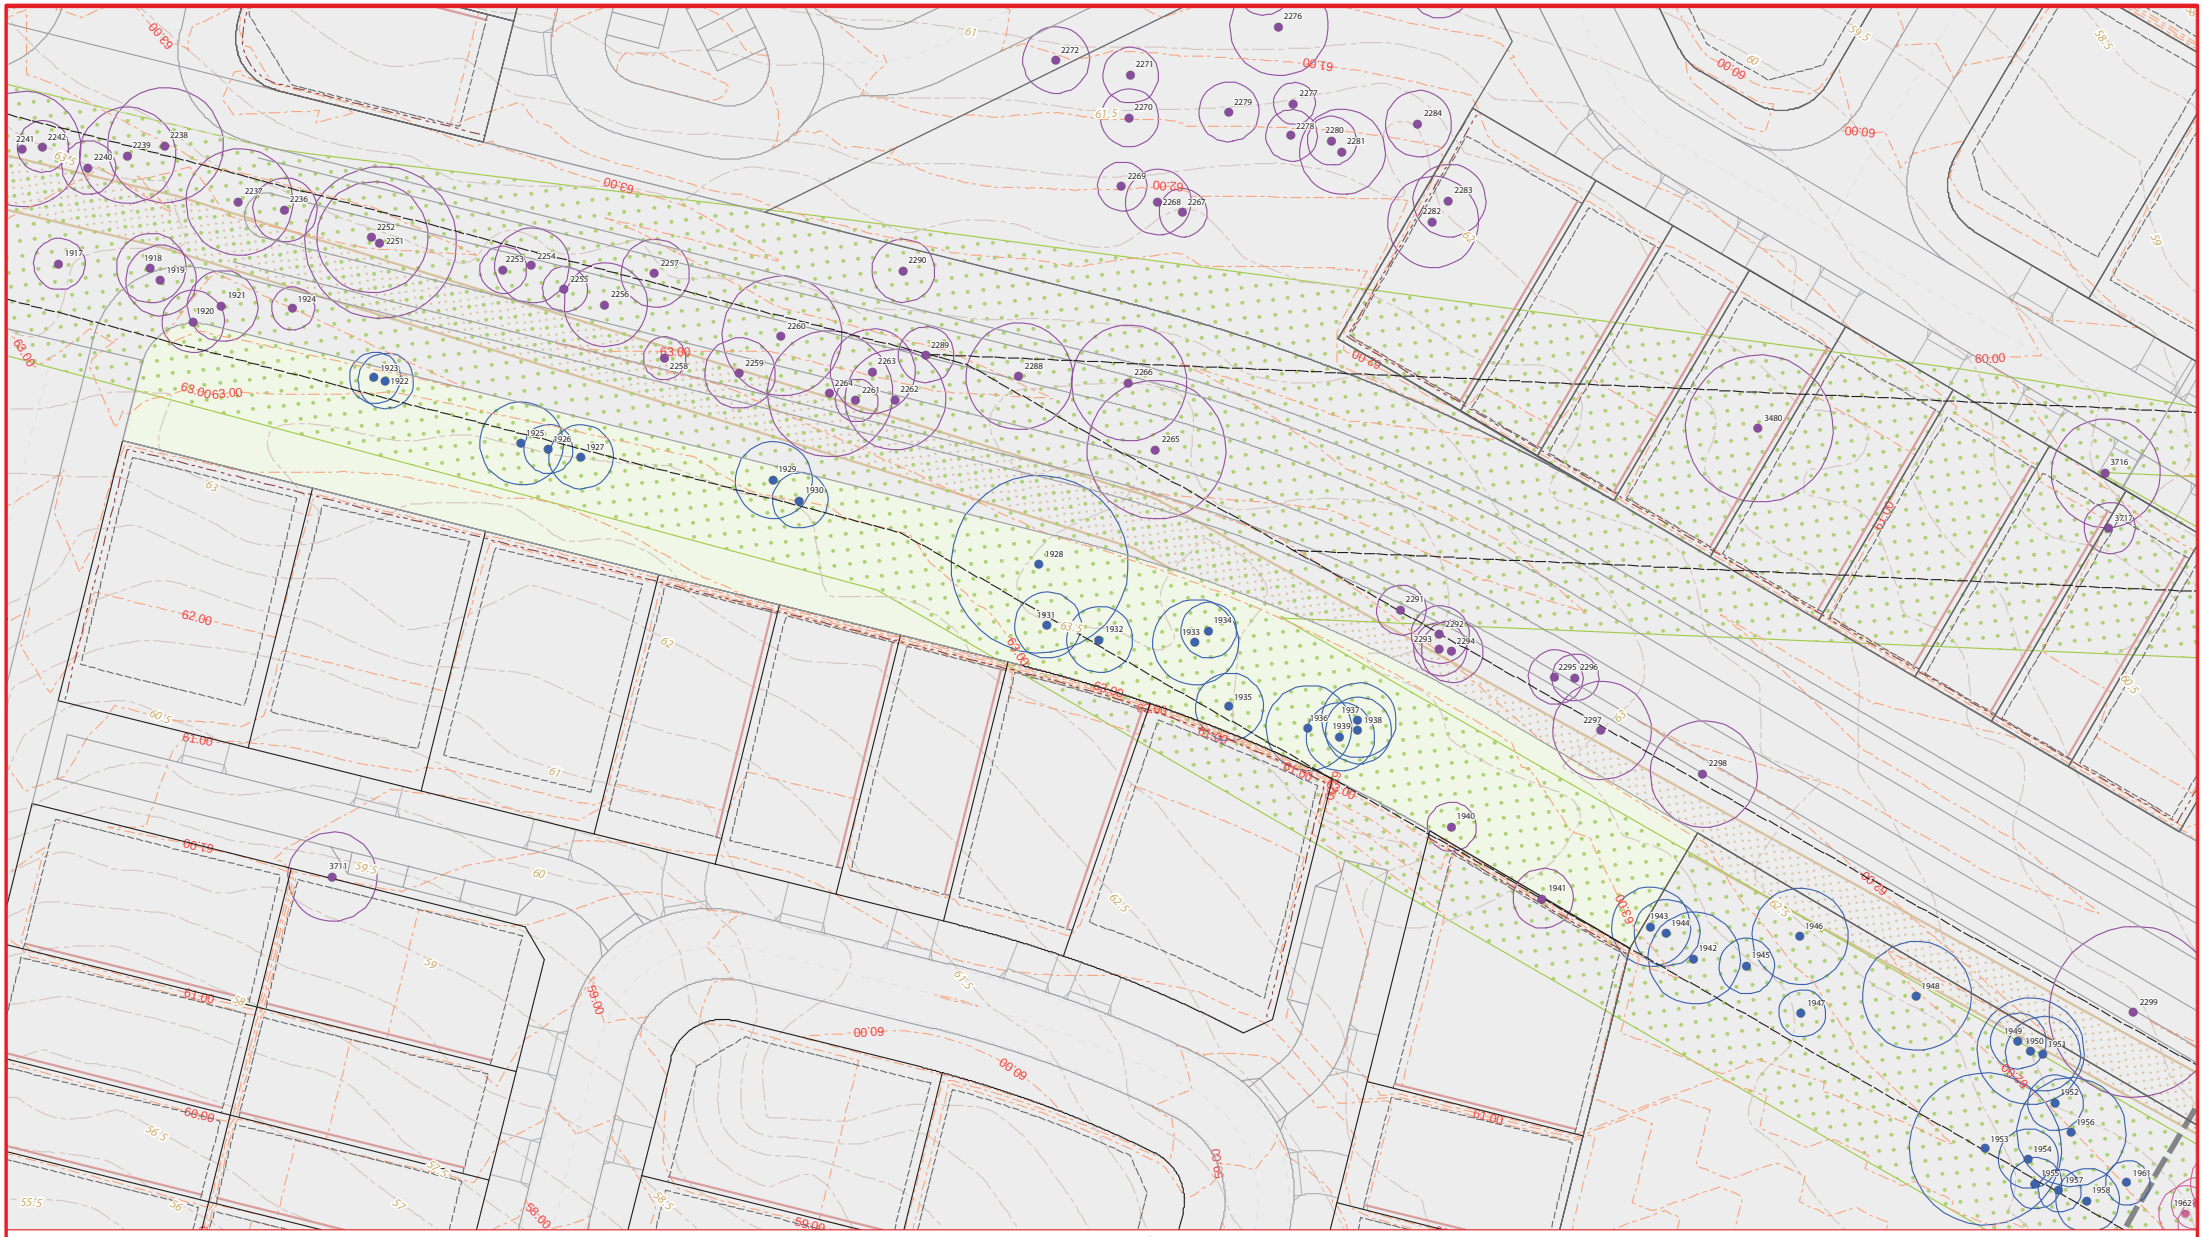

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 29

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC

DRAWING No.: 8047 E 29 BAL Stage 2 VMP E

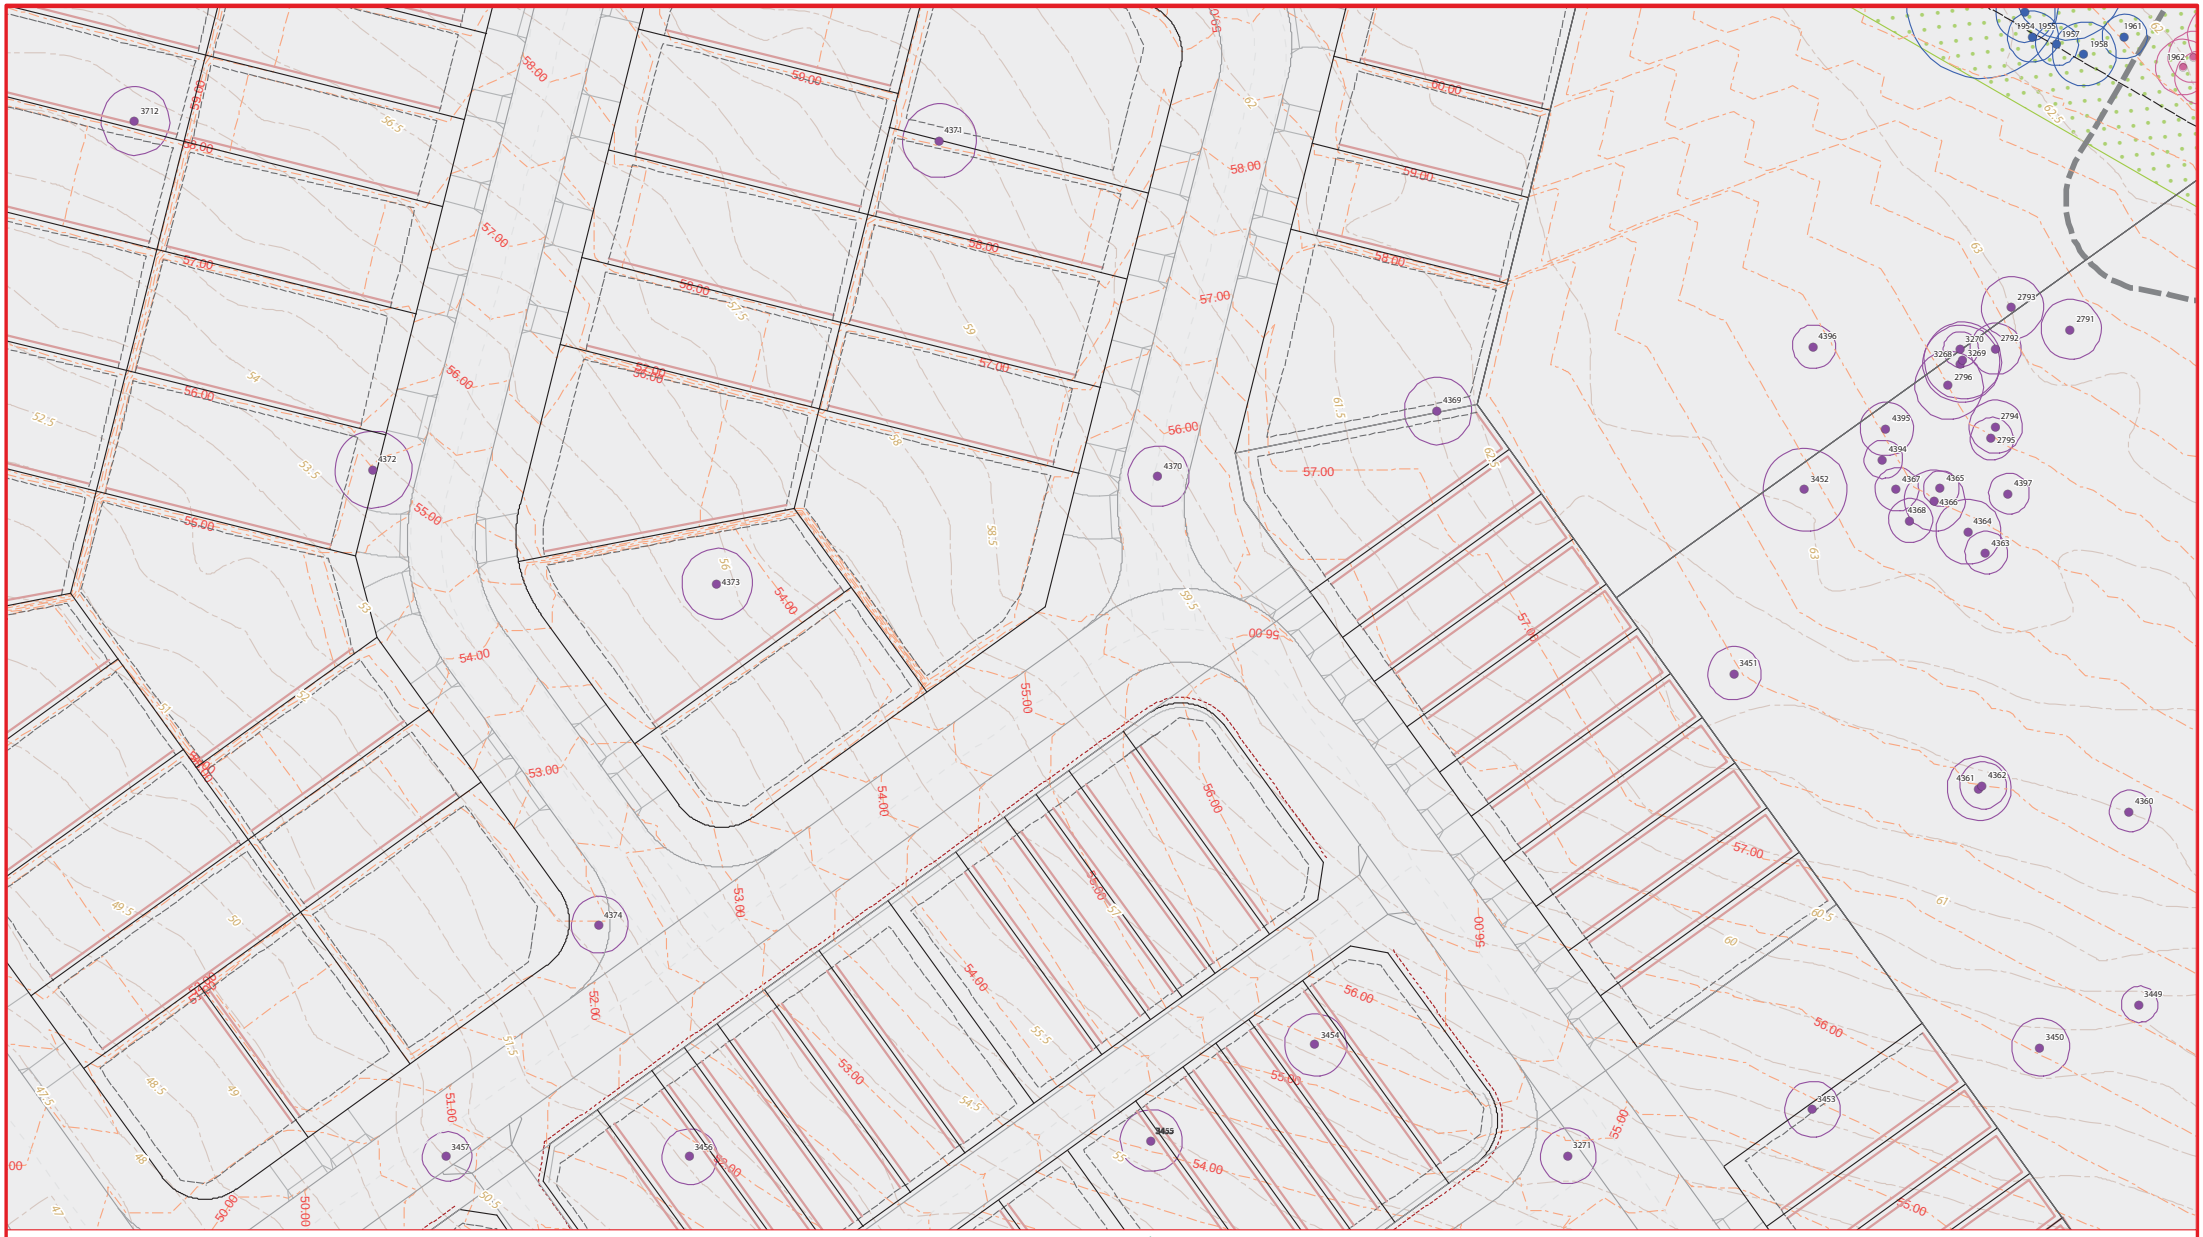

Vegetation Management Plan - Detail Sheet 30

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 30 BAL Stage 2 VMP E	

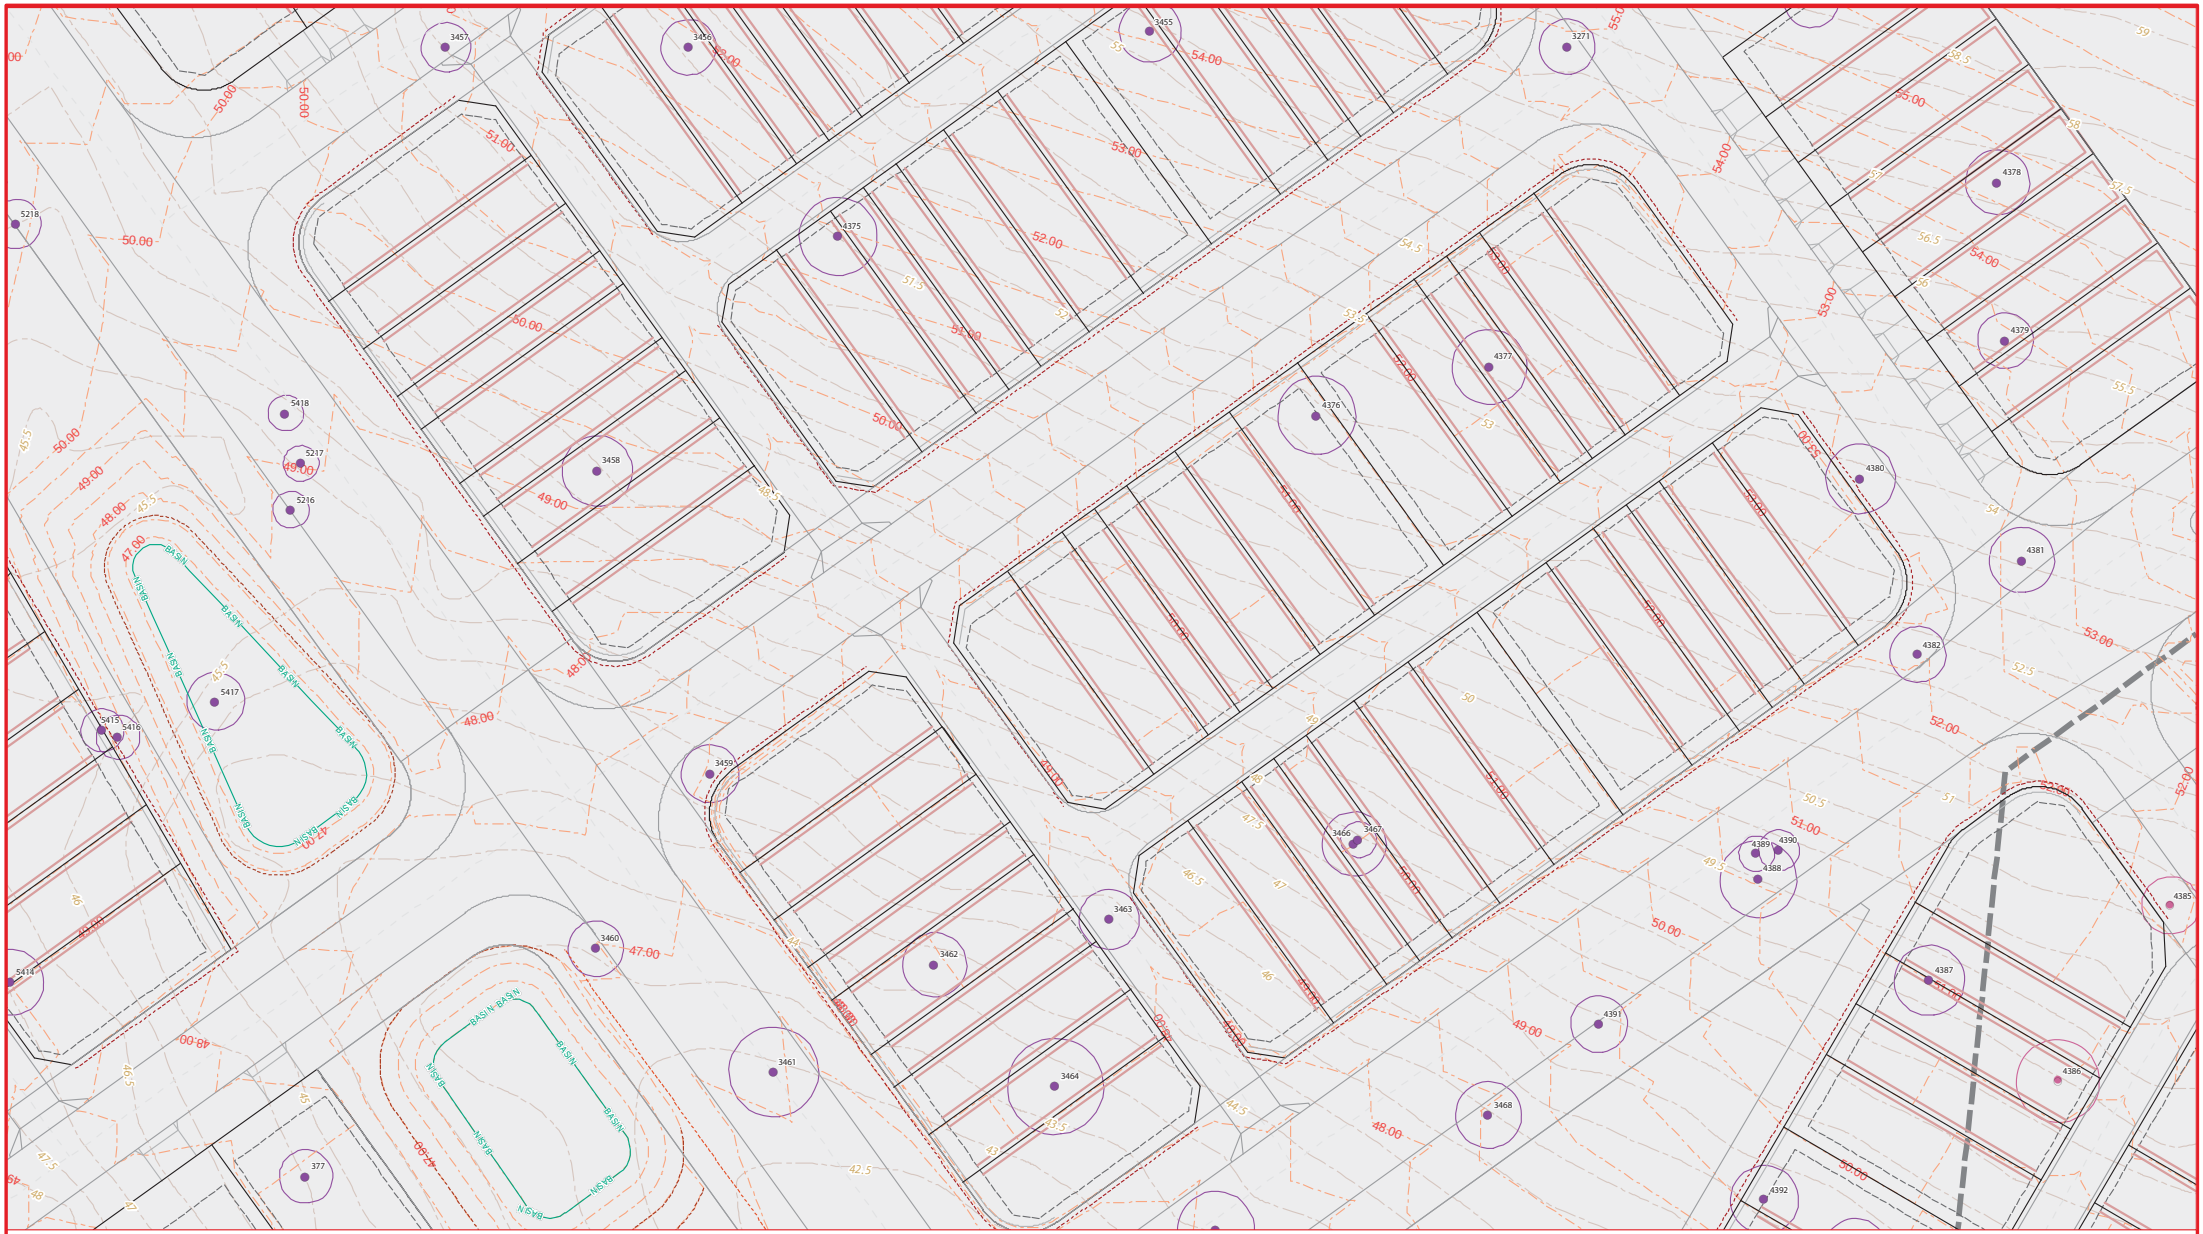

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 31

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 31 BAL Stage 2 VMP E	

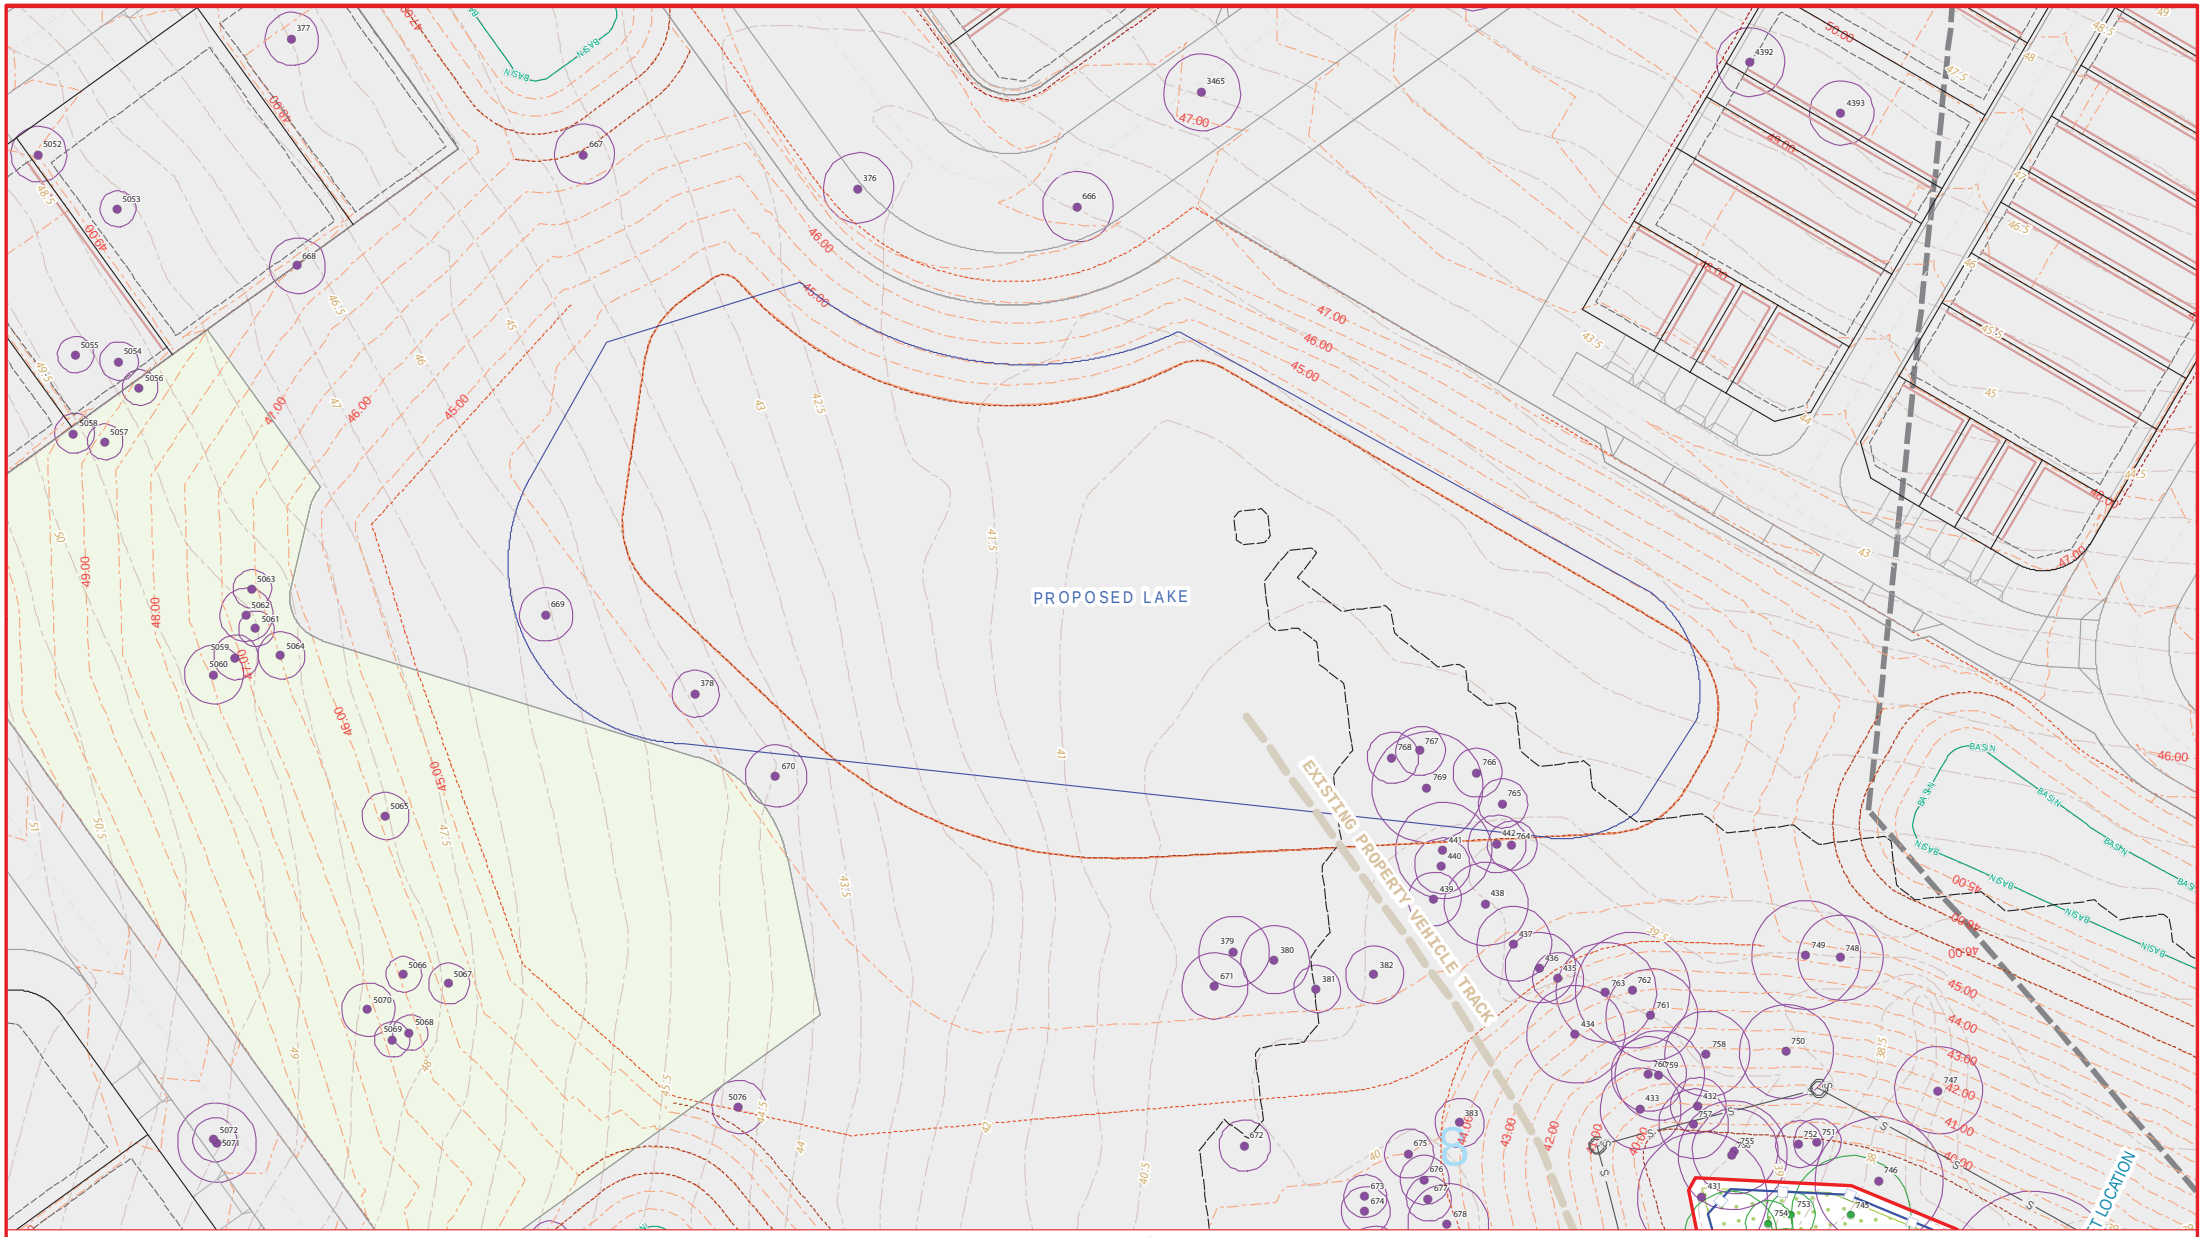

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 32

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 32 BAL Stage 2 VMP E

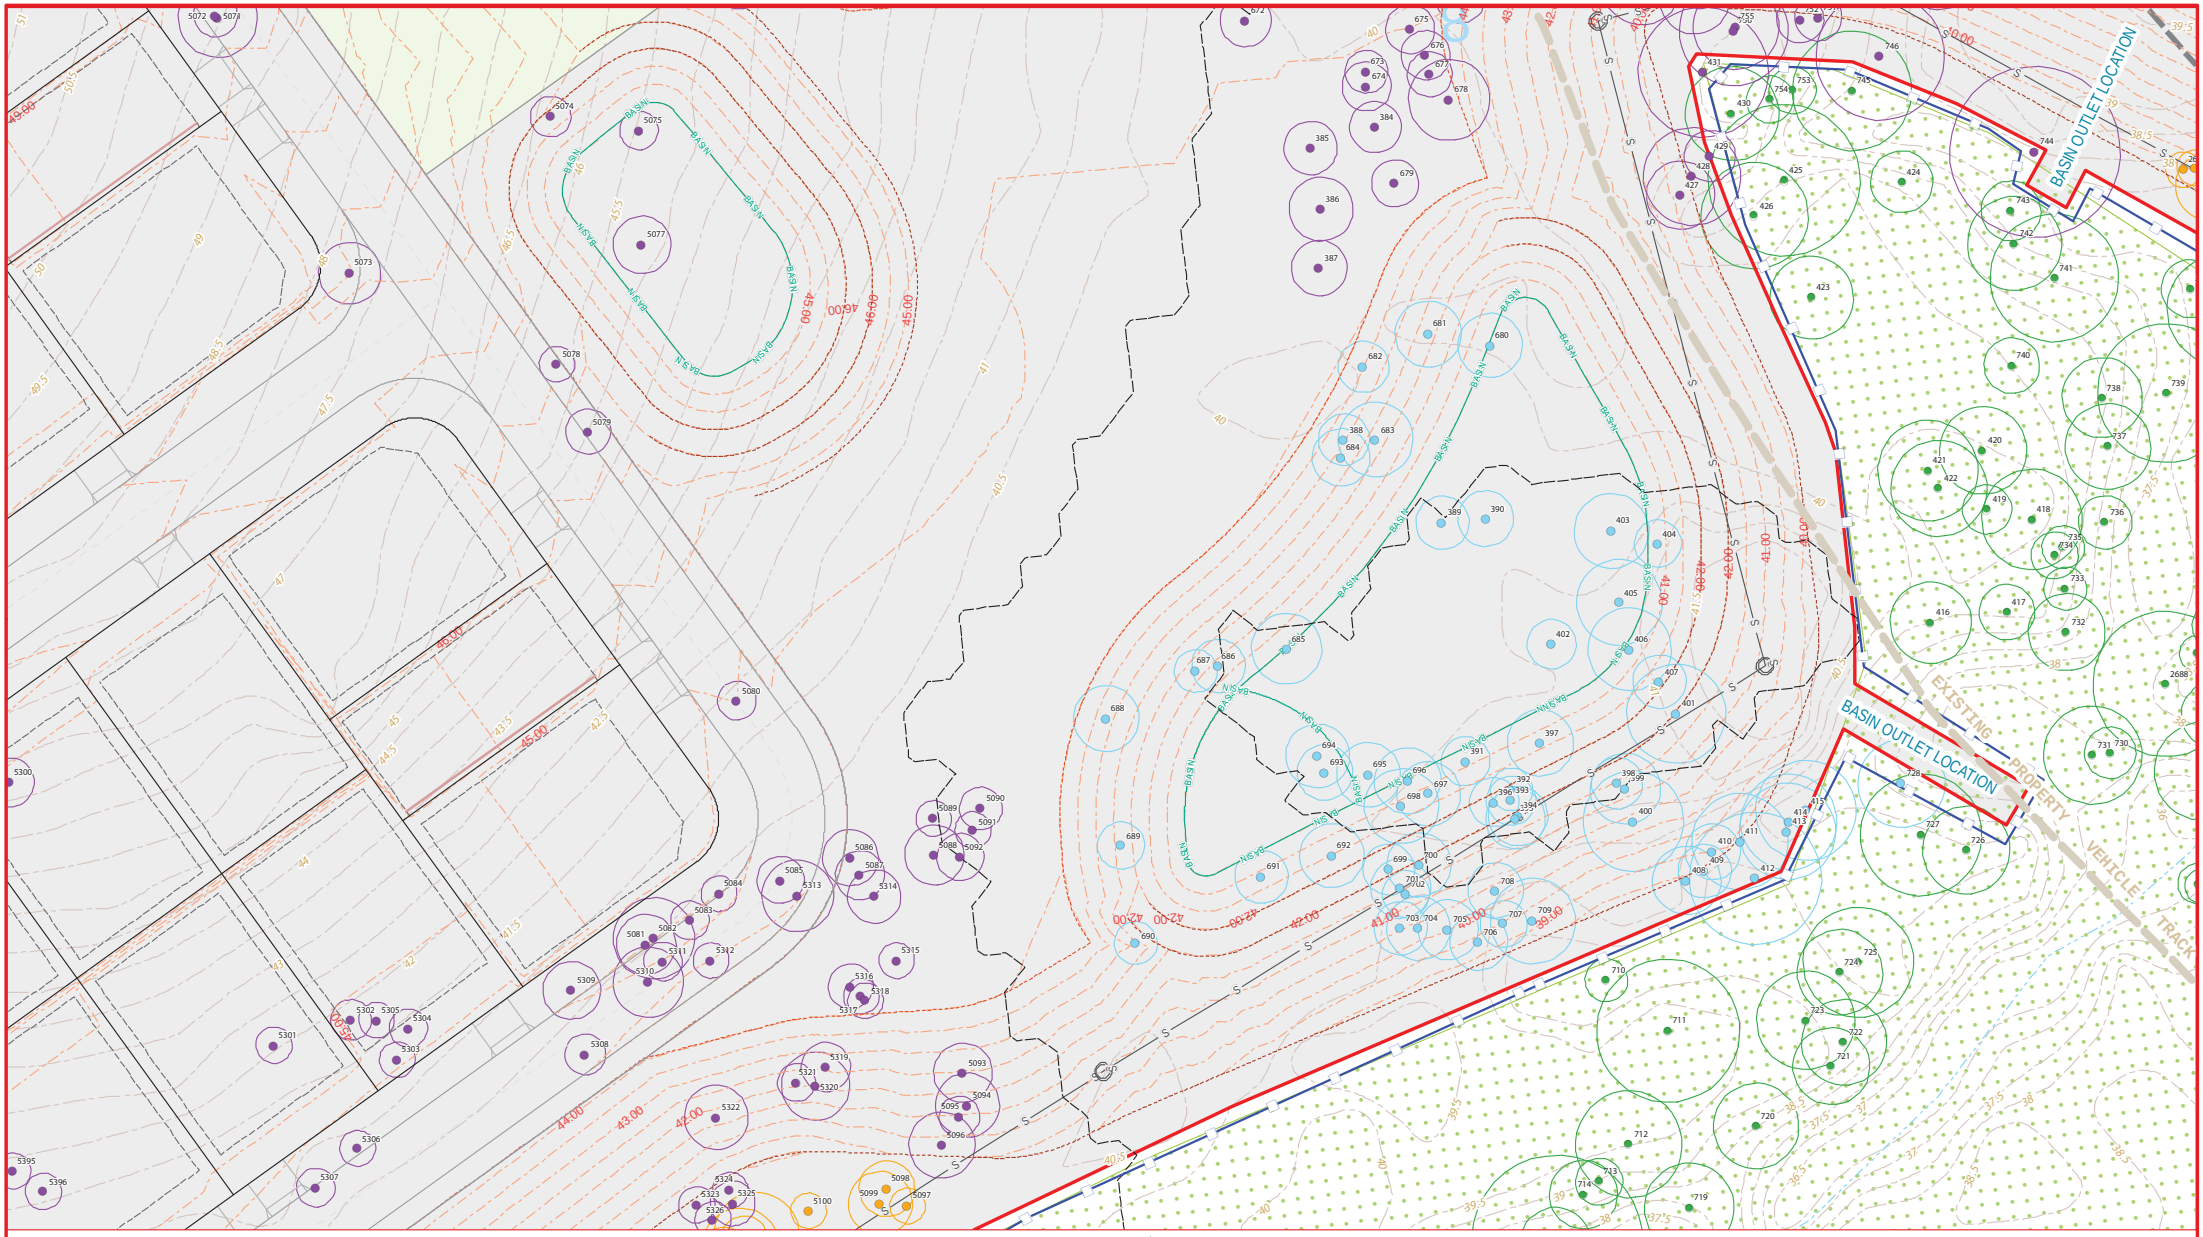

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 33

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 33 BAL Stage 2 VMP E	

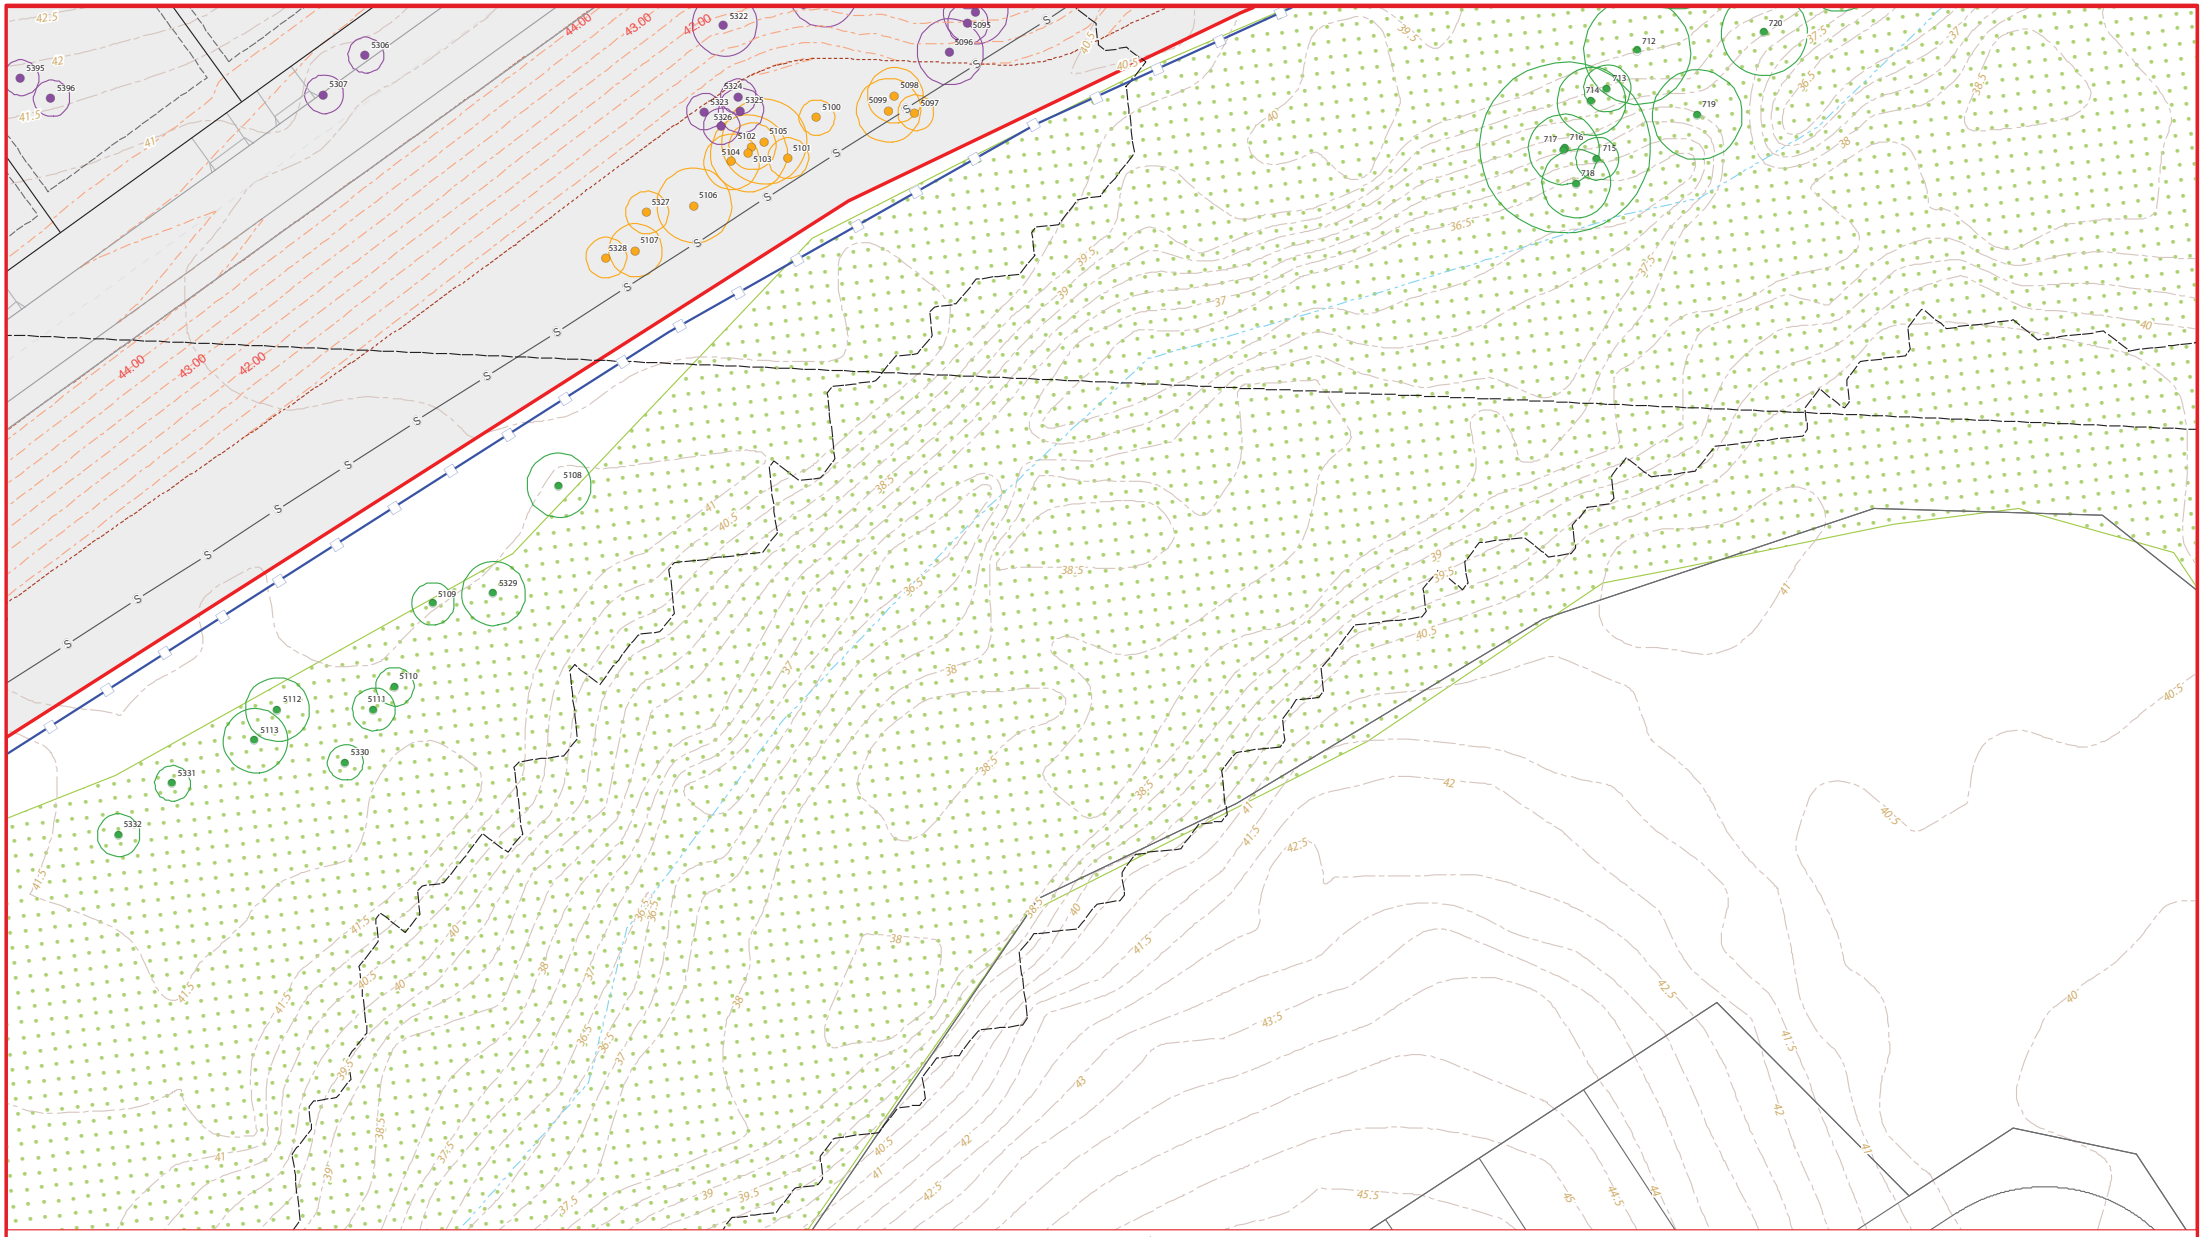

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 34

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 34 BAL Stage 2 VMP E	

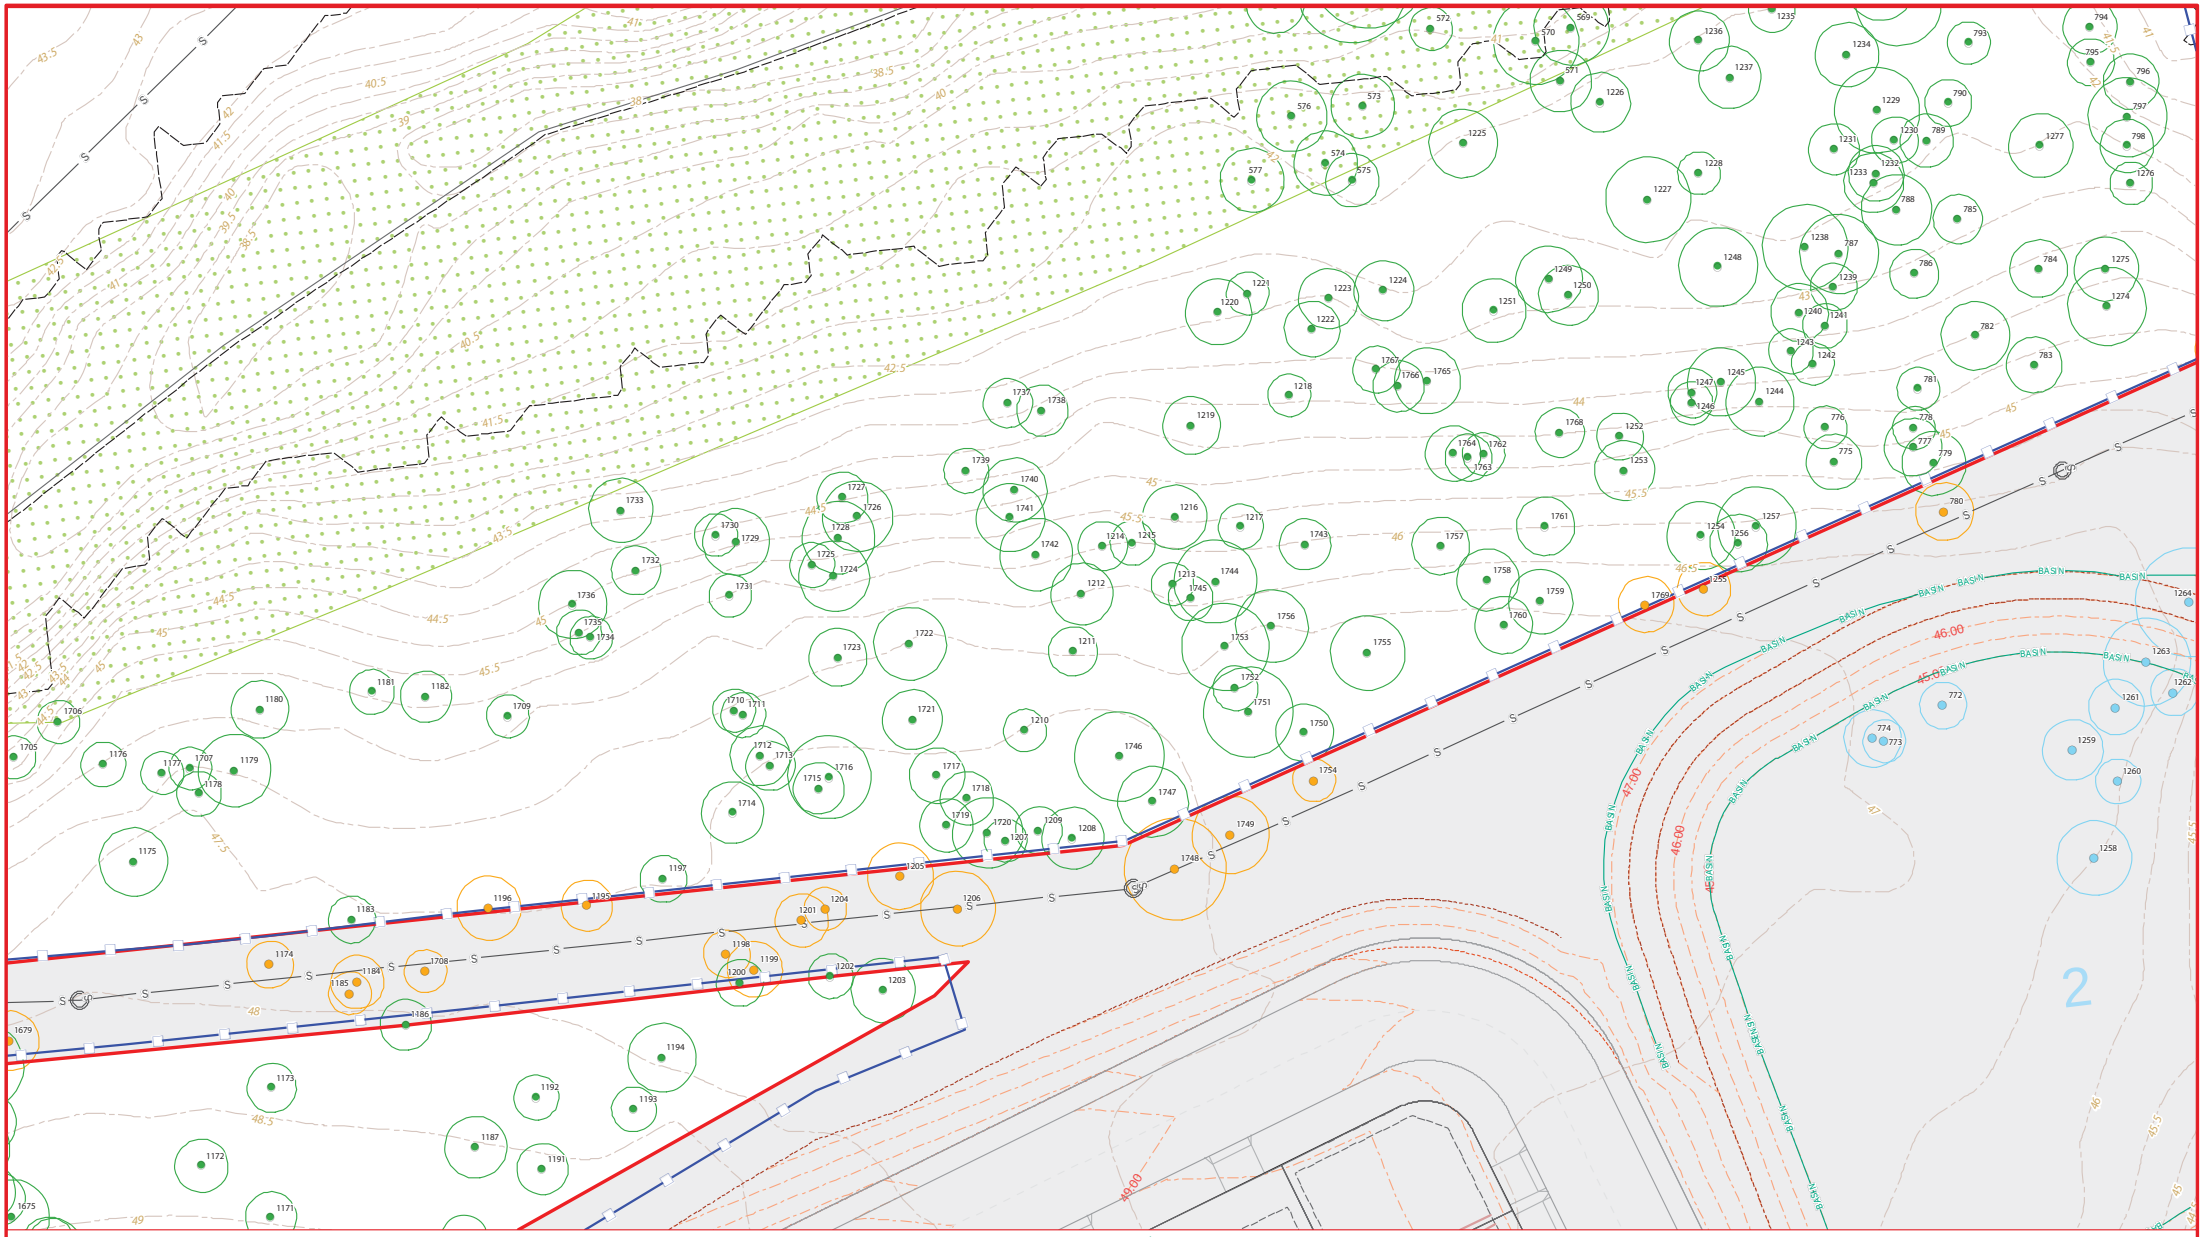

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 35

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 35 BAL Stage 2 VMP E

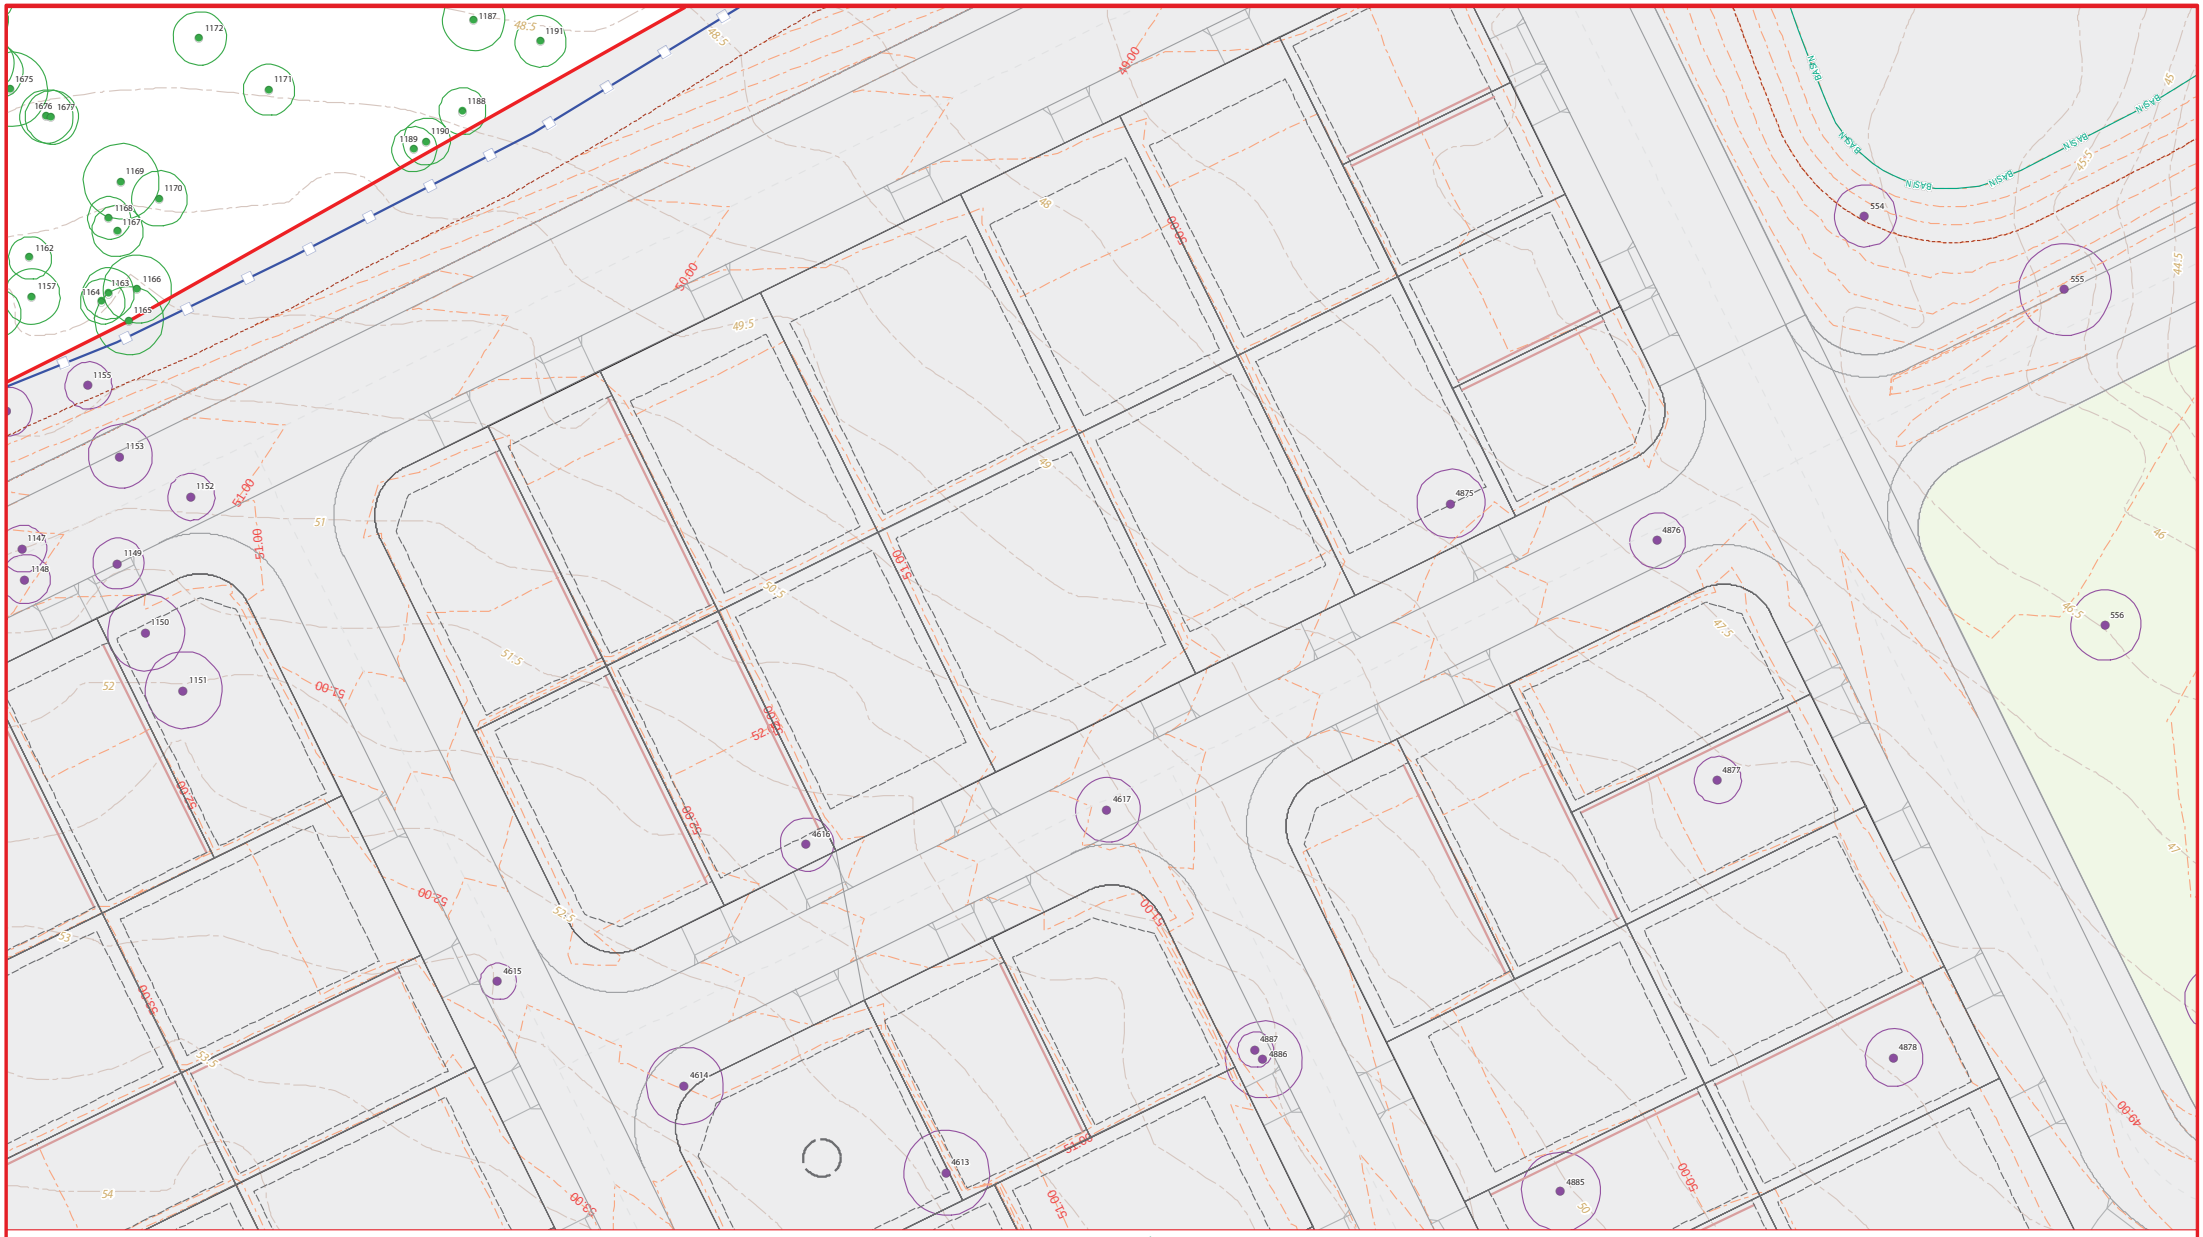

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of the Stage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 36

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 36 BAL Stage 2 VMP E	

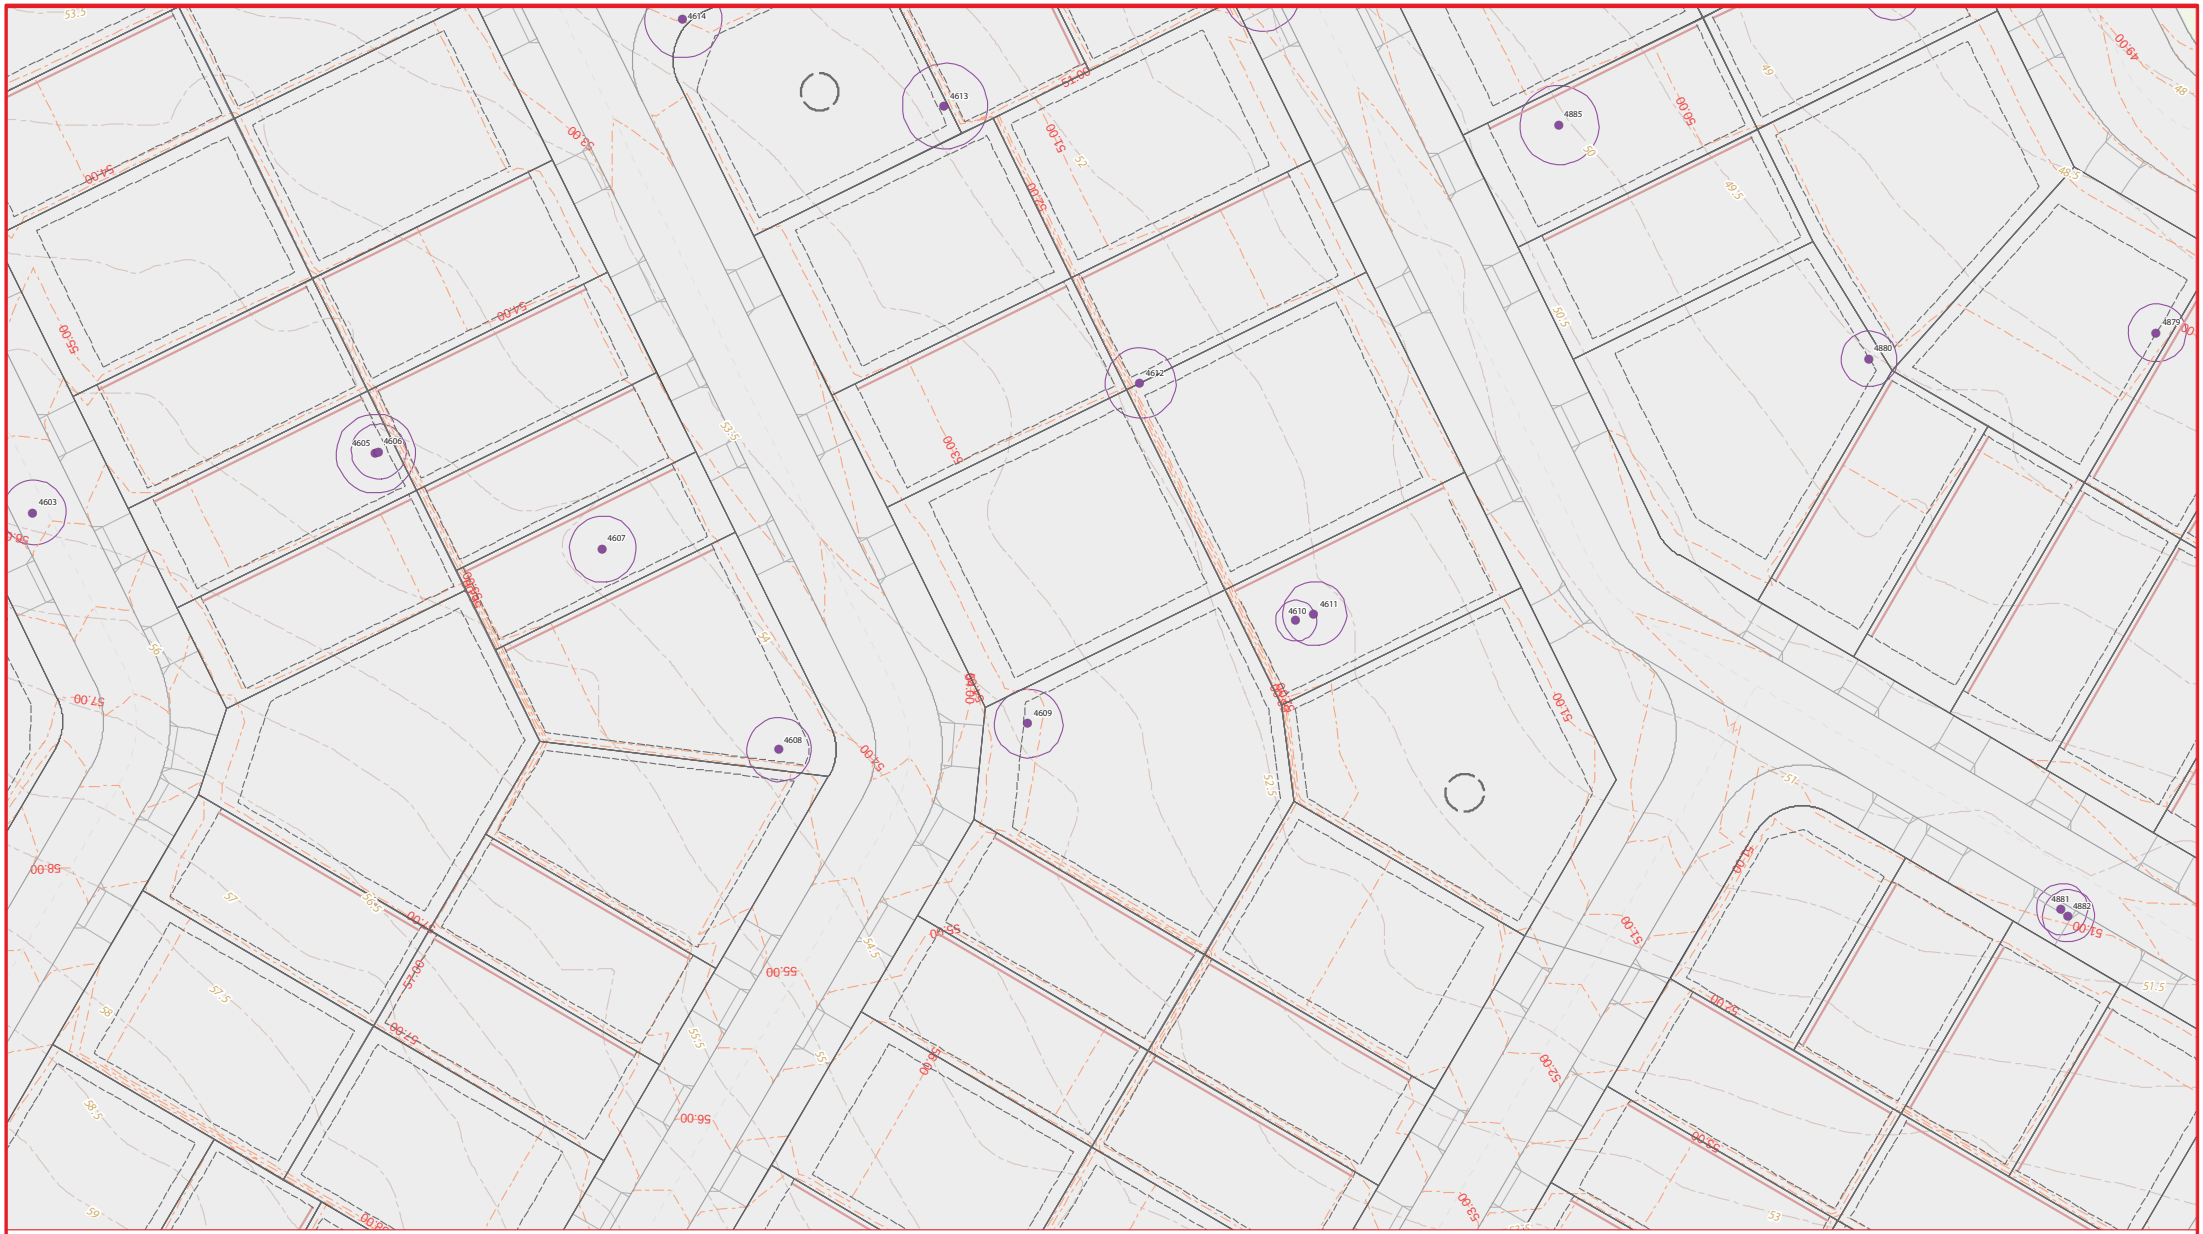

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 37

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 37 BAL Stage 2 VMP E

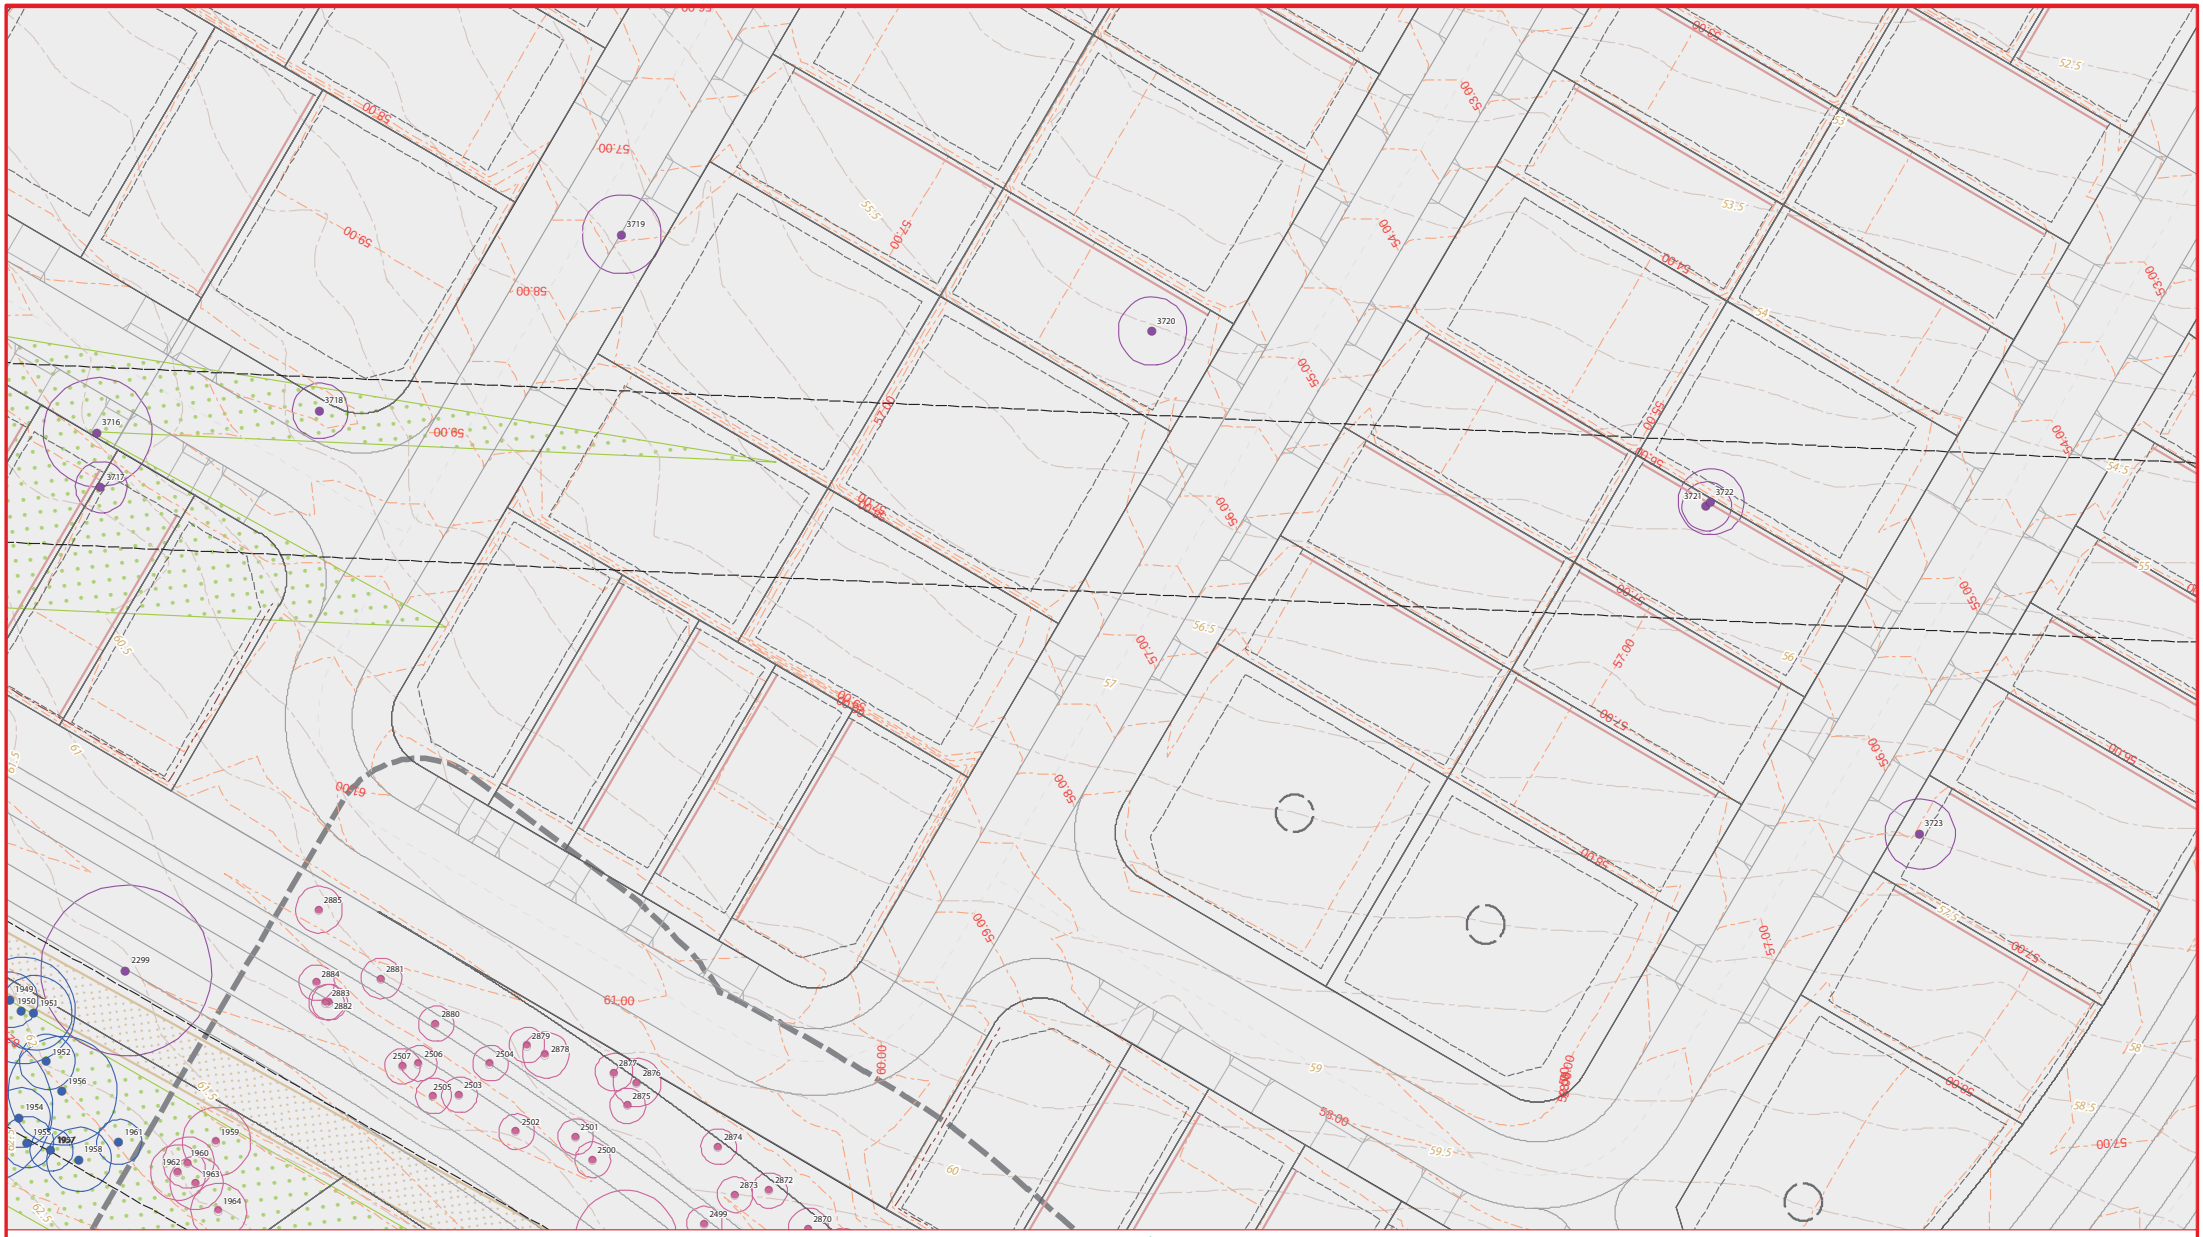

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 38

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 38 BAL Stage 2 VMP E	

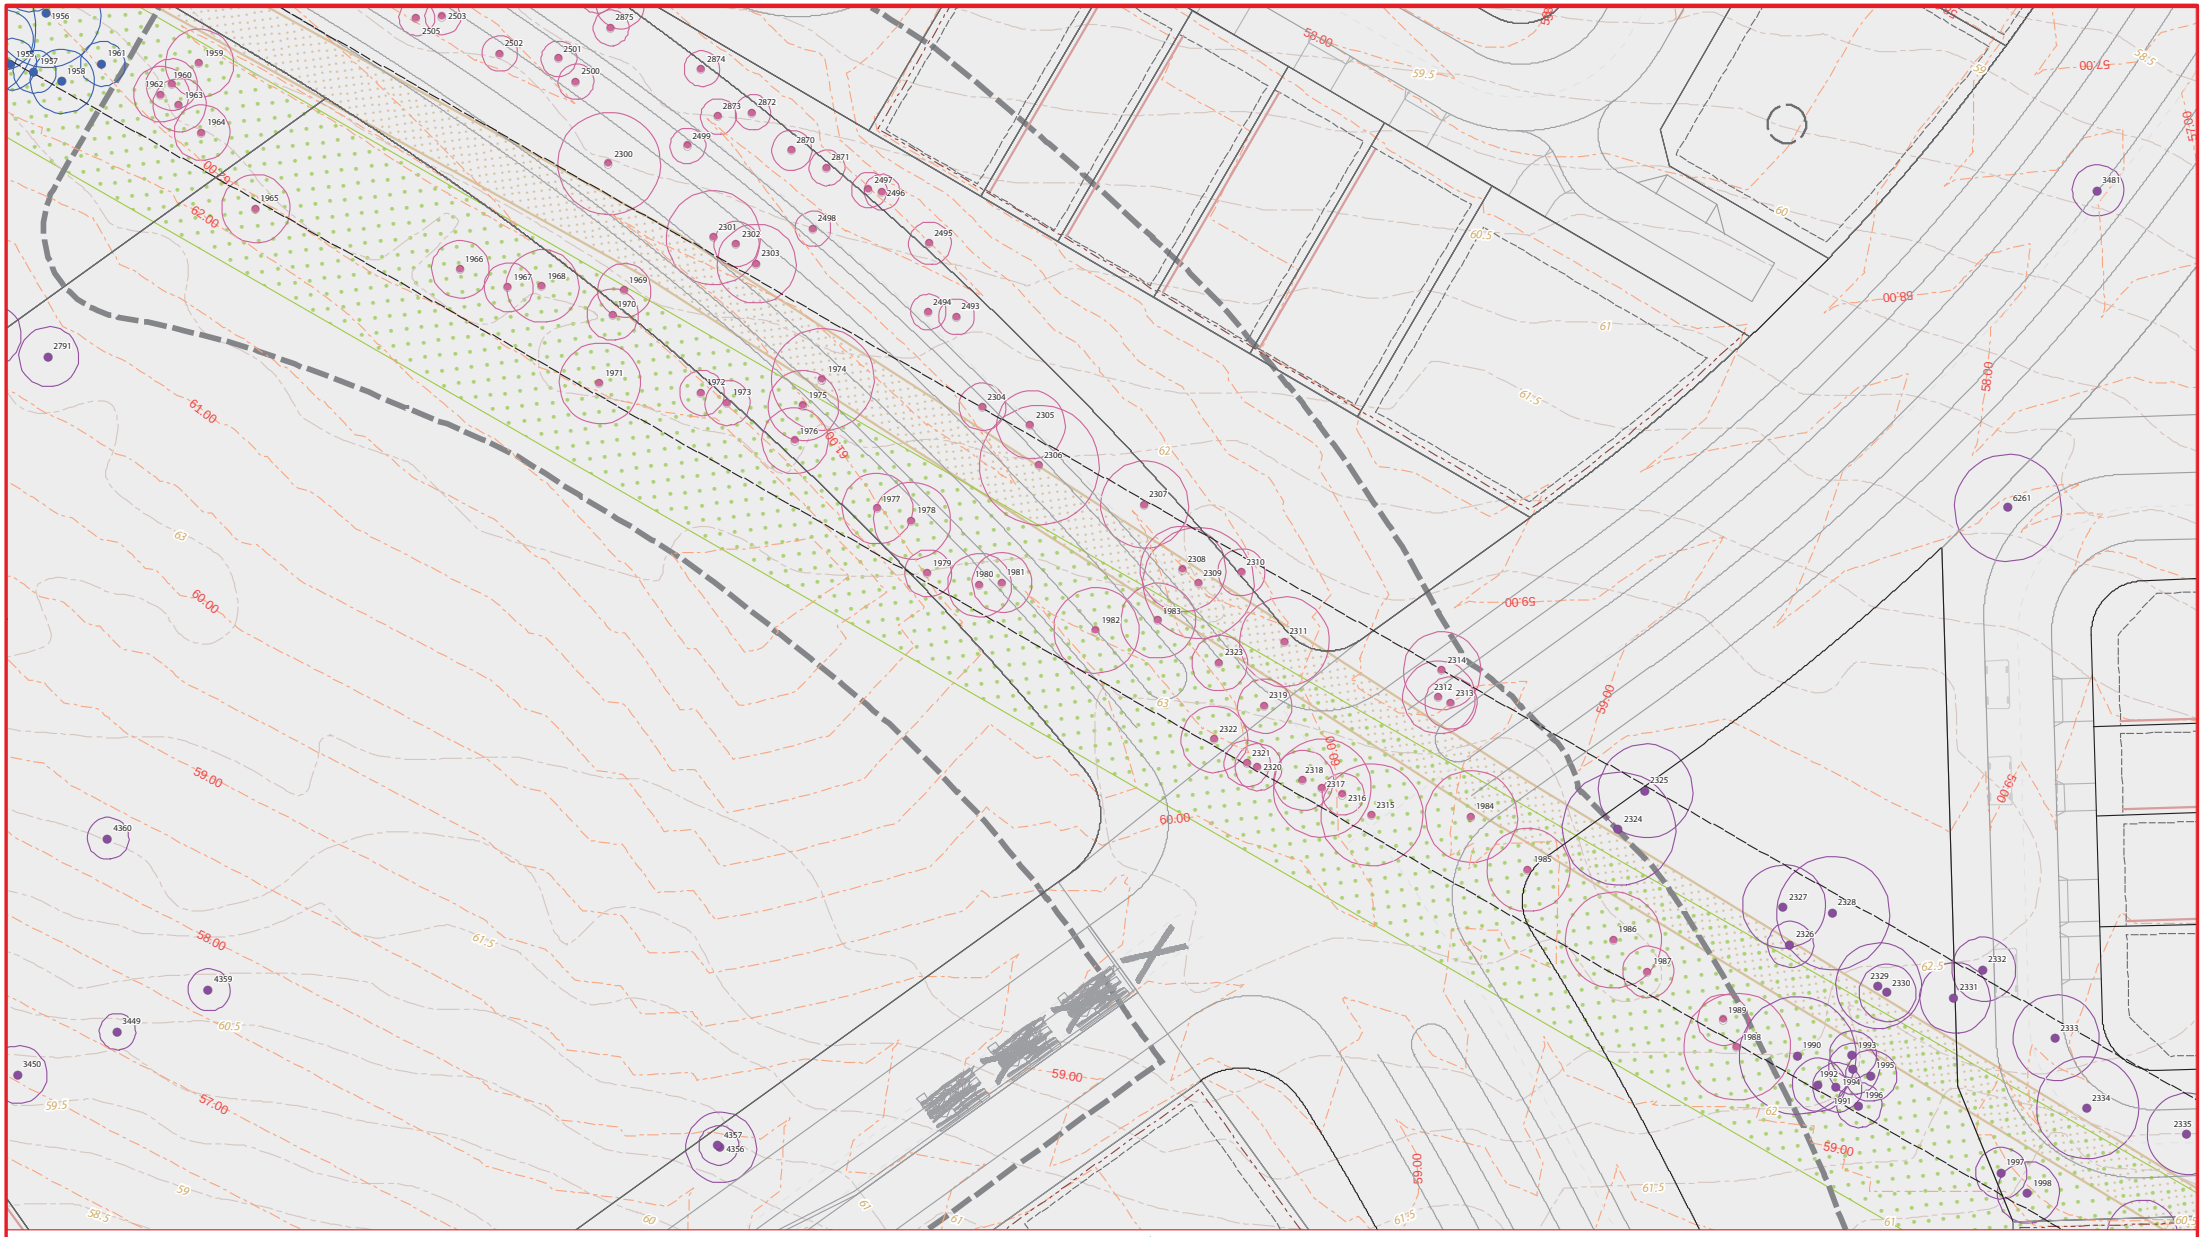

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 39

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 39 BAL Stage 2 VMP E	

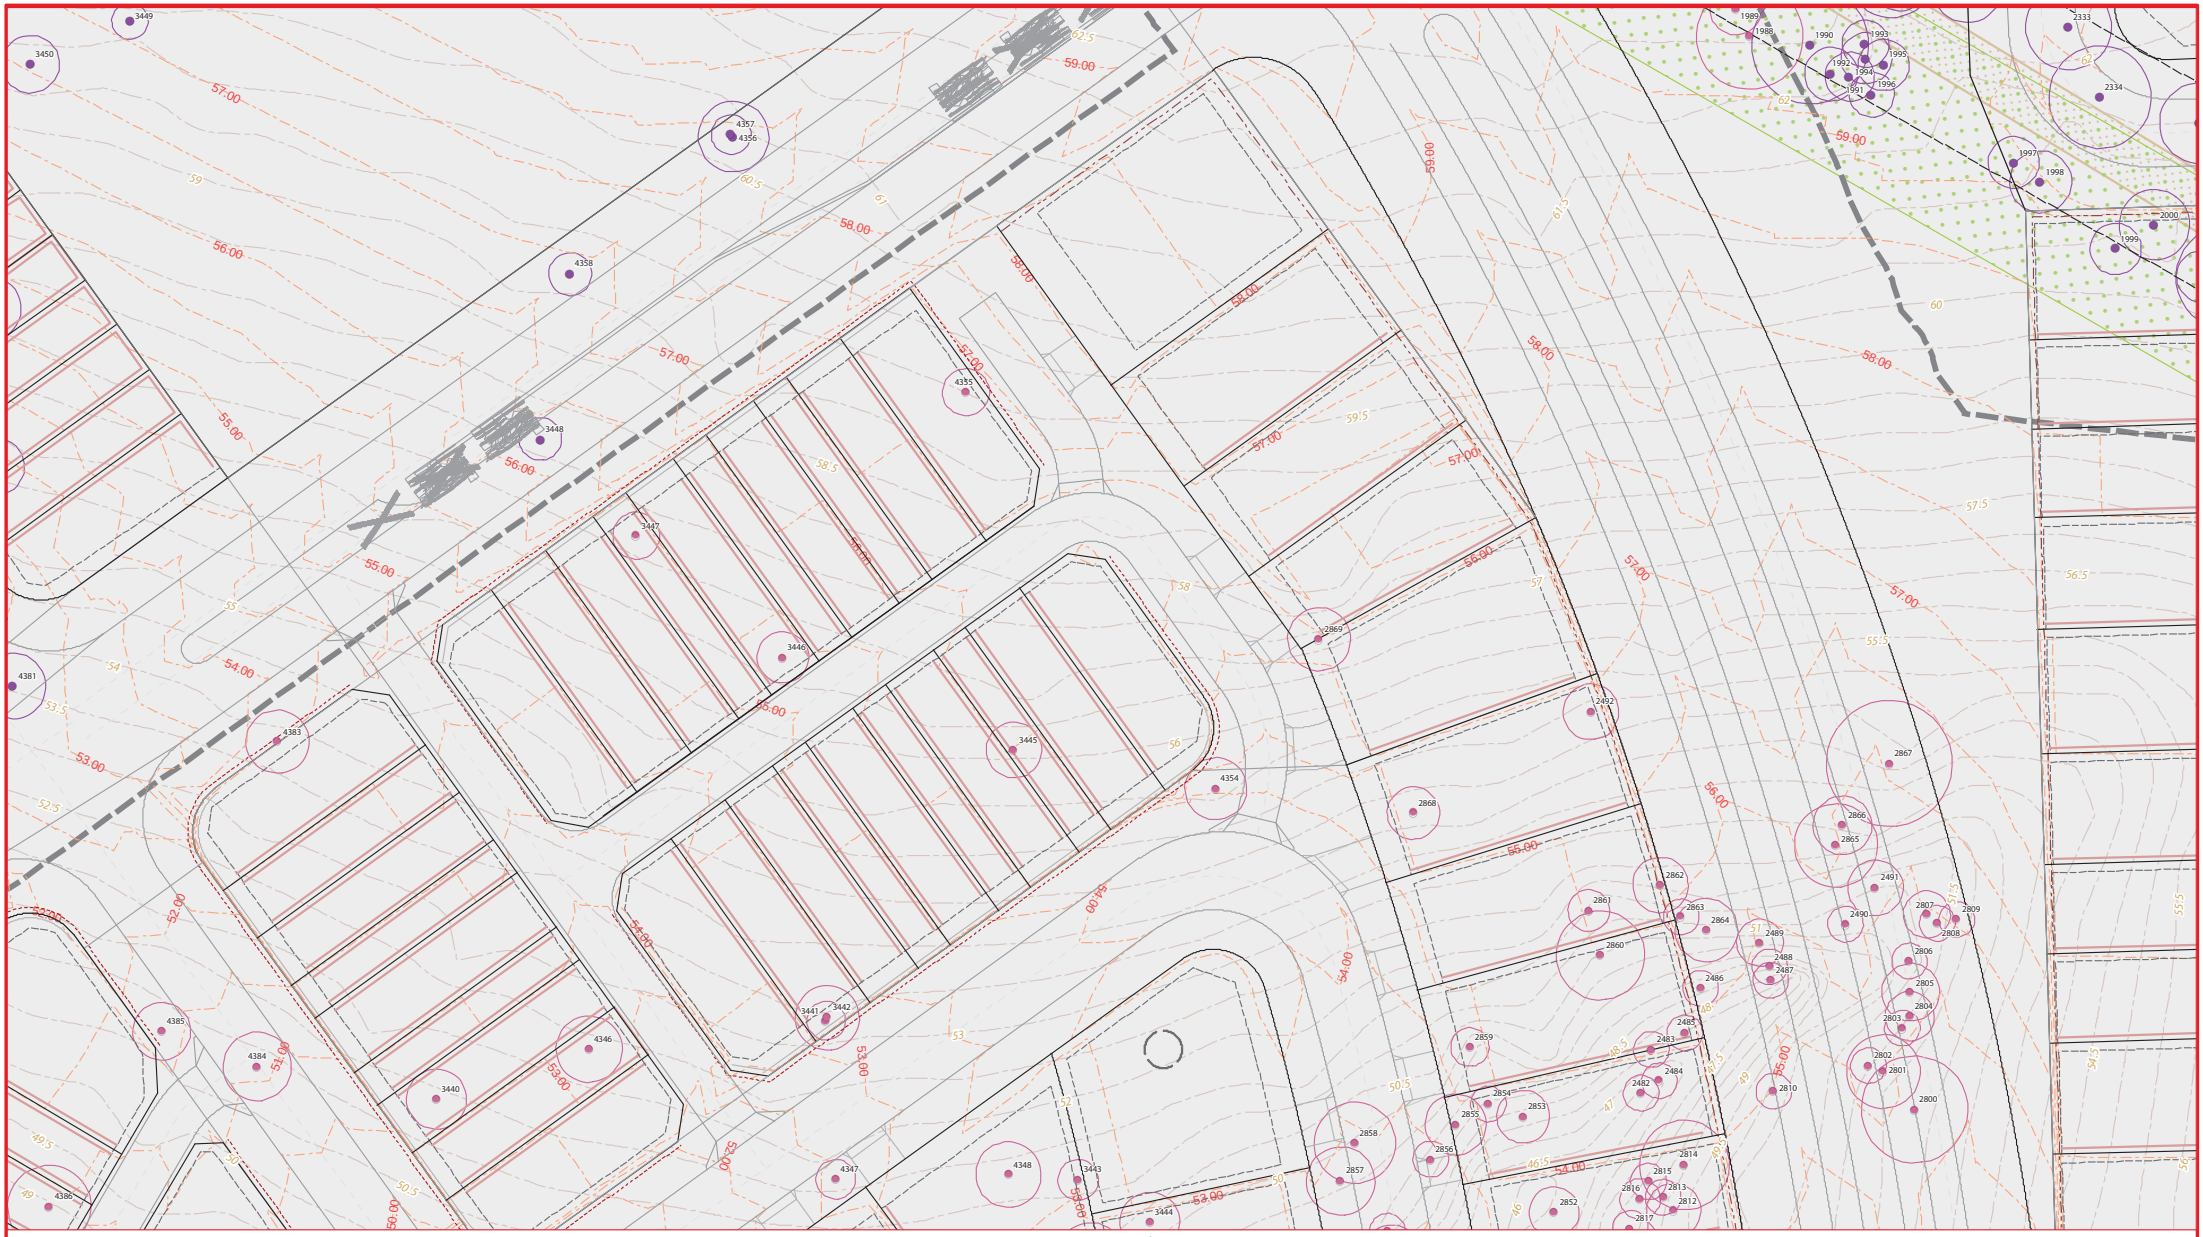

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 40

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 40 BAL Stage 2 VMP E

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 41

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 41 BAL Stage 2 VMP E	

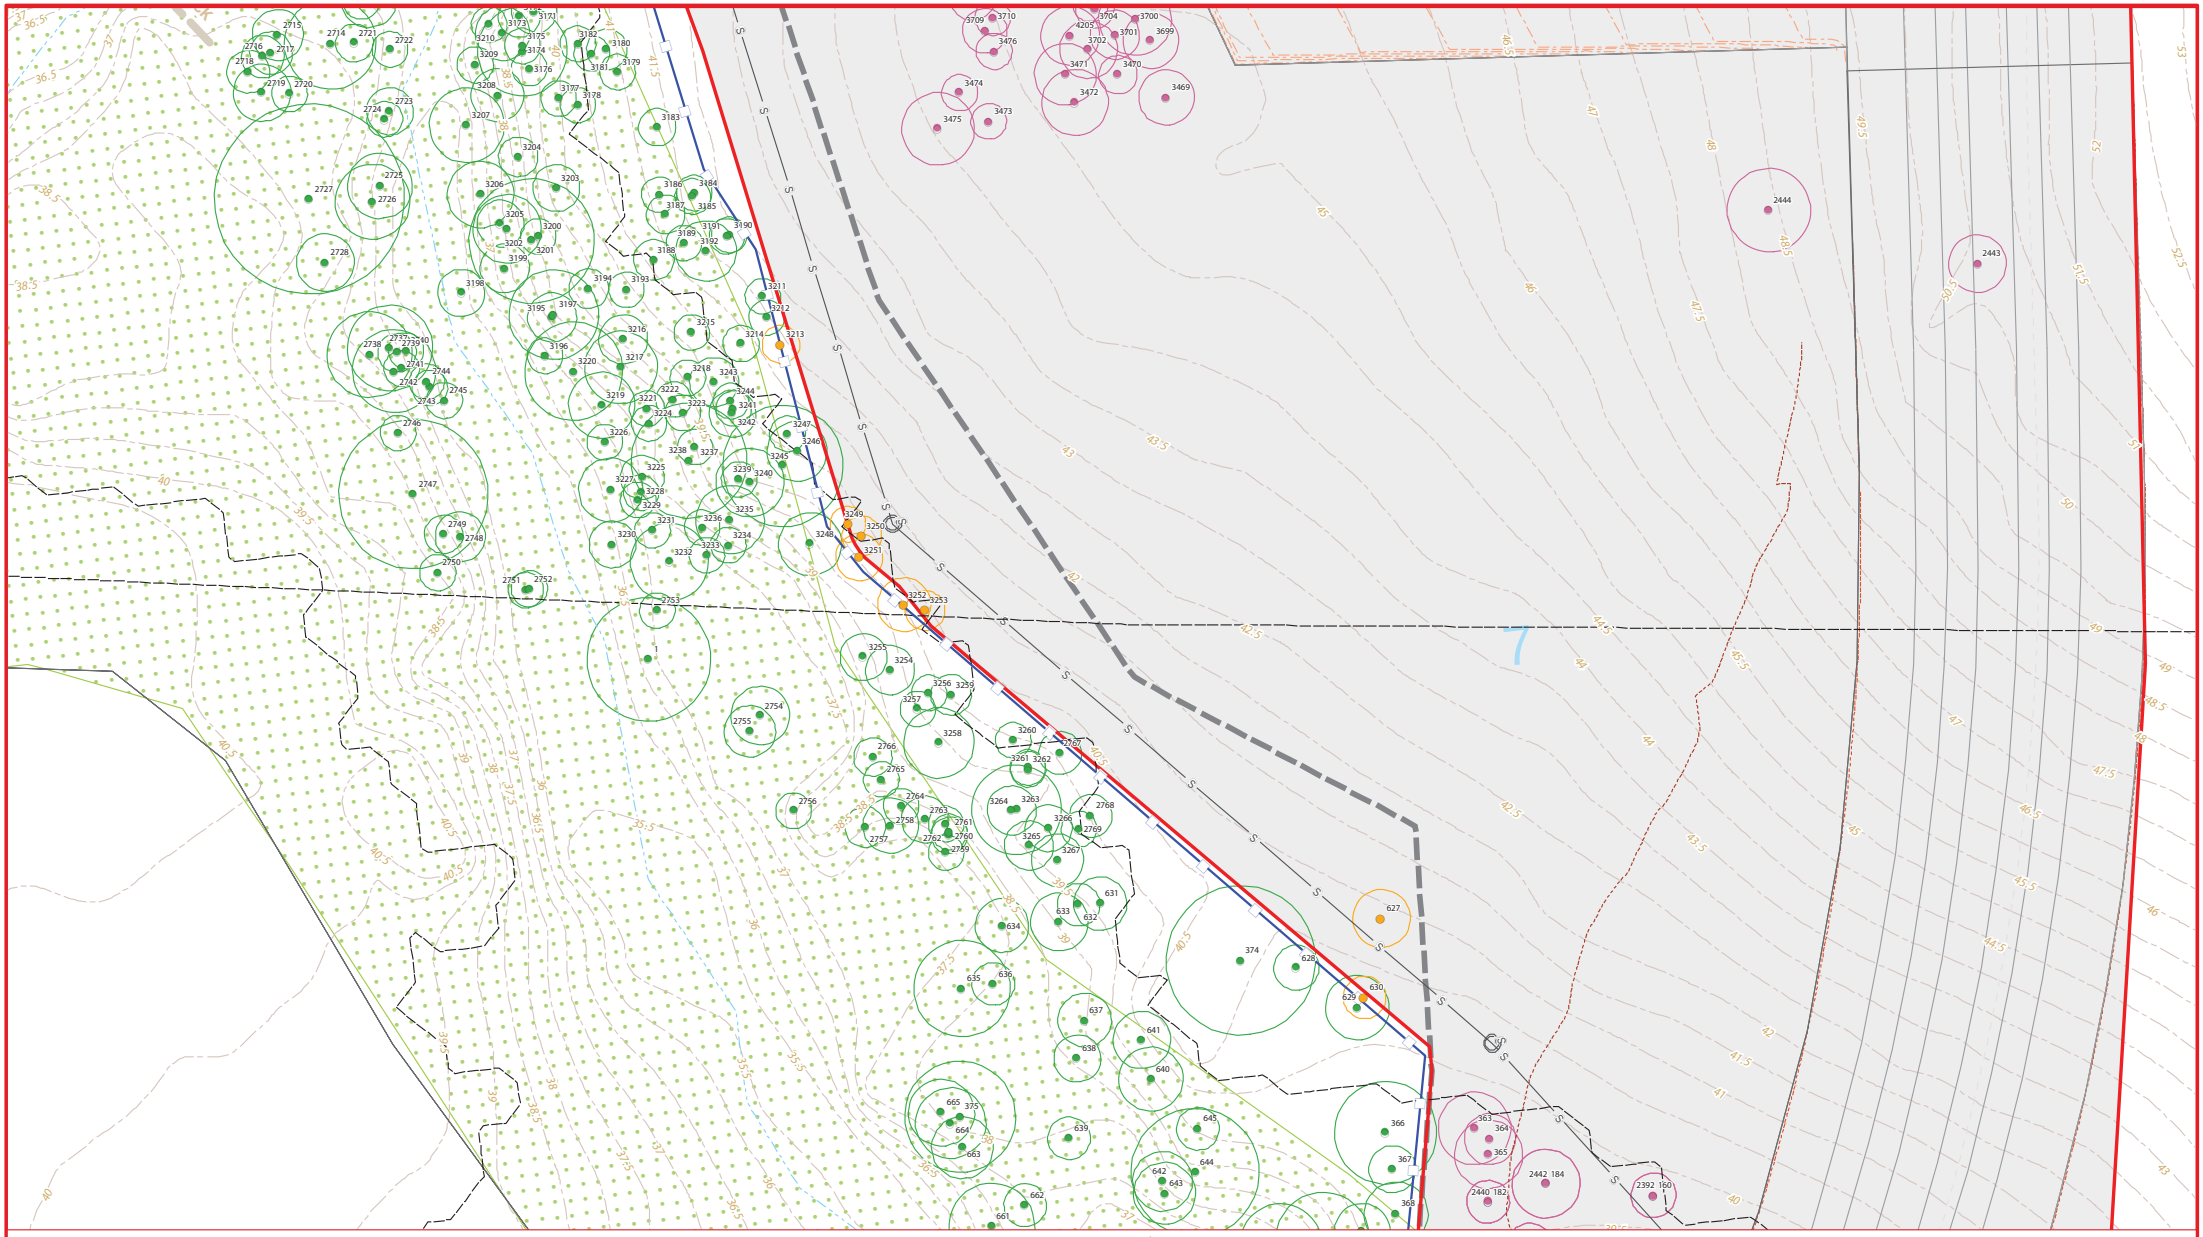

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 42

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 42 BAL Stage 2 VMP E	

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 43

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 43 BAL Stage 2 VMP E	

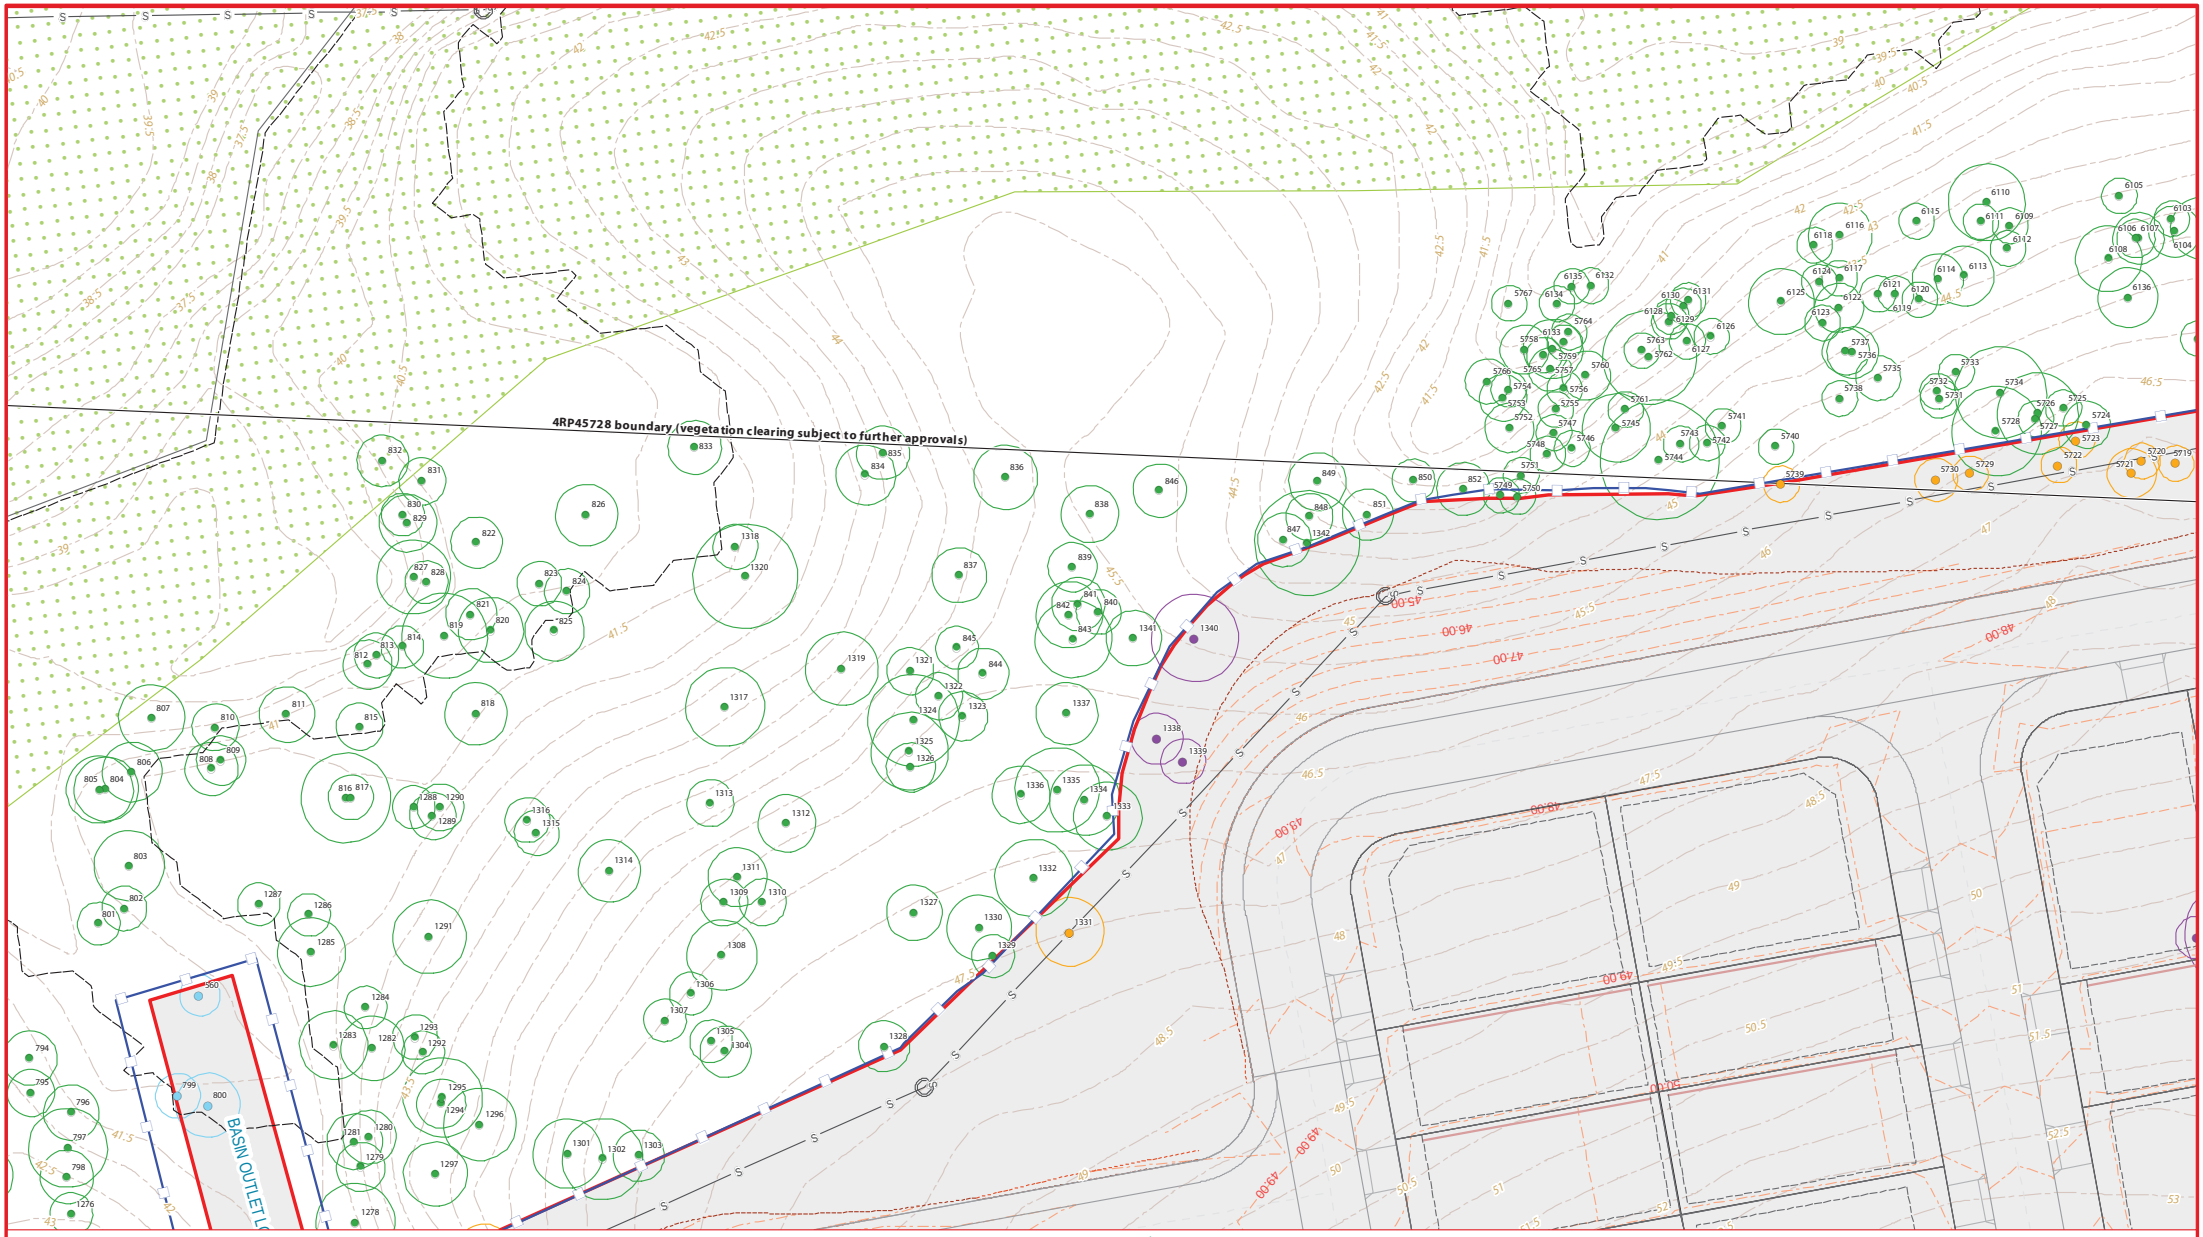

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 44

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 44 BAL Stage 2 VMP E

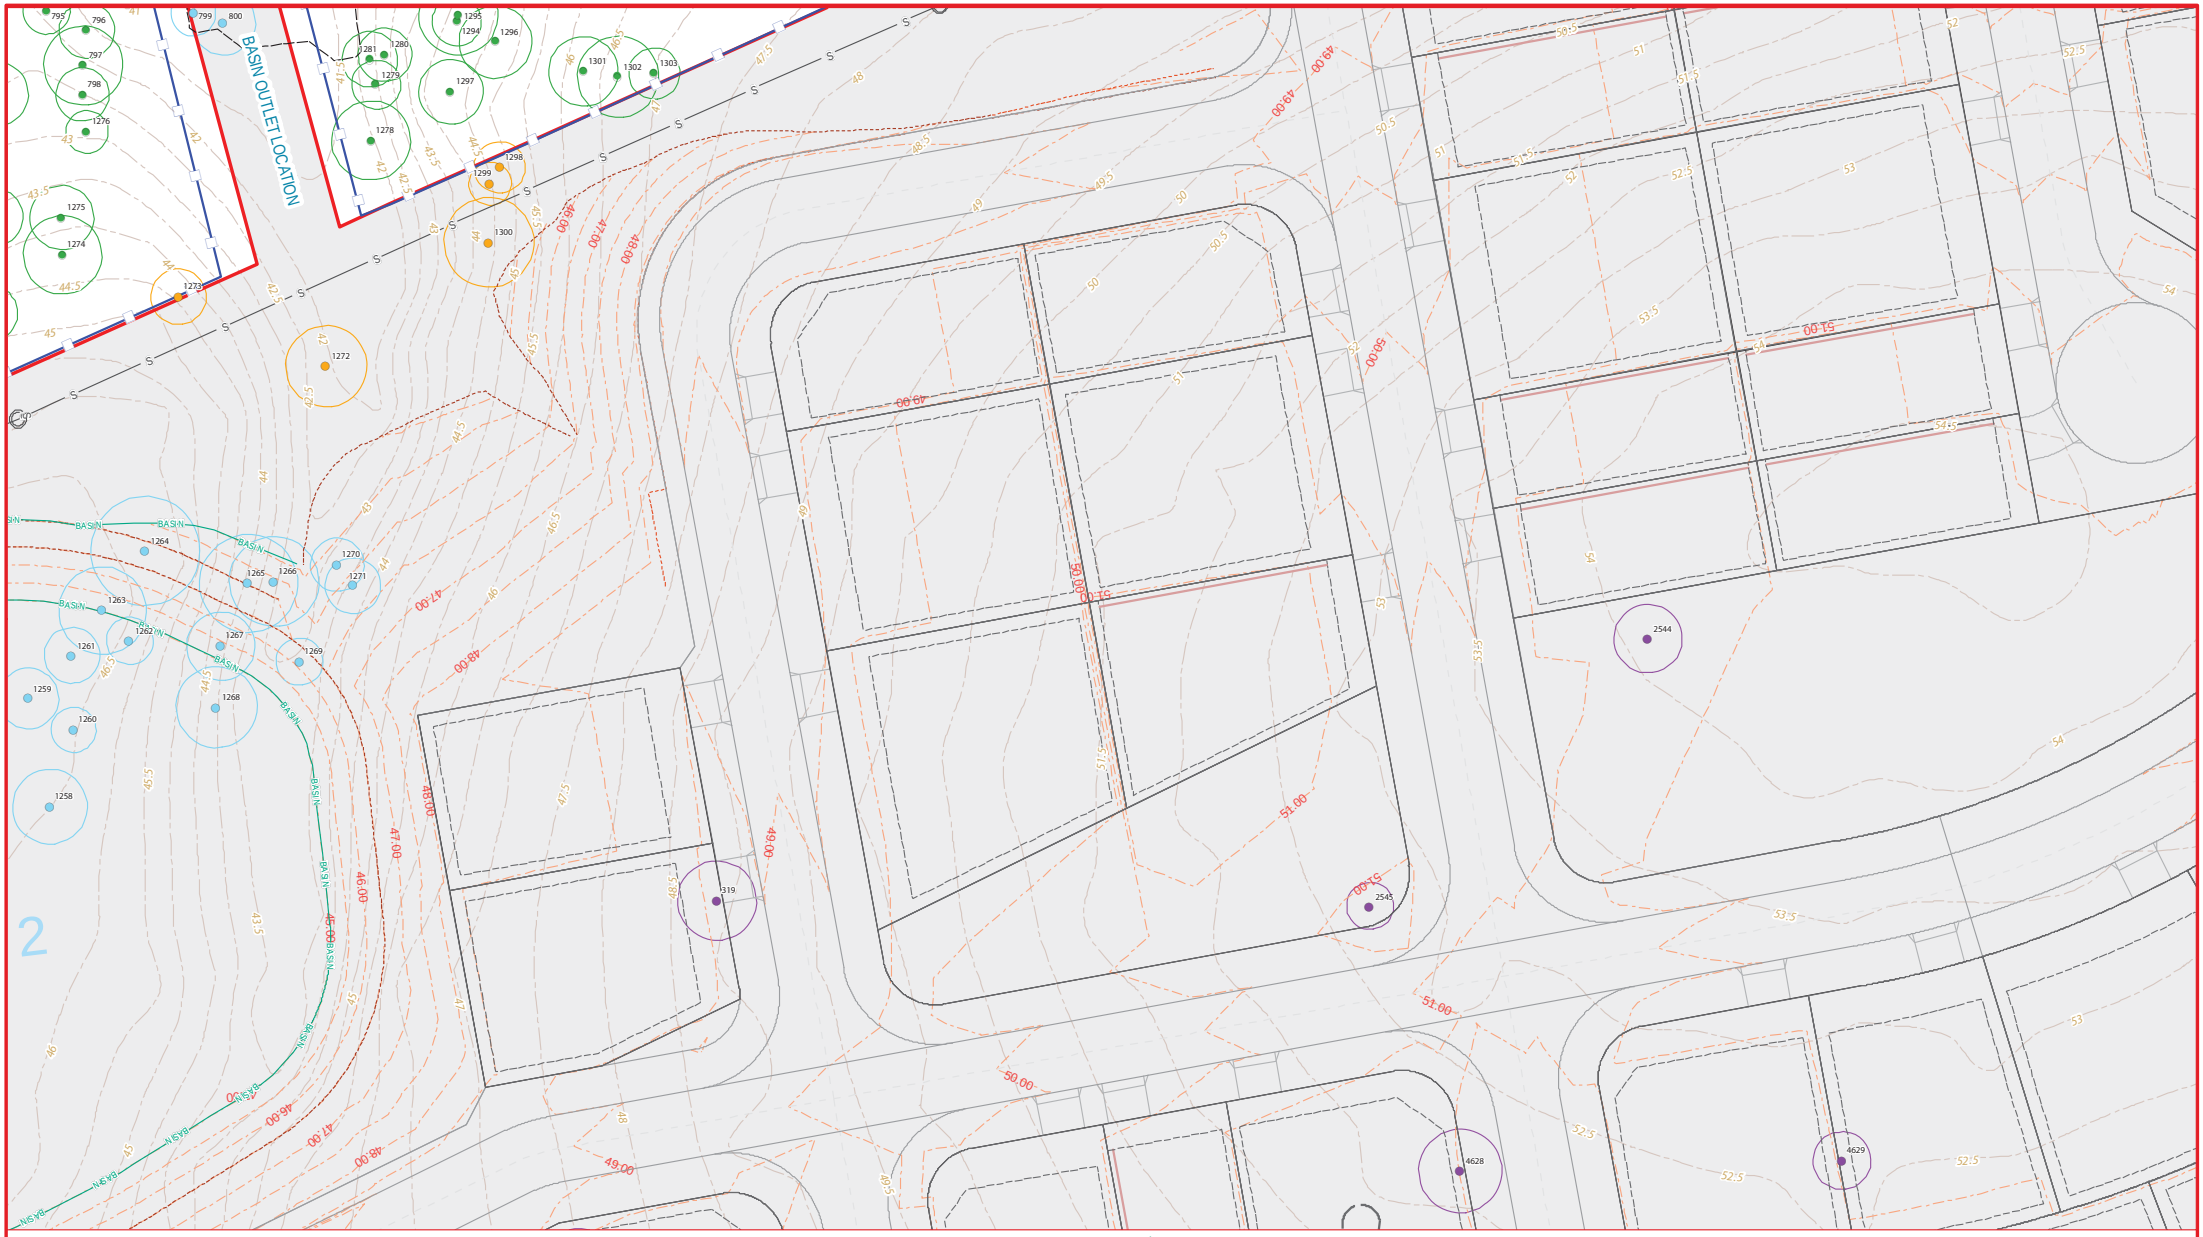

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 45

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 45 BAL Stage 2 VMP E	

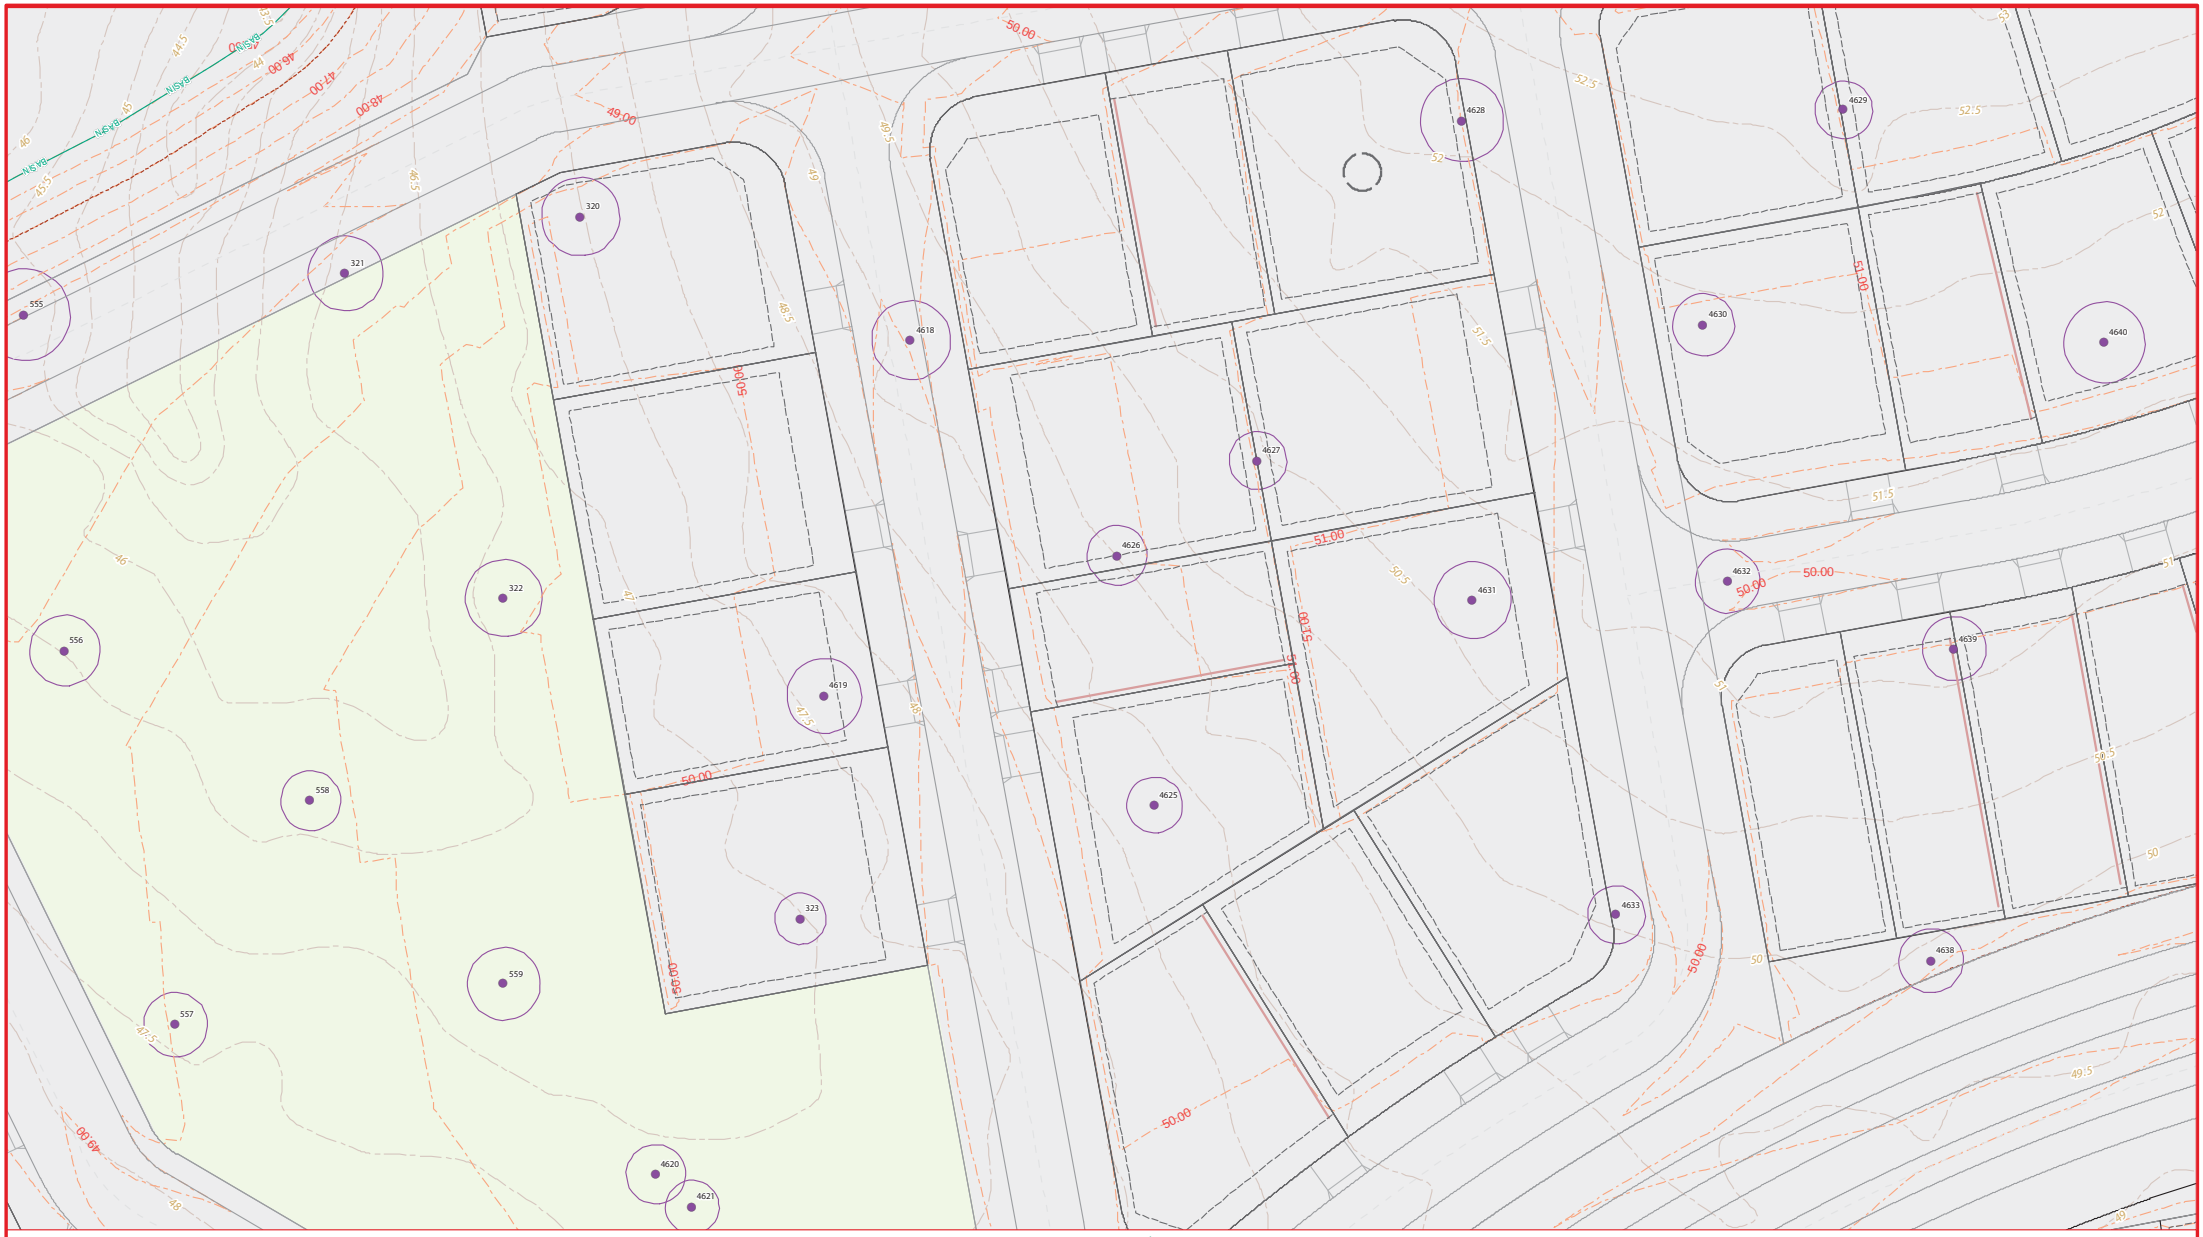

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 46

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 46 BAL Stage 2 VMP E	

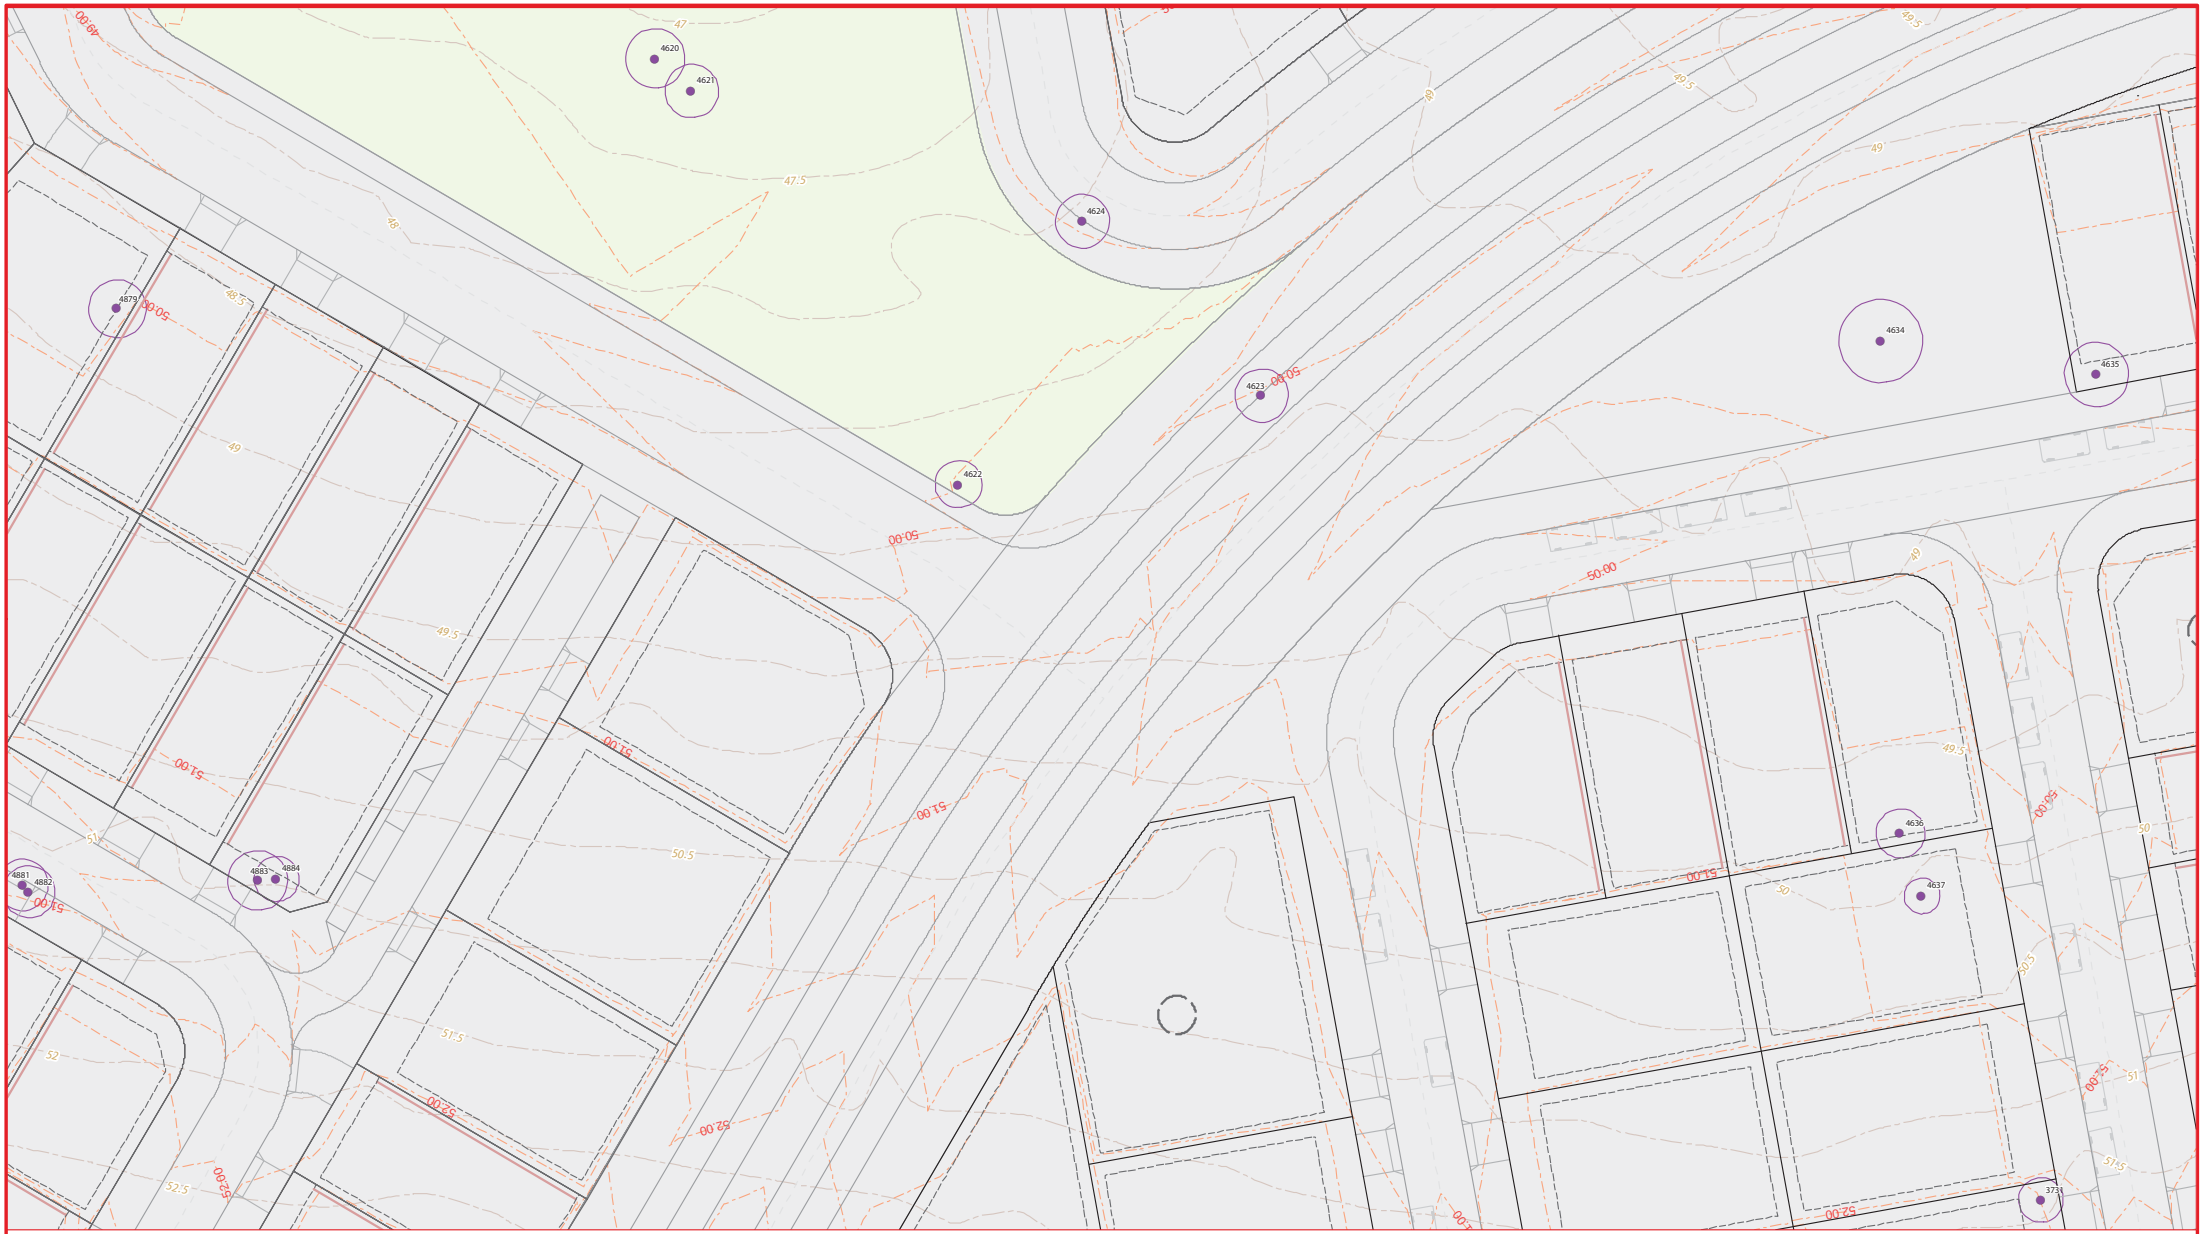

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 47

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 47 BAL Stage 2 VMP E

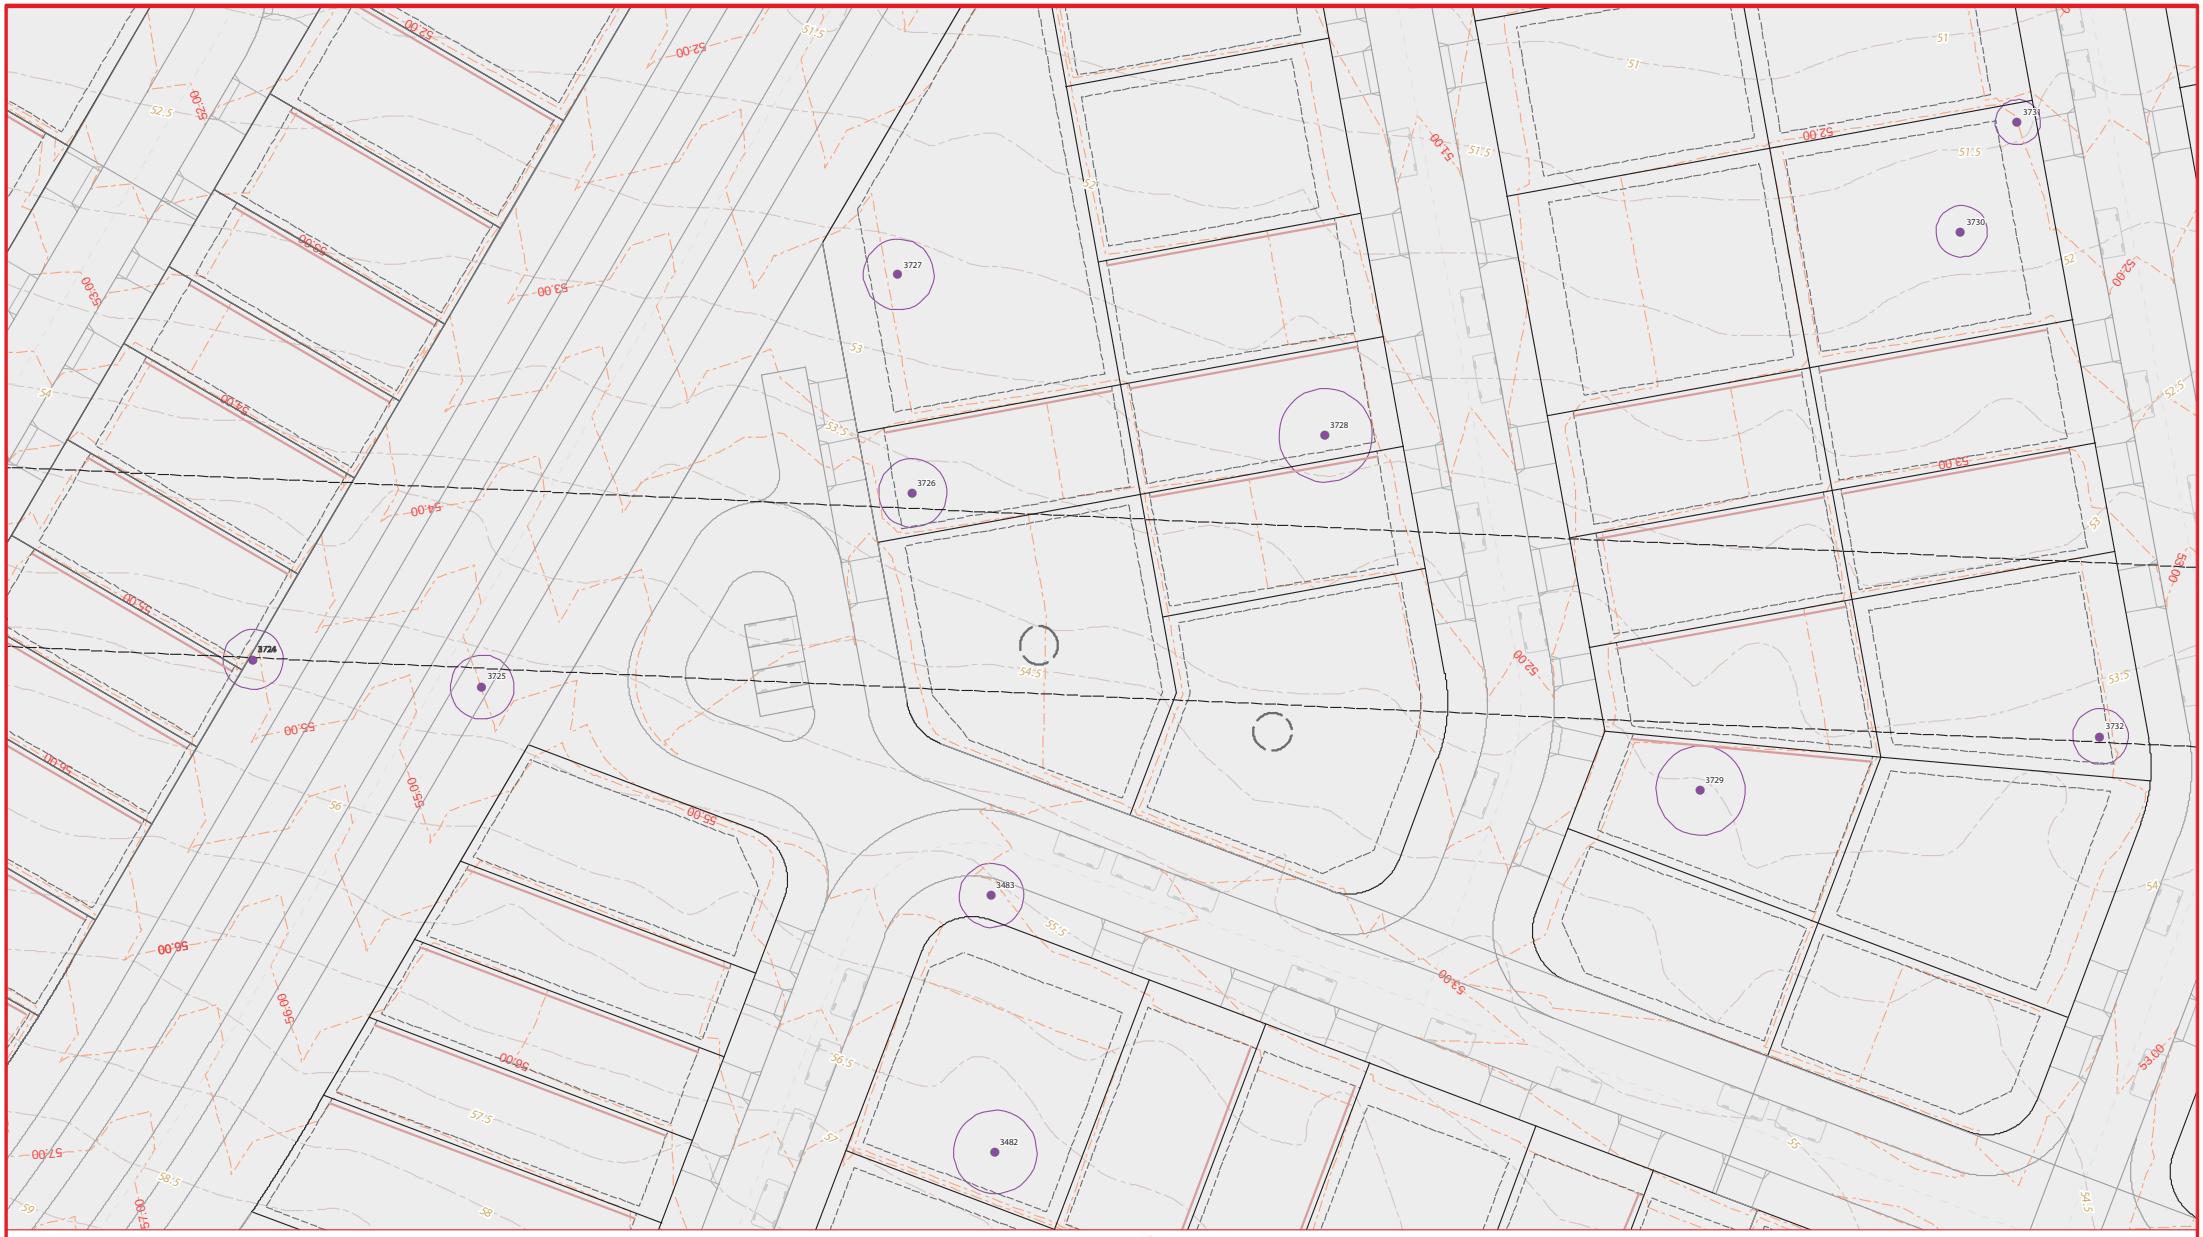

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 48

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 48 BAL Stage 2 VMP E	

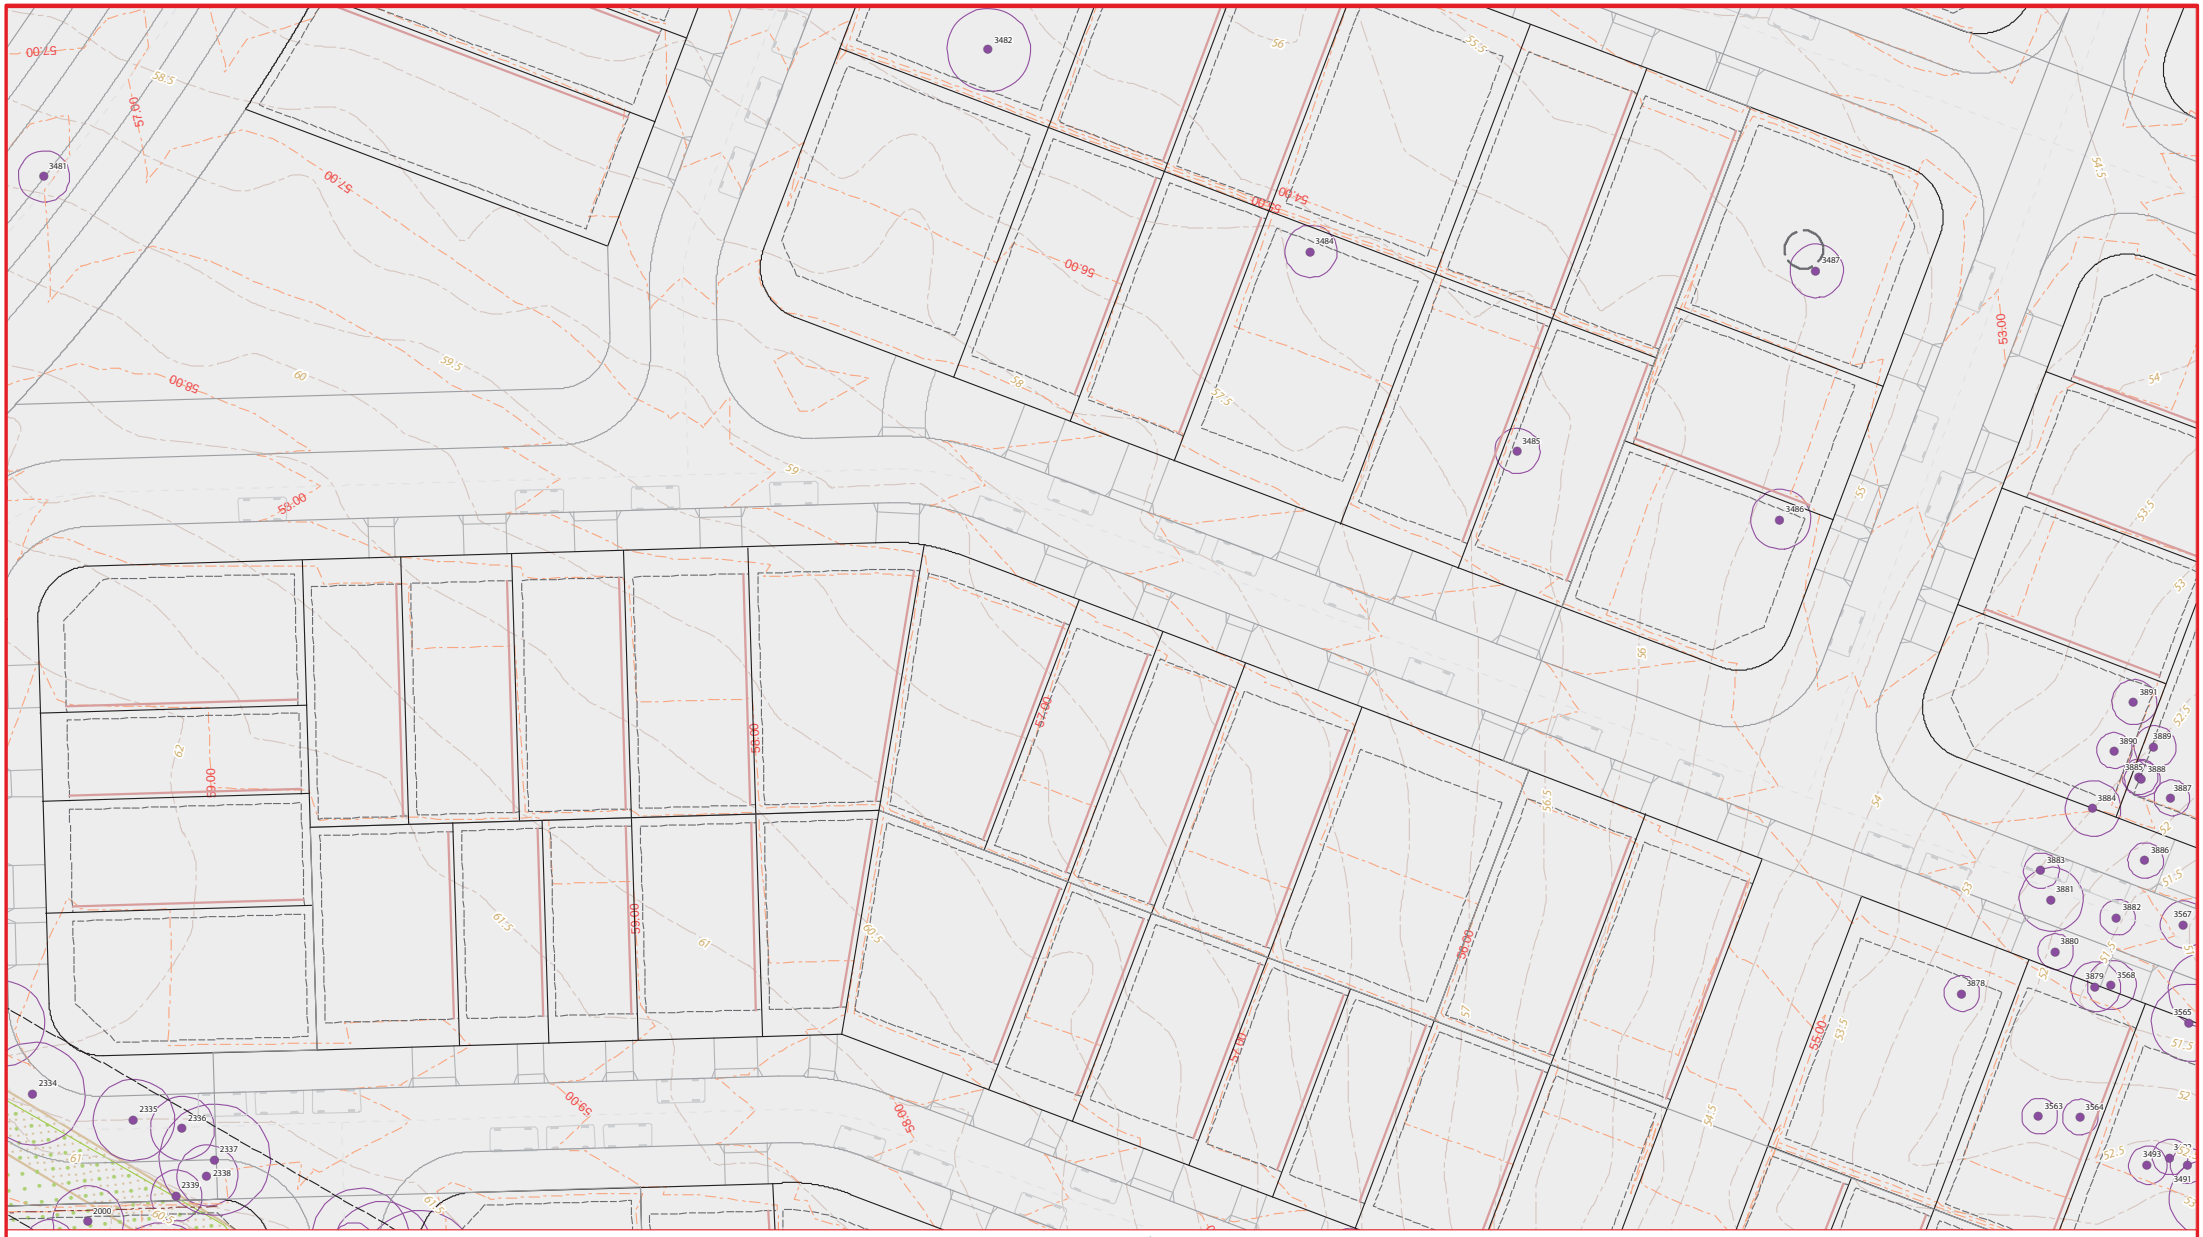

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 49

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 49 BAL Stage 2 VMP E	

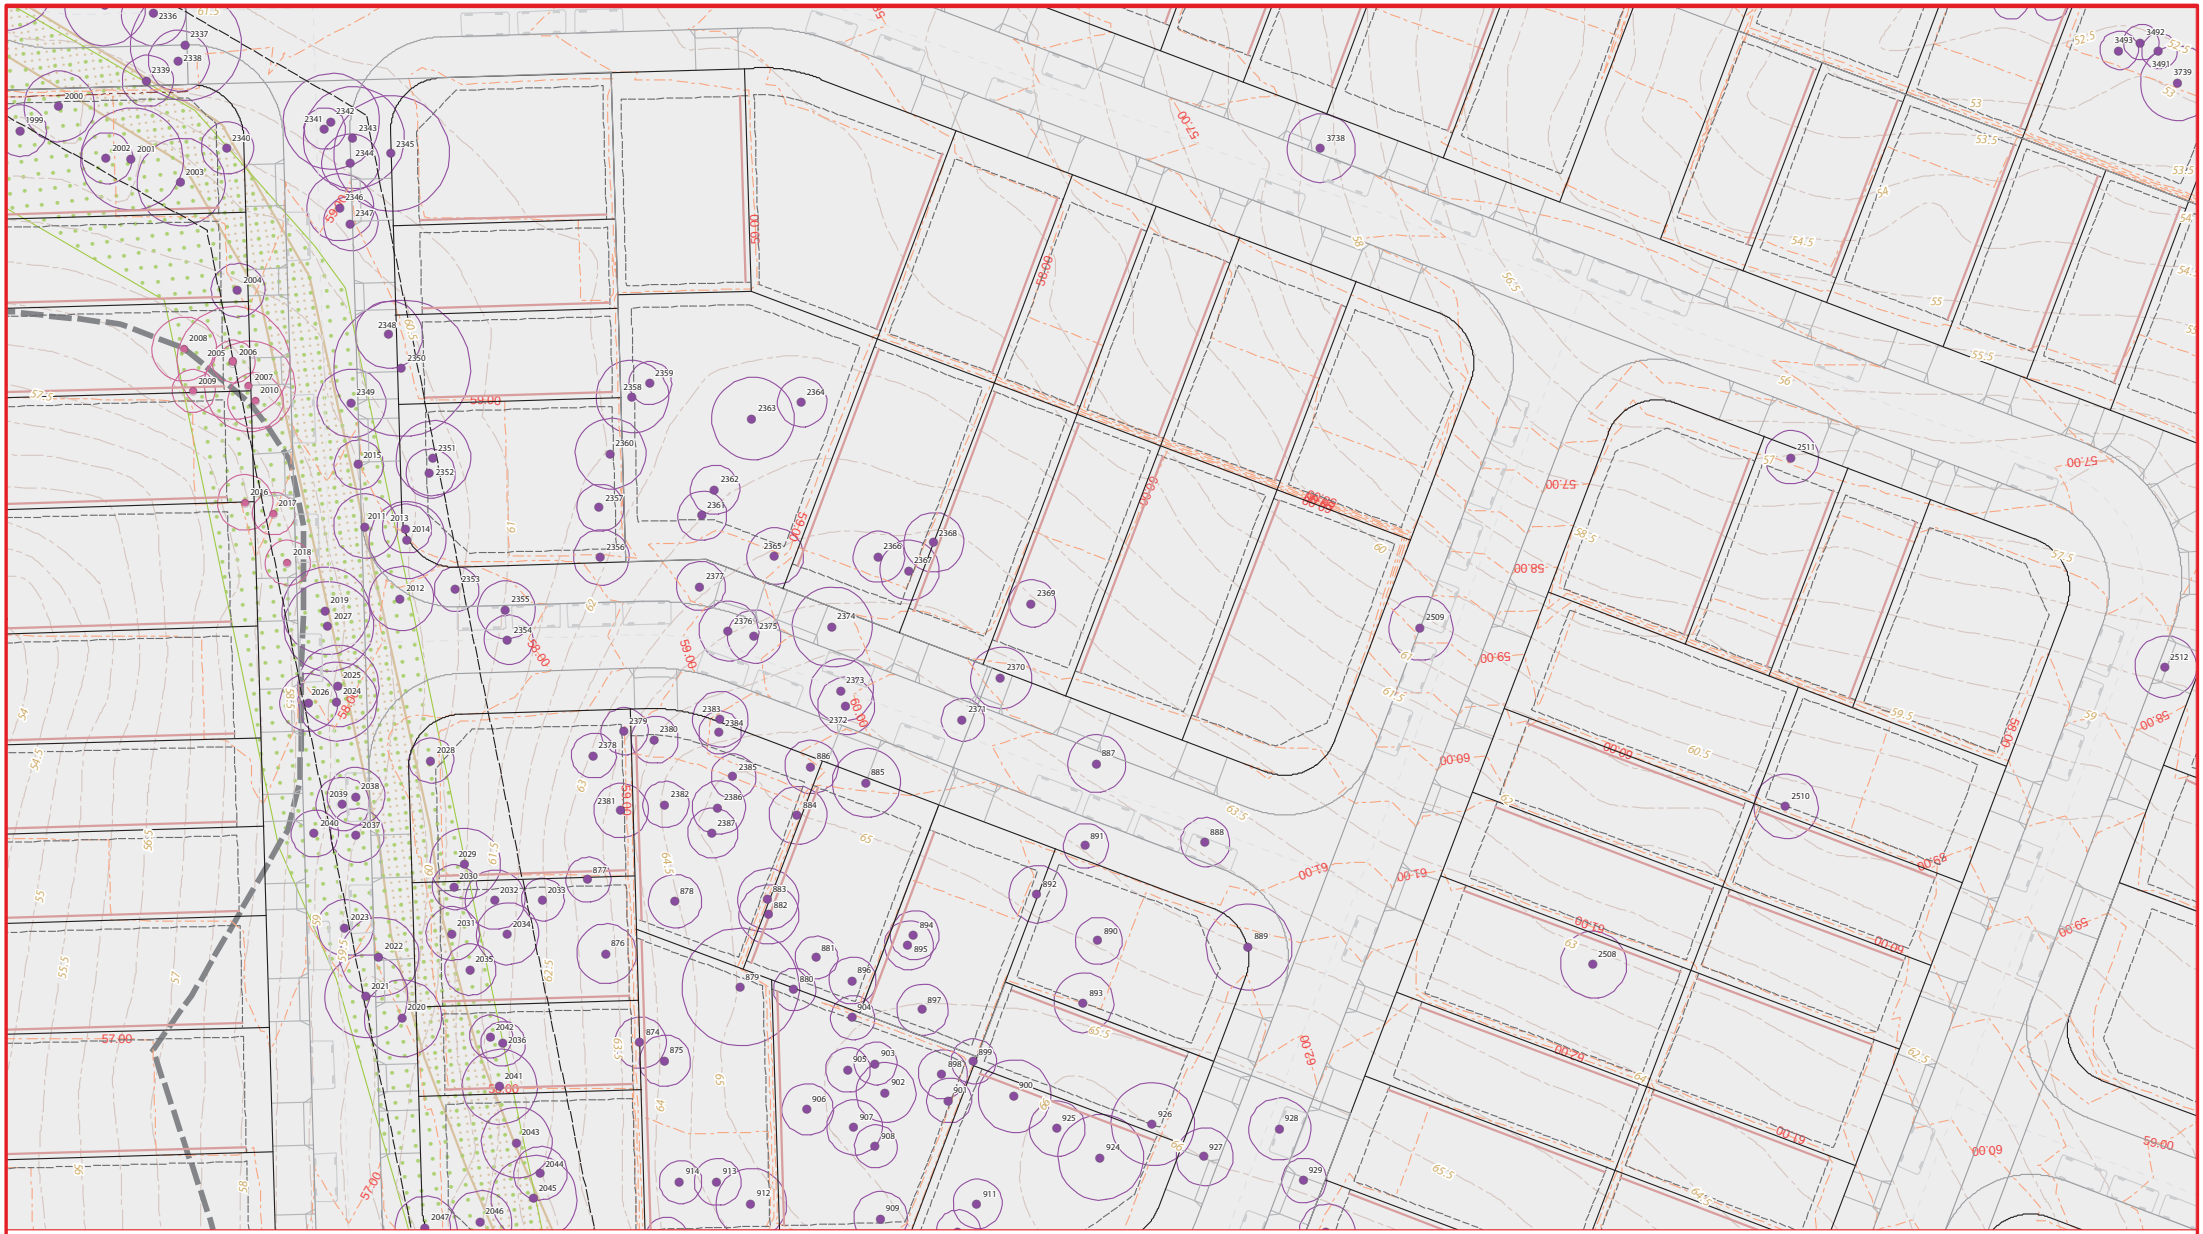

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 50

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 50 BAL Stage 2 VMP E	

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 51

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC

DRAWING No.: 8047 E 51 BAL Stage 2 VMP E

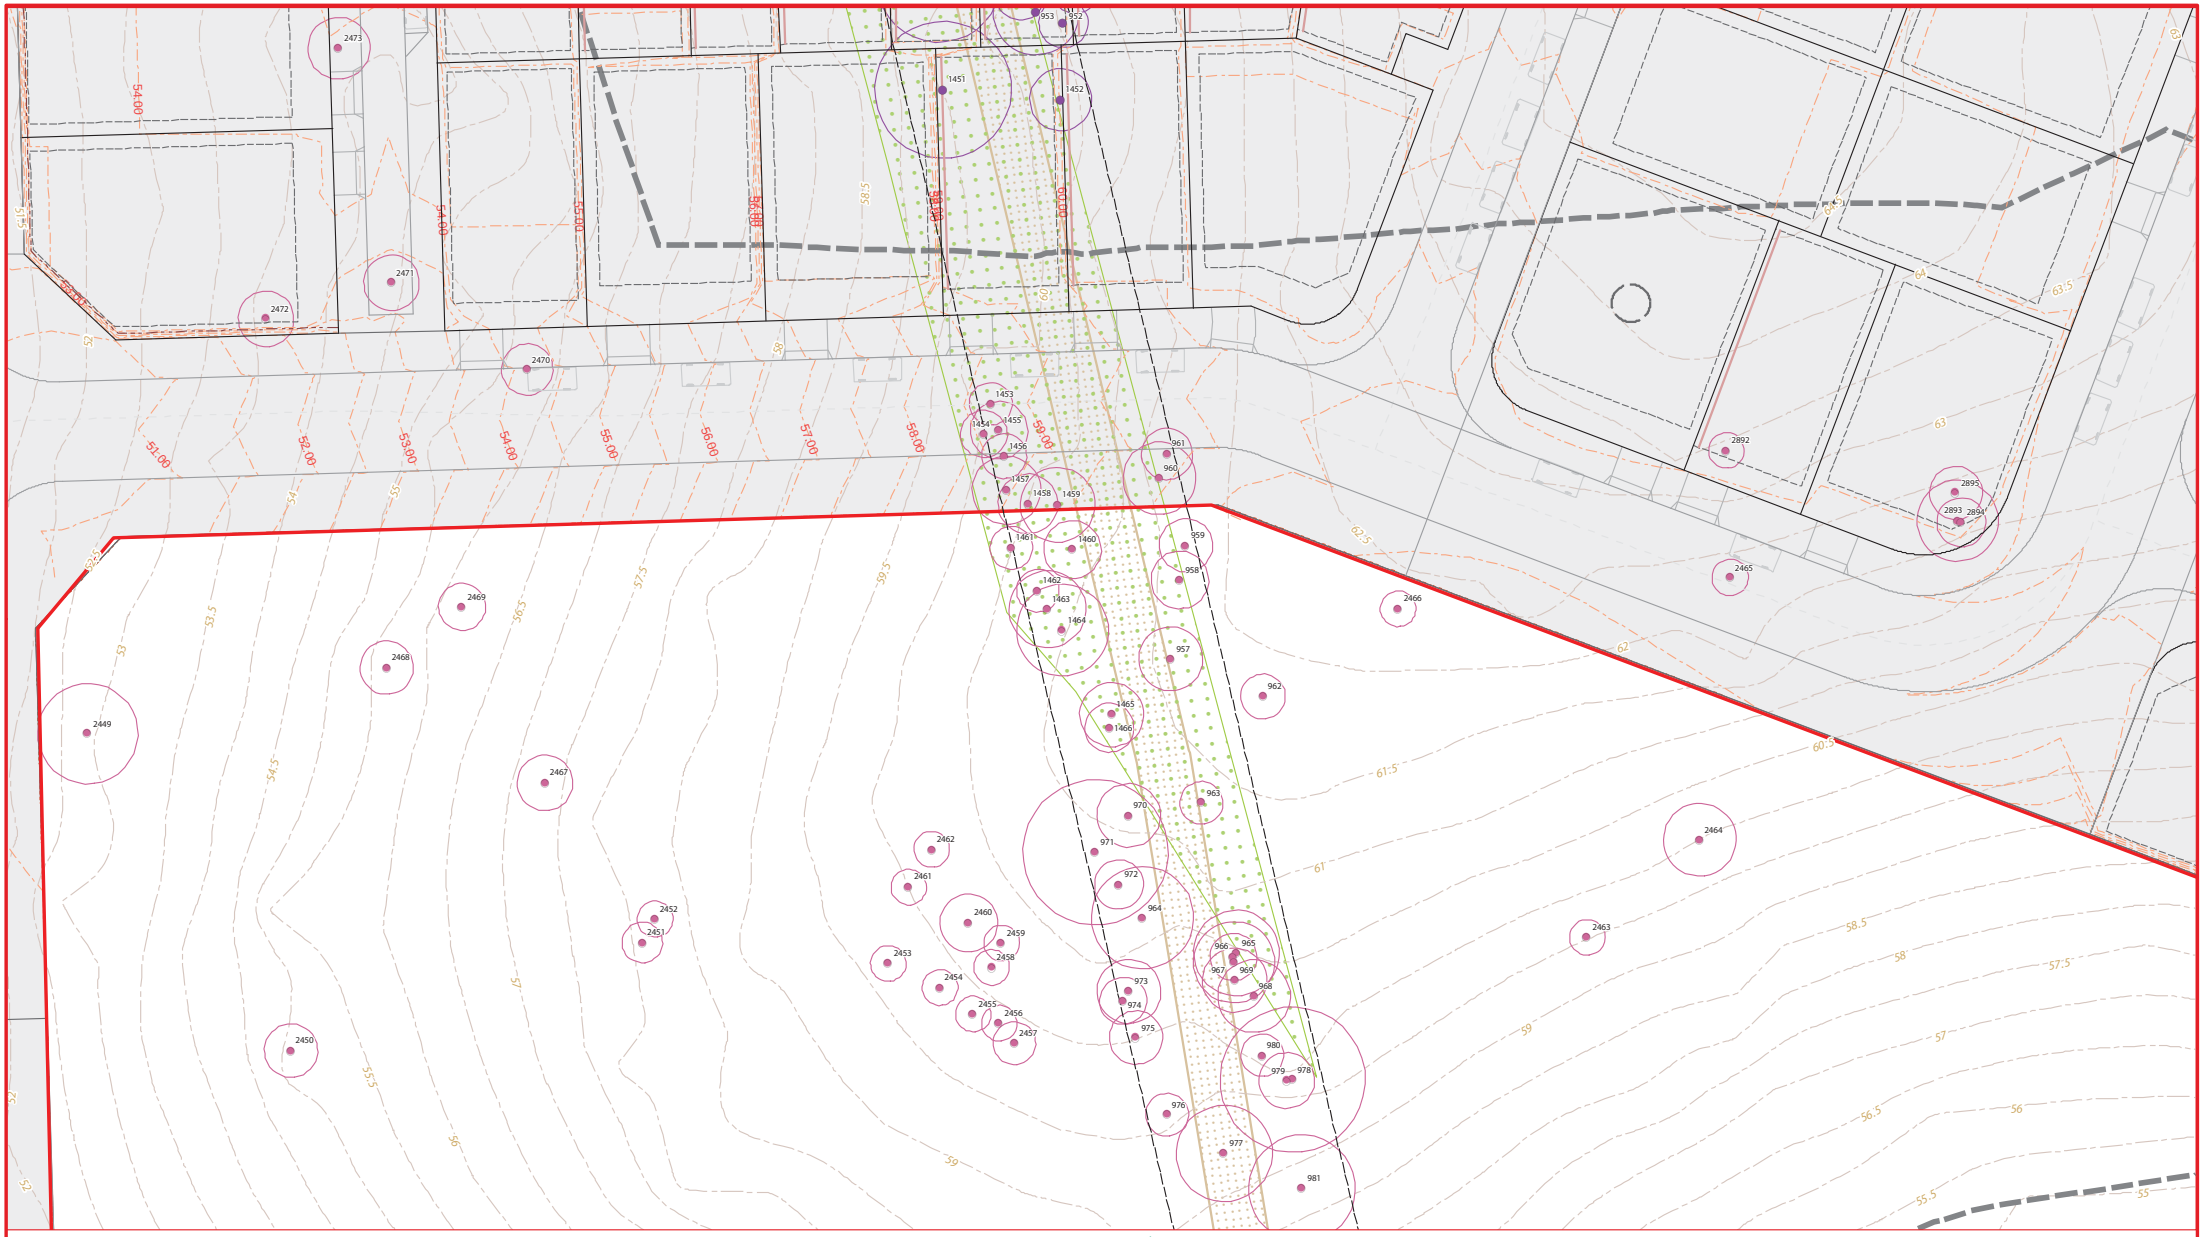

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 52

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 52 BAL Stage 2 VMP E

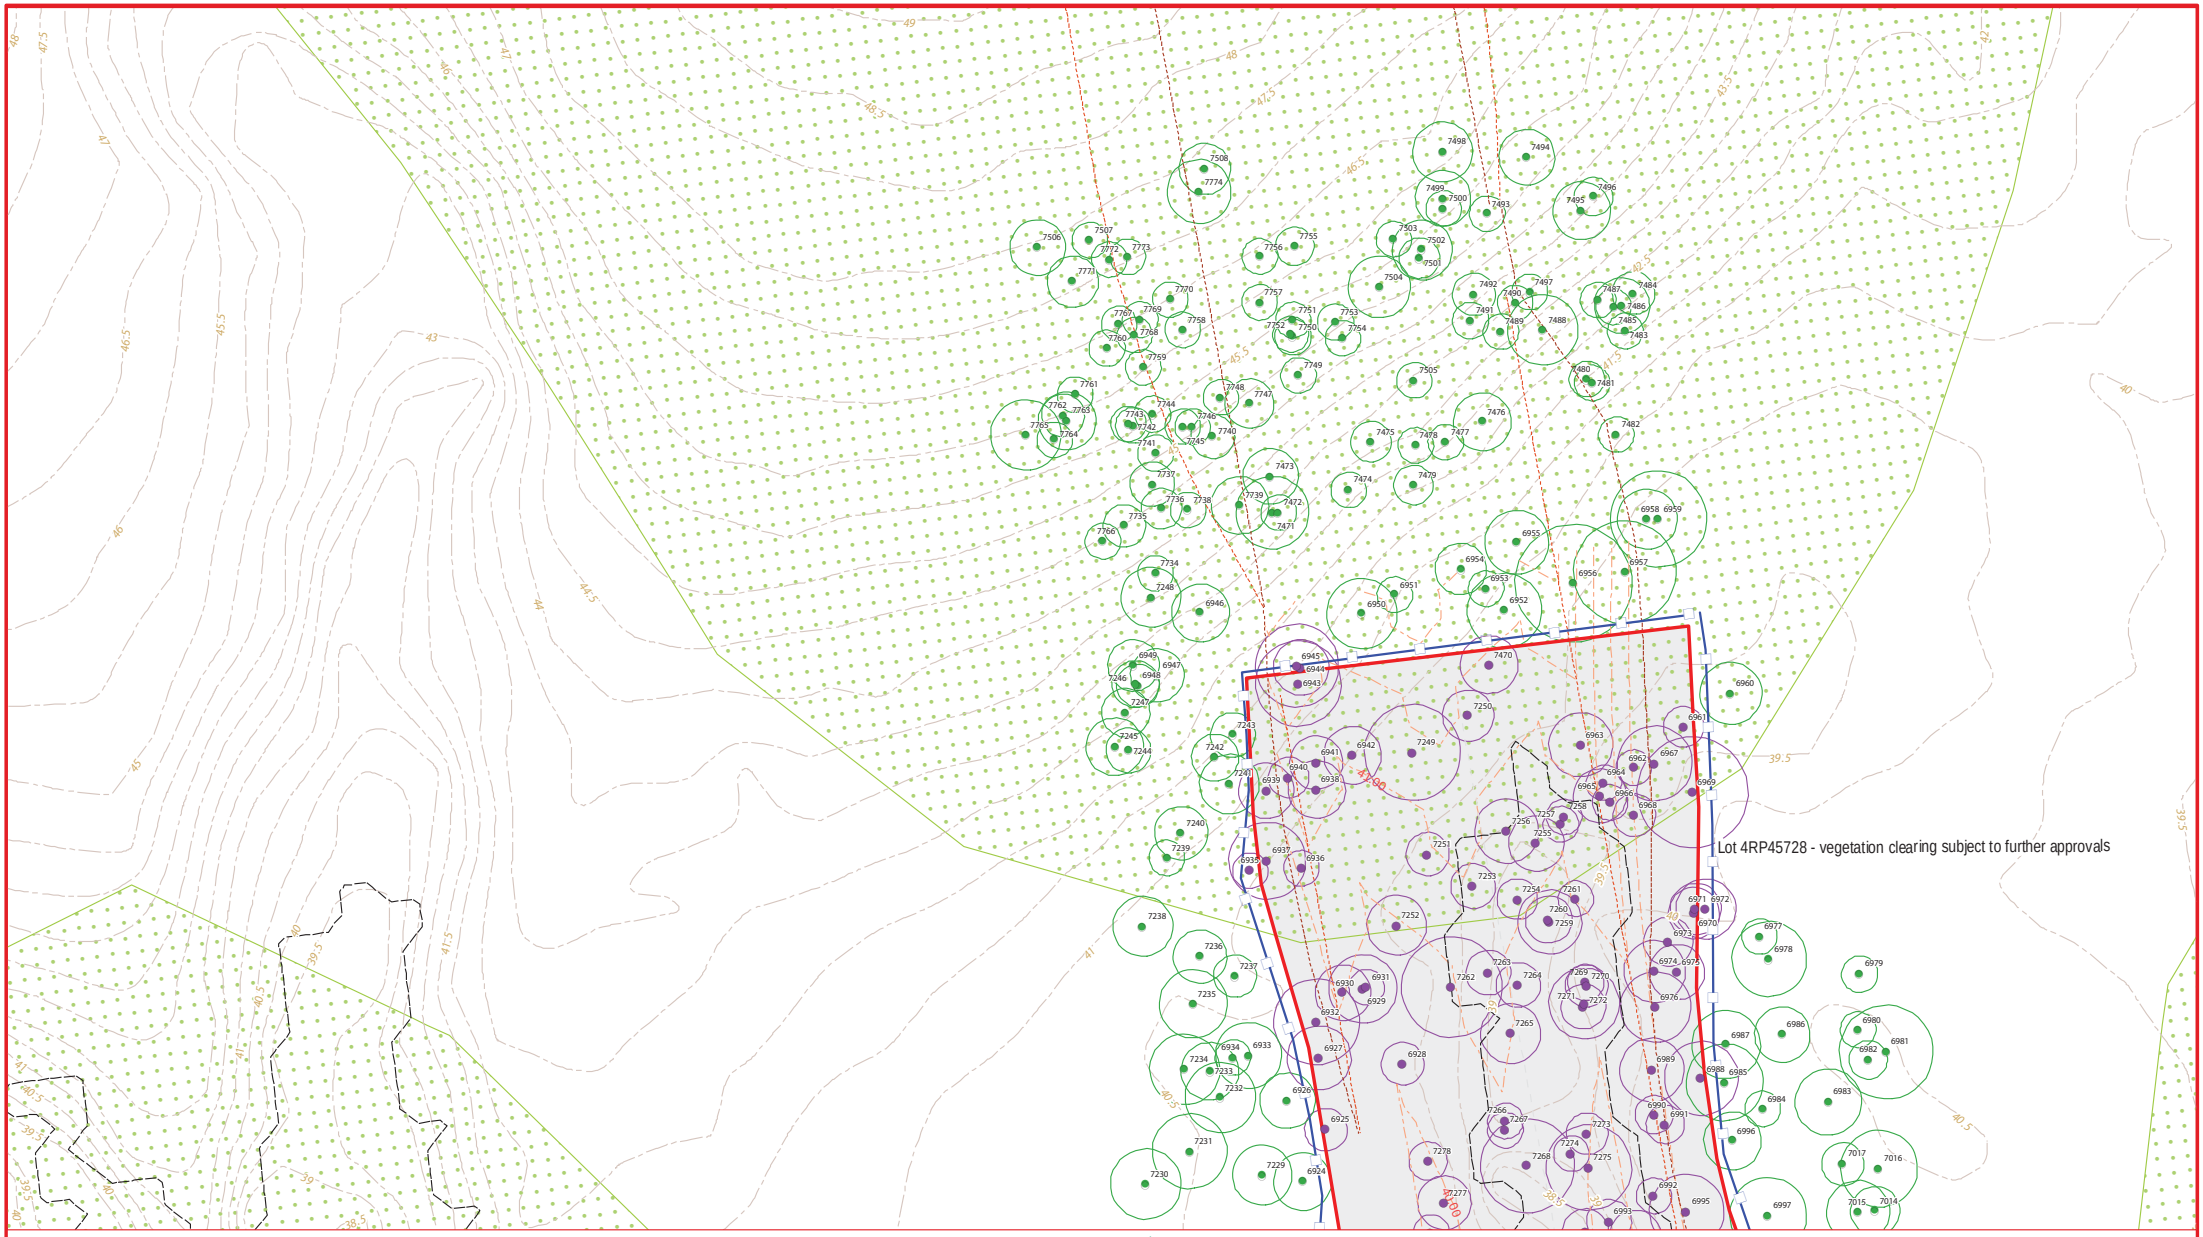

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 53

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 53 BAL Stage 2 VMP E	

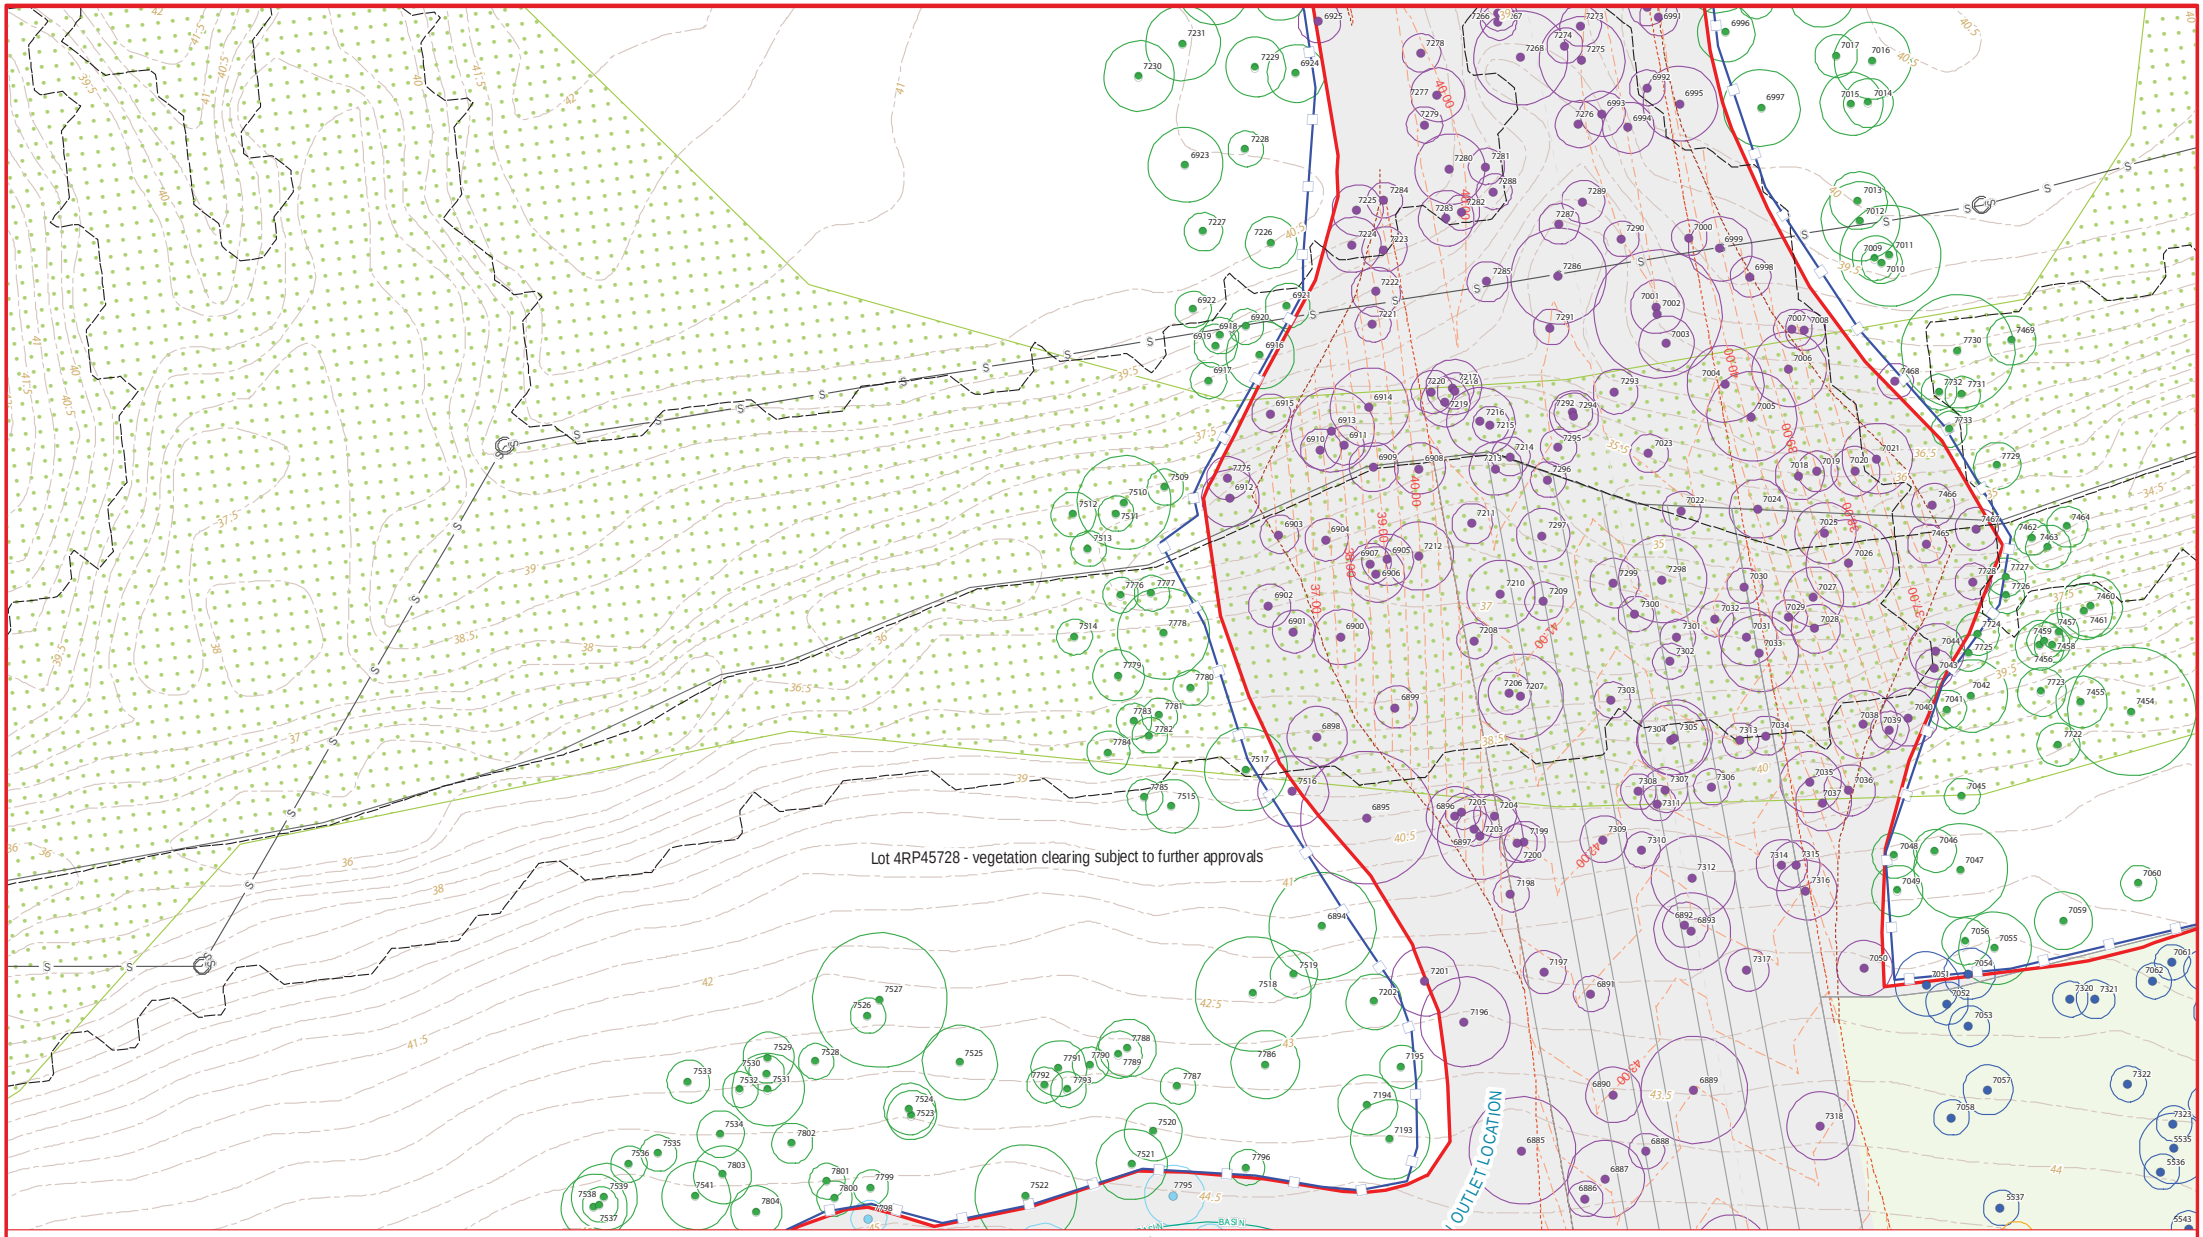

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 54

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC
DRAWING No.:	8047 E 54 BAL Stage 2 VMP E		

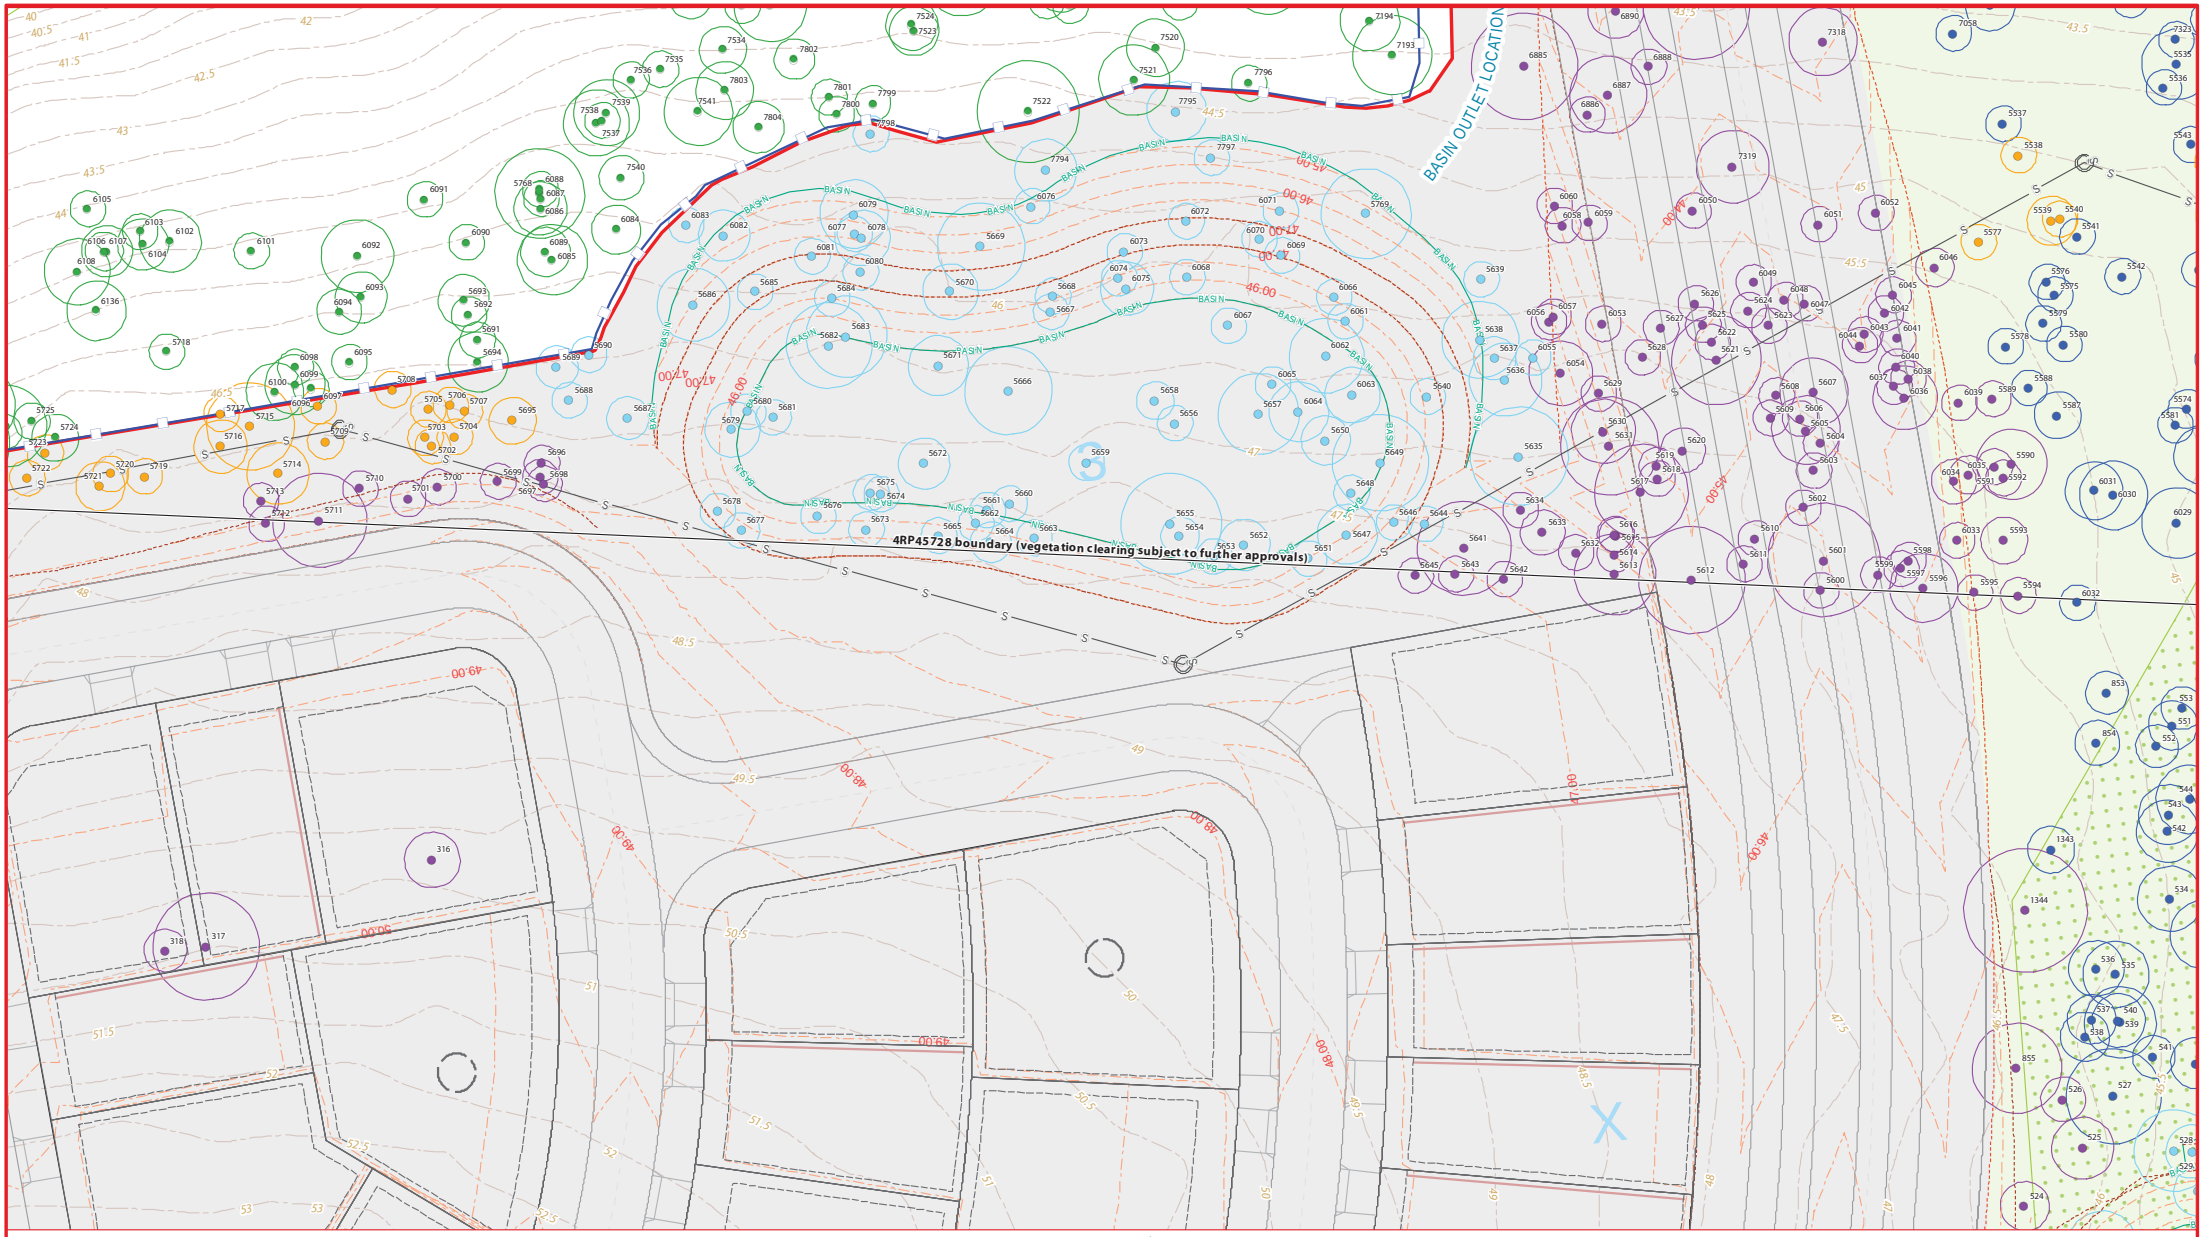

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

Civil trunk sewer

Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 55

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF: 8047 DRAWN: TC

DRAWING No.: 8047 E 55 BAL Stage 2 VMP E

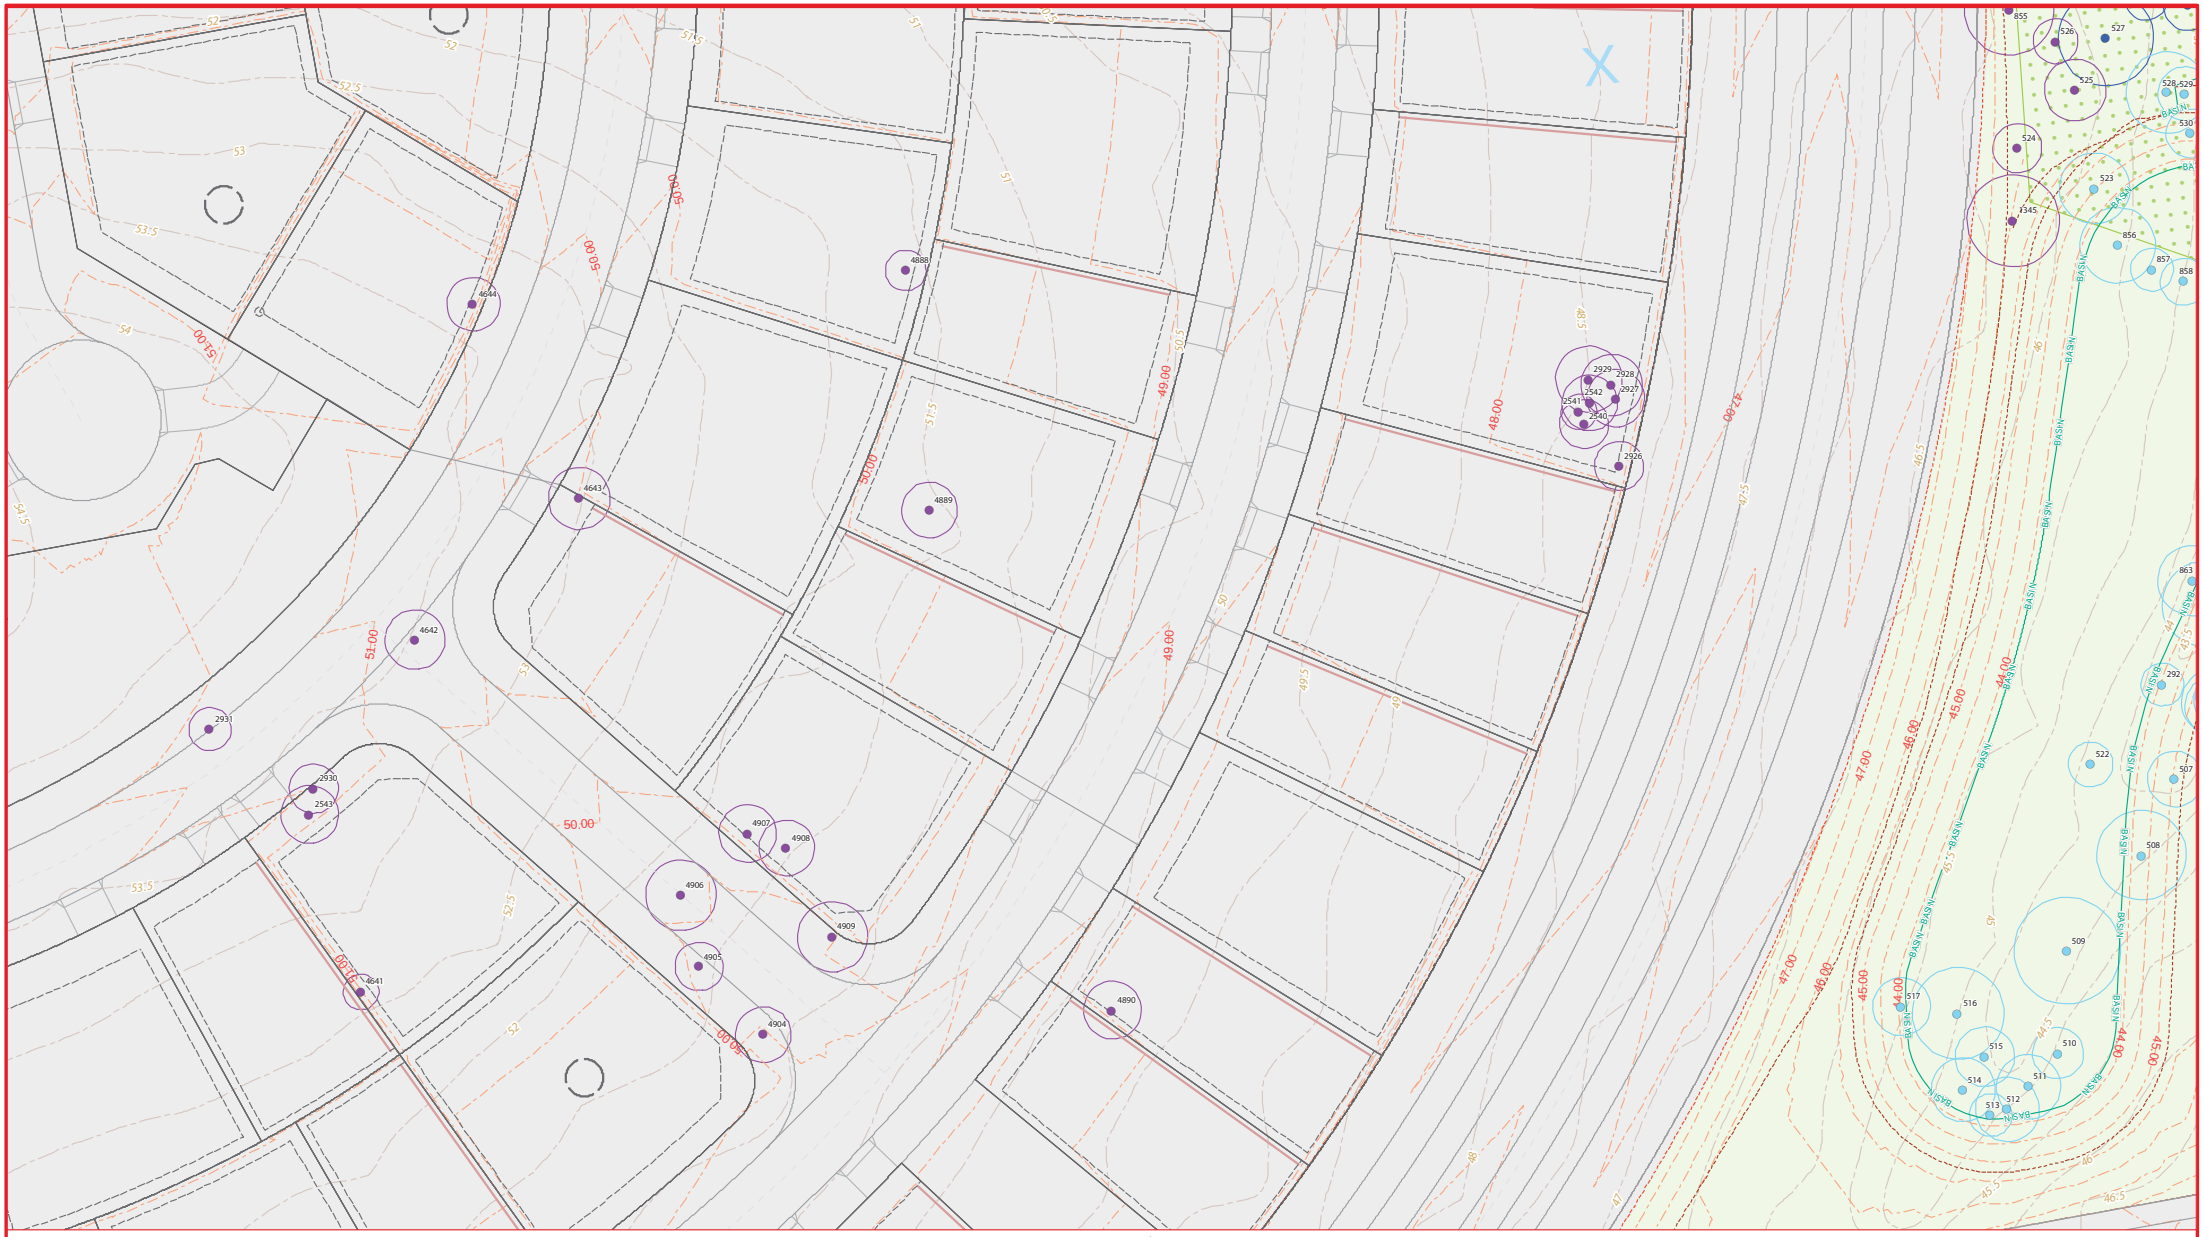

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 56

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 56 BAL Stage 2 VMP E	

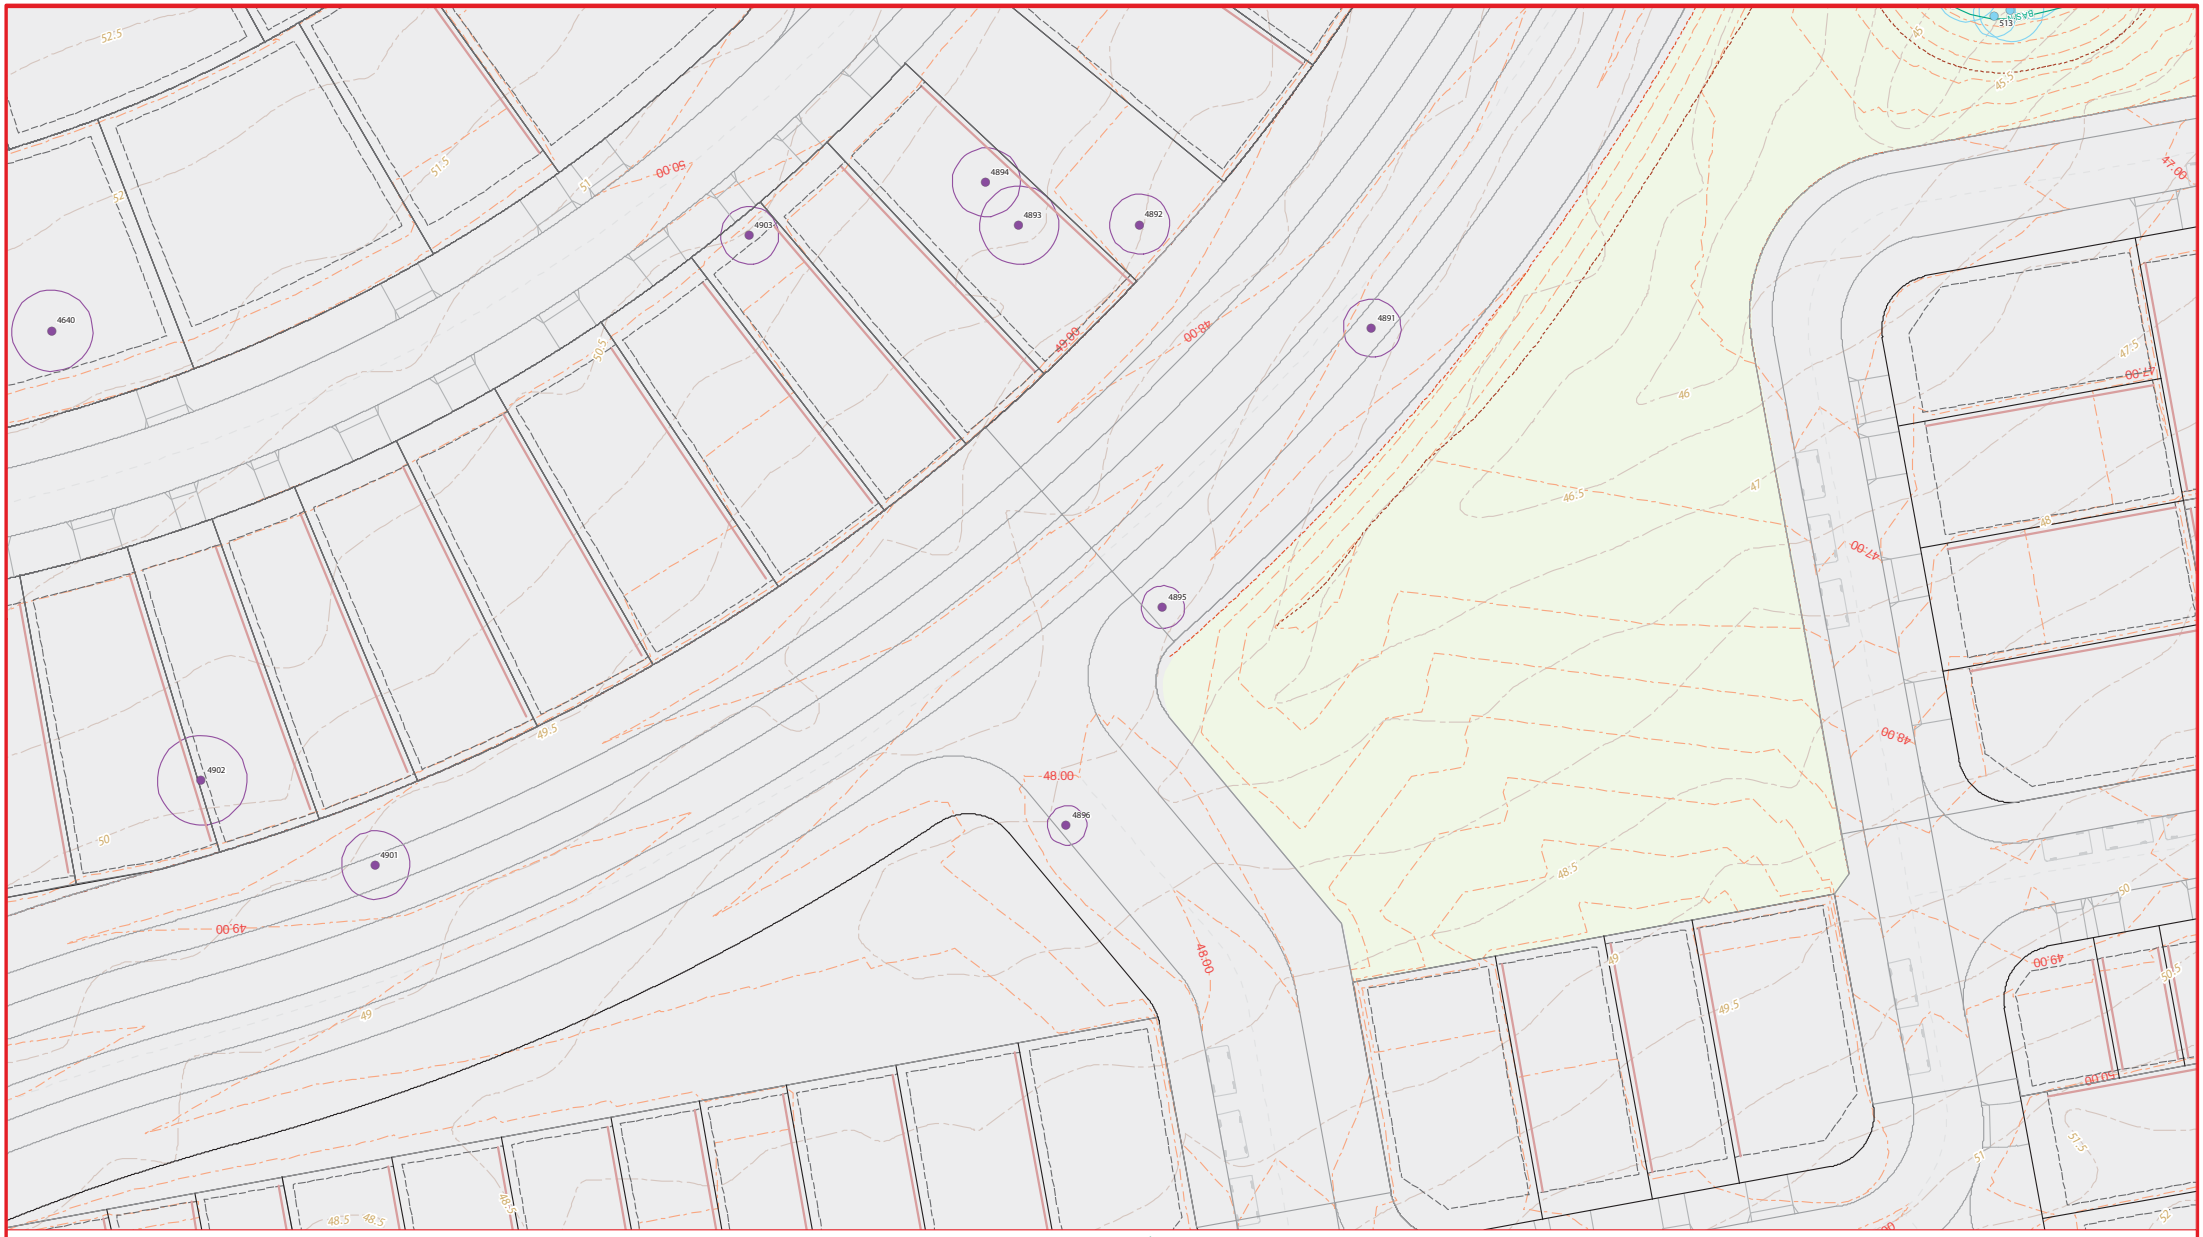

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 57

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 57 BAL Stage 2 VMP E	

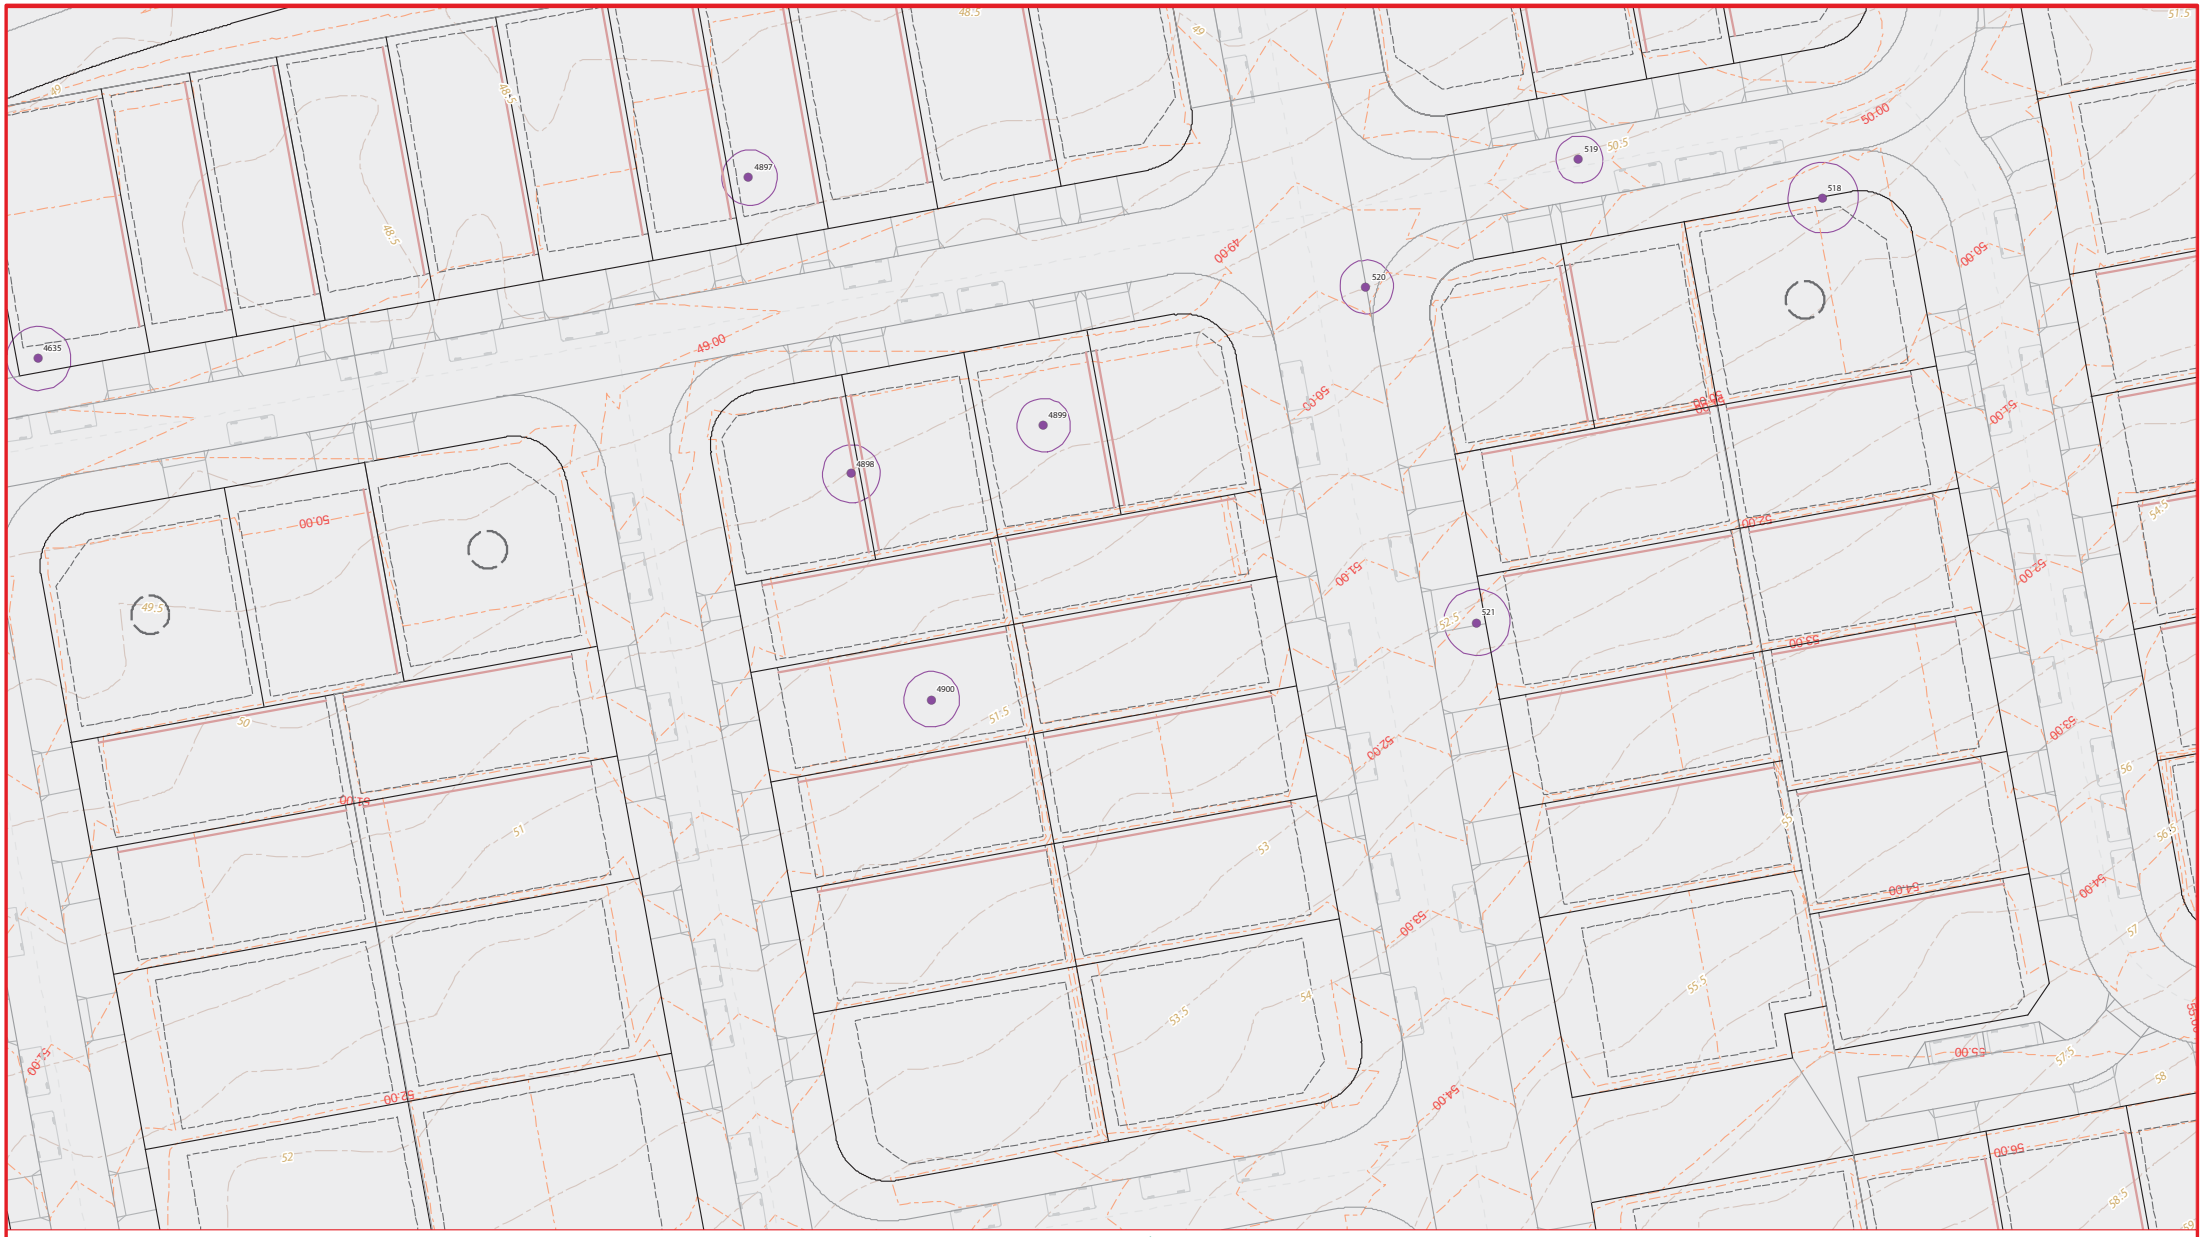

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 58

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 58 BAL Stage 2 VMP E	

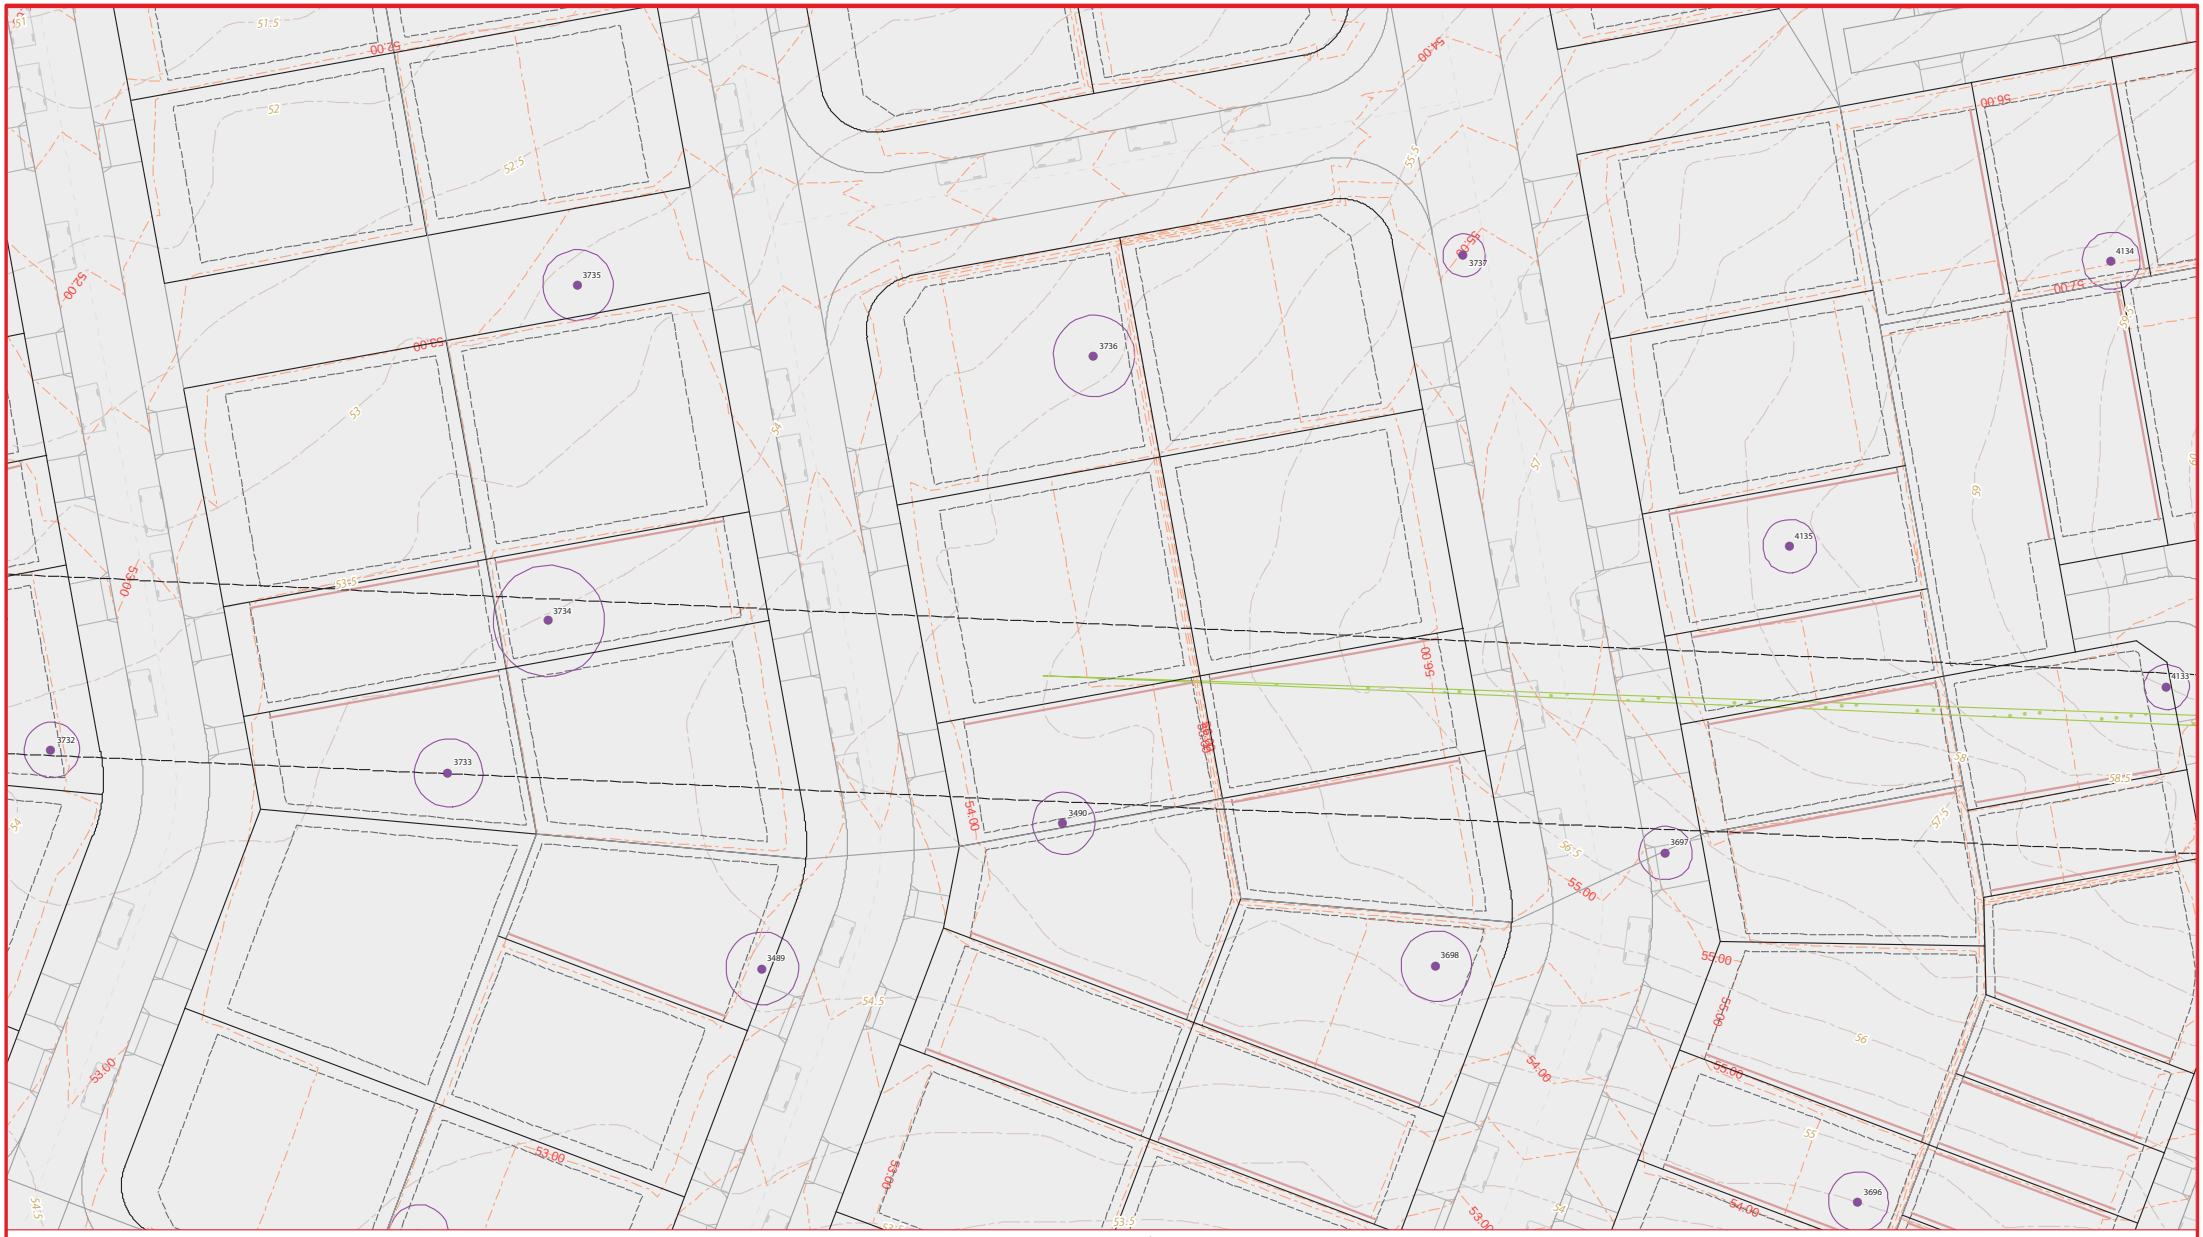

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 59

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 59 BAL Stage 2 VMP E

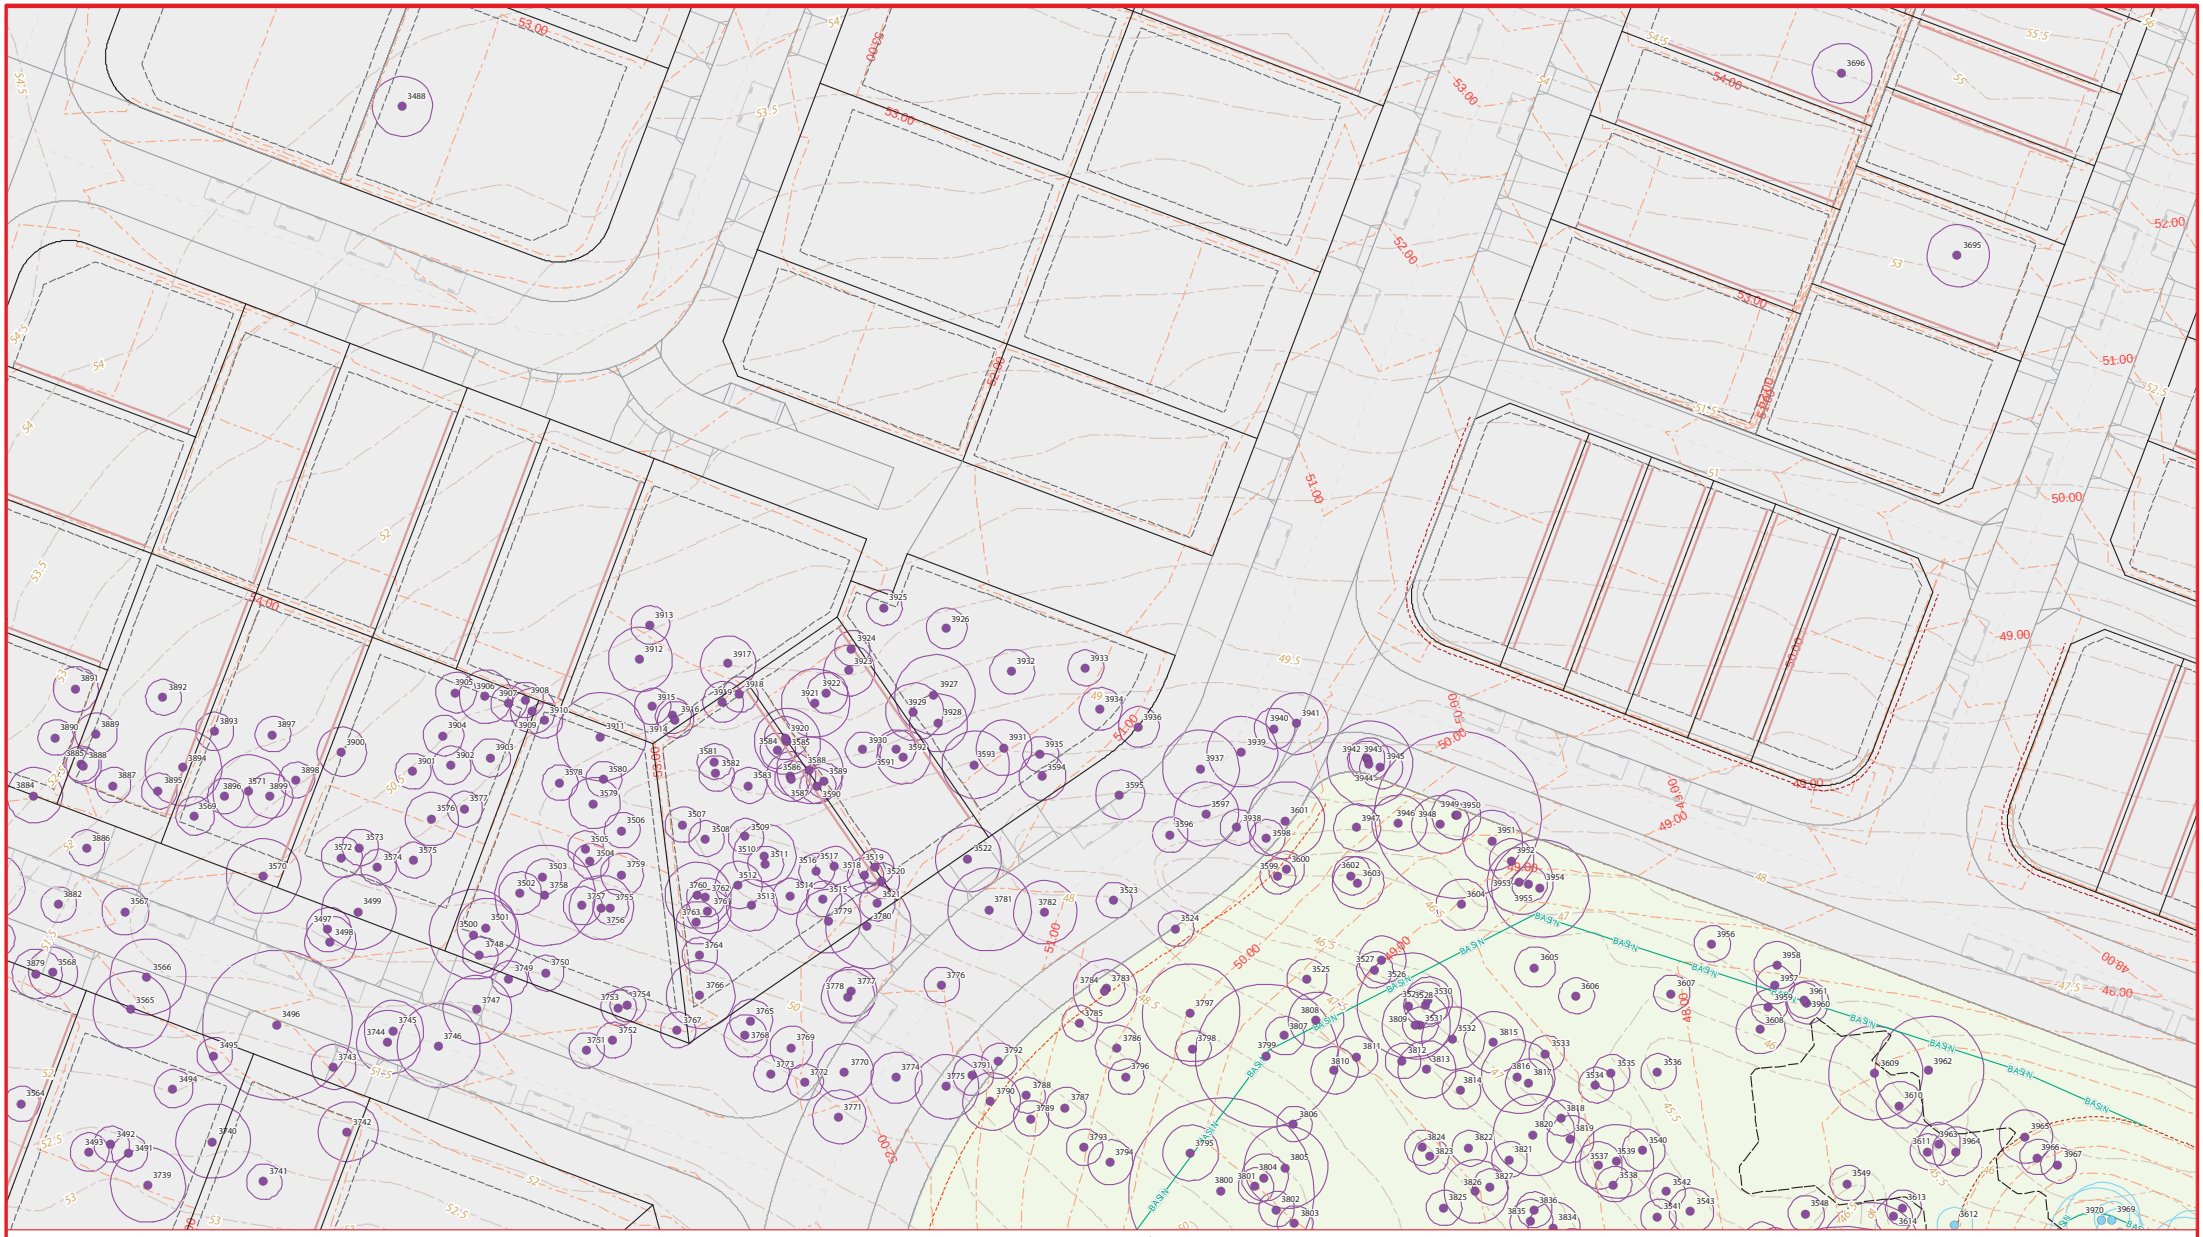

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

Civil trunk sewer

Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 60

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC
DRAWING No.: 8047 E 60 BAL Stage 2 VMP E	

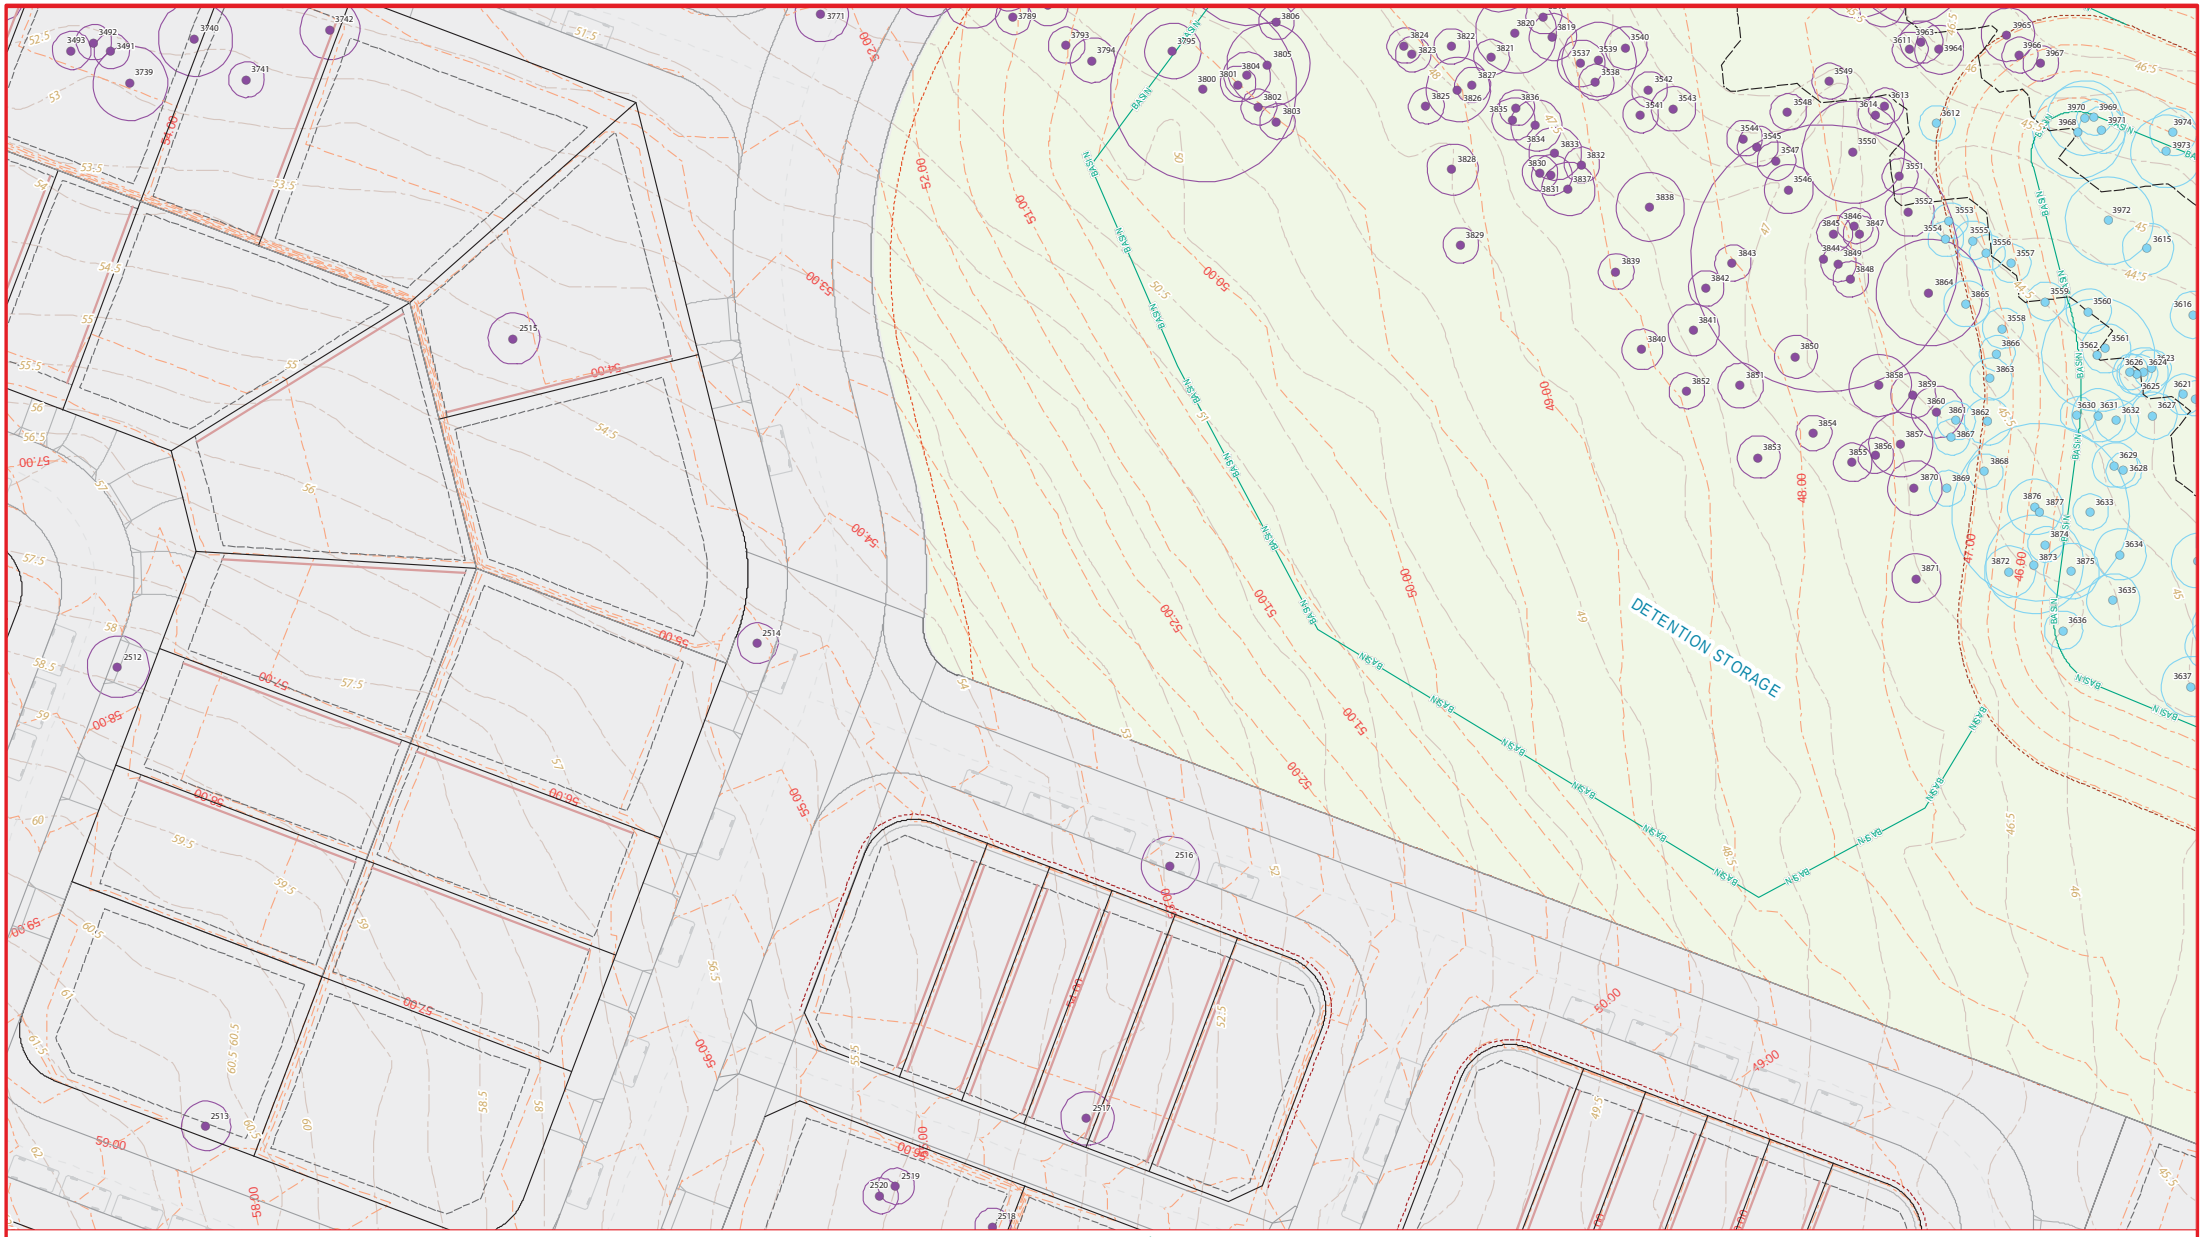

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 61

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC

DRAWING No.: 8047 E 61 BAL Stage 2 VMP E

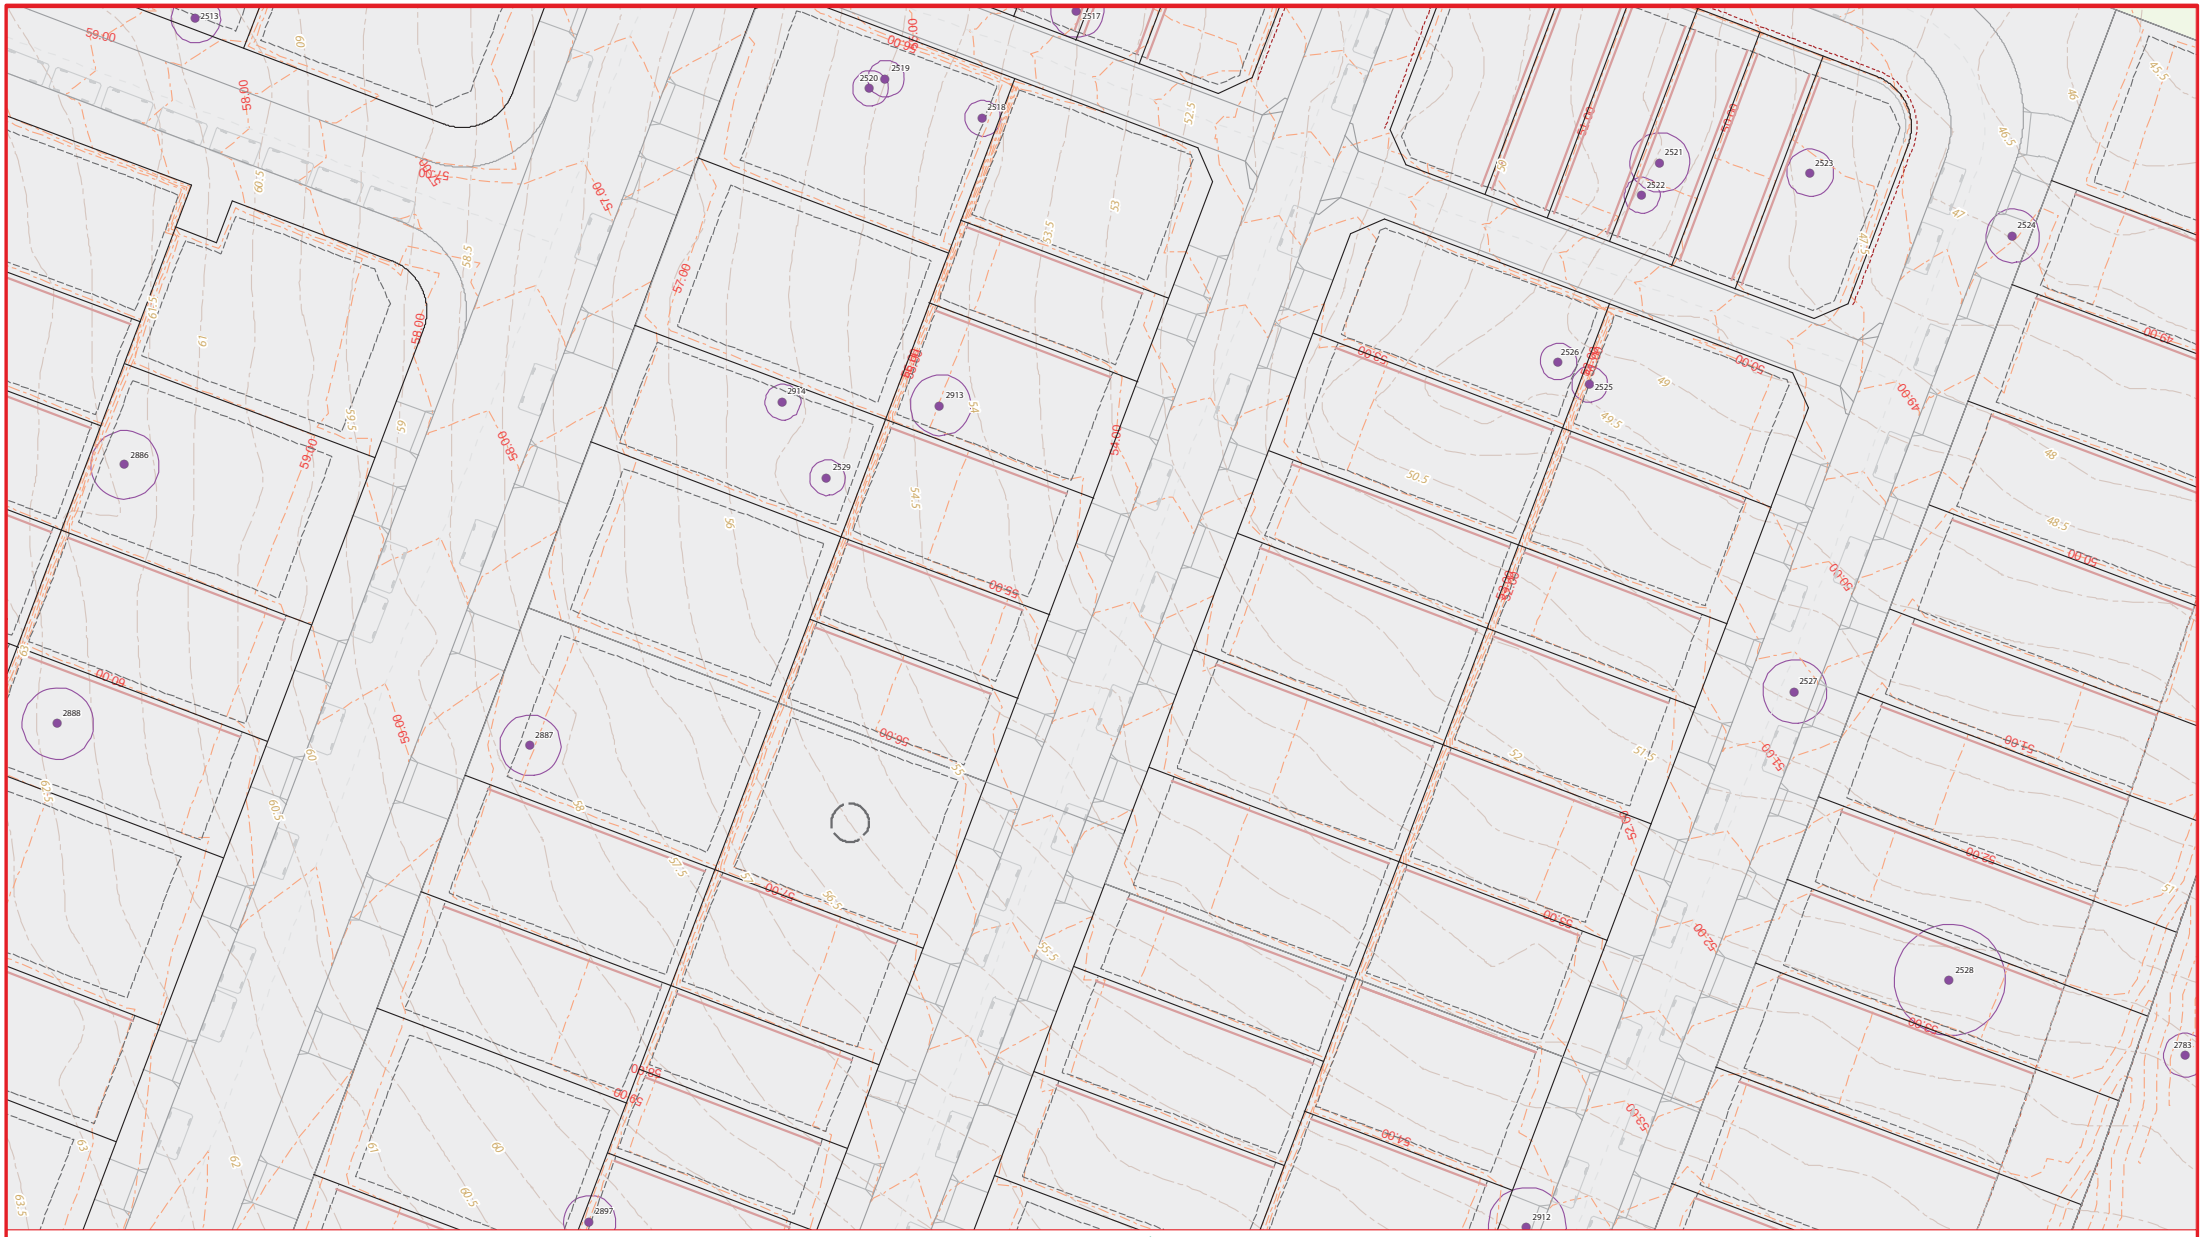

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 62

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 62 BAL Stage 2 VMP E

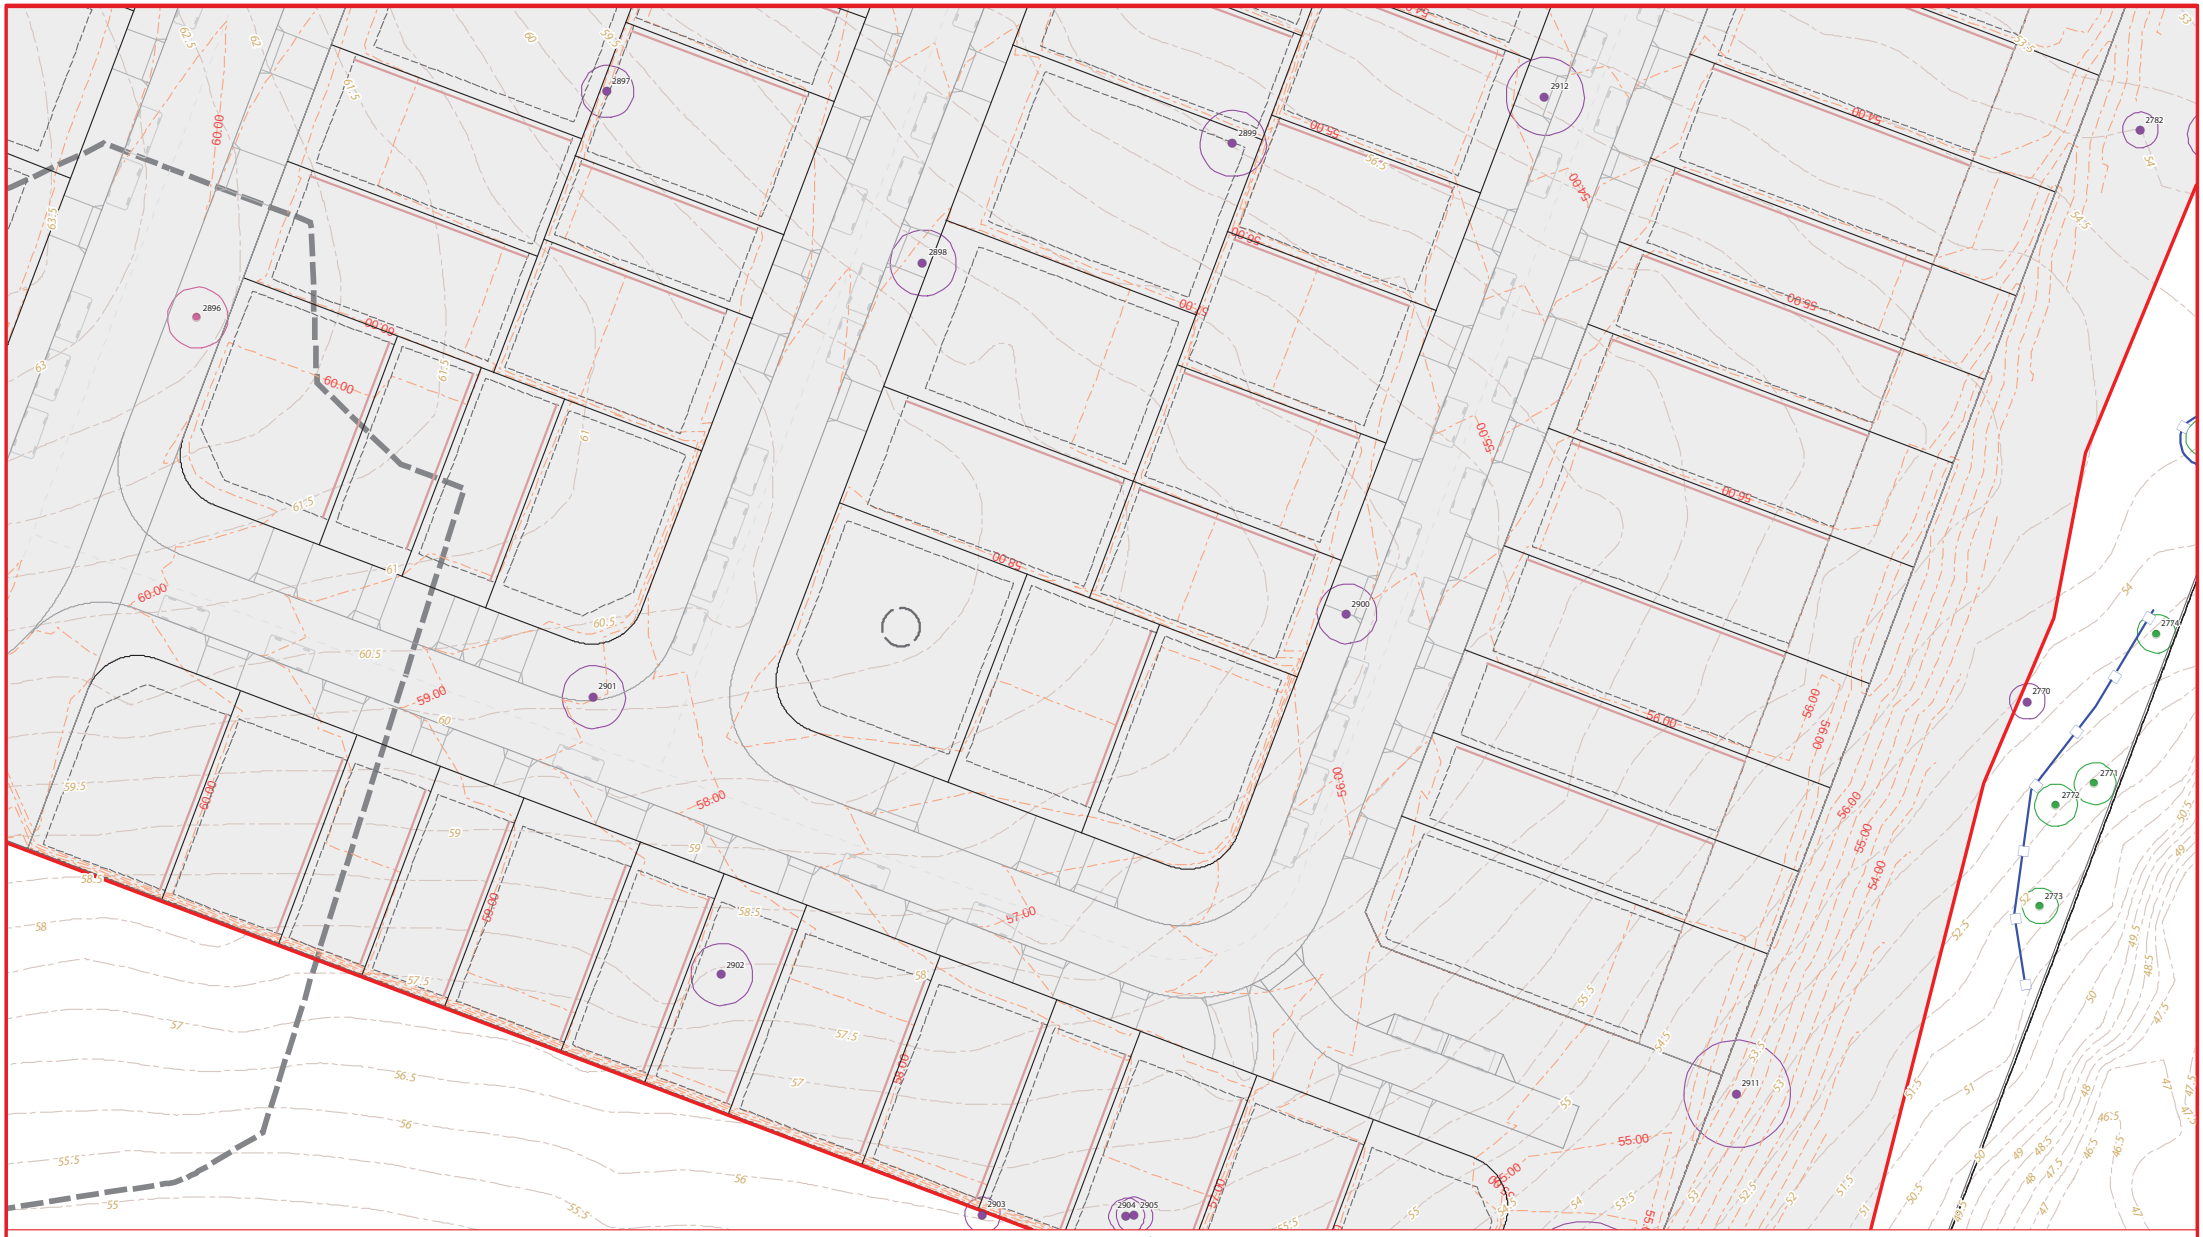

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 63

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF:	8047	DRAWN:	TC
DRAWING No.:	8047 E 63 BAL Stage 2 VMP E		

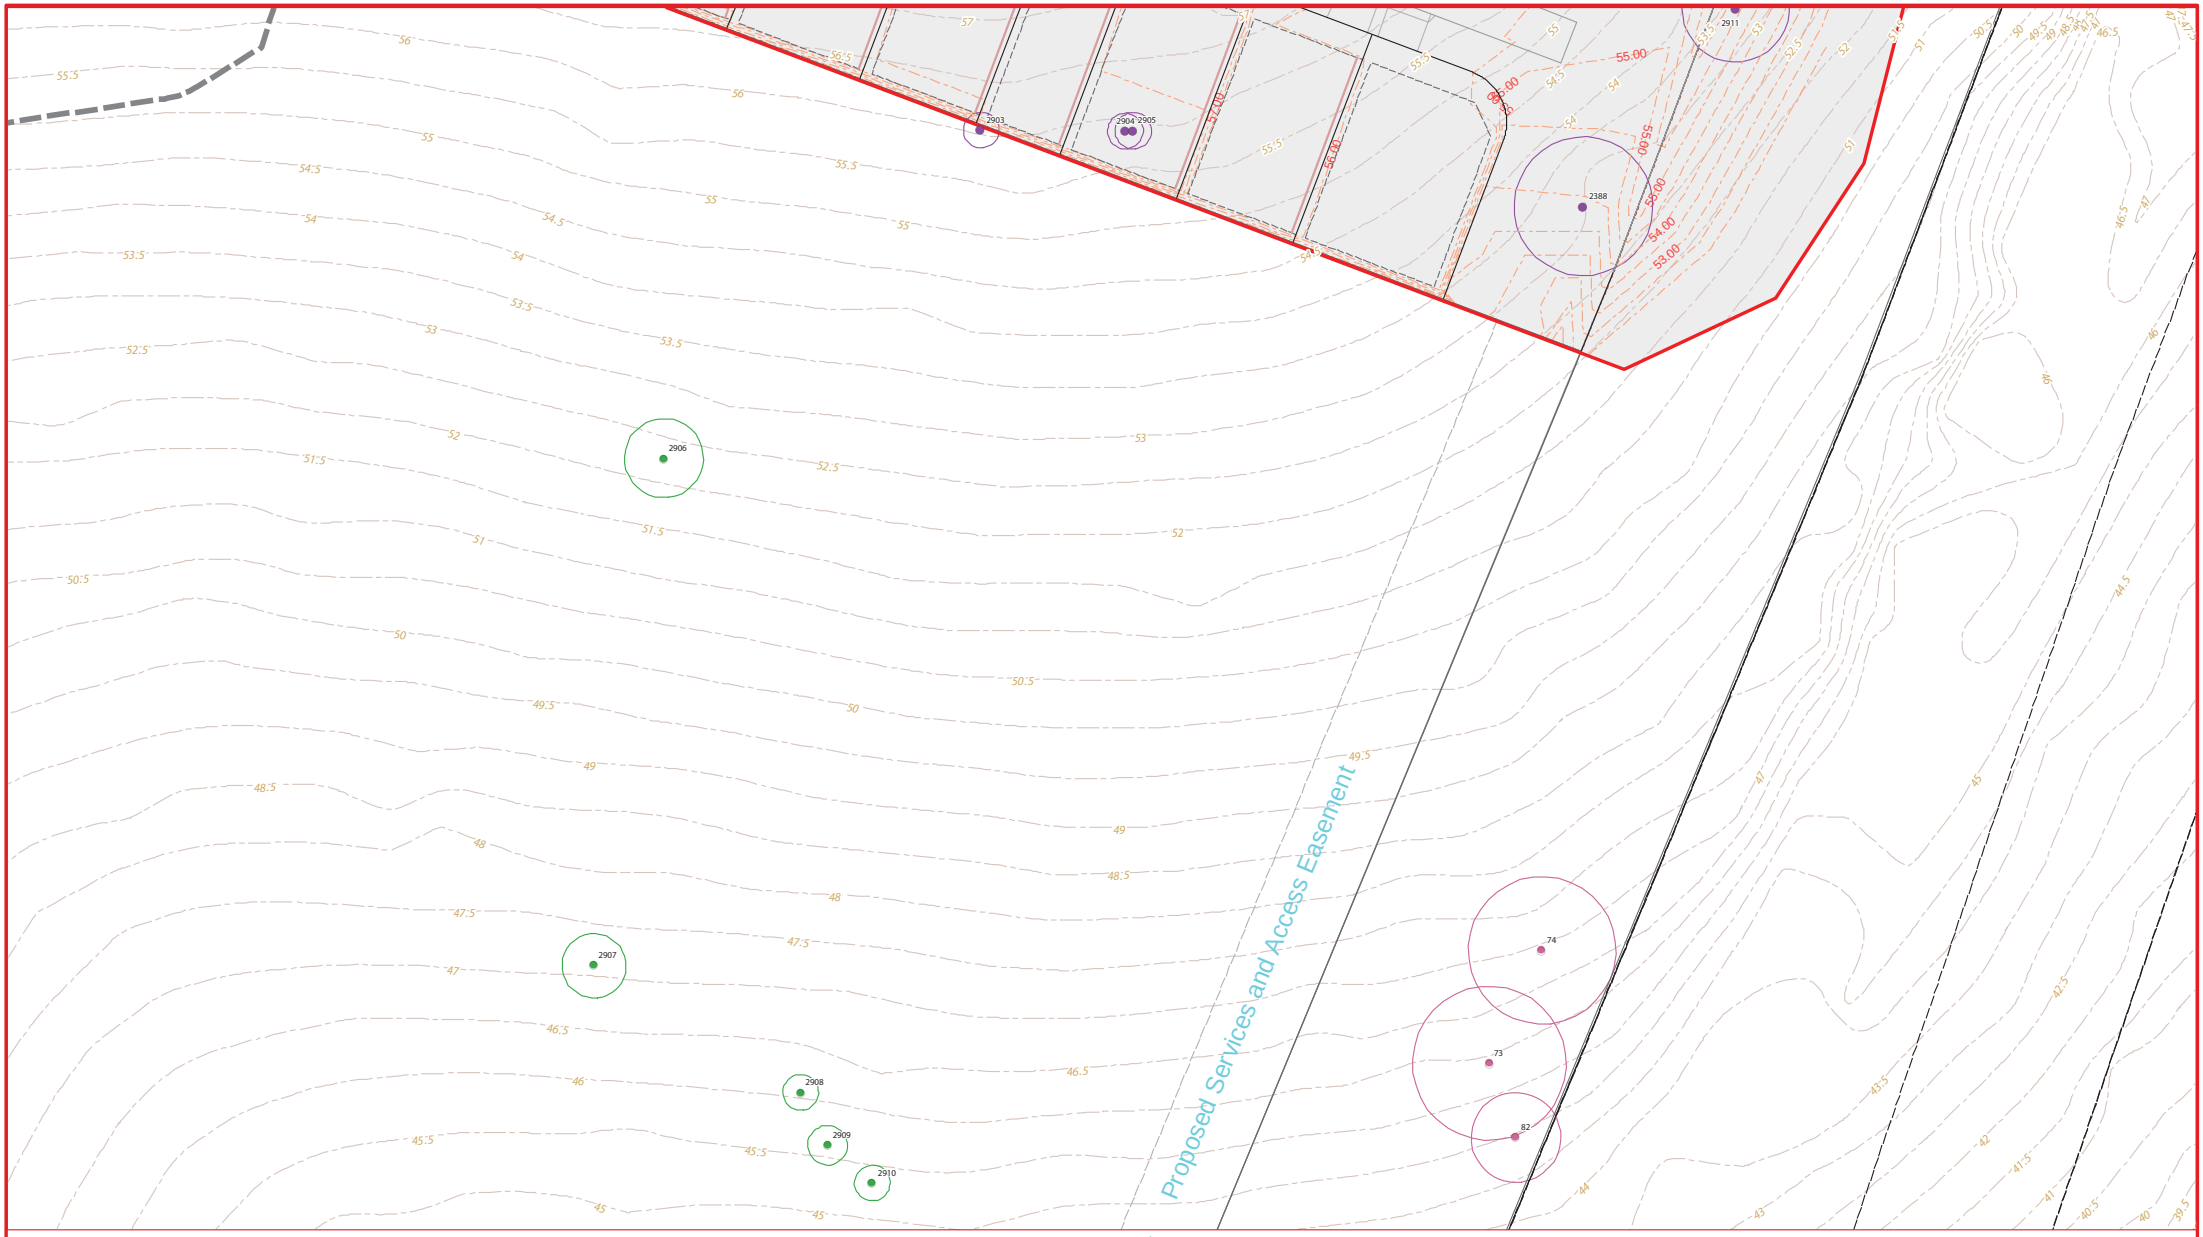

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 64

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 64 BAL Stage 2 VMP E	

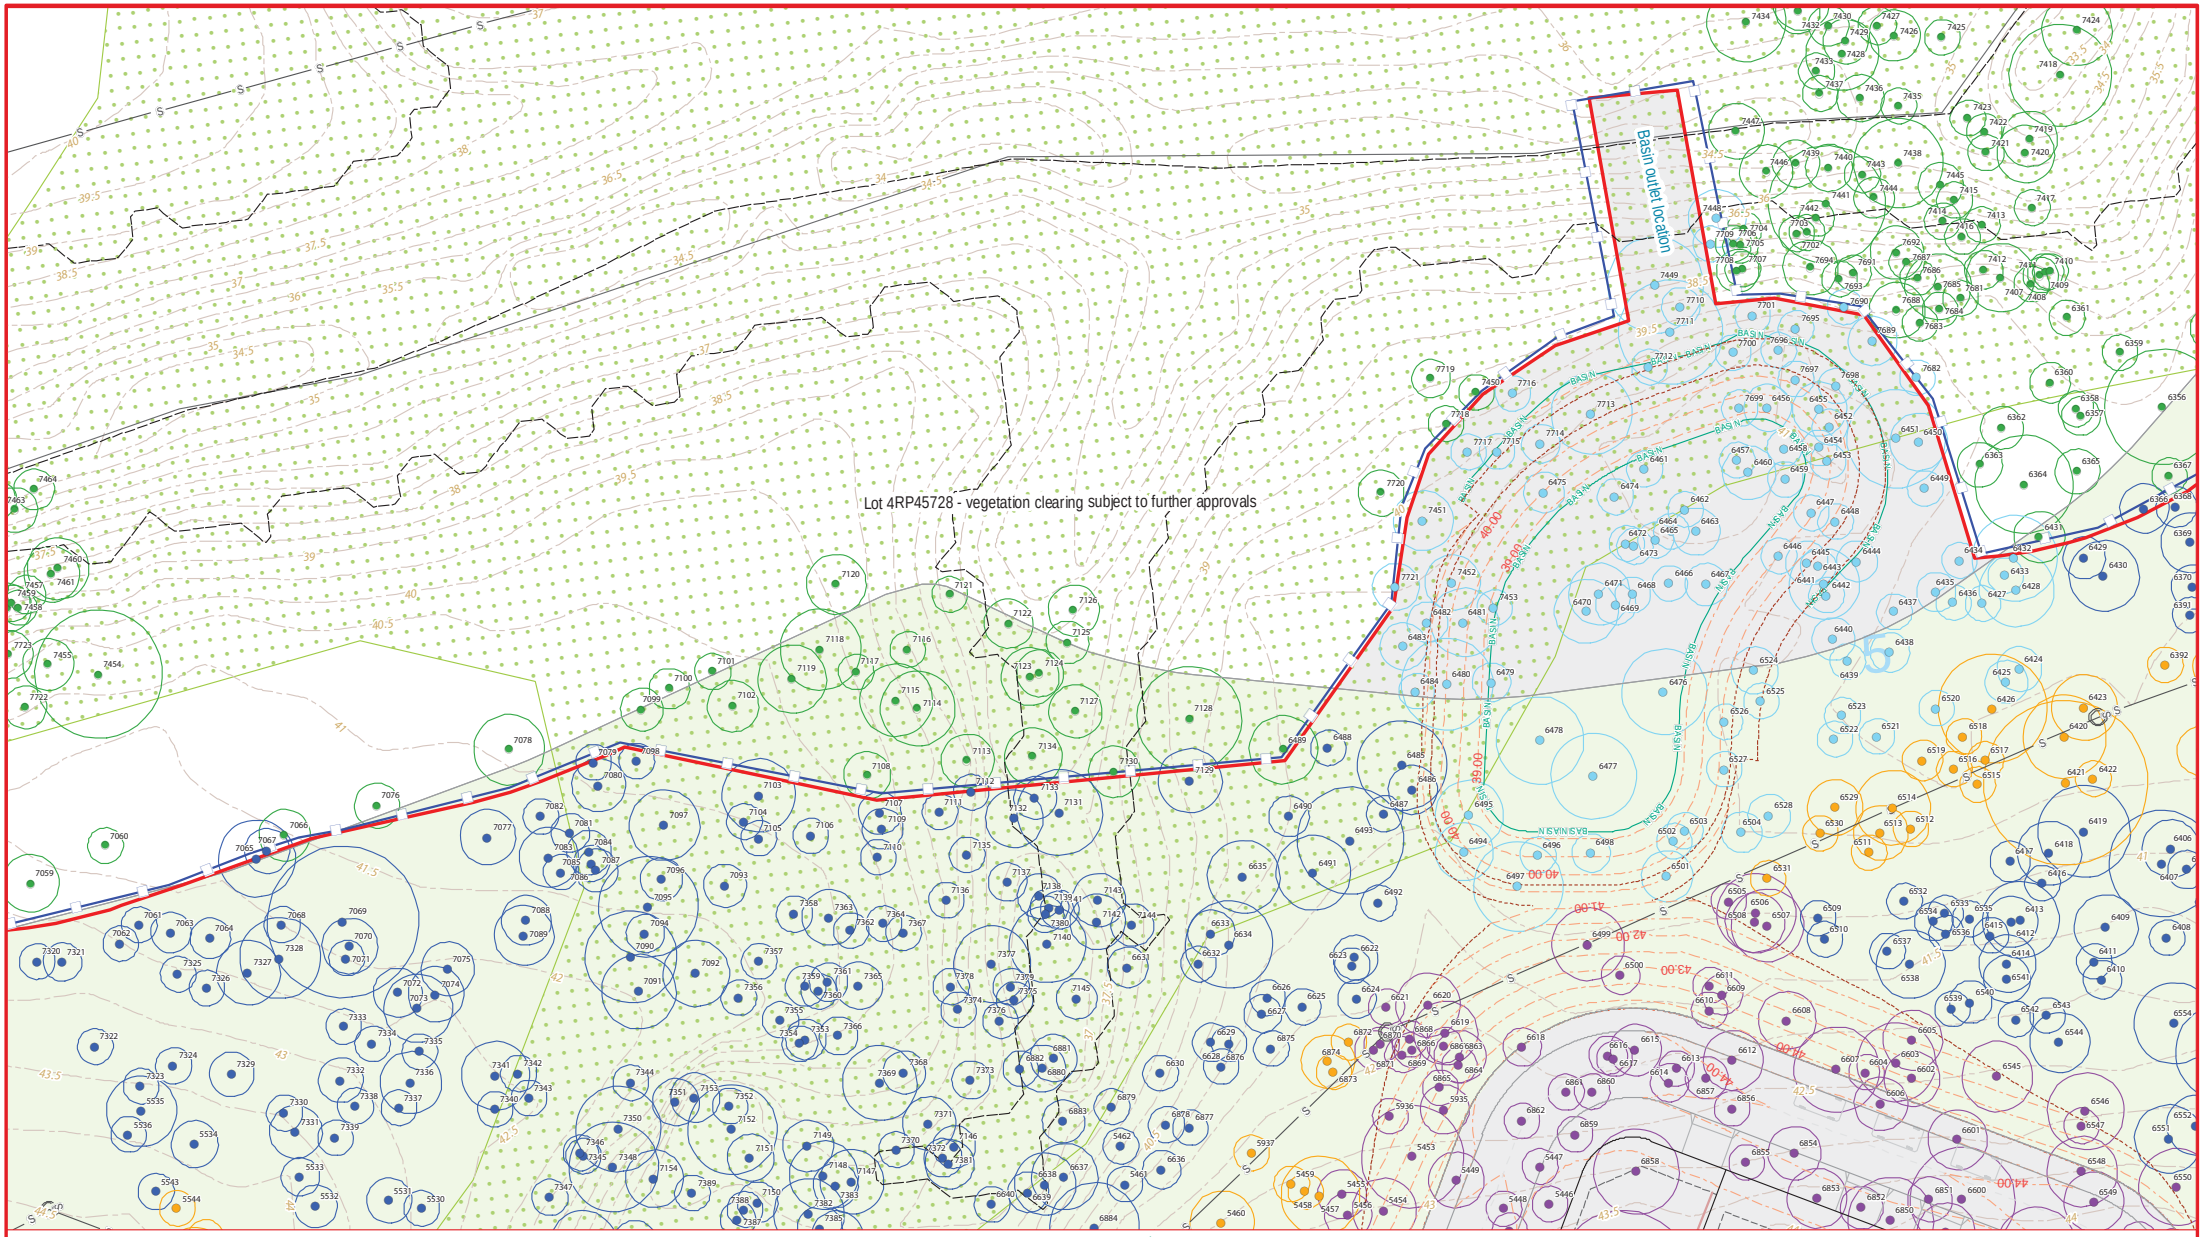

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 65

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF: 8047	DRAWN: TC

DRAWING No.: 8047 E 65 BAL Stage 2 VMP E

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 66

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 66 BAL Stage 2 VMP E

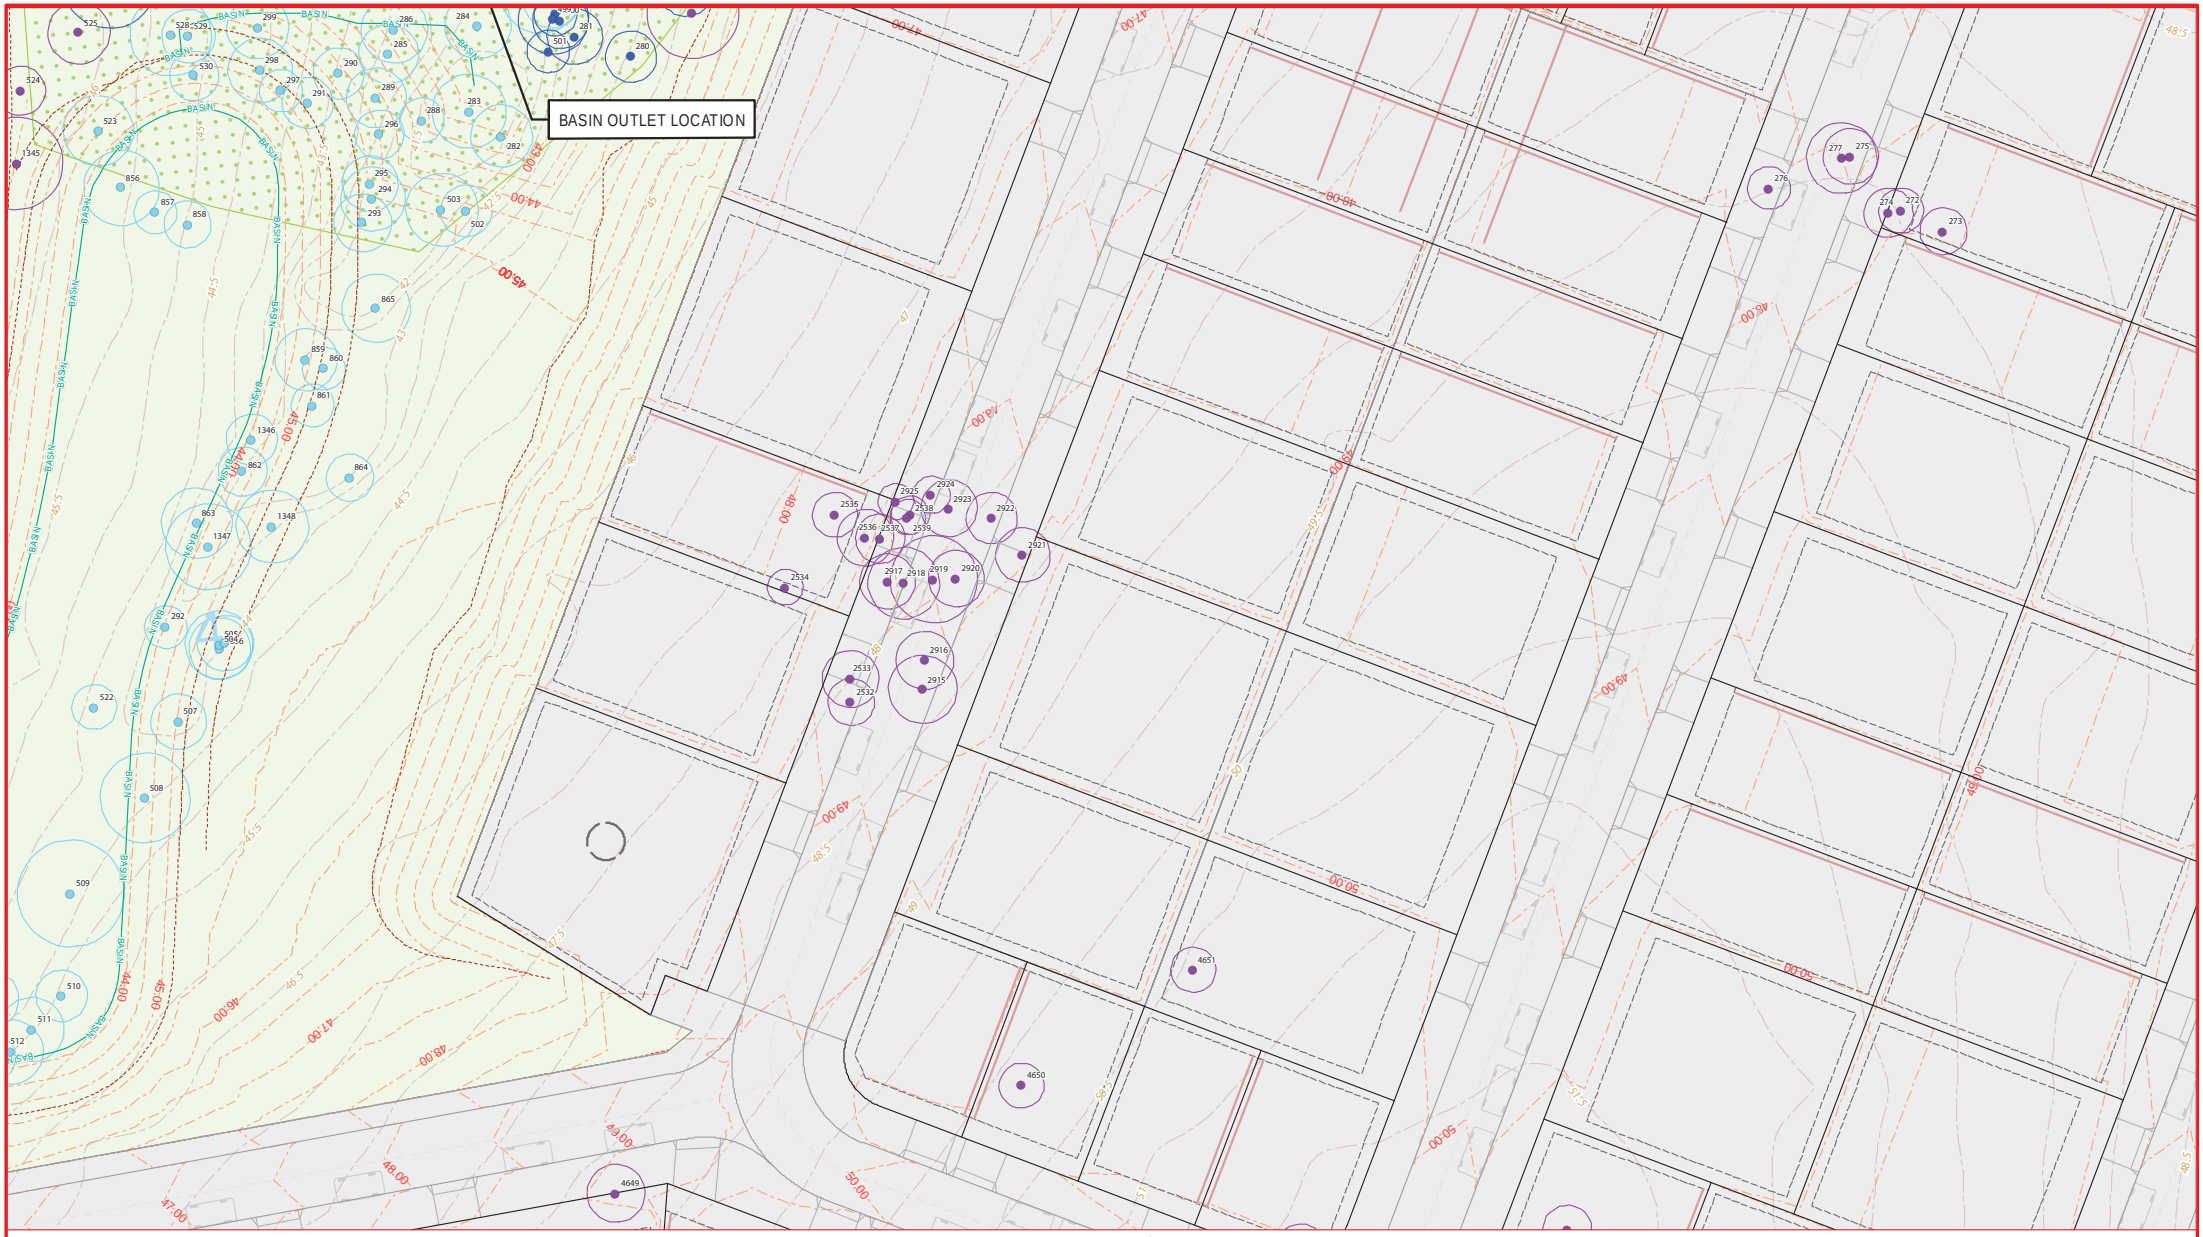

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 67

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 67 BAL Stage 2 VMP E

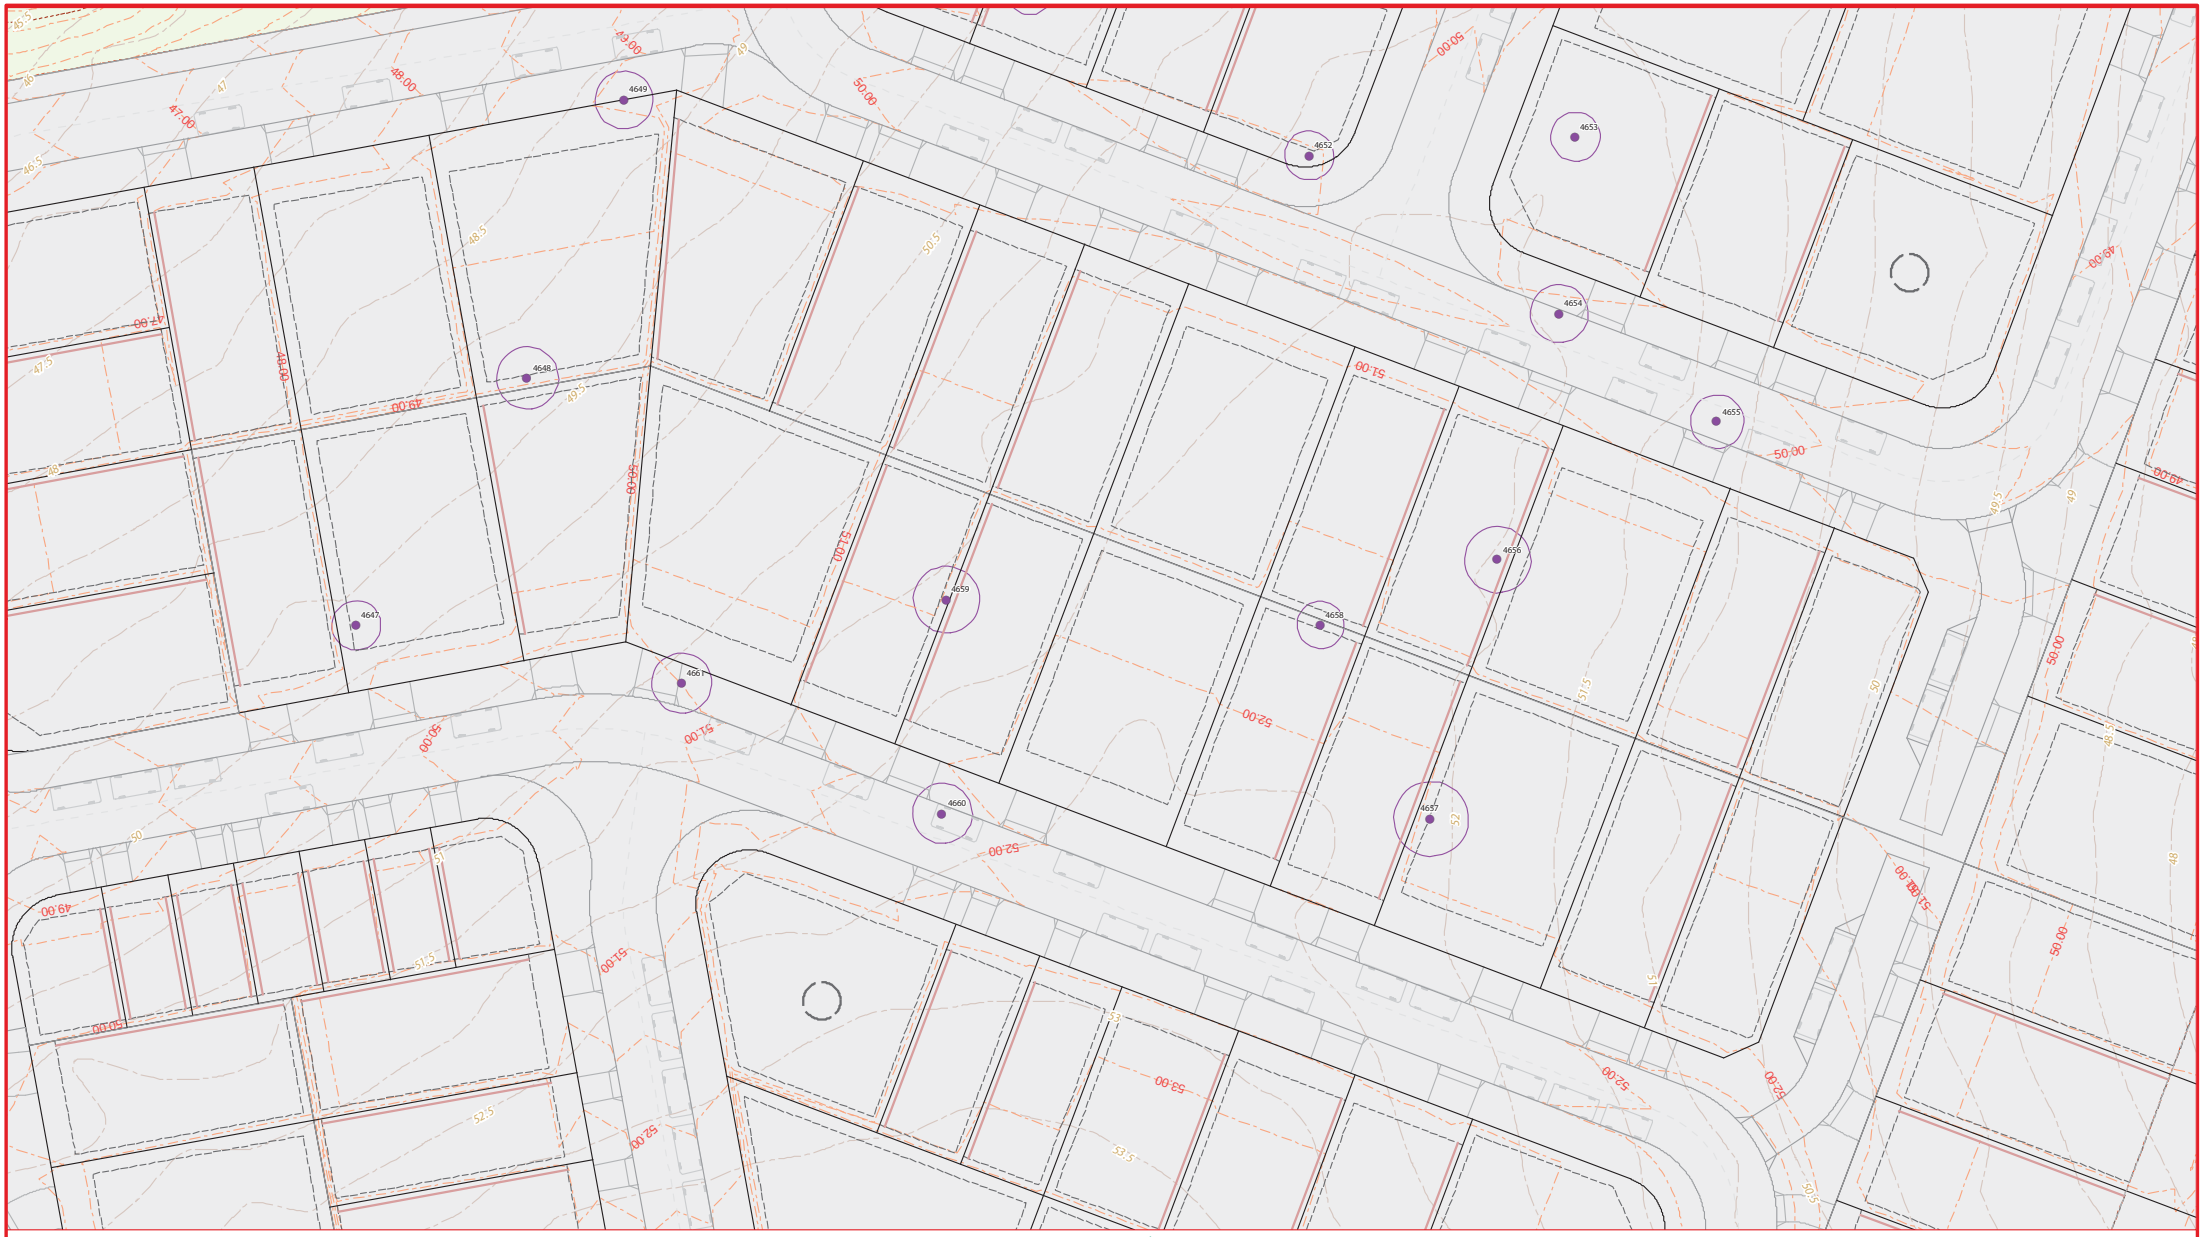

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 68

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THEEXCLUSIVE USE OF THE CLIENT.SAUNDERSHAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCEUPON THECONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ONSITE PRIOR TOCONSTRUCTION.ANDDO NOTSCALEFROM THDRAWINGS.ALL DIMENSIONS ARE IN MILLIMETRES.ANY DISCREPANCIESSHOULDBE CLARIFIEDIN WRITINGWITH SAUNDERS HAVILL GROUP PRIORTOTHECOMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTIONON SITE,THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUNDSERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC
DRAWING No.:	8047 E 68 BAL Stage 2 VMP E		

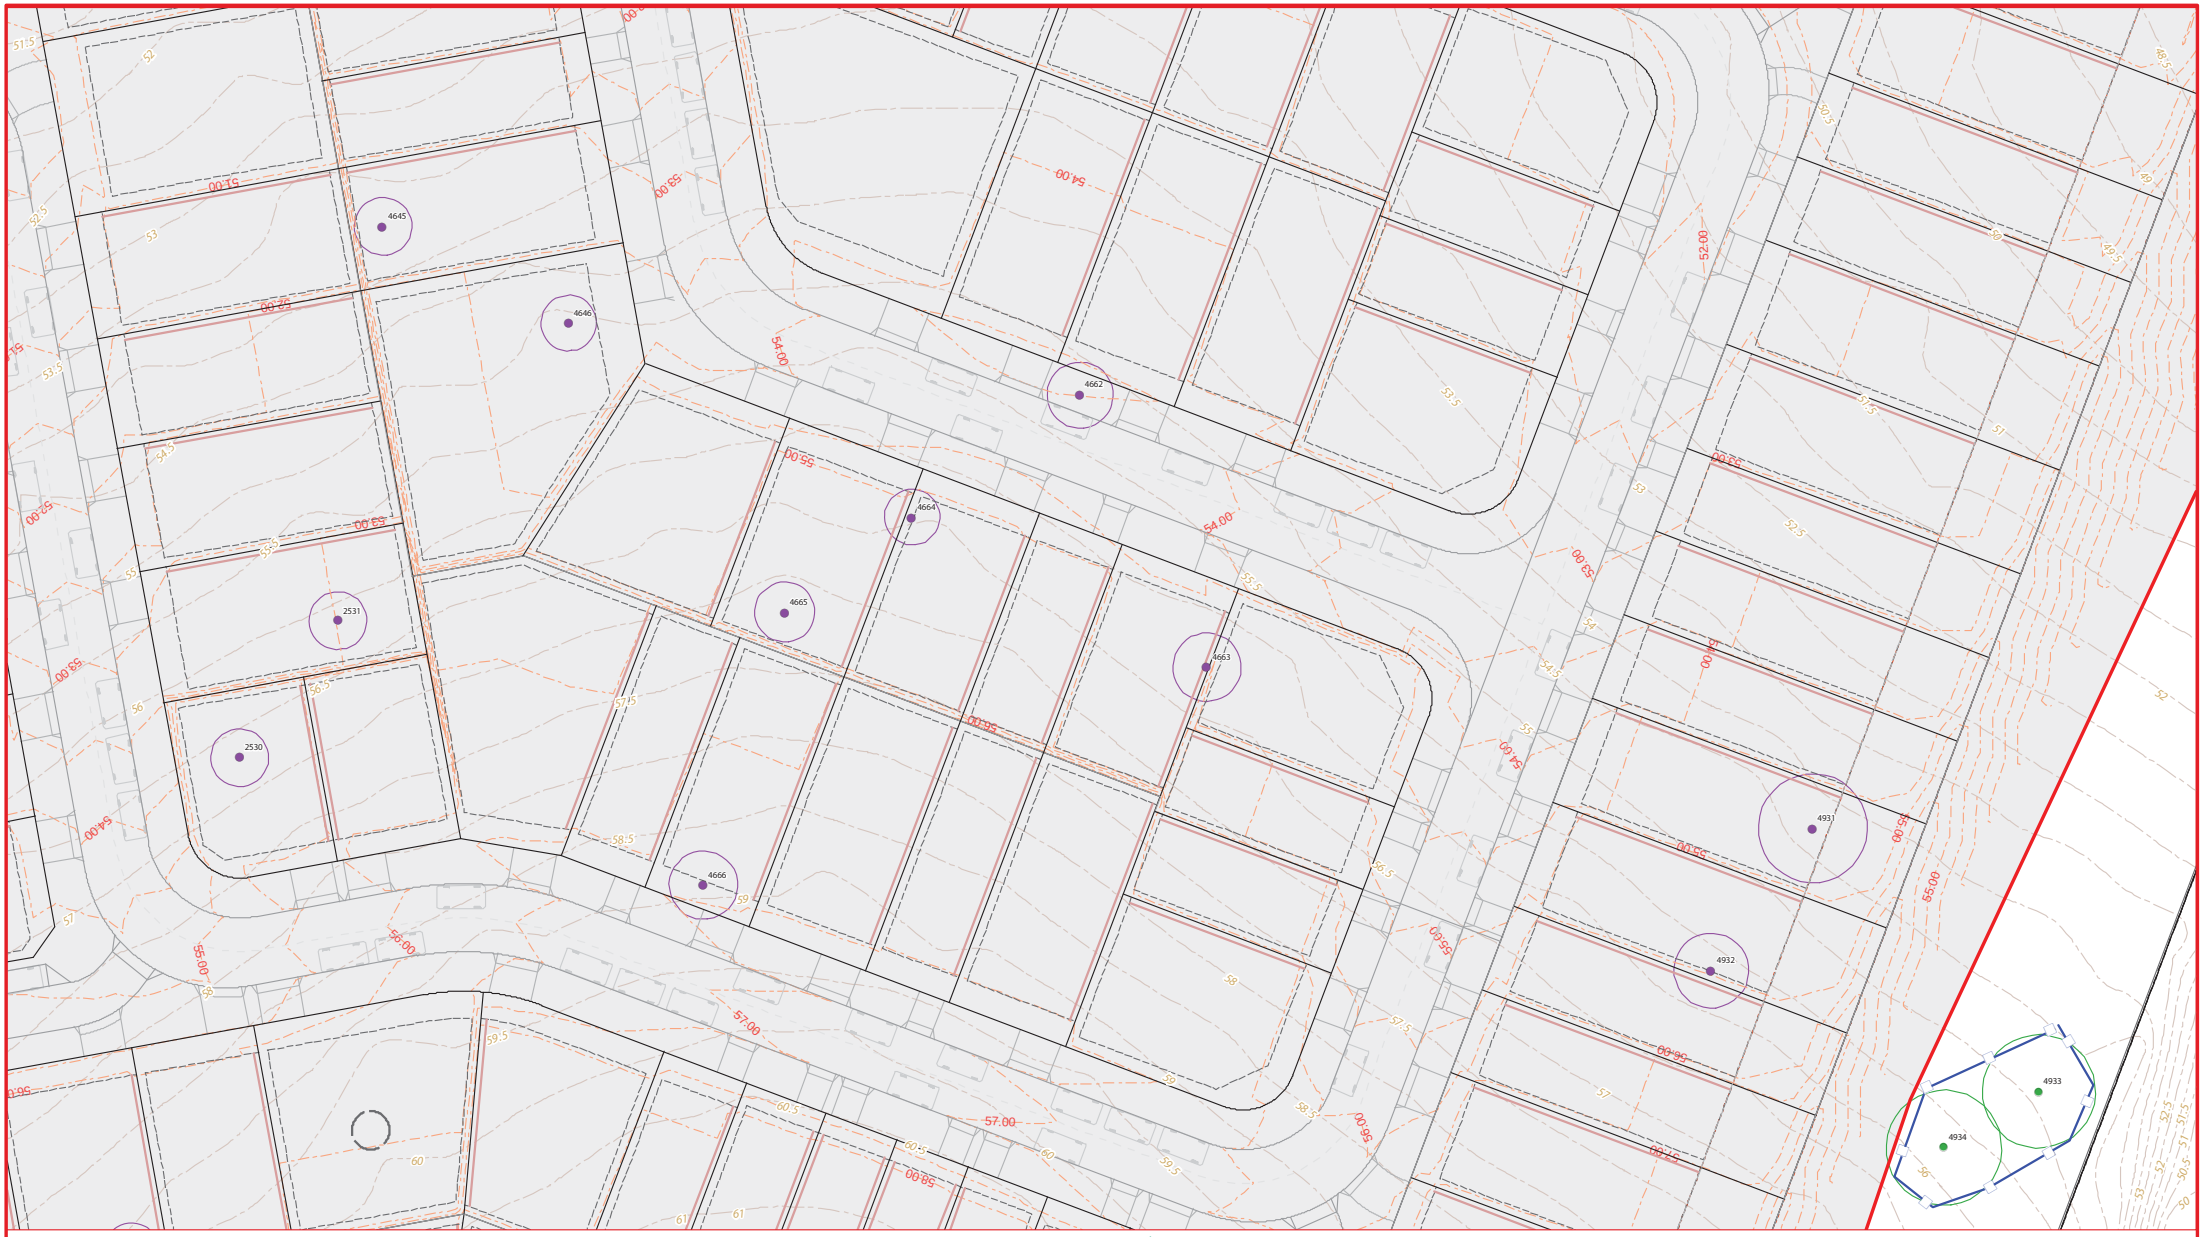

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- Civil trunk sewer
- Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 69

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 69 BAL Stage 2 VMP E	

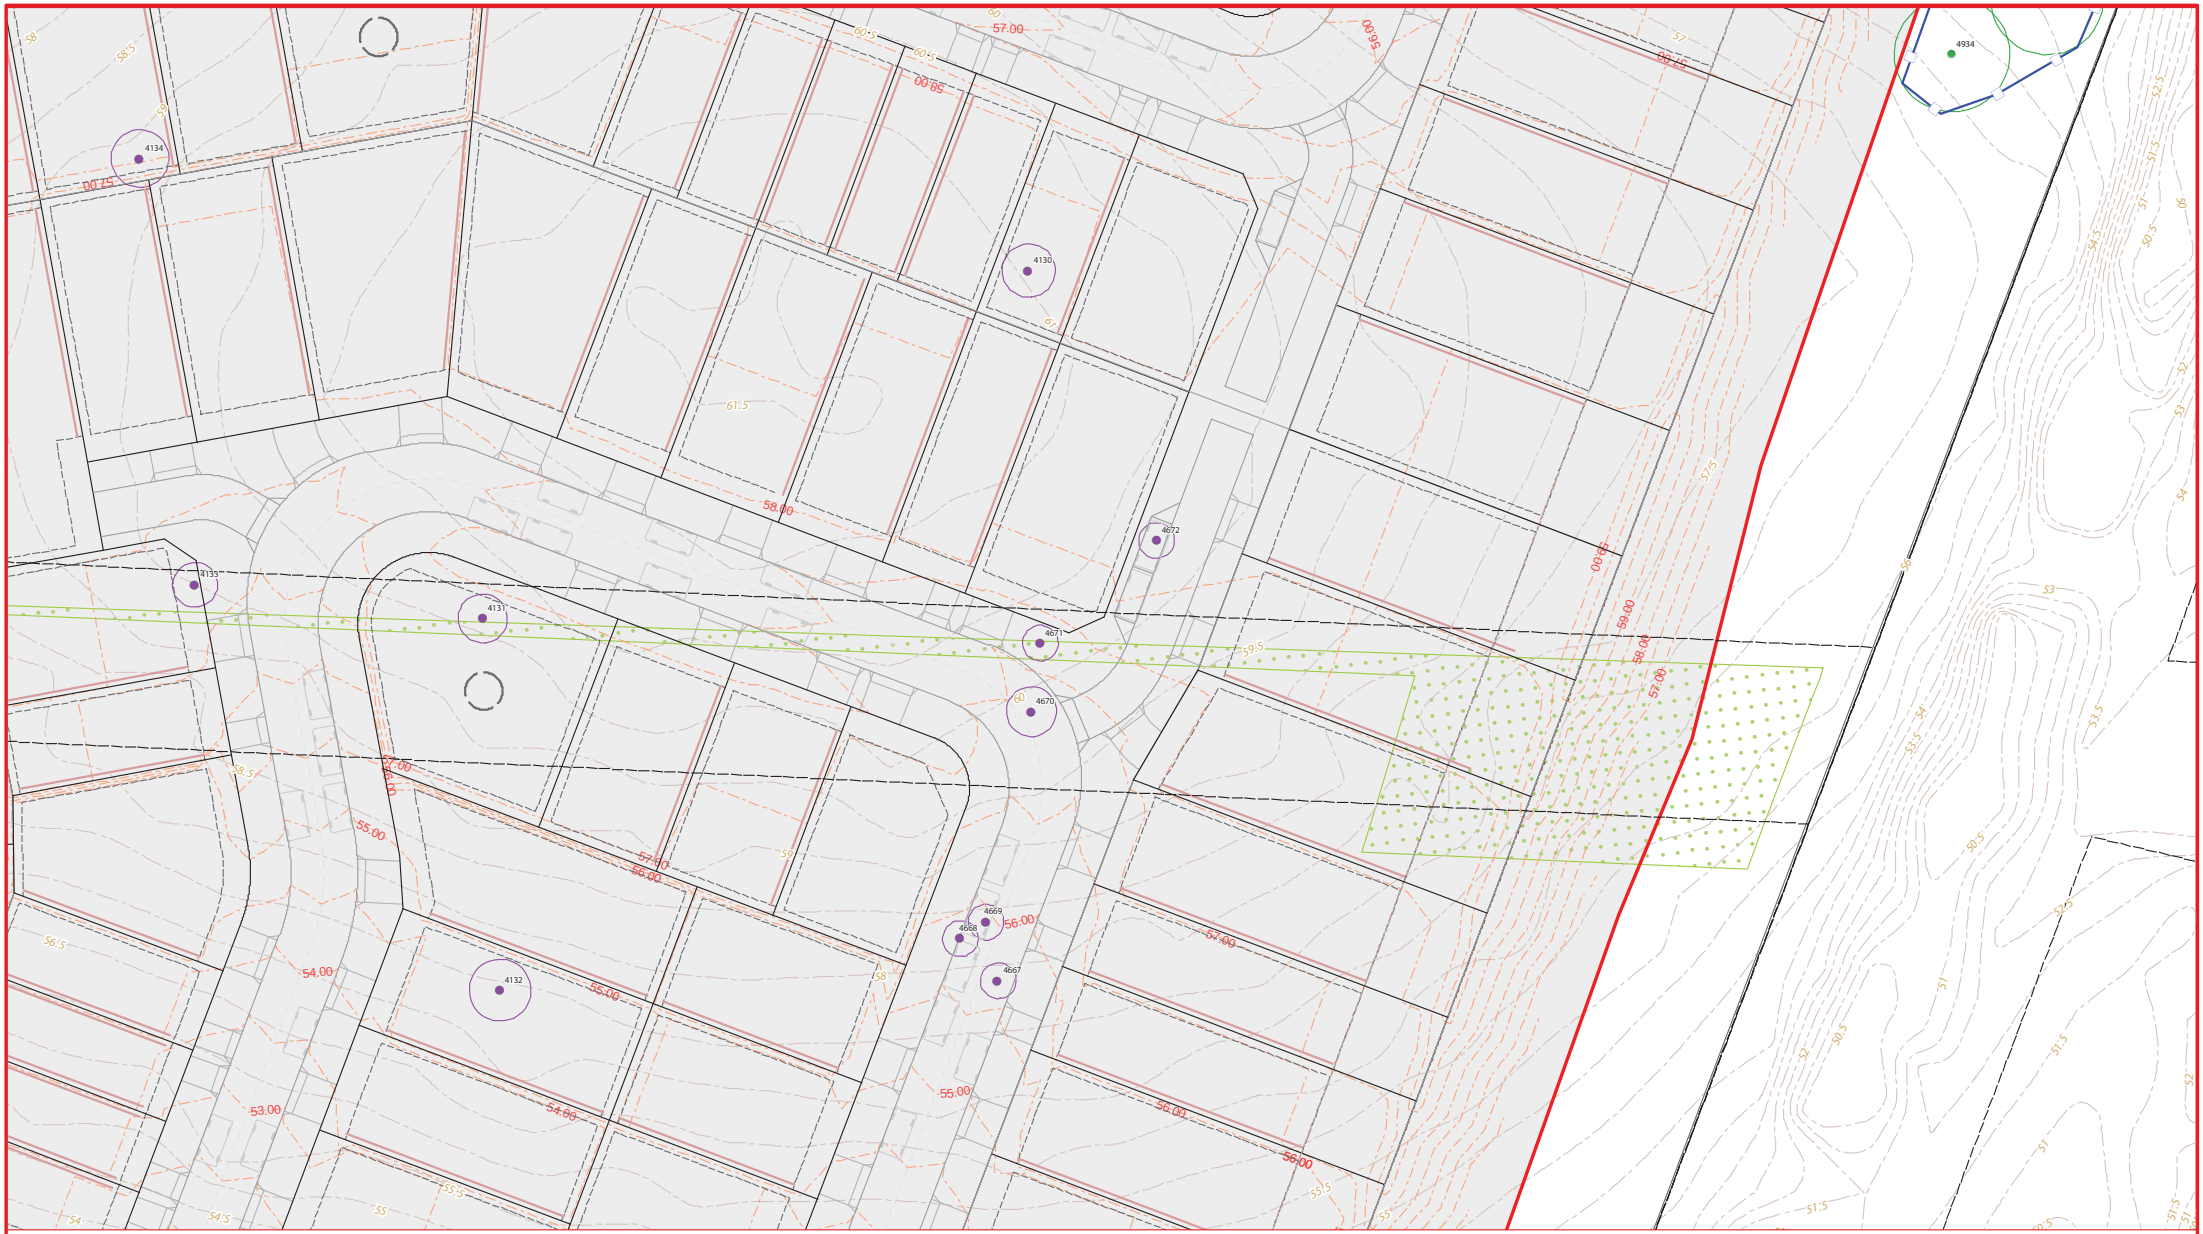

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 70

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 70 BAL Stage 2 VMP E	

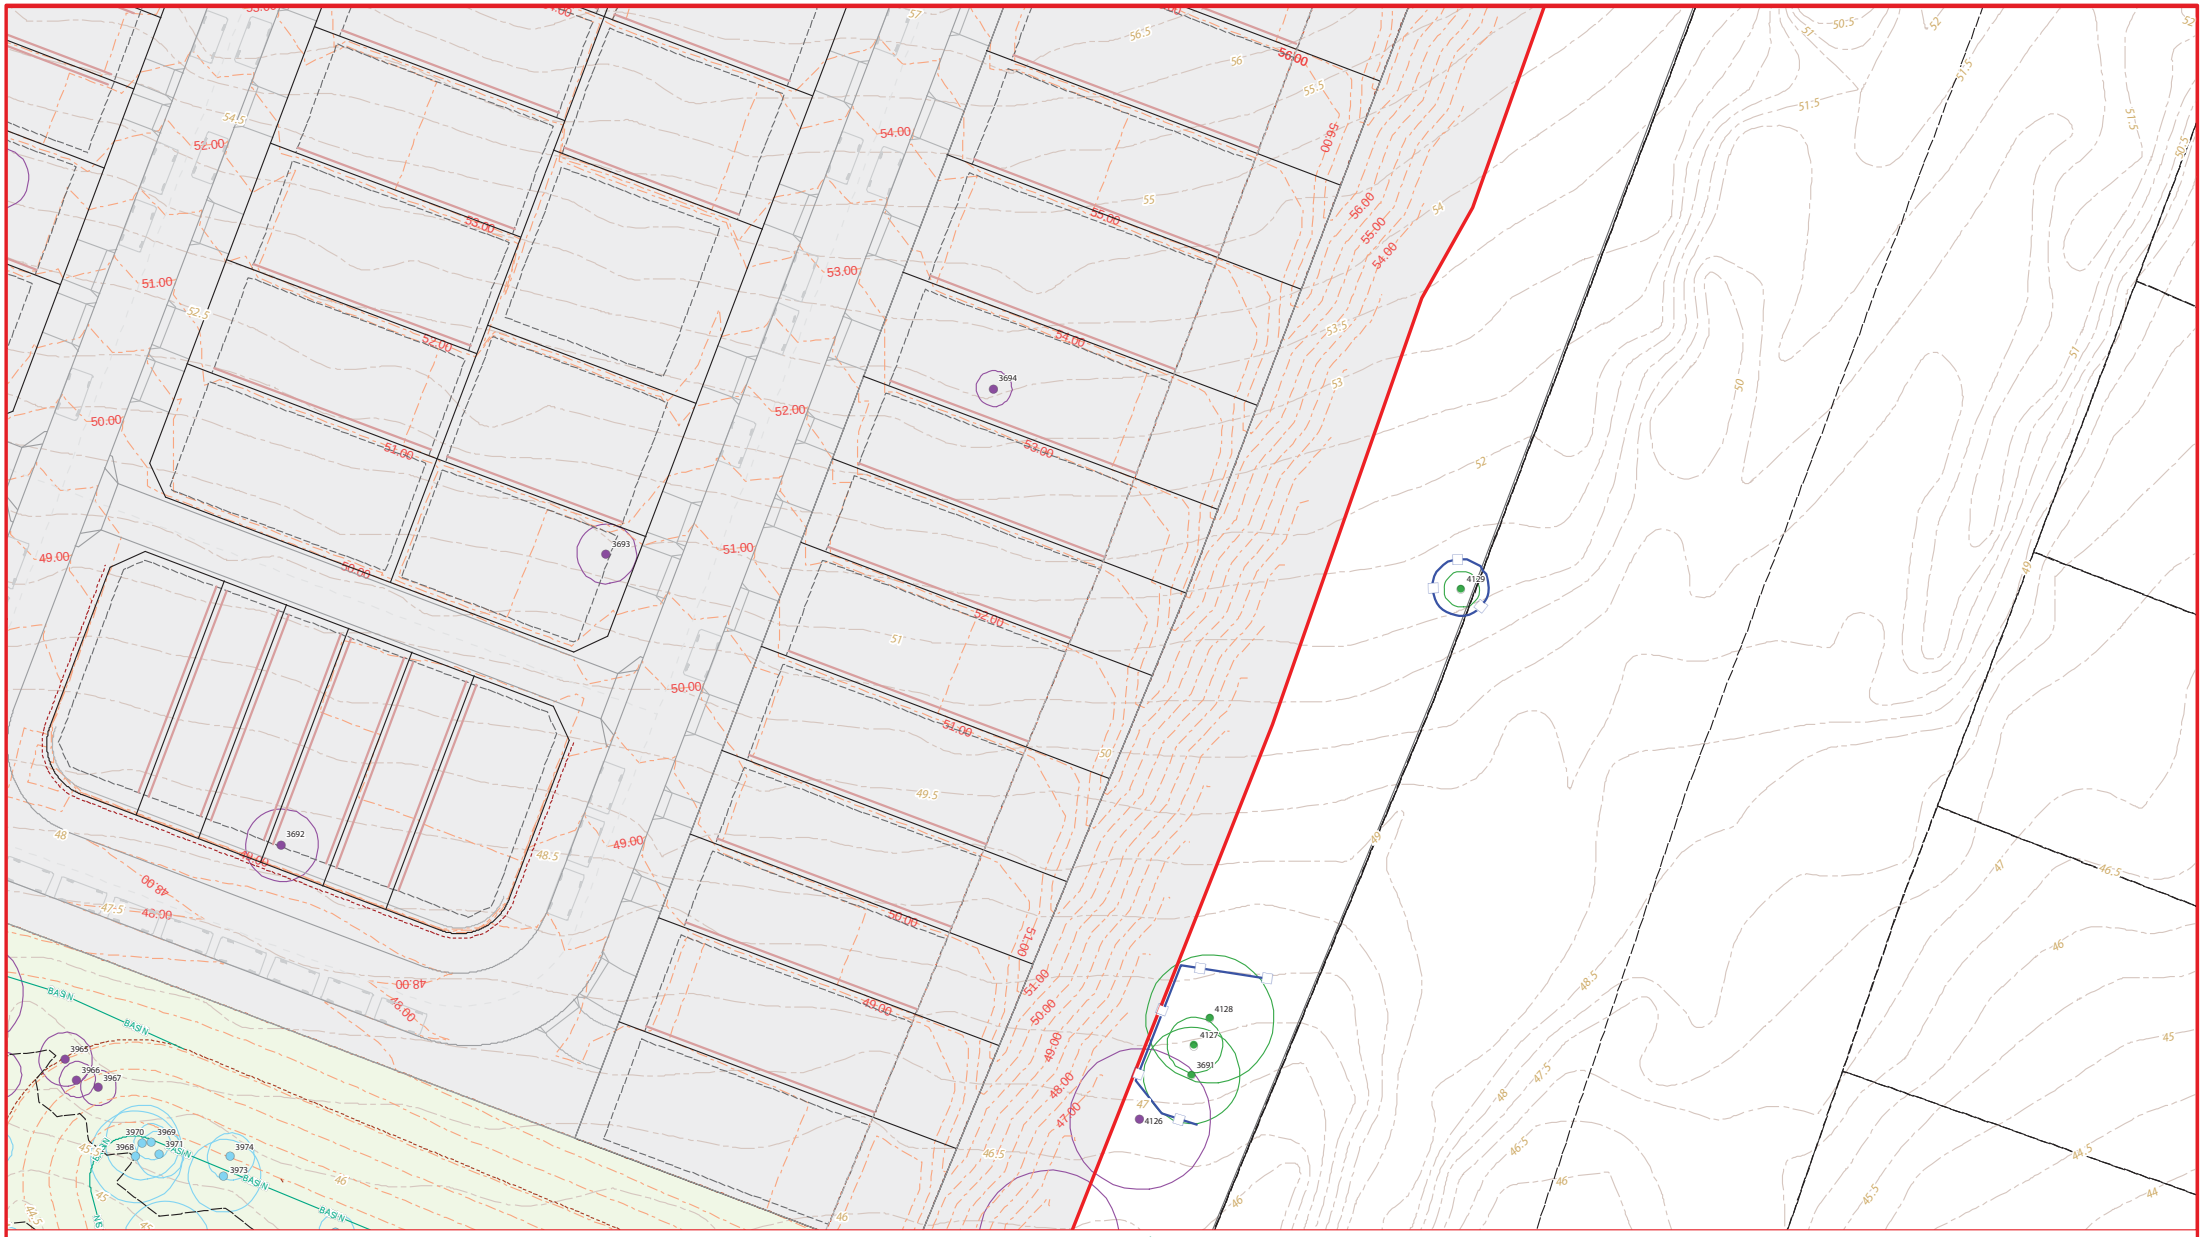

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 71

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC
DRAWING No.:	8047 E 71 BAL Stage 2 VMP E		

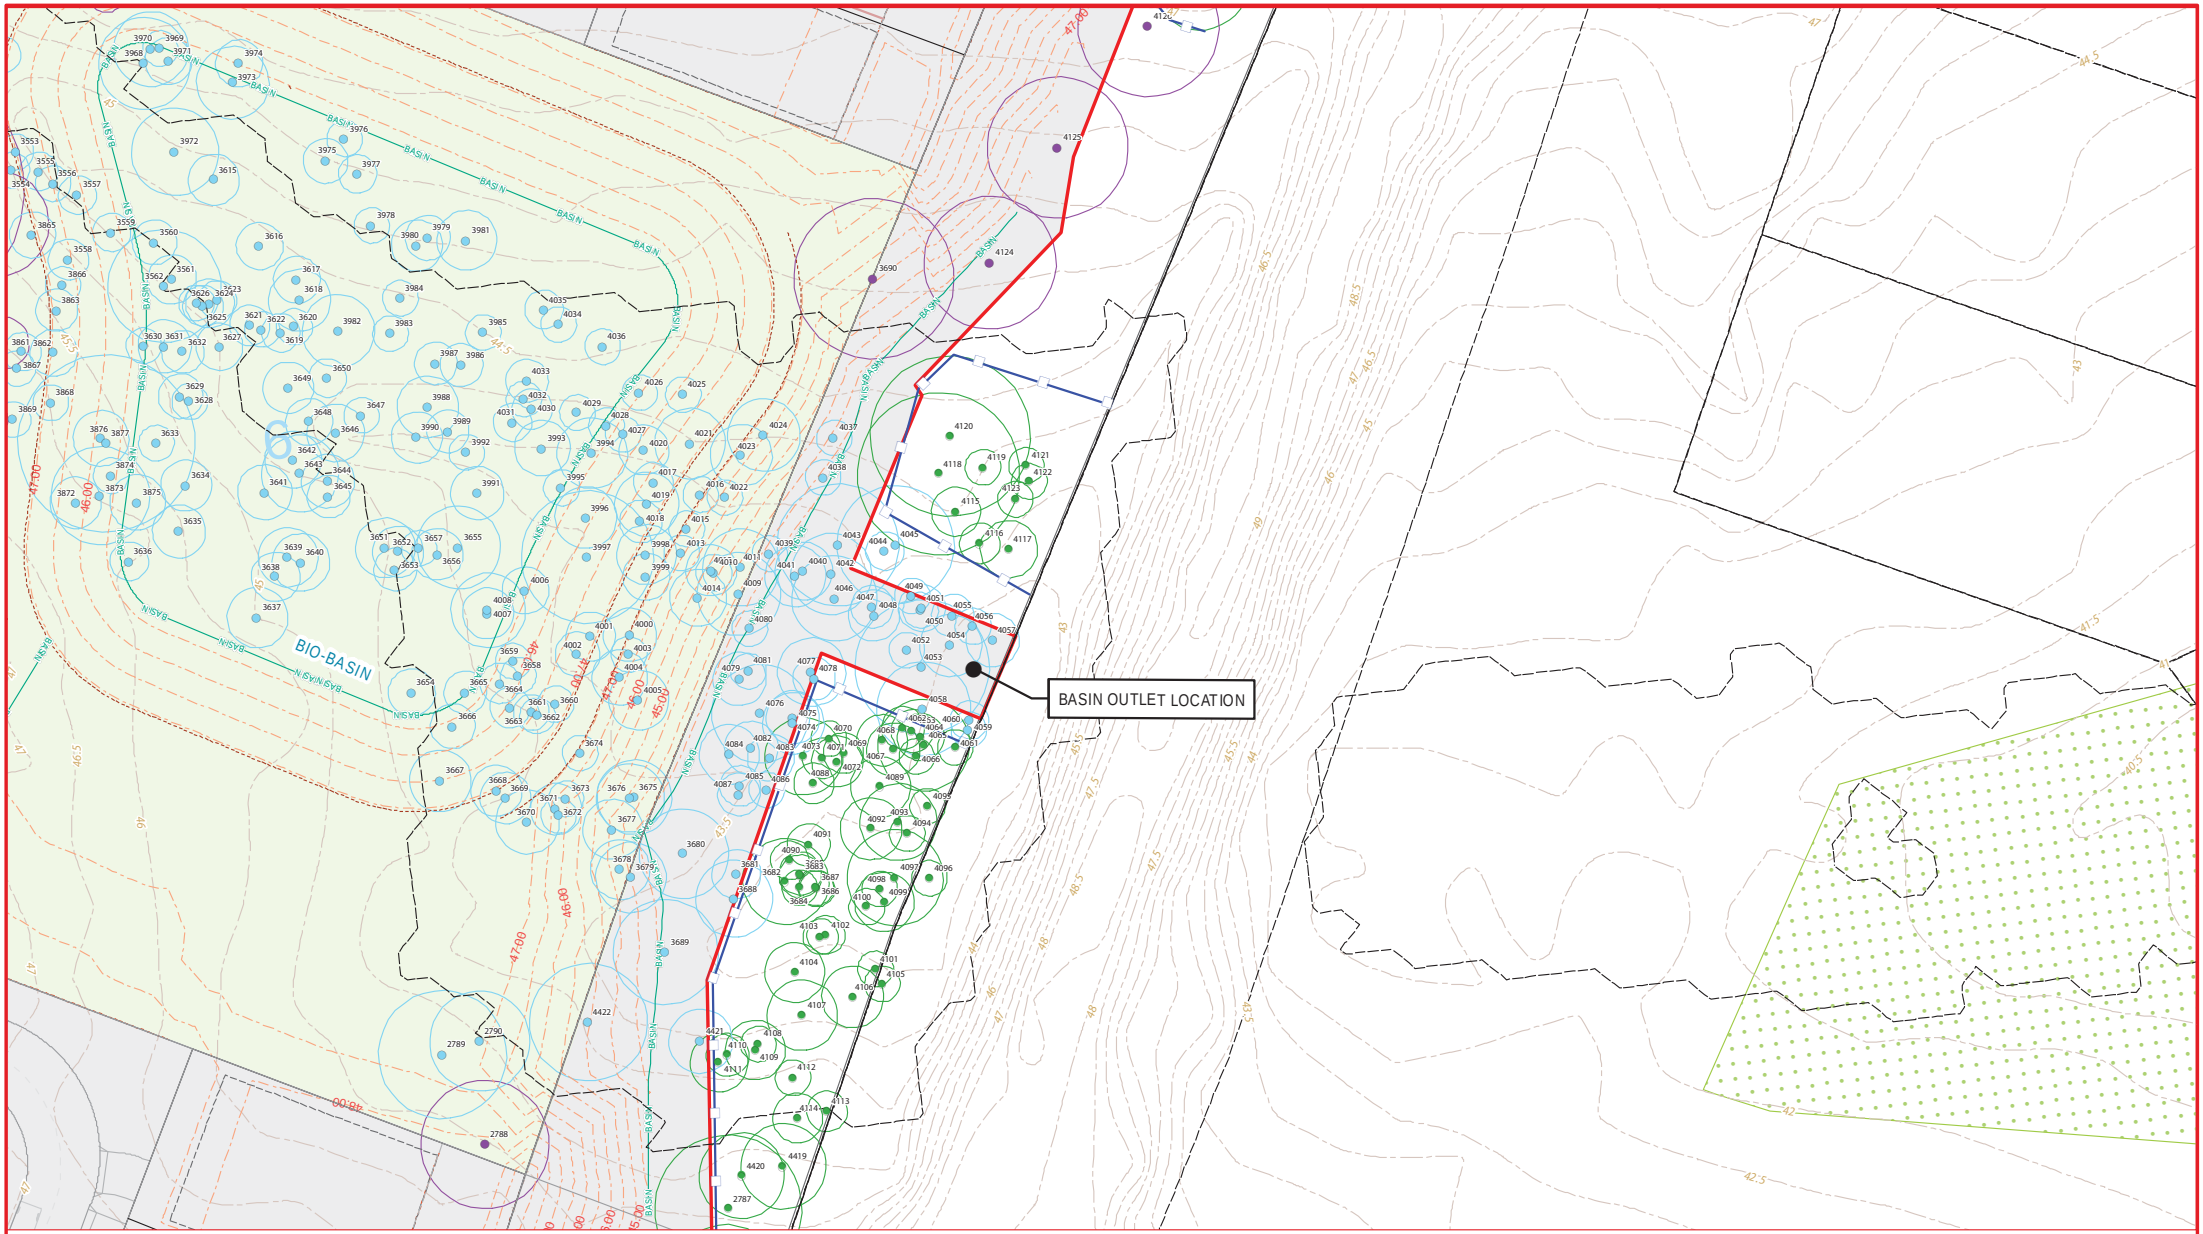

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

Civil trunk sewer

Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 72

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019 CHECKED: AD

JOB REF.: 8047 DRAWN: TC

DRAWING No.: 8047 E 72 BAL Stage 2 VMP E

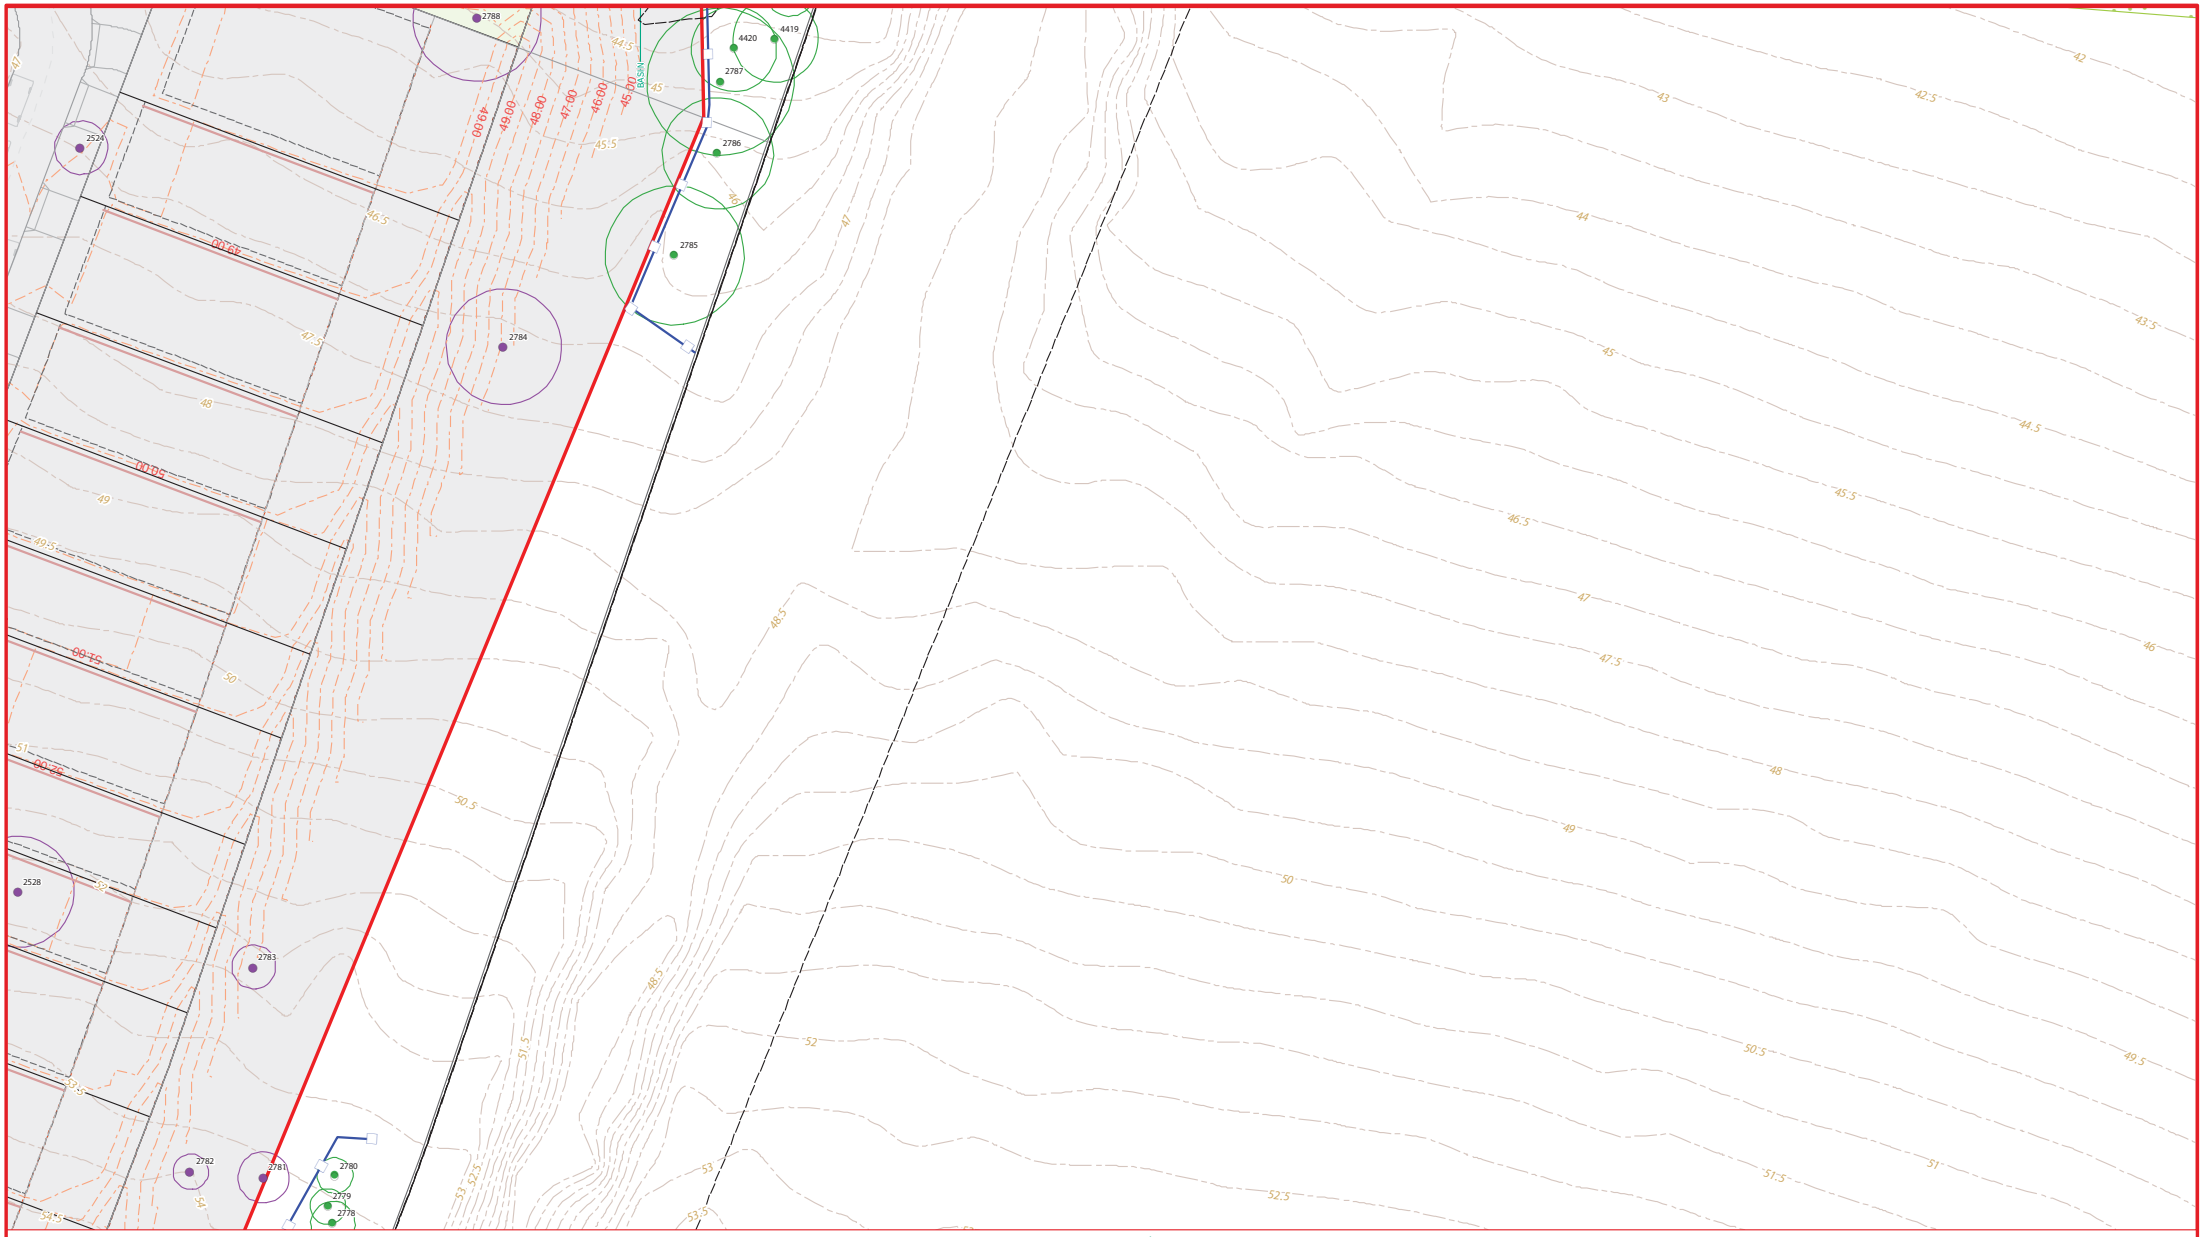

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 73

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 73 BAL Stage 2 VMP E

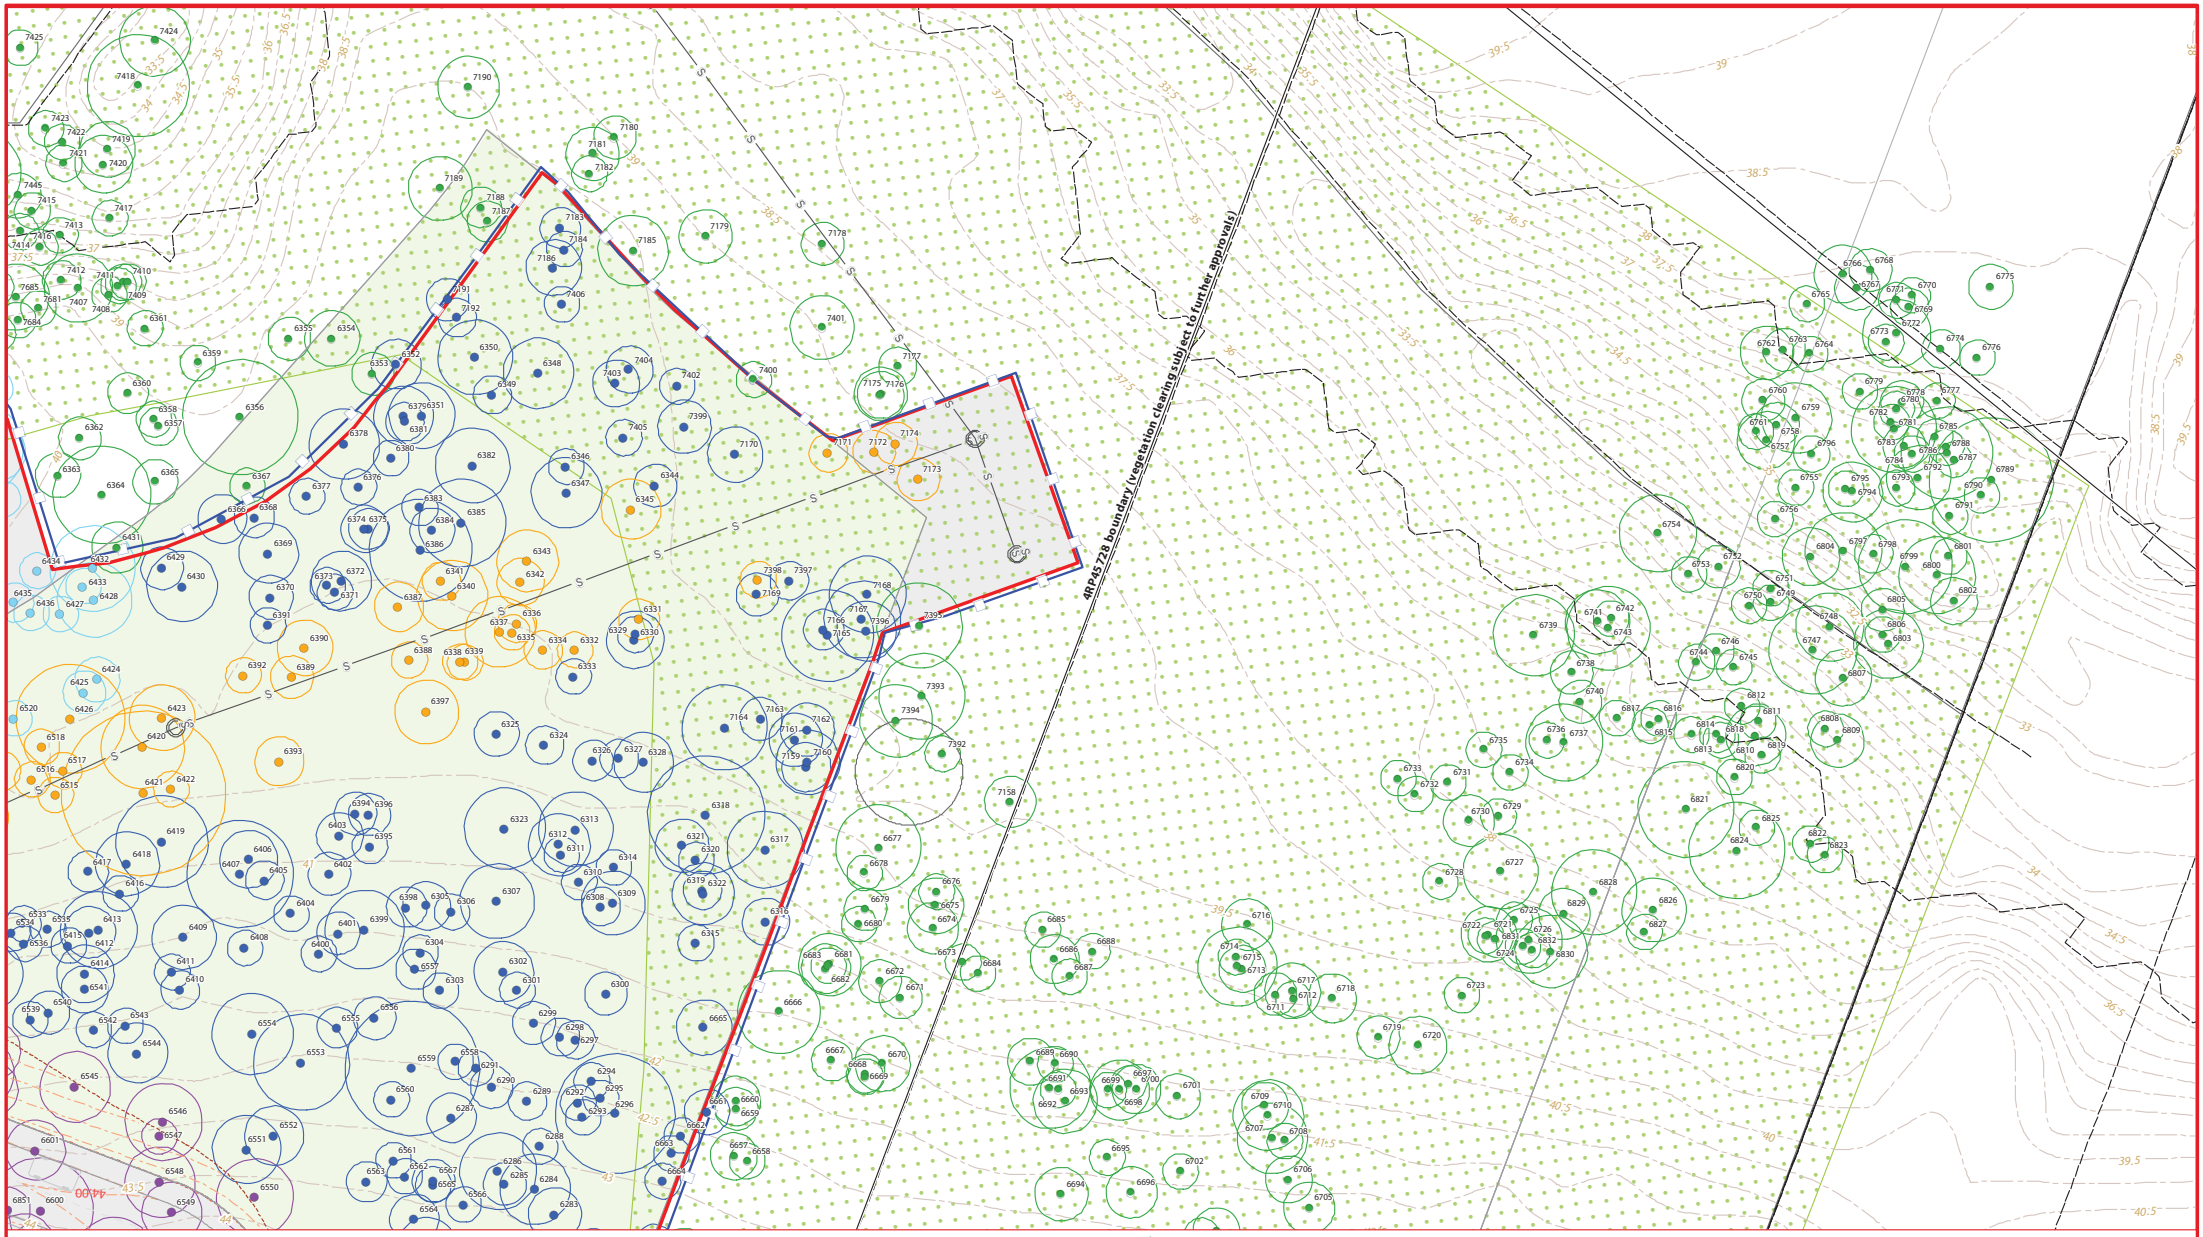

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 74

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 74 BAL Stage 2 VMP E	

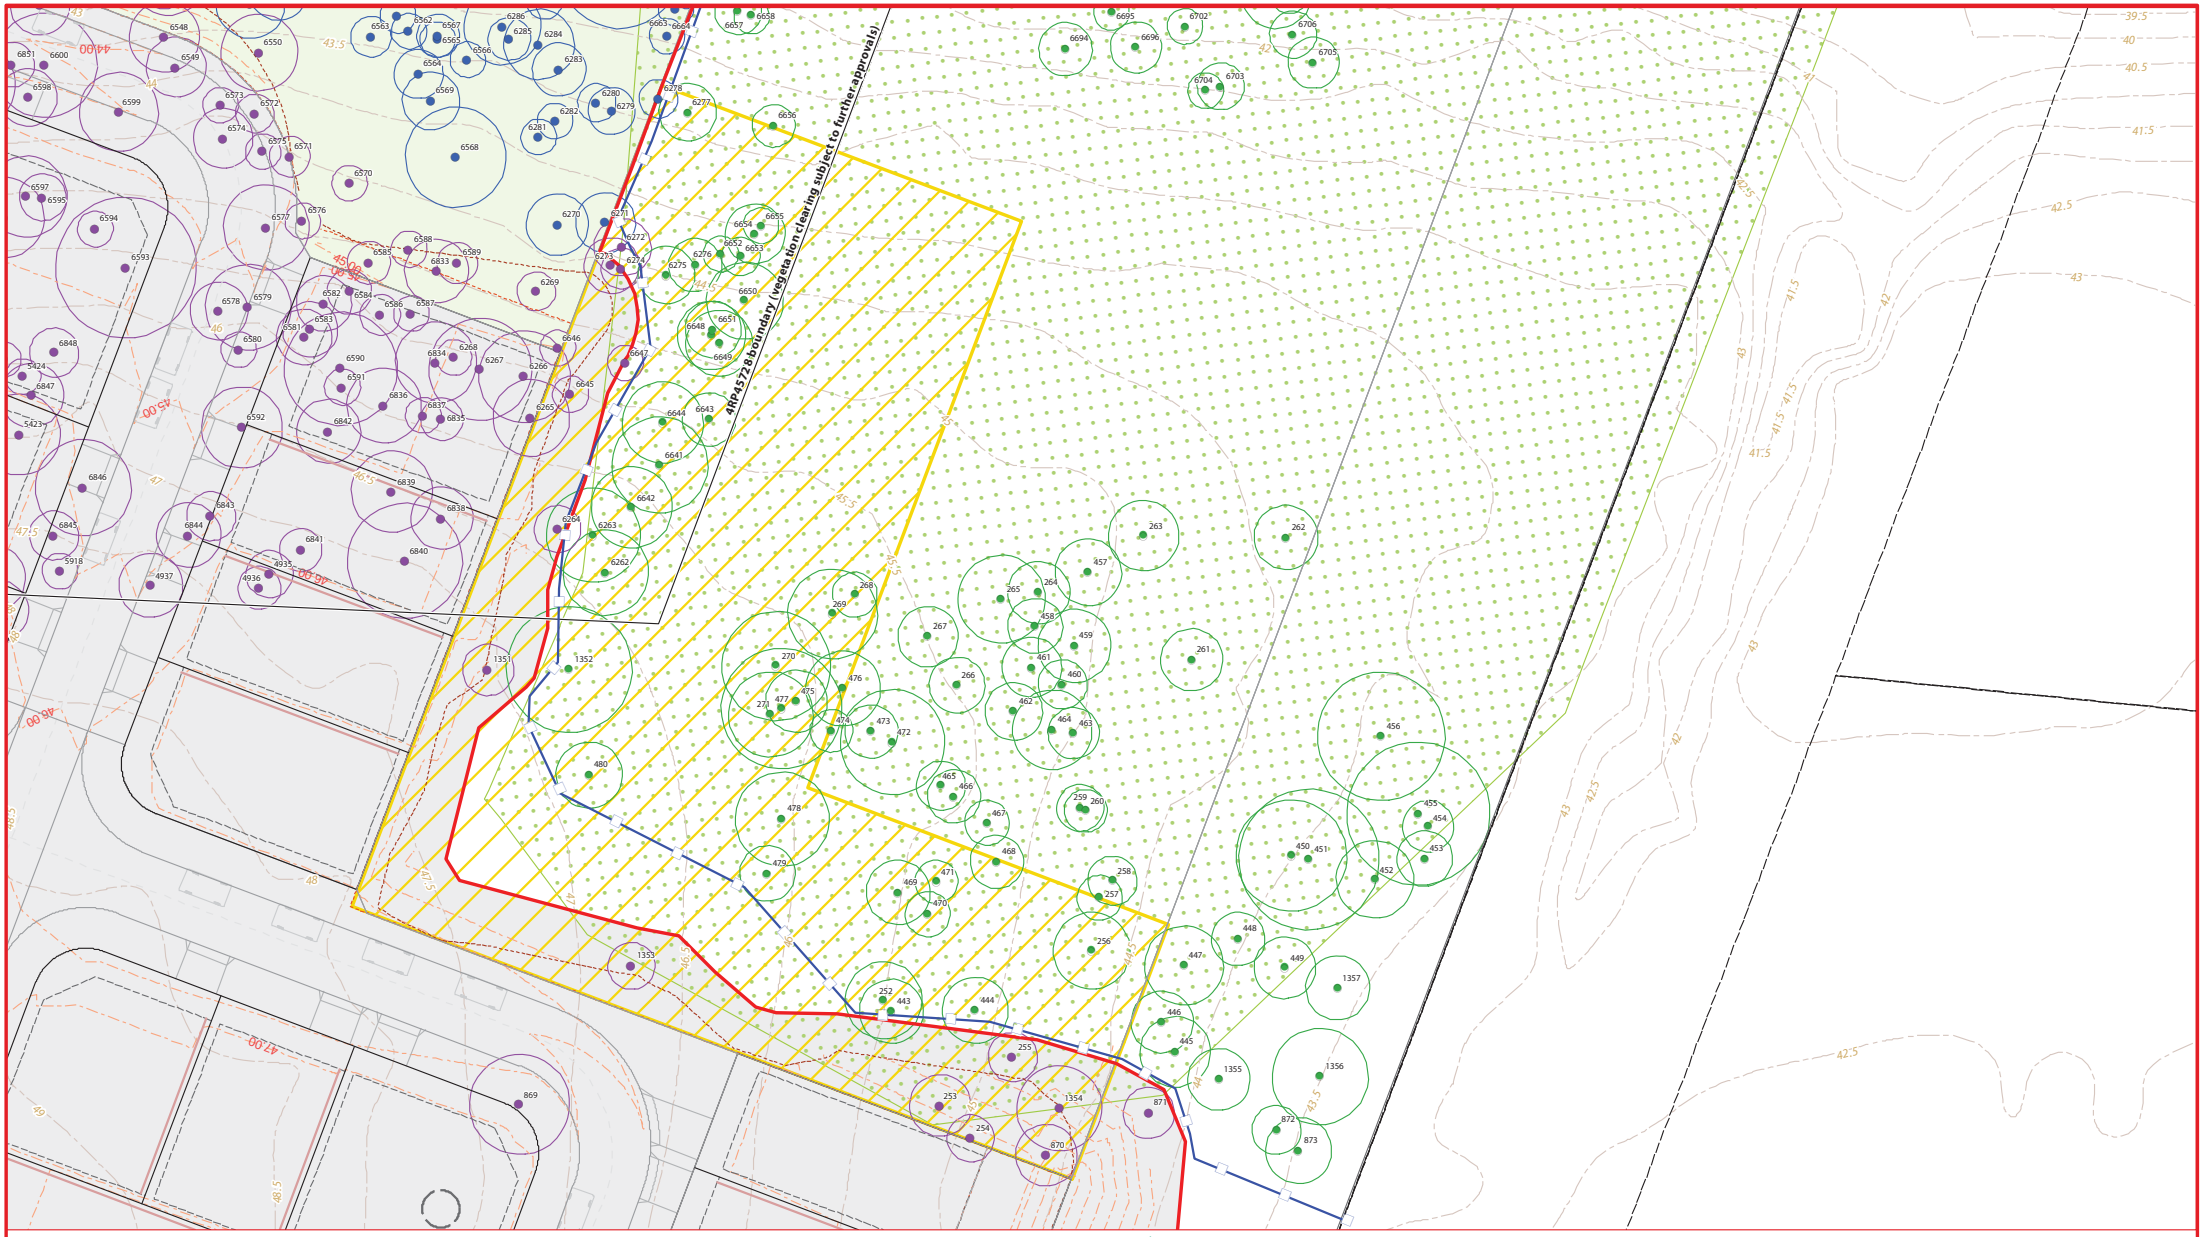

Tree (with TPZ) to retain

Tree (with TPZ) to remove in development design/ construction acess

Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management

Tree (with TPZ) to remove for trunk sewer works

Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design

Tree to remove as part of theStage 2-5 Phase 1 /School VMP application

Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)

Stage boundary

Proposed lots

Road pavement design

S — S Civil trunk sewer

BASIN Conceptual civil basin location - batters TBC at detail design stage

Building envelopes

Civil batter top/toe (ind. basins)

Civil design contours for development area

Stockpile location (indicative)

Bushfire Managed Zone - maintain cleared understory

Approved Phase 1 & School site VMP area

Existing New Beith Rd (dirt track)

Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer

Remnant Vegetation extent

Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 75

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 75 BAL Stage 2 VMP E	

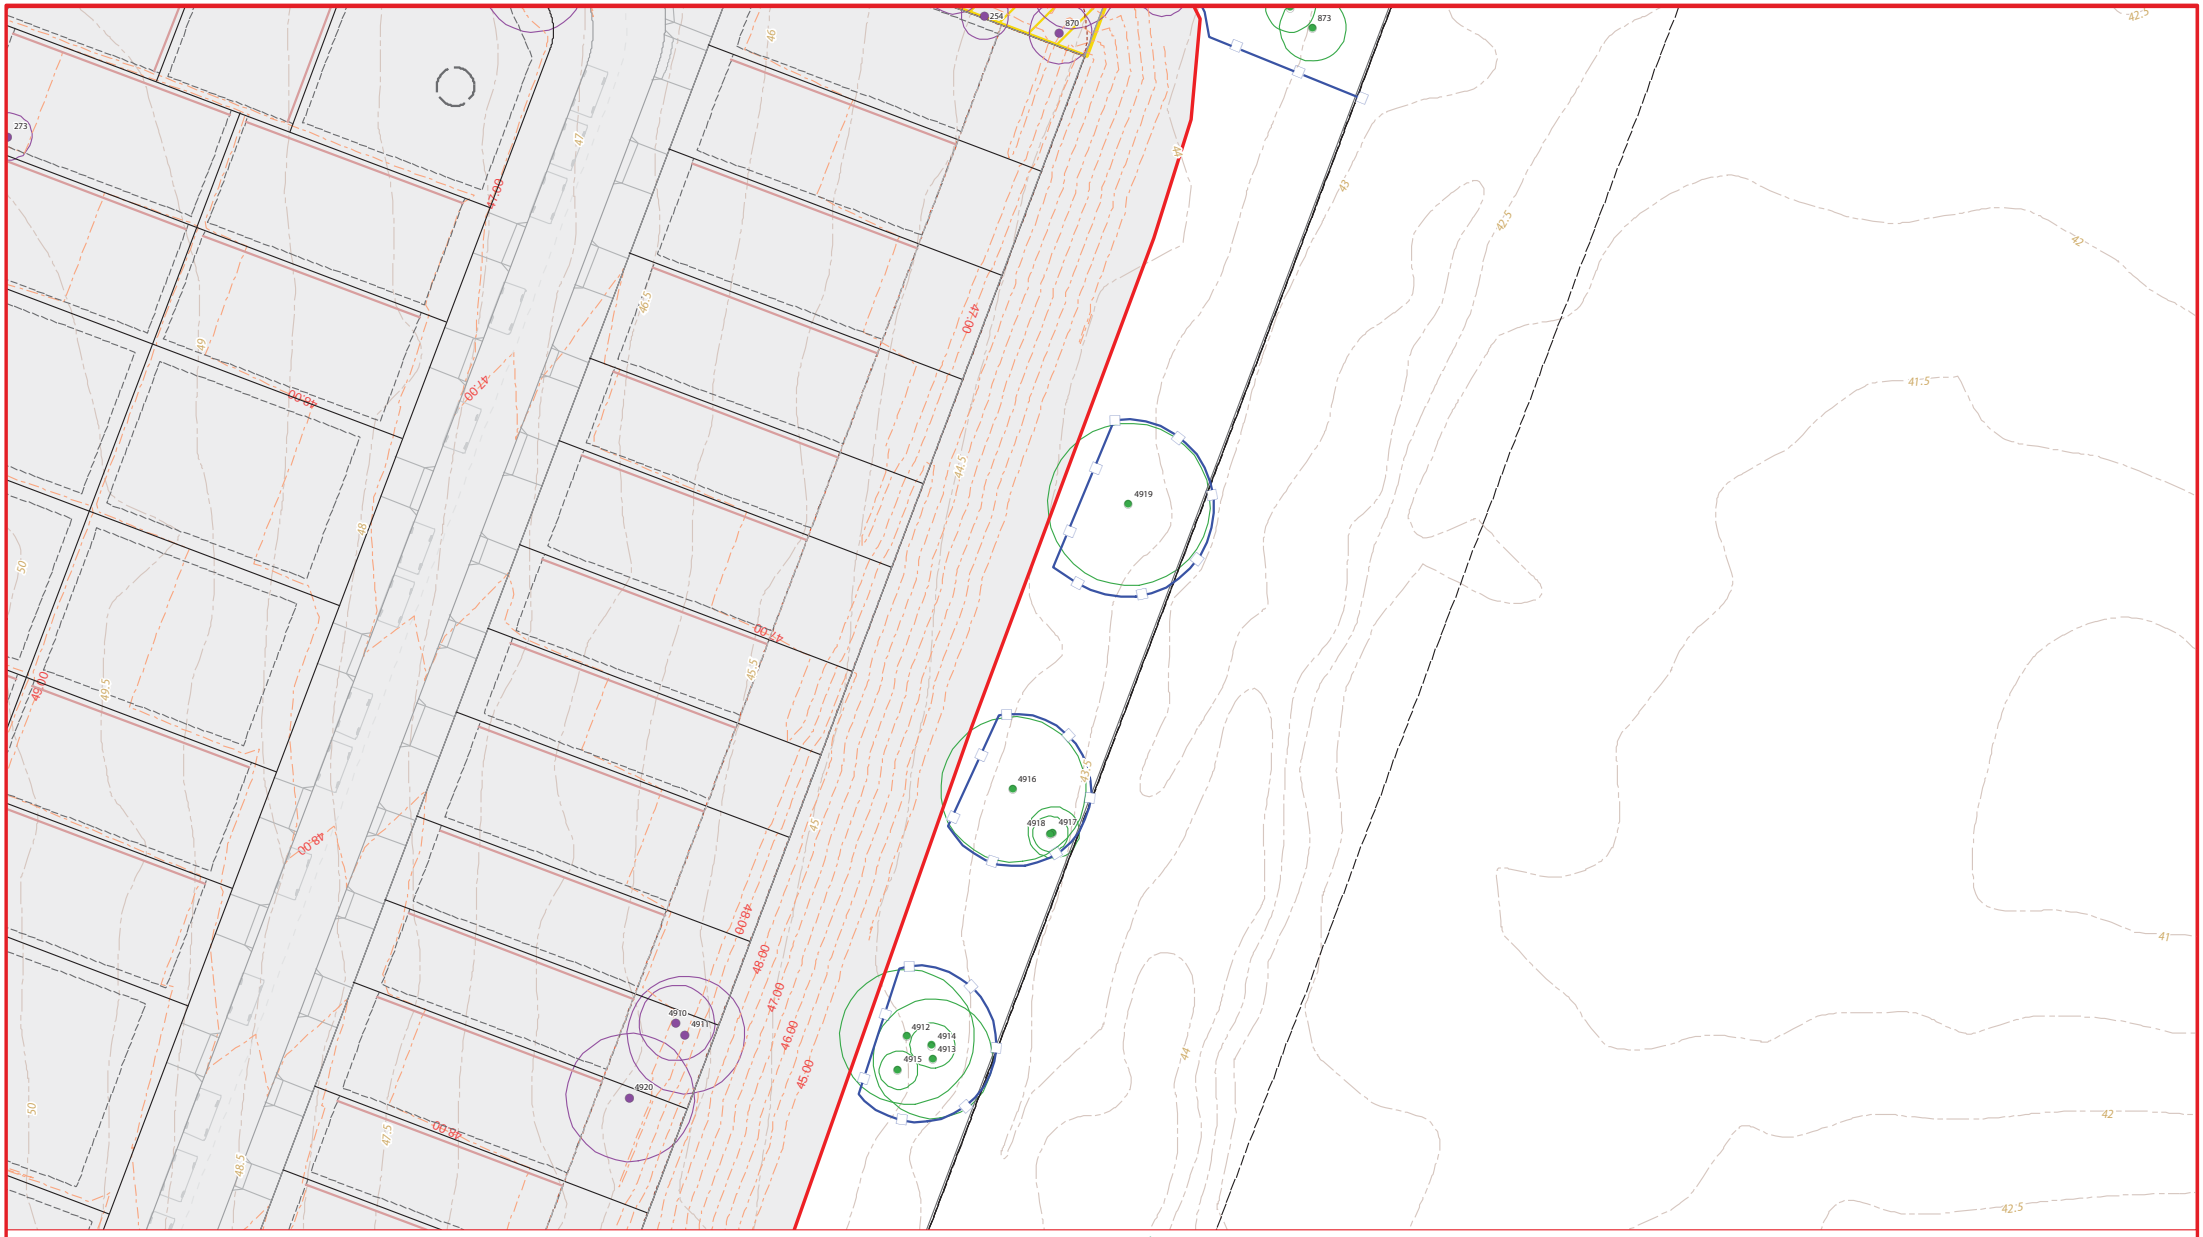

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 76

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THIS DRAWING AS ALL DIMENSIONS ARE IN MILLIMETRE'S. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 76 BAL Stage 2 VMP E

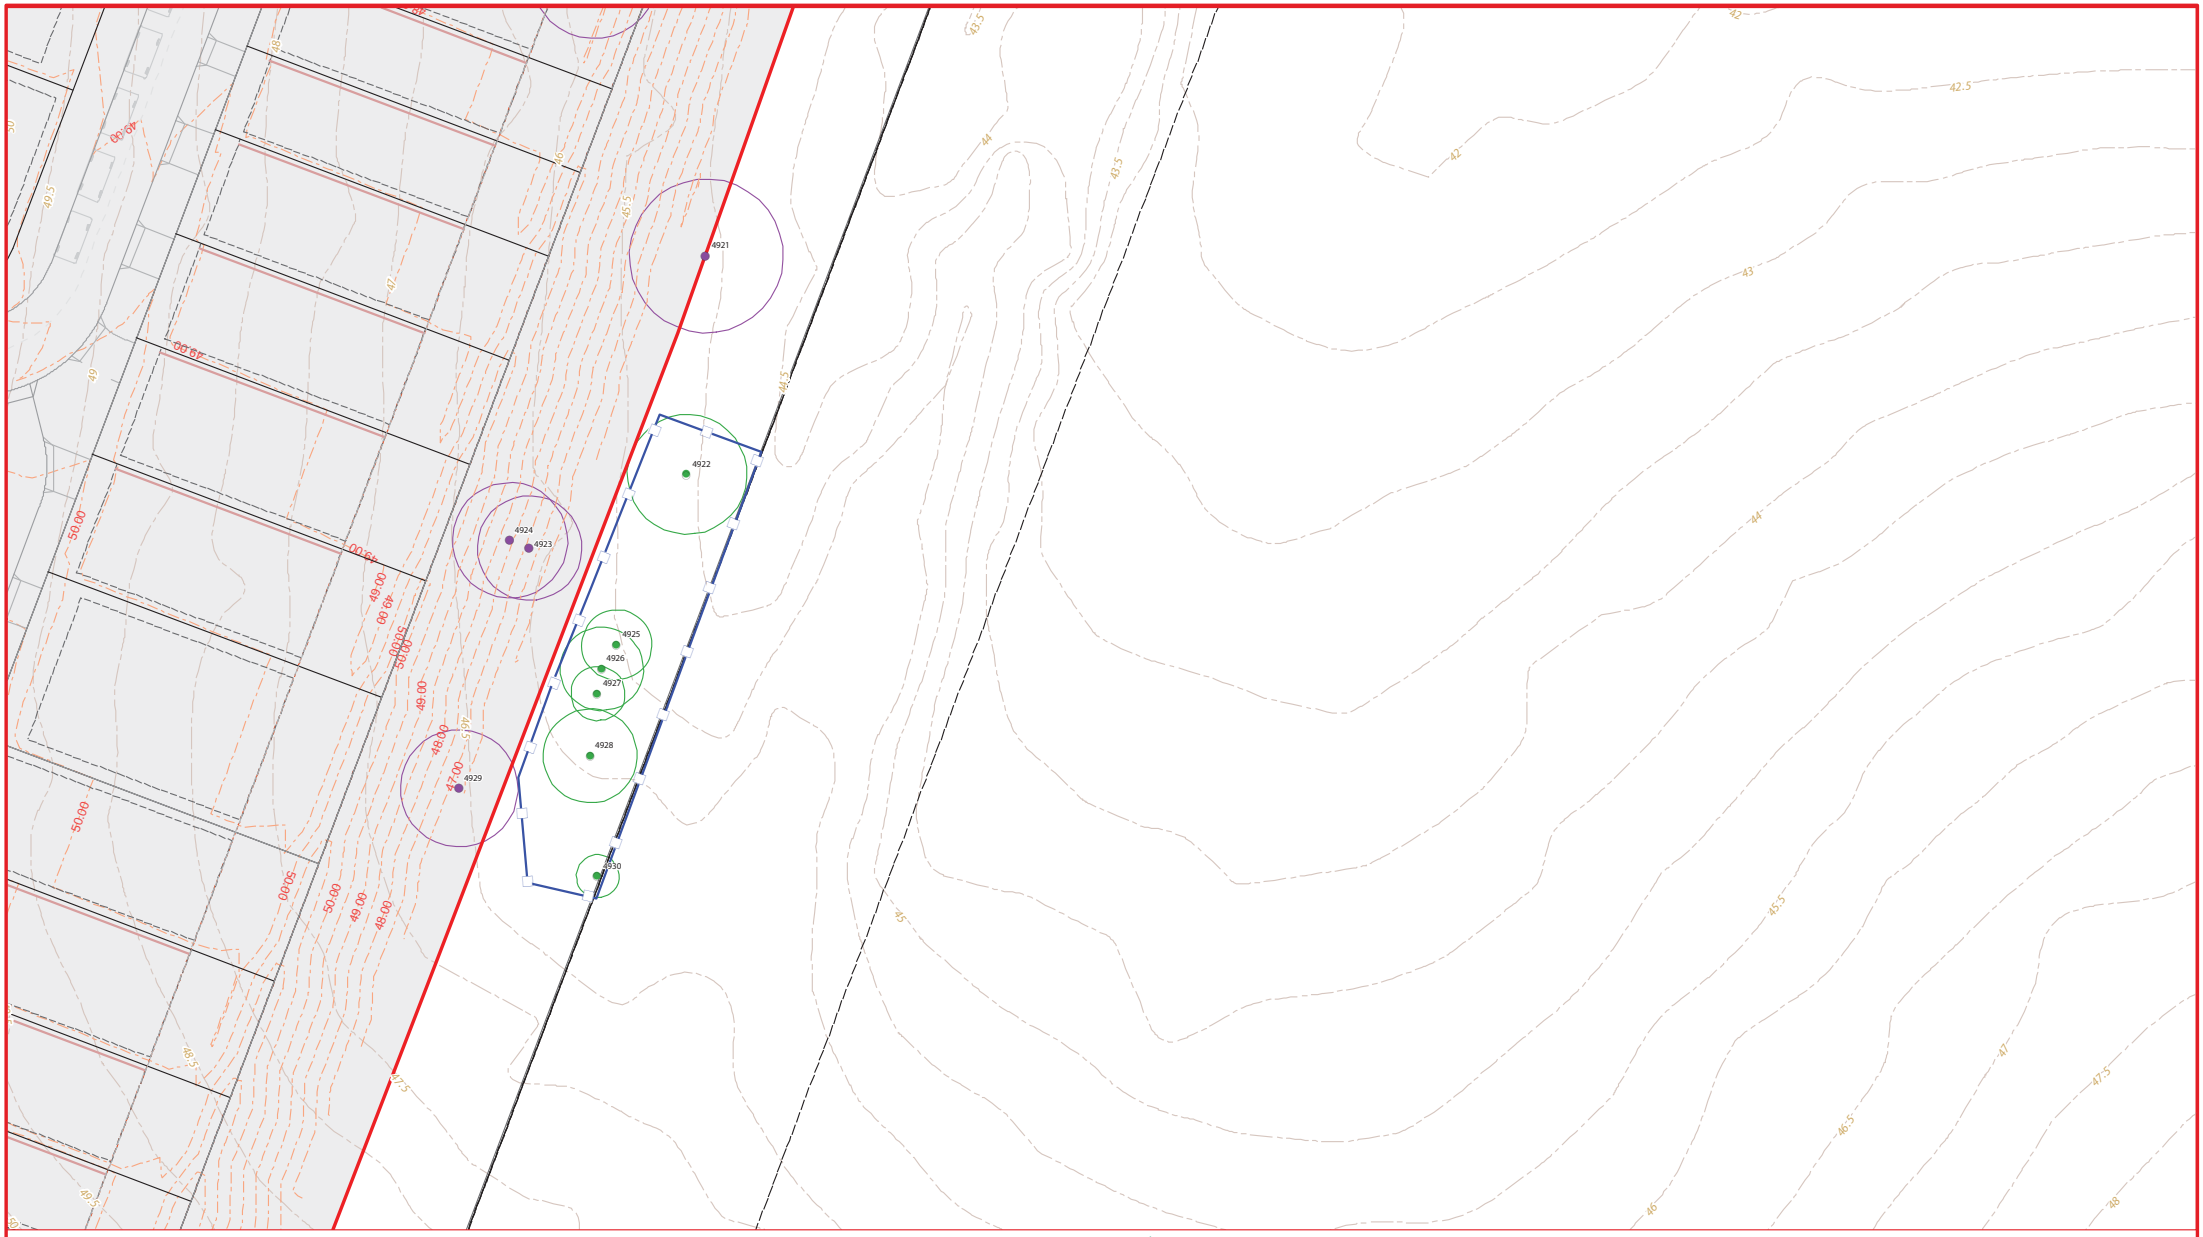

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree (with TPZ) removal to be confirmed at detail design stage of stormwater management
- Tree (with TPZ) to remove for trunk sewer works
- Tree (with TPZ) retention status TBC in park by CPTED principles & park detail design
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access & areas of CPTED selective clearing)
- Stage boundary
- Proposed lots
- Road pavement design
- S — S Civil trunk sewer
- BASIN Conceptual civil basin location - batters TBC at detail design stage
- Building envelopes
- Civil batter top/toe (ind. basins)
- Civil design contours for development area
- Stockpile location (indicative)
- Bushfire Managed Zone - maintain cleared understory
- Approved Phase 1 & School site VMP area
- Existing New Beith Rd (dirt track)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent
- Existing contours (0.5m)

Vegetation Management Plan - Detail Sheet 77

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/2018	Landscape updates	AD
D	30/11/2018	Layout updates	AD
E	25/02/2019	RFI	AD

0 10 20 40 m

1:600 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE:	25/02/2019	CHECKED:	AD
JOB REF.:	8047	DRAWN:	TC

DRAWING No.: 8047 E 77 BAL Stage 2 VMP E

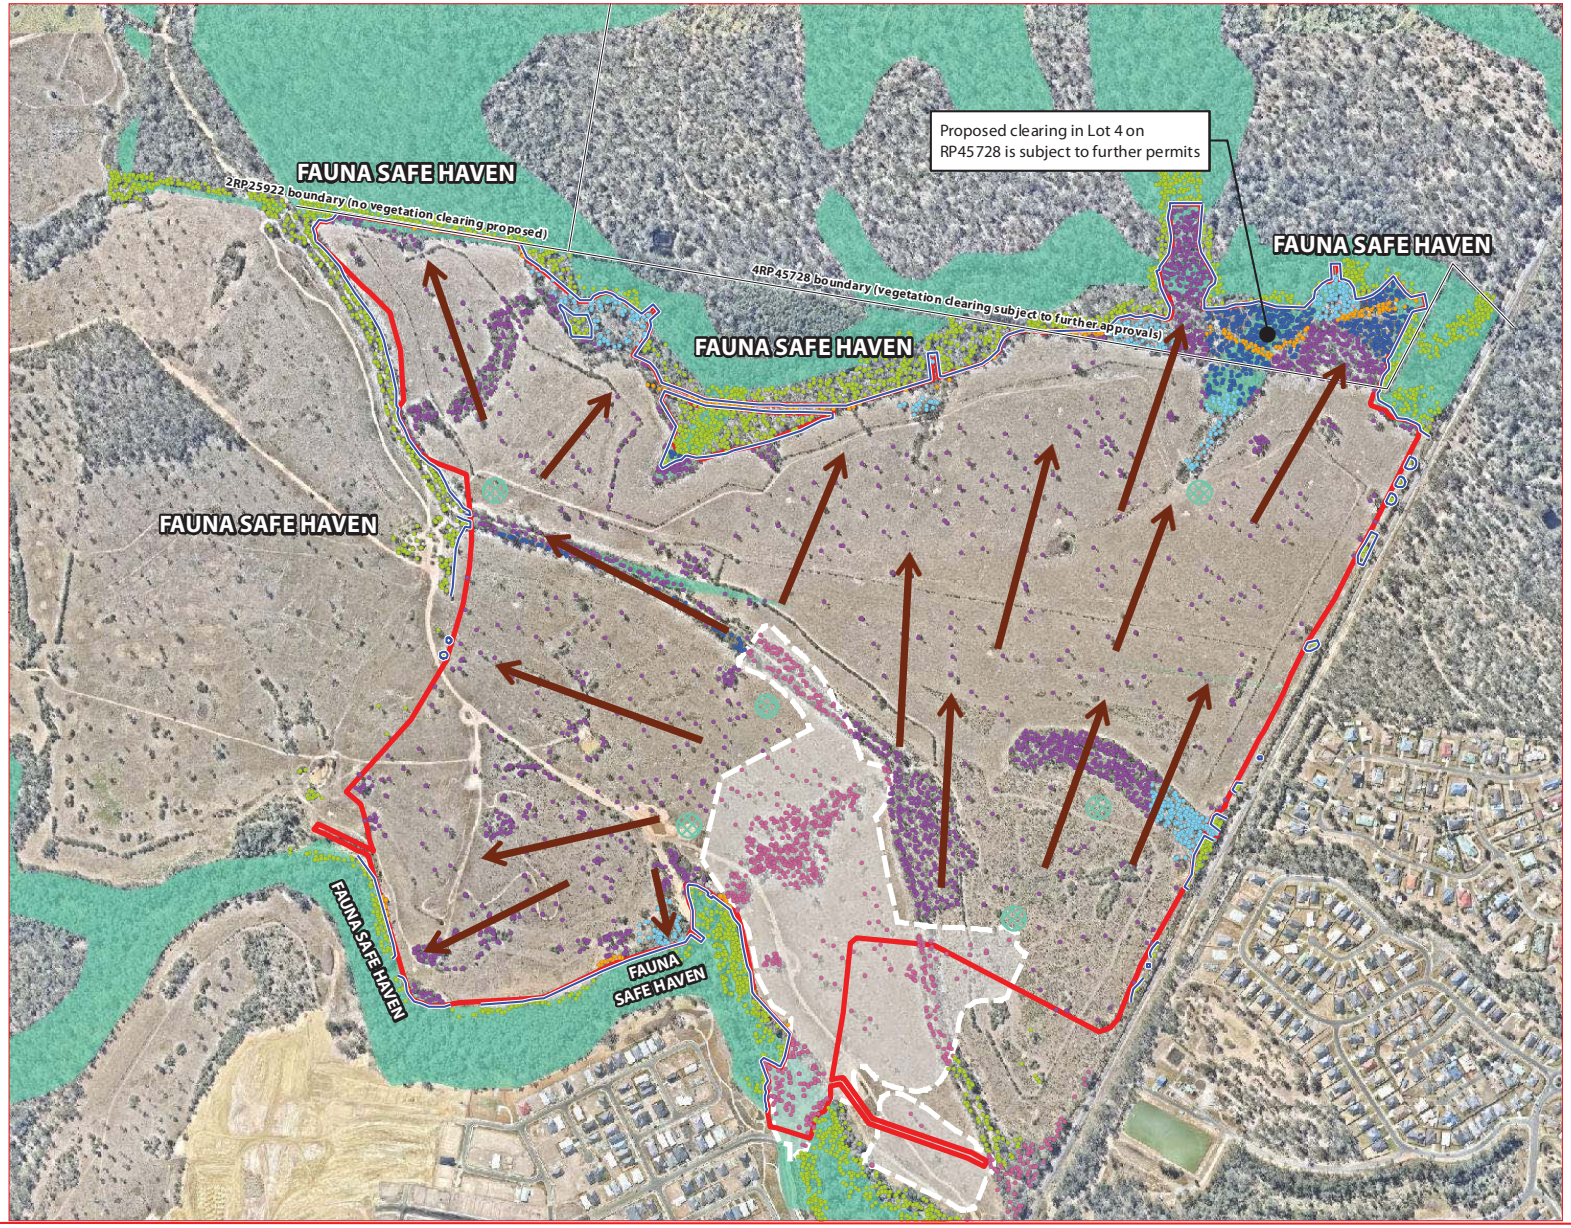

- Tree (with TPZ) to retain
- Tree (with TPZ) to remove in development design/ construction acess
- Tree to remove as part of theStage 2-5 Phase 1 /School VMP application
- Tree (with TPZ) to remove for trunk sewer
- Tree (with TPZ) to remove for stormwater management/basin design - detail design TBC
- Tree (with TPZ) retention status TBC in park by CPTED principles
- Clearing direction
- Stage 2-5 phase 2 site works (including additional vegetation clearing for construction access)
- Stockpile location (indicative)
- Previous Stage 2-5 phase 1 & school VMP site works (including additional 10m vegetation clearing for construction access)
- Tree protection fencing - to be fauna friendly design & subject to minor changes by Arborist and civil engineer
- Remnant Vegetation extent

Vegetation Management Plan - Clearing Direction

saunders havill group

PEET Flagstone

DISCLAIMER:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THESE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ONSITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

REFERENCES:

AMENDMENTS:

Issue	Date	Description	Checked
B	23/07/2018	Engineering updates	AD
C	3/08/ 2018	Landscape updates	AD
D	25/02/2019	Layout updates	AD
E	25/02/2019	RFI	AD

0 50 100 200 300 400 500 600 m

1:8,500 @ A3

CLIENT: PEET Limited

PROJECT: Flagstone City Stage 2-5 - Phase 2

environmental management

PLAN OF: Vegetation Management Plan

DATE: 25/02/2019	CHECKED: AD
JOB REF.: 8047	DRAWN: TC
DRAWING No.: 8047 E 78 BAL Stage 2 VMP E	

saunders havill group

Tree Schedule - 8047 (v6 2019.02.22)
Context Plan 1 - Stages 2 to 5 (Flagstone City), New Beith (Peet Flagstone City Pty Ltd)
25/05/2018

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1	Eucalyptus tereticornis	Forest Red Gum	580		580	24	8	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2	Corymbia intermedia	Pink Bloodwood	260		260	11	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3	Corymbia citriodora	Spotted Gum	200		200	13	4	2.4	1.7	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4	Corymbia citriodora	Spotted Gum	270		270	20	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5	Corymbia citriodora	Spotted Gum	470		470	27	7	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6	Corymbia citriodora	Spotted Gum	400		400	27	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7	Corymbia citriodora	Spotted Gum	300		300	21	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
8	Corymbia citriodora	Spotted Gum	340		340	22	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
9	Eucalyptus tereticornis	Forest Red Gum	770		770	26	10	9.2	3.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	Large	-	-	-		Retain
10	Corymbia citriodora	Spotted Gum	600		600	30	14	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
11	Corymbia intermedia	Pink Bloodwood	260		260	15	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
12	Corymbia citriodora	Spotted Gum	130	340	364	17	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
13	Corymbia citriodora	Spotted Gum	380		380	27	8	4.6	2.2	Irregular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
14	Corymbia citriodora	Spotted Gum	300		300	20	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
15	Corymbia citriodora	Spotted Gum	320		320	26	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
16	DEAD/STAG		1250		1250	12	1	15.0	3.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	High		Approved to remove
17	Corymbia citriodora	Spotted Gum	370		370	21	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
18	Corymbia citriodora	Spotted Gum	320		320	21	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
19	Corymbia citriodora	Spotted Gum	640		640	28	7	7.7	2.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
20	Corymbia citriodora	Spotted Gum	300	170	345	19	5	4.1	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
21	Corymbia citriodora	Spotted Gum	510		510	25	9	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
22	Corymbia citriodora	Spotted Gum	380		380	26	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
23	Corymbia citriodora	Spotted Gum	290		290	19	5	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
24	Eucalyptus tereticornis	Forest Red Gum	370		370	21	6	4.4	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
25	Corymbia citriodora	Spotted Gum	290		290	19	3	3.5	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
26	Eucalyptus tereticornis	Forest Red Gum	500		500	22	8	6.0	2.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
27	Corymbia citriodora	Spotted Gum	330		330	19	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
28	Corymbia citriodora	Spotted Gum	620		620	32	11	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
29	Corymbia citriodora	Spotted Gum	560		560	26	11	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
30	Corymbia citriodora	Spotted Gum	370		370	23	7	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
31	Eucalyptus tereticornis	Forest Red Gum	340		340	19	2	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
32	Corymbia citriodora	Spotted Gum	460		460	21	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
33	Corymbia citriodora	Spotted Gum	300		300	21	5	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
34	Eucalyptus tereticornis	Forest Red Gum	550		550	33	12	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
35	Eucalyptus tereticornis	Forest Red Gum	520		520	28	8	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
36	Angophora leiocarpa	Smooth-barked Apple	370		370	20	6	4.4	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
37	Lophostemon suaveolens	Swamp Box	530		530	16	6	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
38	Corymbia tessellaris	Moreton Bay Ash	420		420	23	6	5.0	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
39	Eucalyptus tereticornis	Forest Red Gum	680		680	23	11	8.2	2.8	Regular	-	Thinning	Die-back	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
40	Glochidion ferdinandi	Cheese Tree	200	180, 150	308	8	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
41	Eucalyptus tereticornis	Forest Red Gum	920		920	38	14	11.0	3.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
42	Angophora subvelutina	Broad-leaved Apple	360		360	17	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
43	Eucalyptus tereticornis	Forest Red Gum	480		480	23	7	5.8	2.4	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
44	Lophostemon suaveolens	Swamp Box	340		340	15	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
45	Eucalyptus tereticornis	Forest Red Gum	400		400	25	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
46	Eucalyptus tereticornis	Forest Red Gum	620		620	28	11	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
47	Angophora subvelutina	Broad-leaved Apple	510		510	18	8	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
48	Eucalyptus tereticornis	Forest Red Gum	520		520	26	9	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
49	Corymbia tessellaris	Moreton Bay Ash	390		390	21	4	4.7	2.2	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
50	Eucalyptus tereticornis	Forest Red Gum	400		400	19	5	4.8	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
51	Eucalyptus tereticornis	Forest Red Gum	730		730	28	12	8.8	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
52	Eucalyptus tereticornis	Forest Red Gum	680		680	32	11	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
53	Lophostemon suaveolens	Swamp Box	380		380	16	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
54	Eucalyptus tereticornis	Forest Red Gum	620		620	36	12	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
55	Eucalyptus tereticornis	Forest Red Gum	540		540	28	7	6.5	2.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
56	Eucalyptus tereticornis	Forest Red Gum	620		620	33	12	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
57	Eucalyptus tereticornis	Forest Red Gum	320		320	23	6	3.8	2.1	One-sided	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
58	Eucalyptus tereticornis	Forest Red Gum	500		500	28	9	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
59	Eucalyptus tereticornis	Forest Red Gum	330		330	26	4	4.0	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
60	Corymbia tessellaris	Moreton Bay Ash	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
61	Eucalyptus tereticornis	Forest Red Gum	490		490	29	9	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
62	Angophora leiocarpa	Smooth-barked Apple	270		270	17	5	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
63	DEAD/STAG		450		450	29	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
64	Eucalyptus tereticornis	Forest Red Gum	280		280	19	2	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
65	Corymbia citriodora	Spotted Gum	590	210	626	34	12	7.5	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
66	Eucalyptus tereticornis	Forest Red Gum	540		540	33	9	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
67	Corymbia citriodora	Spotted Gum	450		450	32	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
68	Corymbia trachyphloia	Brown Bloodwood	320		320	17	7	3.8	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
69	Corymbia citriodora	Spotted Gum	480		480	23	7	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
70	Corymbia citriodora	Spotted Gum	500		500	32	9	6.0	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
71	Corymbia citriodora	Spotted Gum	710		710	36	12	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
72	Corymbia citriodora	Spotted Gum	670		670	38	12	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
73	Corymbia citriodora	Spotted Gum	720		720	28	12	8.6	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
74	Corymbia citriodora	Spotted Gum	690		690	34	14	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
75	Eucalyptus tereticornis	Forest Red Gum	300		300	12	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
76	Eucalyptus tereticornis	Forest Red Gum	280		280	13	5	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
77	Eucalyptus tereticornis	Forest Red Gum	940		940	21	7	11.3	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
78	Corymbia citriodora	Spotted Gum	550		550	25	7	6.6	2.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
79	Eucalyptus tereticornis	Forest Red Gum	530		530	21	6	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
80	Angophora leiocarpa	Smooth-barked Apple	330		330	15	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
81	Corymbia citriodora	Spotted Gum	610		610	29	8	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
82	Corymbia citriodora	Spotted Gum	420		420	16	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
83	Corymbia citriodora	Spotted Gum	1400		1400	33	14	15.0	3.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	Large	Small	Termites	High		Retain
84	Corymbia citriodora	Spotted Gum	640		640	32	14	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
85	Corymbia citriodora	Spotted Gum	540		540	29	12	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
86	Corymbia citriodora	Spotted Gum	210		210	18	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
87	Lophostemon suaveolens	Swamp Box	330		330	14	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
88	Angophora subvelutina	Broad-leaved Apple	290		290	15	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
89	Acacia disparrima	Hickory Wattle	230		230	10	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
90	Melaleuca viminalis	Weeping Bottlebrush	250		250	9	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
91	Melaleuca viminalis	Weeping Bottlebrush	260		260	9	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
92	Melaleuca viminalis	Weeping Bottlebrush	200		200	8	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
93	Alphitonia excelsa	Soap Tree	300		300	15	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
94	Angophora subvelutina	Broad-leaved Apple	570		570	21	12	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
95	Waterhousea floribunda	Weeping Lilly Pilly	300		300	14	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
96	Aphananthe philippinensis	Native Elm	520	300	600	19	11	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
97	Alphitonia excelsa	Soap Tree	370		370	17	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
98	Lophostemon suaveolens	Swamp Box	370		370	22	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
99	Lophostemon suaveolens	Swamp Box	430		430	18	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
100	Lophostemon suaveolens	Swamp Box	360		360	13	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
101	Melaleuca bracteata	Black Tea Tree	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
102	Lophostemon suaveolens	Swamp Box	530		530	14	8	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
103	Eucalyptus tereticornis	Forest Red Gum	420		420	25	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
104	Angophora subvelutina	Broad-leaved Apple	250		250	13	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
105	Eucalyptus tereticornis	Forest Red Gum	560		560	27	9	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
106	Eucalyptus tereticornis	Forest Red Gum	390		390	22	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
107	Angophora subvelutina	Broad-leaved Apple	340		340	16	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
108	Eucalyptus tereticornis	Forest Red Gum	620		620	30	14	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
109	Corymbia intermedia	Pink Bloodwood	290		290	18	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
110	Lophostemon suaveolens	Swamp Box	300	200, 190	408	16	8	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
111	Eucalyptus tereticornis	Forest Red Gum	420		420	29	12	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
112	Eucalyptus tereticornis	Forest Red Gum	260		260	19	5	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
113	Eucalyptus tereticornis	Forest Red Gum	300		300	18	5	3.6	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
114	Corymbia tessellaris	Moreton Bay Ash	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
115	Lophostemon suaveolens	Swamp Box	210		210	13	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
116	Lophostemon suaveolens	Swamp Box	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
117	Eucalyptus tereticornis	Forest Red Gum	460		460	27	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
118	Eucalyptus tereticornis	Forest Red Gum	370		370	23	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
119	Lophostemon suaveolens	Swamp Box	290		290	16	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
120	Lophostemon suaveolens	Swamp Box	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
121	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	24	6	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
122	Acacia disparrima	Hickory Wattle	350	220	413	16	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
123	Acacia disparrima	Hickory Wattle	240		240	16	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
124	Acacia disparrima	Hickory Wattle	240		240	11	9	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
125	Corymbia citriodora	Spotted Gum	200		200	17	2	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
126	Lophostemon suaveolens	Swamp Box	330		330	14	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
127	Acacia disparrima	Hickory Wattle	220	200	297	13	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
128	Eucalyptus moluccana	Gum Topped Box	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
129	Angophora leiocarpa	Smooth-barked Apple	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
130	Corymbia citriodora	Spotted Gum	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
131	Lophostemon suaveolens	Swamp Box	280		280	12	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
132	Alphitonia excelsa	Soap Tree	250		250	12	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
133	Corymbia citriodora	Spotted Gum	340		340	19	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
134	Eucalyptus tereticornis	Forest Red Gum	350		350	20	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
135	Angophora subvelutina	Broad-leaved Apple	220		220	6	2	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
136	Eucalyptus tereticornis	Forest Red Gum	690		690	28	12	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
137	Lophostemon suaveolens	Swamp Box	320		320	10	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
138	Acacia concurrens	Black Wattle	180	130, 100	244	7	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
139	Lophostemon suaveolens	Swamp Box	200	140	244	7	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
140	Angophora subvelutina	Broad-leaved Apple	290		290	7	3	3.5	2.0	Regular	-	Thinning	Die-back	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
141	Corymbia tessellaris	Moreton Bay Ash	480		480	31	12	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
142	Corymbia tessellaris	Moreton Bay Ash	420		420	32	10	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
143	Corymbia tessellaris	Moreton Bay Ash	490		490	30	13	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
144	Lophostemon suaveolens	Swamp Box	280		280	13	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
145	Lophostemon suaveolens	Swamp Box	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
146	Casuarina cunninghamiana	River Sheoak	300		300	15	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
147	Eucalyptus tereticornis	Forest Red Gum	430		430	26	6	5.2	2.3	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
148	Eucalyptus siderophloia	Grey Ironbark	360		360	25	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
149	Eucalyptus siderophloia	Grey Ironbark	440		440	31	12	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
150	Eucalyptus tereticornis	Forest Red Gum	290		290	24	6	3.5	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
151	Eucalyptus tereticornis	Forest Red Gum	640		640	29	16	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
152	Eucalyptus tereticornis	Forest Red Gum	250		250	16	5	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
153	Eucalyptus tereticornis	Forest Red Gum	240		240	18	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
154	Eucalyptus tereticornis	Forest Red Gum	560		560	30	16	6.7	2.6	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
155	Eucalyptus tereticornis	Forest Red Gum	280		280	25	5	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
156	Eucalyptus tereticornis	Forest Red Gum	350		350	30	6	4.2	2.1	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
157	Corymbia intermedia	Pink Bloodwood	270	260	375	18	5	4.5	2.2	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
158	Eucalyptus tereticornis	Forest Red Gum	320		320	28	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
159	Lophostemon suaveolens	Swamp Box	250		250	10	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
160	Lophostemon suaveolens	Swamp Box	210		210	11	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
161	Corymbia intermedia	Pink Bloodwood	265		265	15	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
162	Acacia disparrima	Hickory Wattle	250		250	10	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
163	Acacia disparrima	Hickory Wattle	260		260	11	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
164	Corymbia intermedia	Pink Bloodwood	265		265	9	3	3.2	1.9	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
165	Lophostemon suaveolens	Swamp Box	275		275	11	4	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
166	Acacia disparrima	Hickory Wattle	270		270	11	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
167	Lophostemon suaveolens	Swamp Box	285	210	354	12	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
168	Lophostemon suaveolens	Swamp Box	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
169	Angophora floribunda	Rough-barked Apple	365		365	18	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
170	Acacia disparrima	Hickory Wattle	210	150	258	13	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
171	Corymbia intermedia	Pink Bloodwood	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
172	Angophora floribunda	Rough-barked Apple	310		310	17	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
173	Acacia disparrima	Hickory Wattle	250		250	13	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
174	Eucalyptus tereticornis	Forest Red Gum	630		630	26	12	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
175	Casuarina cunninghamiana	River Sheoak	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
176	Casuarina cunninghamiana	River Sheoak	220		220	9	7	2.6	1.8	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
177	Casuarina cunninghamiana	River Sheoak	420		420	17	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
178	Melaleuca viminalis	Weeping Bottlebrush	220		220	12	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
179	Acacia disparrima	Hickory Wattle	200	190, 150	314	13	7	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
180	Eucalyptus tereticornis	Forest Red Gum	265		265	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
181	Eucalyptus tereticornis	Forest Red Gum	485		485	19	7	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
182	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
183	Lophostemon suaveolens	Swamp Box	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
184	Lophostemon suaveolens	Swamp Box	320		320	13	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
185	Corymbia intermedia	Pink Bloodwood	560		560	26	10	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
186	Corymbia tessellaris	Moreton Bay Ash	330		330	24	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
187	Alphitonia excelsa	Soap Tree	190		190	11	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
188	Corymbia tessellaris	Moreton Bay Ash	200		200	4	2	2.4	1.7	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
189	Angophora subvelutina	Broad-leaved Apple	520		520	20	11	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
190	Eucalyptus tereticornis	Forest Red Gum	600		600	27	12	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
191	Lophostemon suaveolens	Swamp Box	390		390	19	6	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
192	Lophostemon suaveolens	Swamp Box	330		330	13	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
193	Lophostemon suaveolens	Swamp Box	340		340	14	6	4.1	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
194	Corymbia tessellaris	Moreton Bay Ash	420		420	24	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
195	Angophora subvelutina	Broad-leaved Apple	290		290	20	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
196	Lophostemon suaveolens	Swamp Box	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
197	Lophostemon suaveolens	Swamp Box	320		320	17	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
198	Lophostemon suaveolens	Swamp Box	270		270	15	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
199	Corymbia tessellaris	Moreton Bay Ash	230		230	20	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
200	Corymbia tessellaris	Moreton Bay Ash	260		260	23	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
201	Acacia disparrima	Hickory Wattle	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
202	Eucalyptus crebra	Narrow-leaved Ironbark	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
203	Angophora subvelutina	Broad-leaved Apple	540		540	26	12	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
204	Angophora subvelutina	Broad-leaved Apple	450		450	26	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
205	Lophostemon suaveolens	Swamp Box	180		180	14	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
206	Corymbia tessellaris	Moreton Bay Ash	280		280	20	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
207	Corymbia tessellaris	Moreton Bay Ash	150		150	20	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
208	Eucalyptus tereticornis	Forest Red Gum	180		180	11	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
209	Eucalyptus crebra	Narrow-leaved Ironbark	450		450	26	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
210	Eucalyptus tereticornis	Forest Red Gum	380		380	26	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
211	Lophostemon suaveolens	Swamp Box	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
212	Corymbia intermedia	Pink Bloodwood	270	330	426	17	9	5.1	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	nestbox	Retain
213	Eucalyptus tereticornis	Forest Red Gum	680		680	34	14	8.2	2.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
214	Corymbia tessellaris	Moreton Bay Ash	450		450	27	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
215	Corymbia tessellaris	Moreton Bay Ash	380		380	25	6	4.6	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
216	Angophora subvelutina	Broad-leaved Apple	600		600	27	12	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
217	Angophora subvelutina	Broad-leaved Apple	200		200	14	4	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
218	Casuarina cunninghamiana	River Sheoak	460		460	22	7	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
219	Melaleuca viminalis	Weeping Bottlebrush	230		230	10	6	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
220	Melaleuca viminalis	Weeping Bottlebrush	260		260	6	8	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
221	Eucalyptus tereticornis	Forest Red Gum	320		320	24	7	3.8	2.1	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
222	Alphitonia excelsa	Soap Tree	210		210	9	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
223	Alphitonia excelsa	Soap Tree	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
224	Alphitonia excelsa	Soap Tree	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
225	Melaleuca linariifolia	Snow-in-summer	290		290	15	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
226	Eucalyptus tereticornis	Forest Red Gum	530		530	22	12	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
227	Corymbia citriodora	Spotted Gum	150		150	14	4	2.0	1.5	One-sided	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
228	Alphitonia excelsa	Soap Tree	150		150	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
229	Alphitonia excelsa	Soap Tree	185		185	12	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
230	Alphitonia excelsa	Soap Tree	150	130	198	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
231	Acacia disparrima	Hickory Wattle	140	140, 130	237	11	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
232	Acacia disparrima	Hickory Wattle	150	130, 120	232	11	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
233	Angophora subvelutina	Broad-leaved Apple	210		210	13	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	nest box	Retain
234	Corymbia intermedia	Pink Bloodwood	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
235	Angophora subvelutina	Broad-leaved Apple	400		400	21	5	4.8	2.3	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
236	Eucalyptus tereticornis	Forest Red Gum	115		115	29	16	2.0	1.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
237	Acacia disparrima	Hickory Wattle	160		160	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
238	Alphitonia excelsa	Soap Tree	135	135	191	11	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
239	Waterhousea floribunda	Weeping Lilly Pilly	290	230	370	12	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
240	Angophora subvelutina	Broad-leaved Apple	365		365	17	7	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
241	Corymbia tessellaris	Moreton Bay Ash	660		660	28	9	7.9	2.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
242	Lophostemon suaveolens	Swamp Box	260		260	13	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
243	Corymbia tessellaris	Moreton Bay Ash	480		480	23	7	5.8	2.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
244	Corymbia tessellaris	Moreton Bay Ash	150		150	17	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
245	Lophostemon suaveolens	Swamp Box	220		220	11	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
246	Eucalyptus tereticornis	Forest Red Gum	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
247	Eucalyptus tereticornis	Forest Red Gum	690		690	32	14	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
248	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
249	Eucalyptus tereticornis	Forest Red Gum	520	260	581	23	9	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
250	Lophostemon suaveolens	Swamp Box	220	100	242	11	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
251	Lophostemon suaveolens	Swamp Box	285		285	13	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
252	Corymbia citriodora	Spotted Gum	360		360	19	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
253	Eucalyptus tereticornis	Forest Red Gum	290		290	16	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
254	Eucalyptus tereticornis	Forest Red Gum	220		220	15	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
255	Eucalyptus saligna	Sydney Blue Gum	230		230	12	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
256	Eucalyptus saligna	Sydney Blue Gum	360		360	13	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
257	Eucalyptus pilularis	Blackbutt	210		210	10	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
258	Eucalyptus pilularis	Blackbutt	230		230	11	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
259	Eucalyptus pilularis	Blackbutt	220		220	10	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
260	Eucalyptus pilularis	Blackbutt	200		200	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
261	Eucalyptus tereticornis	Forest Red Gum	290		290	20	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
262	Eucalyptus pilularis	Blackbutt	300		300	14	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
263	DEAD/STAG		330		330	21	1	4.0	2.1	Irregular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	Large	-	-	-		Retain
264	Eucalyptus pilularis	Blackbutt	210	200	290	16	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
265	Eucalyptus pilularis	Blackbutt	300	280	410	16	8	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
266	Eucalyptus pilularis	Blackbutt	260		260	13	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	Small	-	-	Low	large crack in trunk	Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
267	Eucalyptus pilularis	Blackbutt	210	190	283	12	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
268	Eucalyptus pilularis	Blackbutt	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
269	DEAD/STAG		420		420	17	1	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	Termites	High	large crack in trunk	Retain
270	Eucalyptus pilularis	Blackbutt	510		510	21	12	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	High		Retain
271	Eucalyptus pilularis	Blackbutt	300	260	397	11	12	4.8	2.2	Irregular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
272	Eucalyptus tereticornis	Forest Red Gum	210		210	19	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
273	Eucalyptus tereticornis	Forest Red Gum	220		220	18	11	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
274	Eucalyptus tereticornis	Forest Red Gum	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
275	Eucalyptus tereticornis	Forest Red Gum	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
276	Eucalyptus tereticornis	Forest Red Gum	200		200	17	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
277	Corymbia citriodora	Spotted Gum	330		330	16	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
278	Eucalyptus acmenoides	White Mahogany	500		500	15	9	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
279	Lophostemon suaveolens	Swamp Box	210		210	8	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
280	Lophostemon suaveolens	Swamp Box	240		240	7	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
281	Corymbia intermedia	Pink Bloodwood	260		260	13	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
282	Corymbia intermedia	Pink Bloodwood	290		290	12	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
283	Melaleuca quinquenervia	Broad-leaved Paperbark	250	240	347	9	12	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
284	Angophora leiocarpa	Smooth-barked Apple	310		310	20	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
285	Angophora leiocarpa	Smooth-barked Apple	280		280	20	13	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
286	Eucalyptus acmenoides	White Mahogany	310		310	17	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
287	Angophora leiocarpa	Smooth-barked Apple	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
288	Lophostemon suaveolens	Swamp Box	210		210	12	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
289	Eucalyptus acmenoides	White Mahogany	280		280	16	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
290	Lophostemon suaveolens	Swamp Box	240		240	15	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
291	Eucalyptus acmenoides	White Mahogany	240		240	12	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
292	Lophostemon suaveolens	Swamp Box	200		200	7	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
293	Eucalyptus acmenoides	White Mahogany	270		270	14	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
294	Corymbia intermedia	Pink Bloodwood	300		300	15	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
295	Alphitonia excelsa	Soap Tree	260		260	13	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
296	Lophostemon suaveolens	Swamp Box	230		230	13	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
297	DEAD/STAG		200		200	20	1	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
298	Eucalyptus acmenoides	White Mahogany	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
299	Eucalyptus acmenoides	White Mahogany	290		290	17	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
300	Corymbia intermedia	Pink Bloodwood	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
301	Corymbia intermedia	Pink Bloodwood	400		400	15	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
302	Corymbia intermedia	Pink Bloodwood	380		380	12	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
303	Corymbia intermedia	Pink Bloodwood	320		320	19	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
304	Corymbia intermedia	Pink Bloodwood	410		410	18	12	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
305	Corymbia intermedia	Pink Bloodwood	240		240	16	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
306	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
307	Angophora leiocarpa	Smooth-barked Apple	260		260	21	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
308	Lophostemon suaveolens	Swamp Box	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
309	Acacia disparrima	Hickory Wattle	280		280	9	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
310	Alphitonia excelsa	Soap Tree	270		270	12	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
311	Angophora leiocarpa	Smooth-barked Apple	340		340	22	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
312	Corymbia intermedia	Pink Bloodwood	350		350	20	11	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
313	Eucalyptus tereticornis	Forest Red Gum	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
314	Eucalyptus tereticornis	Forest Red Gum	260		260	22	14	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
315	Corymbia intermedia	Pink Bloodwood	360		360	20	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
316	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
317	Eucalyptus crebra	Narrow-leaved Ironbark	500		500	25	13	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
318	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	25	13	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
319	Eucalyptus crebra	Narrow-leaved Ironbark	370		370	22	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
320	Lophostemon suaveolens	Swamp Box	300	210	366	9	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
321	Corymbia intermedia	Pink Bloodwood	350		350	18	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
322	Corymbia intermedia	Pink Bloodwood	360		360	18	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
323	Lophostemon suaveolens	Swamp Box	240		240	8	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
324	Eucalyptus tereticornis	Forest Red Gum	350		350	18	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
325	Angophora subvelutina	Broad-leaved Apple	360		360	21	14	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
326	Banksia integrifolia	Coast Banksia	320		320	6	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
327	Eucalyptus saligna	Sydney Blue Gum	610	400	729	23	17	8.8	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
328	Casuarina cunninghamiana	River Sheoak	240		240	12	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
329	Casuarina cunninghamiana	River Sheoak	230		230	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
330	Eucalyptus saligna	Sydney Blue Gum	550		550	22	13	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
331	Lophostemon suaveolens	Swamp Box	270		270	12	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
332	Eucalyptus saligna	Sydney Blue Gum	260		260	18	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
333	Eucalyptus tereticornis	Forest Red Gum	590		590	25	16	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
334	Eucalyptus tereticornis	Forest Red Gum	280		280	20	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
335	Angophora subvelutina	Broad-leaved Apple	250		250	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
336	Eucalyptus tereticornis	Forest Red Gum	260		260	17	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
337	Angophora leiocarpa	Smooth-barked Apple	240		240	11	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
338	Angophora leiocarpa	Smooth-barked Apple	210		210	11	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
339	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	17	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
340	Angophora leiocarpa	Smooth-barked Apple	290		290	15	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
341	Angophora subvelutina	Broad-leaved Apple	290		290	13	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
342	Angophora subvelutina	Broad-leaved Apple	400		400	29	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
343	Corymbia tessellaris	Moreton Bay Ash	350		350	32	16	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
344	Angophora subvelutina	Broad-leaved Apple	550		550	28	16	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
345	Angophora subvelutina	Broad-leaved Apple	500		500	27	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
346	Angophora subvelutina	Broad-leaved Apple	370		370	25	11	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
347	Angophora subvelutina	Broad-leaved Apple	320		320	23	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
348	Melaleuca viminalis	Weeping Bottlebrush	400		400	20	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Retain
349	Eucalyptus saligna	Sydney Blue Gum	220		220	20	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
350	Corymbia intermedia	Pink Bloodwood	460		460	26	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
351	Corymbia tessellaris	Moreton Bay Ash	280		280	30	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
352	Angophora subvelutina	Broad-leaved Apple	470		470	23	12	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
353	Angophora subvelutina	Broad-leaved Apple	650		650	23	13	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
354	Eucalyptus tereticornis	Forest Red Gum	580		580	33	13	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
355	Lophostemon suaveolens	Swamp Box	360		360	15	4	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
356	Eucalyptus tereticornis	Forest Red Gum	360		360	20	3	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
357	Eucalyptus tereticornis	Forest Red Gum	570		570	34	14	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
358	Eucalyptus tereticornis	Forest Red Gum	530		530	35	14	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
359	Eucalyptus tereticornis	Forest Red Gum	610		610	35	15	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
360	Angophora subvelutina	Broad-leaved Apple	280	280, 310	503	15	8	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
361	Corymbia intermedia	Pink Bloodwood	560		560	25	13	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
362	Acacia disparrima	Hickory Wattle	340		340	9	4	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
363	Angophora subvelutina	Broad-leaved Apple	340		340	15	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
364	Angophora subvelutina	Broad-leaved Apple	240		240	14	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
365	Angophora subvelutina	Broad-leaved Apple	320		320	16	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
366	Eucalyptus crebra	Narrow-leaved Ironbark	480		480	28	12	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
367	Eucalyptus tereticornis	Forest Red Gum	220		220	25	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
368	Angophora subvelutina	Broad-leaved Apple	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
369	Angophora subvelutina	Broad-leaved Apple	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
370	Corymbia intermedia	Pink Bloodwood	440		440	27	12	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
371	Angophora subvelutina	Broad-leaved Apple	380		380	22	11	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
372	Eucalyptus tereticornis	Forest Red Gum	240		240	25	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
373	Lophostemon suaveolens	Swamp Box	310		310	18	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
374	Eucalyptus tereticornis	Forest Red Gum	700		700	33	19	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
375	Angophora subvelutina	Broad-leaved Apple	520		520	30	15	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
376	Lophostemon suaveolens	Swamp Box	330		330	7	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
377	Angophora leiocarpa	Smooth-barked Apple	250		250	14	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Large	-	-		Remove
378	Petalostigma pubescens	Quinine Bush	220		220	6	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
379	Lophostemon suaveolens	Swamp Box	330		330	10	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
380	Lophostemon suaveolens	Swamp Box	320		320	12	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
381	Acacia disparrima	Hickory Wattle	220		220	5	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
382	Eucalyptus saligna	Sydney Blue Gum	270		270	13	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
383	Lophostemon suaveolens	Swamp Box	230		230	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
384	Lophostemon suaveolens	Swamp Box	240		240	13	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
385	Eucalyptus tereticornis	Forest Red Gum	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
386	Lophostemon suaveolens	Swamp Box	300		300	15	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
387	Eucalyptus tereticornis	Forest Red Gum	260		260	16	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
388	Lophostemon suaveolens	Swamp Box	240		240	13	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
389	Angophora subvelutina	Broad-leaved Apple	250		250	15	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
390	Eucalyptus moluccana	Gum Topped Box	260		260	23	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
391	Angophora subvelutina	Broad-leaved Apple	230		230	12	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
392	Angophora subvelutina	Broad-leaved Apple	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
393	Angophora subvelutina	Broad-leaved Apple	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
394	Angophora subvelutina	Broad-leaved Apple	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
395	Angophora subvelutina	Broad-leaved Apple	280		280	15	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
396	Angophora subvelutina	Broad-leaved Apple	230		230	20	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
397	Eucalyptus tereticornis	Forest Red Gum	310		310	25	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
398	Angophora subvelutina	Broad-leaved Apple	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
399	Angophora subvelutina	Broad-leaved Apple	330		330	25	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
400	Angophora subvelutina	Broad-leaved Apple	470		470	28	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
401	Angophora subvelutina	Broad-leaved Apple	390	250	463	26	9	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
402	Lophostemon suaveolens	Swamp Box	230		230	14	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
403	Eucalyptus tereticornis	Forest Red Gum	350		350	25	12	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
404	Corymbia tessellaris	Moreton Bay Ash	220		220	21	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
405	Angophora subvelutina	Broad-leaved Apple	400		400	26	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
406	Eucalyptus tereticornis	Forest Red Gum	390		390	30	12	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
407	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	22	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
408	Corymbia tessellaris	Moreton Bay Ash	320		320	28	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
409	Angophora subvelutina	Broad-leaved Apple	250		250	24	13	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
410	Angophora subvelutina	Broad-leaved Apple	260		260	15	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
411	Angophora subvelutina	Broad-leaved Apple	450		450	26	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
412	Eucalyptus tereticornis	Forest Red Gum	620		620	32	13	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
413	Eucalyptus tereticornis	Forest Red Gum	450		450	33	16	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
414	Angophora subvelutina	Broad-leaved Apple	450		450	26	11	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
415	Eucalyptus tereticornis	Forest Red Gum	470		470	33	16	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
416	Angophora subvelutina	Broad-leaved Apple	380		380	28	15	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
417	Angophora leiocarpa	Smooth-barked Apple	260		260	19	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
418	Corymbia citriodora	Spotted Gum	470		470	27	13	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
419	Corymbia tessellaris	Moreton Bay Ash	230		230	17	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
420	Eucalyptus tereticornis	Forest Red Gum	410		410	25	11	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
421	Corymbia citriodora	Spotted Gum	470		470	26	13	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Retain
422	Eucalyptus moluccana	Gum Topped Box	450		450	30	14	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
423	Eucalyptus tereticornis	Forest Red Gum	390		390	25	10	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
424	Corymbia citriodora	Spotted Gum	290		290	21	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
425	Eucalyptus moluccana	Gum Topped Box	710		710	30	14	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
426	Eucalyptus moluccana	Gum Topped Box	450	220	501	27	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
427	Eucalyptus moluccana	Gum Topped Box	320		320	20	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
428	Eucalyptus moluccana	Gum Topped Box	360	280	456	26	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
429	Eucalyptus moluccana	Gum Topped Box	240		240	17	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
430	Eucalyptus moluccana	Gum Topped Box	440		440	25	13	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
431	Eucalyptus moluccana	Gum Topped Box	610		610	27	11	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
432	Eucalyptus moluccana	Gum Topped Box	260		260	23	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
433	Eucalyptus moluccana	Gum Topped Box	380		380	25	15	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
434	Eucalyptus moluccana	Gum Topped Box	420	180	457	21	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
435	Eucalyptus tereticornis	Forest Red Gum	240		240	20	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
436	Angophora subvelutina	Broad-leaved Apple	330		330	15	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
437	Eucalyptus tereticornis	Forest Red Gum	350		350	21	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
438	Eucalyptus tereticornis	Forest Red Gum	390		390	27	15	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
439	Eucalyptus tereticornis	Forest Red Gum	250		250	20	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
440	Lophostemon suaveolens	Swamp Box	260		260	14	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
441	Corymbia intermedia	Pink Bloodwood	450		450	26	11	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
442	Eucalyptus tereticornis	Forest Red Gum	270		270	22	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
443	Eucalyptus tereticornis	Forest Red Gum	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
444	Eucalyptus tereticornis	Forest Red Gum	310		310	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
445	Eucalyptus saligna	Sydney Blue Gum	330		330	16	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
446	Eucalyptus saligna	Sydney Blue Gum	290		290	16	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
447	Eucalyptus saligna	Sydney Blue Gum	370		370	17	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
448	Eucalyptus tereticornis	Forest Red Gum	250		250	15	2	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
449	Eucalyptus tereticornis	Forest Red Gum	290		290	19	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
450	Eucalyptus pilularis	Blackbutt	520		520	18	12	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
451	Eucalyptus pilularis	Blackbutt	480	450	658	21	10	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
452	Corymbia intermedia	Pink Bloodwood	270	190, 150	363	14	5	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
453	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
454	Angophora leiocarpa	Smooth-barked Apple	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
455	Eucalyptus pilularis	Blackbutt	670		670	20	12	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
456	Eucalyptus pilularis	Blackbutt	600		600	18	10	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
457	Eucalyptus pilularis	Blackbutt	230	210	311	17	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
458	Eucalyptus pilularis	Blackbutt	210	150	258	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
459	Eucalyptus pilularis	Blackbutt	190	180, 170, 140	342	16	4	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
460	Eucalyptus pilularis	Blackbutt	230		230	18	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
461	Eucalyptus pilularis	Blackbutt	280		280	18	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
462	Eucalyptus pilularis	Blackbutt	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
463	Eucalyptus pilularis	Blackbutt	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
464	Eucalyptus pilularis	Blackbutt	300	220	372	19	7	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
465	Eucalyptus pilularis	Blackbutt	230		230	17	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
466	Eucalyptus pilularis	Blackbutt	250		250	19	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
467	Eucalyptus pilularis	Blackbutt	210		210	18	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
468	Angophora leiocarpa	Smooth-barked Apple	250		250	17	4	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
469	Eucalyptus pilularis	Blackbutt	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
470	Eucalyptus pilularis	Blackbutt	210		210	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
471	Eucalyptus pilularis	Blackbutt	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
472	Eucalyptus pilularis	Blackbutt	490		490	20	11	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
473	Eucalyptus pilularis	Blackbutt	250		250	15	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
474	Eucalyptus pilularis	Blackbutt	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
475	Eucalyptus pilularis	Blackbutt	290		290	17	3	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
476	Eucalyptus pilularis	Blackbutt	350		350	19	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
477	Eucalyptus pilularis	Blackbutt	400	400	566	21	11	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
478	Eucalyptus siderophloia	Grey Ironbark	440		440	21	10	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Retain
479	Eucalyptus pilularis	Blackbutt	260		260	12	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
480	Eucalyptus tereticornis	Forest Red Gum	310		310	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
481	Corymbia intermedia	Pink Bloodwood	310		310	18	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
482	Corymbia intermedia	Pink Bloodwood	380		380	19	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
483	Corymbia intermedia	Pink Bloodwood	290		290	18	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
484	Lophostemon suaveolens	Swamp Box	220		220	11	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
485	Corymbia intermedia	Pink Bloodwood	260		260	18	8	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
486	Corymbia intermedia	Pink Bloodwood	340		340	20	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
487	Corymbia intermedia	Pink Bloodwood	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
488	Corymbia intermedia	Pink Bloodwood	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
489	Corymbia intermedia	Pink Bloodwood	260		260	18	4	3.1	1.9	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
490	Eucalyptus acmenoides	White Mahogany	270	230	355	16	7	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
491	Lophostemon suaveolens	Swamp Box	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
492	Lophostemon suaveolens	Swamp Box	200		200	9	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
493	Lophostemon suaveolens	Swamp Box	270		270	8	2	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
494	Angophora leiocarpa	Smooth-barked Apple	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
495	Lophostemon suaveolens	Swamp Box	270		270	10	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
496	Angophora leiocarpa	Smooth-barked Apple	210		210	16	5	2.5	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
497	Lophostemon suaveolens	Swamp Box	270		270	9	5	3.2	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
498	Lophostemon suaveolens	Swamp Box	200		200	14	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
499	Angophora leiocarpa	Smooth-barked Apple	330		330	18	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
500	Angophora leiocarpa	Smooth-barked Apple	260		260	17	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
501	Lophostemon suaveolens	Swamp Box	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
502	Acacia disparrima	Hickory Wattle	240		240	10	4	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Poor	Major	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
503	Eucalyptus tereticornis	Forest Red Gum	340		340	18	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
504	Eucalyptus tereticornis	Forest Red Gum	290		290	19	7	3.5	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
505	Corymbia intermedia	Pink Bloodwood	320		320	18	3	3.8	2.1	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
506	Corymbia intermedia	Pink Bloodwood	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
507	Corymbia intermedia	Pink Bloodwood	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
508	Corymbia intermedia	Pink Bloodwood	420		420	20	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
509	Eucalyptus tereticornis	Forest Red Gum	500		500	19	11	6.0	2.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	Small	-	-		Remove for basin works
510	Lophostemon suaveolens	Swamp Box	240		240	10	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
511	Corymbia intermedia	Pink Bloodwood	300		300	18	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
512	Angophora leiocarpa	Smooth-barked Apple	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
513	Lophostemon suaveolens	Swamp Box	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
514	Corymbia intermedia	Pink Bloodwood	300		300	18	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
515	Corymbia intermedia	Pink Bloodwood	280		280	17	4	3.4	1.9	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
516	Corymbia intermedia	Pink Bloodwood	430		430	19	10	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
517	Eucalyptus acmenoides	White Mahogany	270		270	16	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
518	Eucalyptus siderophloia	Grey Ironbark	330		330	18	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
519	Lophostemon suaveolens	Swamp Box	220		220	11	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
520	Corymbia intermedia	Pink Bloodwood	250		250	16	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
521	Corymbia citriodora	Spotted Gum	310		310	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
522	Lophostemon suaveolens	Swamp Box	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
523	Eucalyptus acmenoides	White Mahogany	330		330	17	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
524	Eucalyptus acmenoides	White Mahogany	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
525	Eucalyptus acmenoides	White Mahogany	290		290	18	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
526	Corymbia intermedia	Pink Bloodwood	210		210	19	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
527	Eucalyptus acmenoides	White Mahogany	330	300	446	18	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
528	Corymbia intermedia	Pink Bloodwood	270	270	382	18	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
529	Eucalyptus acmenoides	White Mahogany	250		250	14	7	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
530	Corymbia intermedia	Pink Bloodwood	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
531	Corymbia intermedia	Pink Bloodwood	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
532	Eucalyptus tereticornis	Forest Red Gum	270		270	18	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
533	Eucalyptus acmenoides	White Mahogany	250	200	320	17	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
534	Eucalyptus acmenoides	White Mahogany	200	230	305	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
535	Eucalyptus acmenoides	White Mahogany	230	210	311	16	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
536	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
537	Eucalyptus tereticornis	Forest Red Gum	230		230	19	4	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
538	Eucalyptus acmenoides	White Mahogany	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
539	Eucalyptus acmenoides	White Mahogany	270	200	336	17	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
540	Eucalyptus tereticornis	Forest Red Gum	250		250	20	6	3.0	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
541	Eucalyptus acmenoides	White Mahogany	200		200	16	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
542	Eucalyptus tereticornis	Forest Red Gum	290		290	20	6	3.5	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
543	Corymbia intermedia	Pink Bloodwood	280		280	18	5	3.4	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
544	Eucalyptus acmenoides	White Mahogany	320		320	16	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
545	Eucalyptus tereticornis	Forest Red Gum	200		200	15	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
546	Eucalyptus tereticornis	Forest Red Gum	240		240	17	3	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
547	Corymbia intermedia	Pink Bloodwood	240	170	294	17	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
548	Lophostemon suaveolens	Swamp Box	250		250	10	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
549	Corymbia intermedia	Pink Bloodwood	340		340	18	7	4.1	2.1	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
550	Corymbia intermedia	Pink Bloodwood	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
551	Eucalyptus acmenoides	White Mahogany	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
552	Corymbia intermedia	Pink Bloodwood	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
553	Eucalyptus acmenoides	White Mahogany	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
554	Angophora leiocarpa	Smooth-barked Apple	290		290	19	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
555	Eucalyptus siderophloia	Grey Ironbark	430		430	19	9	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
556	Angophora leiocarpa	Smooth-barked Apple	330		330	21	8	4.0	2.1	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
557	Lophostemon suaveolens	Swamp Box	300		300	12	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
558	Corymbia intermedia	Pink Bloodwood	280		280	16	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
559	Angophora leiocarpa	Smooth-barked Apple	340		340	18	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
560	Lophostemon suaveolens	Swamp Box	190		190	14	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
561	Eucalyptus saligna	Sydney Blue Gum	300		300	18	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
562	Banksia integrifolia	Coast Banksia	240		240	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
563	Angophora subvelutina	Broad-leaved Apple	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
564	Angophora subvelutina	Broad-leaved Apple	320		320	16	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
565	Angophora subvelutina	Broad-leaved Apple	380		380	18	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
566	Alphitonia excelsa	Soap Tree	280		280	16	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
567	Casuarina cunninghamiana	River Sheoak	190	160	248	17	4	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
568	Lophostemon suaveolens	Swamp Box	260	280	382	18	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
569	Eucalyptus saligna	Sydney Blue Gum	350		350	20	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
570	Eucalyptus siderophloia	Grey Ironbark	400		400	25	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
571	Eucalyptus saligna	Sydney Blue Gum	290		290	24	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
572	Corymbia intermedia	Pink Bloodwood	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
573	Angophora subvelutina	Broad-leaved Apple	300		300	14	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
574	Eucalyptus saligna	Sydney Blue Gum	300		300	22	12	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
575	Eucalyptus saligna	Sydney Blue Gum	250		250	20	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
576	Eucalyptus saligna	Sydney Blue Gum	330		330	25	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
577	Lophostemon suaveolens	Swamp Box	300		300	15	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
578	Eucalyptus saligna	Sydney Blue Gum	520		520	25	12	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
579	Eucalyptus acmenoides	White Mahogany	400		400	16	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
580	Eucalyptus tereticornis	Forest Red Gum	270		270	18	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
581	Eucalyptus tereticornis	Forest Red Gum	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
582	Angophora subvelutina	Broad-leaved Apple	300		300	16	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
583	Angophora subvelutina	Broad-leaved Apple	450		450	17	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
584	Corymbia intermedia	Pink Bloodwood	180	140	228	10	3	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
585	Angophora leiocarpa	Smooth-barked Apple	230		230	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
586	Acacia concurrens	Black Wattle	220		220	11	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
587	Lophostemon suaveolens	Swamp Box	210		210	16	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
588	Alphitonia excelsa	Soap Tree	330		330	17	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
589	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
590	Angophora subvelutina	Broad-leaved Apple	380		380	16	7	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
591	Lophostemon suaveolens	Swamp Box	290		290	16	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
592	Angophora subvelutina	Broad-leaved Apple	660		660	22	14	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
593	Ficus coronata	Sandpaper Fig	200		200	8	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
594	Angophora subvelutina	Broad-leaved Apple	390		390	18	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
595	Angophora subvelutina	Broad-leaved Apple	400	320	512	17	9	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
596	Melaleuca viminalis	Weeping Bottlebrush	300		300	12	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Retain
597	Lophostemon suaveolens	Swamp Box	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
598	Alphitonia excelsa	Soap Tree	390		390	10	5	4.7	2.2	One-sided	-	-	-	-	-	Typical	Major	Introduced	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retain
599	Eucalyptus tereticornis	Forest Red Gum	600		600	25	8	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
600	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
601	Corymbia tessellaris	Moreton Bay Ash	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
602	Lophostemon suaveolens	Swamp Box	280		280	16	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
603	Lophostemon suaveolens	Swamp Box	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
604	Acacia disparrima	Hickory Wattle	250	220	333	14	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
605	Acacia disparrima	Hickory Wattle	280		280	13	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
606	Corymbia tessellaris	Moreton Bay Ash	380		380	22	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
607	Corymbia tessellaris	Moreton Bay Ash	320		320	17	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
608	Acacia disparrima	Hickory Wattle	280		280	10	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
609	Eucalyptus tereticornis	Forest Red Gum	560		560	24	9	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
610	Corymbia tessellaris	Moreton Bay Ash	280		280	21	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
611	Melaleuca viminalis	Weeping Bottlebrush	290	200	352	10	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
612	Casuarina cunninghamiana	River Sheoak	390		390	20	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
613	Lophostemon suaveolens	Swamp Box	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
614	Casuarina cunninghamiana	River Sheoak	480		480	20	10	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
615	Casuarina cunninghamiana	River Sheoak	400		400	24	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
616	Casuarina cunninghamiana	River Sheoak	330		330	18	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
617	Acacia disparrima	Hickory Wattle	330		330	12	5	4.0	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
618	Corymbia intermedia	Pink Bloodwood	300		300	18	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Retain
619	Acacia disparrima	Hickory Wattle	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
620	Angophora subvelutina	Broad-leaved Apple	550		550	20	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
621	Lophostemon suaveolens	Swamp Box	300		300	16	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
622	Lophostemon suaveolens	Swamp Box	350		350	17	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
623	Alphitonia excelsa	Soap Tree	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
624	Corymbia tessellaris	Moreton Bay Ash	230		230	18	4	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
625	Eucalyptus tereticornis	Forest Red Gum	550		550	23	9	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
626	Eucalyptus tereticornis	Forest Red Gum	300		300	24	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
627	Eucalyptus tereticornis	Forest Red Gum	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
628	Lophostemon suaveolens	Swamp Box	210		210	13	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
629	Eucalyptus tereticornis	Forest Red Gum	300		300	17	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
630	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
631	Corymbia tessellaris	Moreton Bay Ash	250		250	17	4	3.0	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
632	Corymbia tessellaris	Moreton Bay Ash	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
633	Lophostemon suaveolens	Swamp Box	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
634	Lophostemon suaveolens	Swamp Box	250		250	17	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
635	Eucalyptus major	Grey Gum	450		450	25	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
636	Lophostemon suaveolens	Swamp Box	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
637	Lophostemon suaveolens	Swamp Box	250		250	13	4	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
638	Lophostemon suaveolens	Swamp Box	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
639	Eucalyptus tereticornis	Forest Red Gum	200		200	12	4	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
640	Corymbia tessellaris	Moreton Bay Ash	300		300	19	5	3.6	2.0	One-sided	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
641	Angophora subvelutina	Broad-leaved Apple	270		270	15	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
642	Lophostemon suaveolens	Swamp Box	280		280	18	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
643	Lophostemon suaveolens	Swamp Box	290		290	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
644	Eucalyptus tereticornis	Forest Red Gum	600		600	25	10	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
645	Lophostemon suaveolens	Swamp Box	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
646	Eucalyptus tereticornis	Forest Red Gum	450		450	27	14	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
647	Eucalyptus tereticornis	Forest Red Gum	660		660	28	10	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
648	Lophostemon suaveolens	Swamp Box	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
649	Casuarina cunninghamiana	River Sheoak	430		430	18	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
650	Casuarina cunninghamiana	River Sheoak	280		280	19	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
651	Casuarina cunninghamiana	River Sheoak	350		350	22	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
652	Casuarina cunninghamiana	River Sheoak	300		300	18	7	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
653	Casuarina cunninghamiana	River Sheoak	500		500	22	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
654	Casuarina cunninghamiana	River Sheoak	370		370	19	4	4.4	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
655	Casuarina cunninghamiana	River Sheoak	400		400	20	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
656	Casuarina cunninghamiana	River Sheoak	200		200	15	5	2.4	1.7	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
657	Casuarina cunninghamiana	River Sheoak	400		400	20	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
658	Casuarina cunninghamiana	River Sheoak	210		210	17	4	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
659	Casuarina cunninghamiana	River Sheoak	240		240	10	5	2.9	1.8	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
660	Casuarina cunninghamiana	River Sheoak	360		360	20	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
661	Casuarina cunninghamiana	River Sheoak	400		400	15	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
662	Acacia disparrima	Hickory Wattle	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
663	Lophostemon suaveolens	Swamp Box	290		290	15	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
664	Casuarina cunninghamiana	River Sheoak	330		330	20	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
665	Lophostemon suaveolens	Swamp Box	310		310	17	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
666	Eucalyptus tereticornis	Forest Red Gum	330		330	21	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
667	Eucalyptus tereticornis	Forest Red Gum	280		280	20	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
668	Eucalyptus siderophloia	Grey Ironbark	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
669	Eucalyptus siderophloia	Grey Ironbark	250		250	17	4	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
670	Eucalyptus siderophloia	Grey Ironbark	290		290	18	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
671	Eucalyptus tereticornis	Forest Red Gum	310		310	15	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
672	Eucalyptus tereticornis	Forest Red Gum	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
673	Eucalyptus tereticornis	Forest Red Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
674	Eucalyptus tereticornis	Forest Red Gum	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
675	Lophostemon suaveolens	Swamp Box	230		230	16	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
676	Corymbia tessellaris	Moreton Bay Ash	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
677	Lophostemon suaveolens	Swamp Box	210		210	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
678	Eucalyptus tereticornis	Forest Red Gum	380		380	19	4	4.6	2.2	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
679	Eucalyptus tereticornis	Forest Red Gum	220		220	20	4	2.6	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
680	Eucalyptus tereticornis	Forest Red Gum	300		300	22	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
681	Eucalyptus siderophloia	Grey Ironbark	310		310	20	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Remove for basin works
682	Lophostemon suaveolens	Swamp Box	240		240	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
683	Eucalyptus moluccana	Gum Topped Box	250	200, 140	349	16	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
684	Eucalyptus tereticornis	Forest Red Gum	270		270	18	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
685	Eucalyptus tereticornis	Forest Red Gum	330		330	20	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
686	Eucalyptus tereticornis	Forest Red Gum	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
687	Lophostemon suaveolens	Swamp Box	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
688	Eucalyptus tereticornis	Forest Red Gum	250	180	308	16	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
689	Eucalyptus tereticornis	Forest Red Gum	220		220	17	5	2.6	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
690	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
691	Eucalyptus tereticornis	Forest Red Gum	250		250	20	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Remove for basin works
692	Angophora subvelutina	Broad-leaved Apple	300		300	17	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
693	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
694	Angophora subvelutina	Broad-leaved Apple	300		300	16	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
695	Angophora subvelutina	Broad-leaved Apple	300		300	17	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
696	Eucalyptus tereticornis	Forest Red Gum	310		310	28	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
697	Eucalyptus tereticornis	Forest Red Gum	300		300	25	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
698	Eucalyptus tereticornis	Forest Red Gum	350		350	28	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
699	Angophora subvelutina	Broad-leaved Apple	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
700	Angophora subvelutina	Broad-leaved Apple	300		300	18	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
701	Eucalyptus tereticornis	Forest Red Gum	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
702	Angophora subvelutina	Broad-leaved Apple	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
703	Angophora subvelutina	Broad-leaved Apple	250		250	21	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
704	Angophora subvelutina	Broad-leaved Apple	300		300	21	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
705	Angophora subvelutina	Broad-leaved Apple	280		280	20	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
706	Corymbia tessellaris	Moreton Bay Ash	270		270	20	5	3.2	1.9	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
707	Corymbia tessellaris	Moreton Bay Ash	220		220	23	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
708	Lophostemon suaveolens	Swamp Box	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
709	Eucalyptus tereticornis	Forest Red Gum	400		400	27	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
710	Acacia disparrima	Hickory Wattle	200		200	14	4	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
711	Eucalyptus tereticornis	Forest Red Gum	670		670	28	14	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
712	Eucalyptus tereticornis	Forest Red Gum	500		500	30	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
713	Corymbia tessellaris	Moreton Bay Ash	220		220	18	5	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
714	Corymbia tessellaris	Moreton Bay Ash	320		320	27	8	3.8	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
715	Lophostemon suaveolens	Swamp Box	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
716	Angophora subvelutina	Broad-leaved Apple	800		800	30	16	9.6	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
717	Casuarina cunninghamiana	River Sheoak	330		330	21	6	4.0	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
718	Casuarina cunninghamiana	River Sheoak	320		320	18	9	3.8	2.1	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
719	Casuarina cunninghamiana	River Sheoak	420		420	21	12	5.0	2.3	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
720	Casuarina cunninghamiana	River Sheoak	400		400	22	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
721	Casuarina cunninghamiana	River Sheoak	360		360	20	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
722	Casuarina cunninghamiana	River Sheoak	400		400	19	5	4.8	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
723	Casuarina cunninghamiana	River Sheoak	460		460	20	8	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
724	Casuarina cunninghamiana	River Sheoak	400		400	21	5	4.8	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
725	Casuarina cunninghamiana	River Sheoak	350	380	517	20	8	6.2	2.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
726	Eucalyptus tereticornis	Forest Red Gum	410		410	25	10	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
727	Corymbia tessellaris	Moreton Bay Ash	570		570	22	10	6.8	2.6	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
728	Corymbia tessellaris	Moreton Bay Ash	410		410	30	14	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
729	Casuarina cunninghamiana	River Sheoak	460		460	20	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
730	Casuarina cunninghamiana	River Sheoak	240		240	18	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
731	Eucalyptus tereticornis	Forest Red Gum	460		460	22	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
732	Angophora subvelutina	Broad-leaved Apple	360		360	18	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
733	Lophostemon suaveolens	Swamp Box	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
734	Corymbia tessellaris	Moreton Bay Ash	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
735	Angophora leiocarpa	Smooth-barked Apple	200		200	20	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
736	Eucalyptus tereticornis	Forest Red Gum	250		250	18	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
737	Corymbia citriodora	Spotted Gum	400		400	24	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
738	Corymbia citriodora	Spotted Gum	340	160	376	24	8	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
739	Eucalyptus tereticornis	Forest Red Gum	650		650	25	9	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
740	Corymbia citriodora	Spotted Gum	260		260	21	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
741	Eucalyptus moluccana	Gum Topped Box	600		600	25	14	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
742	Corymbia citriodora	Spotted Gum	440		440	29	8	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
743	Lophostemon suaveolens	Swamp Box	280		280	16	5	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
744	Eucalyptus moluccana	Gum Topped Box	800		800	28	10	9.6	3.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
745	Eucalyptus moluccana	Gum Topped Box	560		560	27	7	6.7	2.6	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
746	Eucalyptus moluccana	Gum Topped Box	600		600	29	10	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
747	Angophora leiocarpa	Smooth-barked Apple	410		410	19	4	4.9	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
748	Eucalyptus moluccana	Gum Topped Box	400		400	22	8	4.8	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
749	Eucalyptus moluccana	Gum Topped Box	510		510	24	10	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
750	Eucalyptus moluccana	Gum Topped Box	440		440	22	8	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
751	Eucalyptus moluccana	Gum Topped Box	220		220	19	3	2.6	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
752	Lophostemon suaveolens	Swamp Box	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
753	Eucalyptus moluccana	Gum Topped Box	220		220	16	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
754	Eucalyptus moluccana	Gum Topped Box	220		220	19	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
755	Eucalyptus moluccana	Gum Topped Box	400		400	30	9	4.8	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
756	Eucalyptus moluccana	Gum Topped Box	510		510	26	8	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
757	Eucalyptus moluccana	Gum Topped Box	290	150	326	27	6	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
758	Eucalyptus moluccana	Gum Topped Box	400		400	20	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
759	Eucalyptus moluccana	Gum Topped Box	420		420	26	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
760	Eucalyptus moluccana	Gum Topped Box	350		350	19	4	4.2	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
761	Eucalyptus moluccana	Gum Topped Box	430		430	27	9	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
762	Eucalyptus moluccana	Gum Topped Box	540		540	27	13	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
763	Eucalyptus moluccana	Gum Topped Box	470		470	30	8	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
764	Eucalyptus tereticornis	Forest Red Gum	230		230	17	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
765	Acacia disparrima	Hickory Wattle	230		230	8	3	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
766	Corymbia intermedia	Pink Bloodwood	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
767	Lophostemon suaveolens	Swamp Box	230		230	14	4	2.8	1.8	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
768	Lophostemon suaveolens	Swamp Box	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
769	Eucalyptus tereticornis	Forest Red Gum	520		520	21	9	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
770	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
771	Eucalyptus tereticornis	Forest Red Gum	520	260	581	23	9	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
772	Acacia disparrima	Hickory Wattle	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
773	Eucalyptus siderophloia	Grey Ironbark	200		200	12	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
774	Eucalyptus tereticornis	Forest Red Gum	270		270	20	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
775	Eucalyptus saligna	Sydney Blue Gum	260		260	20	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
776	Acacia disparrima	Hickory Wattle	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
777	Eucalyptus saligna	Sydney Blue Gum	270		270	19	6	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
778	Corymbia tessellaris	Moreton Bay Ash	200		200	21	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
779	Eucalyptus saligna	Sydney Blue Gum	300		300	20	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
780	Corymbia intermedia	Pink Bloodwood	270		270	23	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
781	Corymbia intermedia	Pink Bloodwood	200		200	22	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
782	Eucalyptus saligna	Sydney Blue Gum	320		320	23	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
783	Allocasuarina littoralis	Black She Oak	260		260	14	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
784	Corymbia tessellaris	Moreton Bay Ash	270		270	21	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
785	Acacia disparrima	Hickory Wattle	230		230	12	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
786	Eucalyptus saligna	Sydney Blue Gum	230		230	22	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
787	Eucalyptus saligna	Sydney Blue Gum	370		370	22	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
788	Eucalyptus saligna	Sydney Blue Gum	330		330	22	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
789	Eucalyptus saligna	Sydney Blue Gum	250		250	24	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
790	Eucalyptus tereticornis	Forest Red Gum	220		220	19	3	2.6	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
791	Eucalyptus saligna	Sydney Blue Gum	400		400	24	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
792	Eucalyptus saligna	Sydney Blue Gum	320		320	23	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
793	Acacia disparrima	Hickory Wattle	200		200	8	4	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
794	Acacia disparrima	Hickory Wattle	160	140, 140	255	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
795	Acacia disparrima	Hickory Wattle	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
796	Eucalyptus tereticornis	Forest Red Gum	260		260	24	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
797	Eucalyptus saligna	Sydney Blue Gum	370		370	24	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
798	Eucalyptus saligna	Sydney Blue Gum	250		250	23	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
799	Lophostemon suaveolens	Swamp Box	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
800	Lophostemon suaveolens	Swamp Box	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
801	Alphitonia excelsa	Soap Tree	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
802	Eucalyptus siderophloia	Grey Ironbark	210		210	22	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
803	Eucalyptus saligna	Sydney Blue Gum	330		330	23	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
804	Corymbia tessellaris	Moreton Bay Ash	300		300	27	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
805	Petalostigma pubescens	Quinine Bush	210	200, 120	314	12	7	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
806	Angophora subvelutina	Broad-leaved Apple	280		280	20	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
807	Corymbia intermedia	Pink Bloodwood	310		310	25	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
808	Eucalyptus siderophloia	Grey Ironbark	250		250	21	4	3.0	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
809	Angophora subvelutina	Broad-leaved Apple	230		230	20	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
810	Acacia disparrima	Hickory Wattle	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
811	Corymbia intermedia	Pink Bloodwood	260		260	20	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
812	Lophostemon suaveolens	Swamp Box	230		230	20	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
813	Eucalyptus siderophloia	Grey Ironbark	210		210	20	4	2.5	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
814	Lophostemon suaveolens	Swamp Box	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
815	Angophora subvelutina	Broad-leaved Apple	220		220	22	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
816	Corymbia tessellaris	Moreton Bay Ash	420		420	23	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
817	Lophostemon suaveolens	Swamp Box	210		210	17	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
818	Lophostemon suaveolens	Swamp Box	220	190	291	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
819	Eucalyptus tereticornis	Forest Red Gum	400		400	24	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
820	Corymbia intermedia	Pink Bloodwood	240	190	306	22	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
821	Corymbia intermedia	Pink Bloodwood	240		240	19	5	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
822	Lophostemon suaveolens	Swamp Box	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
823	Eucalyptus tereticornis	Forest Red Gum	210		210	20	4	2.5	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
824	Lophostemon suaveolens	Swamp Box	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
825	Eucalyptus tereticornis	Forest Red Gum	280		280	22	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
826	Eucalyptus tereticornis	Forest Red Gum	290		290	23	5	3.5	2.0	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
827	Corymbia tessellaris	Moreton Bay Ash	250	240	347	17	5	4.2	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
828	Eucalyptus siderophloia	Grey Ironbark	200		200	19	4	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
829	Angophora subvelutina	Broad-leaved Apple	270		270	22	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
830	Alphitonia excelsa	Soap Tree	200		200	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
831	Acacia disparrima	Hickory Wattle	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
832	Corymbia intermedia	Pink Bloodwood	240		240	21	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
833	Eucalyptus tereticornis	Forest Red Gum	250		250	22	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
834	Angophora leiocarpa	Smooth-barked Apple	280		280	19	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
835	Eucalyptus tereticornis	Forest Red Gum	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
836	Angophora leiocarpa	Smooth-barked Apple	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
837	Lophostemon suaveolens	Swamp Box	210	150	258	12	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
838	Corymbia citriodora	Spotted Gum	270		270	19	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
839	Corymbia intermedia	Pink Bloodwood	230		230	20	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
840	Eucalyptus tereticornis	Forest Red Gum	210		210	20	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
841	Corymbia intermedia	Pink Bloodwood	250		250	18	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
842	Corymbia citriodora	Spotted Gum	310		310	20	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
843	Eucalyptus tereticornis	Forest Red Gum	360		360	21	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
844	Corymbia citriodora	Spotted Gum	240		240	23	7	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
845	Acacia disparrima	Hickory Wattle	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
846	Lophostemon suaveolens	Swamp Box	250		250	16	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
847	Corymbia henryi	Large-leaved Spotted Gum	250		250	19	5	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
848	Lophostemon suaveolens	Swamp Box	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
849	Eucalyptus tereticornis	Forest Red Gum	270		270	20	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
850	Allocasuarina littoralis	Black She Oak	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
851	Corymbia intermedia	Pink Bloodwood	240		240	16	4	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
852	Allocasuarina littoralis	Black She Oak	180	170	248	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
853	Eucalyptus tereticornis	Forest Red Gum	200		200	15	4	2.4	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
854	Angophora leiocarpa	Smooth-barked Apple	210		210	13	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
855	Eucalyptus acmenoides	White Mahogany	420		420	16	6	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
856	Angophora leiocarpa	Smooth-barked Apple	320	150	353	18	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
857	Eucalyptus acmenoides	White Mahogany	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
858	Eucalyptus acmenoides	White Mahogany	220		220	16	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
859	Eucalyptus tereticornis	Forest Red Gum	290		290	20	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
860	Lophostemon suaveolens	Swamp Box	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
861	Lophostemon suaveolens	Swamp Box	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
862	Corymbia intermedia	Pink Bloodwood	230		230	17	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
863	Corymbia intermedia	Pink Bloodwood	330		330	17	6	4.0	2.1	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
864	Lophostemon suaveolens	Swamp Box	220		220	14	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
865	Corymbia intermedia	Pink Bloodwood	320		320	16	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
866	Eucalyptus tereticornis	Forest Red Gum	430		430	20	5	5.2	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
867	Corymbia intermedia	Pink Bloodwood	350		350	18	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
868	Angophora leiocarpa	Smooth-barked Apple	220	190	291	16	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
869	Corymbia citriodora	Spotted Gum	470		470	20	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
870	Eucalyptus saligna	Sydney Blue Gum	290		290	19	5	3.5	2.0	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
871	Corymbia intermedia	Pink Bloodwood	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
872	Eucalyptus tereticornis	Forest Red Gum	230		230	17	5	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
873	Eucalyptus tereticornis	Forest Red Gum	310		310	20	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
874	Corymbia citriodora	Spotted Gum	240		240	19	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
875	Corymbia citriodora	Spotted Gum	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
876	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	20	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
877	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
878	Corymbia citriodora	Spotted Gum	250		250	18	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
879	Eucalyptus crebra	Narrow-leaved Ironbark	550		550	24	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
880	Corymbia citriodora	Spotted Gum	200		200	17	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
881	Corymbia citriodora	Spotted Gum	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
882	Eucalyptus moluccana	Gum Topped Box	280		280	17	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
883	Corymbia citriodora	Spotted Gum	230	150, 80	286	16	4	3.4	2.0	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
884	Corymbia citriodora	Spotted Gum	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
885	Corymbia citriodora	Spotted Gum	320		320	19	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
886	Corymbia citriodora	Spotted Gum	250		250	17	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
887	Corymbia citriodora	Spotted Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
888	Corymbia citriodora	Spotted Gum	230		230	17	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
889	Corymbia citriodora	Spotted Gum	360	180	402	22	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
890	Corymbia citriodora	Spotted Gum	220		220	14	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
891	Corymbia citriodora	Spotted Gum	210		210	16	3	2.5	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
892	Corymbia citriodora	Spotted Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
893	Corymbia citriodora	Spotted Gum	280		280	17	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
894	Corymbia citriodora	Spotted Gum	230		230	15	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
895	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	18	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
896	Corymbia citriodora	Spotted Gum	220		220	19	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
897	Corymbia citriodora	Spotted Gum	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
898	Corymbia citriodora	Spotted Gum	230		230	22	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
899	Corymbia citriodora	Spotted Gum	210		210	19	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
900	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	17	6	4.1	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
901	Corymbia citriodora	Spotted Gum	210		210	20	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
902	Corymbia citriodora	Spotted Gum	280		280	23	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
903	Corymbia citriodora	Spotted Gum	200		200	20	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
904	Corymbia citriodora	Spotted Gum	190	80	206	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
905	Corymbia citriodora	Spotted Gum	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
906	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	19	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
907	Corymbia citriodora	Spotted Gum	260		260	22	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
908	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
909	Corymbia citriodora	Spotted Gum	250		250	22	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
910	Corymbia citriodora	Spotted Gum	210		210	20	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
911	Corymbia citriodora	Spotted Gum	230		230	19	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
912	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	25	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
913	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	18	4	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
914	Corymbia citriodora	Spotted Gum	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
915	Corymbia citriodora	Spotted Gum	200		200	18	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
916	Corymbia citriodora	Spotted Gum	230		230	20	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
917	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	19	4	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
918	Corymbia citriodora	Spotted Gum	210		210	18	4	2.5	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
919	Corymbia citriodora	Spotted Gum	250		250	18	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
920	Corymbia citriodora	Spotted Gum	200		200	22	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
921	Corymbia citriodora	Spotted Gum	220		220	19	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
922	Corymbia citriodora	Spotted Gum	210		210	19	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
923	Corymbia citriodora	Spotted Gum	350		350	20	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
924	Eucalyptus crebra	Narrow-leaved Ironbark	400		400	22	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
925	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	19	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
926	Eucalyptus siderophloia	Grey Ironbark	390		390	19	7	4.7	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
927	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	18	4	3.2	1.9	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
928	Corymbia citriodora	Spotted Gum	290		290	18	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
929	Corymbia citriodora	Spotted Gum	210		210	18	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
930	Corymbia citriodora	Spotted Gum	220	140	261	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
931	Corymbia citriodora	Spotted Gum	230	170	286	16	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
932	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	18	5	3.5	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
933	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	23	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
934	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
935	Eucalyptus crebra	Narrow-leaved Ironbark	230	130	264	18	3	3.2	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
936	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
937	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	12	3	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
938	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	17	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
939	Corymbia citriodora	Spotted Gum	240		240	21	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
940	Corymbia citriodora	Spotted Gum	220		220	19	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
941	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	23	10	4.2	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
942	Eucalyptus siderophloia	Grey Ironbark	210		210	17	3	2.5	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
943	Corymbia citriodora	Spotted Gum	300		300	25	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
944	Eucalyptus tereticornis	Forest Red Gum	320		320	20	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
945	Eucalyptus major	Grey Gum	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
946	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	20	3	3.5	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
947	Corymbia citriodora	Spotted Gum	270		270	21	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
948	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
949	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	20	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
950	Corymbia citriodora	Spotted Gum	260		260	19	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
951	Corymbia citriodora	Spotted Gum	220		220	16	3	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
952	Eucalyptus tereticornis	Forest Red Gum	230		230	17	3	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
953	Eucalyptus tereticornis	Forest Red Gum	400		400	22	8	4.8	2.3	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
954	Corymbia citriodora	Spotted Gum	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
955	Eucalyptus siderophloia	Grey Ironbark	280		280	24	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
956	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	20	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
957	Corymbia citriodora	Spotted Gum	300		300	20	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
958	Corymbia citriodora	Spotted Gum	270		270	21	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
959	Corymbia citriodora	Spotted Gum	250		250	22	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
960	Corymbia citriodora	Spotted Gum	340		340	24	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
961	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
962	Corymbia citriodora	Spotted Gum	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
963	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	16	5	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
964	Corymbia citriodora	Spotted Gum	480		480	26	7	5.8	2.4	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
965	Corymbia citriodora	Spotted Gum	400		400	22	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
966	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	16	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
967	Corymbia citriodora	Spotted Gum	380		380	25	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
968	Corymbia citriodora	Spotted Gum	340		340	16	5	4.1	2.1	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
969	Corymbia citriodora	Spotted Gum	300		300	18	3	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
970	Eucalyptus siderophloia	Grey Ironbark	200	170, 140	297	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
971	Corymbia citriodora	Spotted Gum	680		680	25	10	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Approved to remove
972	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	18	3	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
973	Eucalyptus tereticornis	Forest Red Gum	300		300	18	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
974	Corymbia citriodora	Spotted Gum	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
975	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	16	5	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
976	Eucalyptus siderophloia	Grey Ironbark	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
977	Corymbia citriodora	Spotted Gum	450		450	20	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Approved to remove
978	Corymbia citriodora	Spotted Gum	680		680	26	10	8.2	2.8	Regular	-	-	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
979	Corymbia citriodora	Spotted Gum	260		260	18	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
980	Corymbia citriodora	Spotted Gum	200		200	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
981	Eucalyptus siderophloia	Grey Ironbark	500		500	23	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
982	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	18	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
983	Eucalyptus crebra	Narrow-leaved Ironbark	100	100	120	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
984	Corymbia citriodora	Spotted Gum	420		420	16	3	5.0	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	Large	-	-	-		Approved to remove
985	Corymbia citriodora	Spotted Gum	320		320	19	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
986	Corymbia citriodora	Spotted Gum	410		410	28	12	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
987	Corymbia citriodora	Spotted Gum	370		370	16	6	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
988	Corymbia citriodora	Spotted Gum	470		470	22	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
989	Corymbia citriodora	Spotted Gum	550		550	27	8	6.6	2.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
990	Corymbia citriodora	Spotted Gum	470		470	27	9	5.6	2.4	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
991	Corymbia citriodora	Spotted Gum	240		240	17	4	2.9	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
992	Corymbia citriodora	Spotted Gum	680		680	28	11	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
993	Eucalyptus siderophloia	Grey Ironbark	400		400	20	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
994	Corymbia citriodora	Spotted Gum	470		470	21	5	5.6	2.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
995	Corymbia intermedia	Pink Bloodwood	540		540	30	10	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
996	Corymbia citriodora	Spotted Gum	260		260	21	2	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
997	Corymbia citriodora	Spotted Gum	300		300	24	3	3.6	2.0	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
998	Corymbia citriodora	Spotted Gum	540		540	27	10	6.5	2.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
999	Corymbia citriodora	Spotted Gum	600		600	27	14	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	Large	-	-	-		Retain
1000	Corymbia citriodora	Spotted Gum	650		650	30	16	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Retain
1001	Corymbia citriodora	Spotted Gum	250		250	13	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1002	Eucalyptus tereticornis	Forest Red Gum	260		260	17	5	3.1	1.9	One-sided	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1003	Corymbia citriodora	Spotted Gum	250		250	17	5	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1004	Angophora leiocarpa	Smooth-barked Apple	240		240	14	4	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1005	Corymbia citriodora	Spotted Gum	390		390	17	4	4.7	2.2	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1006	Eucalyptus tereticornis	Forest Red Gum	700		700	24	9	8.4	2.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1007	Corymbia citriodora	Spotted Gum	350		350	18	6	4.2	2.1	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
1008	Corymbia citriodora	Spotted Gum	330		330	27	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1009	Eucalyptus moluccana	Gum Topped Box	400		400	25	11	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1010	Eucalyptus moluccana	Gum Topped Box	310		310	24	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1011	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	17	6	3.6	2.0	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1012	Eucalyptus moluccana	Gum Topped Box	250		250	17	3	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1013	Eucalyptus moluccana	Gum Topped Box	550		550	28	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1014	Eucalyptus moluccana	Gum Topped Box	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1015	Corymbia citriodora	Spotted Gum	340		340	20	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1016	Corymbia intermedia	Pink Bloodwood	220	200	297	18	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1017	Eucalyptus tereticornis	Forest Red Gum	400		400	25	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1018	Lophostemon suaveolens	Swamp Box	220		220	16	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1019	Lophostemon suaveolens	Swamp Box	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1020	Eucalyptus tereticornis	Forest Red Gum	330	300	446	27	8	5.4	2.4	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1021	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1022	Eucalyptus siderophloia	Grey Ironbark	310		310	26	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Approved to remove
1023	Eucalyptus tereticornis	Forest Red Gum	480		480	30	10	5.8	2.4	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1024	Angophora leiocarpa	Smooth-barked Apple	300		300	18	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1025	Lophostemon suaveolens	Swamp Box	200		200	16	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1026	Angophora leiocarpa	Smooth-barked Apple	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1027	Eucalyptus tereticornis	Forest Red Gum	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1028	Eucalyptus tereticornis	Forest Red Gum	220		220	17	4	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1029	Lophostemon suaveolens	Swamp Box	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1030	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1031	Eucalyptus siderophloia	Grey Ironbark	400		400	25	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1032	Eucalyptus tereticornis	Forest Red Gum	280	170	328	17	6	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1033	Eucalyptus tereticornis	Forest Red Gum	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1034	Eucalyptus tereticornis	Forest Red Gum	280		280	20	11	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1035	Eucalyptus seeana	Narrow-leaved Red Gum	380		380	22	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1036	Eucalyptus resinifera	Red Mahogany	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1037	Eucalyptus seeana	Narrow-leaved Red Gum	400		400	27	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1038	Eucalyptus saligna	Sydney Blue Gum	380		380	20	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1039	Eucalyptus siderophloia	Grey Ironbark	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1040	Corymbia intermedia	Pink Bloodwood	180	150, 150, 140	311	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1041	Corymbia citriodora	Spotted Gum	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1042	Corymbia citriodora	Spotted Gum	220		220	16	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1043	Eucalyptus tereticornis	Forest Red Gum	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1044	Corymbia citriodora	Spotted Gum	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1045	Angophora leiocarpa	Smooth-barked Apple	350		350	19	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1046	Alphitonia excelsa	Soap Tree	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1047	Corymbia intermedia	Pink Bloodwood	210	150	258	16	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1048	Corymbia intermedia	Pink Bloodwood	210		210	14	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1049	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	20	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1050	Eucalyptus siderophloia	Grey Ironbark	330		330	19	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1051	Eucalyptus crebra	Narrow-leaved Ironbark	390		390	22	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1052	Angophora woodsiana	Broad-leaved Apple	330		330	18	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1053	Acacia disparrima	Hickory Wattle	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1054	Lophostemon suaveolens	Swamp Box	310		310	16	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1055	Lophostemon suaveolens	Swamp Box	280		280	16	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1056	Corymbia intermedia	Pink Bloodwood	450		450	23	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1057	Angophora leiocarpa	Smooth-barked Apple	360		360	20	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1058	Eucalyptus tereticornis	Forest Red Gum	290		290	21	5	3.5	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1059	Lophostemon suaveolens	Swamp Box	270		270	16	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1060	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	25	6	3.1	1.9	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1061	Corymbia intermedia	Pink Bloodwood	400		400	20	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1062	Lophostemon suaveolens	Swamp Box	270		270	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1063	Lophostemon suaveolens	Swamp Box	220	140	261	12	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1064	Lophostemon suaveolens	Swamp Box	250		250	17	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1065	Eucalyptus tereticornis	Forest Red Gum	270		270	20	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1066	Acacia disparrima	Hickory Wattle	270		270	12	5	3.2	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1067	Eucalyptus tereticornis	Forest Red Gum	460		460	24	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1068	Lophostemon suaveolens	Swamp Box	200	110	228	10	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1069	Eucalyptus siderophloia	Grey Ironbark	330		330	20	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1070	Eucalyptus tereticornis	Forest Red Gum	500		500	22	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1071	Lophostemon suaveolens	Swamp Box	180	200	269	11	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1072	Lophostemon suaveolens	Swamp Box	180	180	255	14	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1073	Eucalyptus tereticornis	Forest Red Gum	490		490	20	12	5.9	2.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	Small	-	-	-		Remove
1074	Lophostemon suaveolens	Swamp Box	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1075	Corymbia intermedia	Pink Bloodwood	250		250	19	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1076	Lophostemon suaveolens	Swamp Box	190	140	236	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1077	Lophostemon suaveolens	Swamp Box	250		250	18	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1078	Lophostemon suaveolens	Swamp Box	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1079	Lophostemon suaveolens	Swamp Box	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1080	Corymbia intermedia	Pink Bloodwood	230		230	19	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1081	Lophostemon suaveolens	Swamp Box	210		210	19	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1082	Lophostemon suaveolens	Swamp Box	215		215	16	5	2.6	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1083	Lophostemon suaveolens	Swamp Box	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1084	Lophostemon suaveolens	Swamp Box	220	140	261	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1085	Lophostemon suaveolens	Swamp Box	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1086	Lophostemon suaveolens	Swamp Box	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1087	Lophostemon suaveolens	Swamp Box	250		250	16	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1088	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1089	Corymbia intermedia	Pink Bloodwood	260		260	18	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1090	Lophostemon suaveolens	Swamp Box	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1091	Lophostemon suaveolens	Swamp Box	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1092	Lophostemon suaveolens	Swamp Box	210		210	14	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1093	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1094	Lophostemon suaveolens	Swamp Box	360		360	19	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1095	Corymbia intermedia	Pink Bloodwood	320		320	25	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1096	Lophostemon suaveolens	Swamp Box	190	150	242	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1097	Eucalyptus tereticornis	Forest Red Gum	580		580	28	14	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1098	Lophostemon suaveolens	Swamp Box	200	180	269	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1099	Corymbia intermedia	Pink Bloodwood	210		210	14	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1100	Acacia melanoxylon	Australian Blackwood	240	180, 170, 120	365	10	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1101	Eucalyptus tereticornis	Forest Red Gum	250		250	20	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1102	Corymbia intermedia	Pink Bloodwood	310		310	21	6	3.7	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1103	Angophora subvelutina	Broad-leaved Apple	170	170, 150	283	14	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1104	Lophostemon suaveolens	Swamp Box	160	150, 140, 140	295	12	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1105	Lophostemon suaveolens	Swamp Box	170	180, 120	275	14	3	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1106	Acacia concurrens	Black Wattle	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1107	Lophostemon suaveolens	Swamp Box	180	160	241	12	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1108	Lophostemon suaveolens	Swamp Box	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1109	Lophostemon suaveolens	Swamp Box	190	150	242	14	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1110	Eucalyptus tereticornis	Forest Red Gum	230		230	19	3	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1111	Lophostemon suaveolens	Swamp Box	210		210	17	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1112	Lophostemon suaveolens	Swamp Box	220	130, 100	274	15	13	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1113	Lophostemon suaveolens	Swamp Box	190	180, 150	302	14	3	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1114	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1115	Eucalyptus tereticornis	Forest Red Gum	280		280	25	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1116	Corymbia citriodora	Spotted Gum	220		220	22	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1117	Corymbia citriodora	Spotted Gum	260		260	25	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1118	Eucalyptus saligna	Sydney Blue Gum	380		380	16	4	4.6	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	Fire Dmg.	Poor	-	-	-	-	-	-		Remove for trunk sewer
1119	Corymbia citriodora	Spotted Gum	280		280	25	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1120	Eucalyptus tereticornis	Forest Red Gum	220		220	18	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1121	Corymbia citriodora	Spotted Gum	240	180	300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1122	Eucalyptus saligna	Sydney Blue Gum	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1123	Angophora leiocarpa	Smooth-barked Apple	230		230	19	8	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1124	Eucalyptus saligna	Sydney Blue Gum	260		260	19	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1125	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1126	Corymbia intermedia	Pink Bloodwood	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1127	Angophora leiocarpa	Smooth-barked Apple	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1128	Corymbia intermedia	Pink Bloodwood	220		220	17	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1129	Eucalyptus siderophloia	Grey Ironbark	200		200	19	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1130	Acacia disparrima	Hickory Wattle	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1131	Angophora leiocarpa	Smooth-barked Apple	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1132	Corymbia intermedia	Pink Bloodwood	250		250	15	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1133	Corymbia intermedia	Pink Bloodwood	300		300	19	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1134	Corymbia intermedia	Pink Bloodwood	210	220	304	15	7	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1135	Corymbia citriodora	Spotted Gum	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1136	Angophora leiocarpa	Smooth-barked Apple	270		270	20	8	3.2	1.9	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1137	Lophostemon suaveolens	Swamp Box	190	140	236	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1138	Lophostemon suaveolens	Swamp Box	240		240	12	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1139	Corymbia intermedia	Pink Bloodwood	210		210	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1140	Lophostemon suaveolens	Swamp Box	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1141	Angophora leiocarpa	Smooth-barked Apple	260		260	20	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1142	Angophora leiocarpa	Smooth-barked Apple	240		240	23	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1143	Angophora leiocarpa	Smooth-barked Apple	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1144	Angophora leiocarpa	Smooth-barked Apple	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1145	Eucalyptus saligna	Sydney Blue Gum	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1146	Angophora leiocarpa	Smooth-barked Apple	240		240	15	4	2.9	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1147	Corymbia intermedia	Pink Bloodwood	220		220	18	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1148	Corymbia intermedia	Pink Bloodwood	190	130	230	14	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1149	Lophostemon suaveolens	Swamp Box	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1150	Corymbia citriodora	Spotted Gum	360		360	25	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1151	Eucalyptus tereticornis	Forest Red Gum	360		360	20	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1152	Corymbia citriodora	Spotted Gum	220		220	24	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1153	Corymbia citriodora	Spotted Gum	300		300	20	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1154	Corymbia citriodora	Spotted Gum	230		230	23	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1155	Alphitonia excelsa	Soap Tree	220		220	16	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1156	Corymbia intermedia	Pink Bloodwood	220		220	19	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1157	Acacia disparrima	Hickory Wattle	260		260	14	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1158	Corymbia citriodora	Spotted Gum	240		240	18	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1159	Corymbia citriodora	Spotted Gum	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1160	Corymbia intermedia	Pink Bloodwood	160	150	219	15	5	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1161	Corymbia citriodora	Spotted Gum	280		280	18	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1162	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1163	Eucalyptus tereticornis	Forest Red Gum	240		240	20	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1164	Angophora leiocarpa	Smooth-barked Apple	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1165	Corymbia citriodora	Spotted Gum	320		320	22	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1166	Angophora leiocarpa	Smooth-barked Apple	320		320	23	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1167	Lophostemon suaveolens	Swamp Box	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1168	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1169	Lophostemon suaveolens	Swamp Box	270	230	355	17	7	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1170	Corymbia intermedia	Pink Bloodwood	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1171	Eucalyptus tereticornis	Forest Red Gum	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1172	Eucalyptus tereticornis	Forest Red Gum	250		250	19	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1173	Corymbia intermedia	Pink Bloodwood	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1174	Alphitonia excelsa	Soap Tree	220		220	14	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1175	Eucalyptus saligna	Sydney Blue Gum	320		320	18	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1176	Corymbia intermedia	Pink Bloodwood	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1177	Eucalyptus saligna	Sydney Blue Gum	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1178	Eucalyptus tereticornis	Forest Red Gum	210		210	19	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1179	Corymbia intermedia	Pink Bloodwood	340		340	21	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1180	Acacia disparrima	Hickory Wattle	200	180	269	12	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1181	Eucalyptus saligna	Sydney Blue Gum	210		210	14	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1182	Eucalyptus saligna	Sydney Blue Gum	240		240	20	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1183	Eucalyptus saligna	Sydney Blue Gum	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1184	Eucalyptus saligna	Sydney Blue Gum	250		250	10	2	3.0	1.8	Regular	-	-	-	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1185	Lophostemon suaveolens	Swamp Box	200		200	14	3	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1186	Eucalyptus saligna	Sydney Blue Gum	240		240	18	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1187	Eucalyptus saligna	Sydney Blue Gum	290		290	10	2	3.5	2.0	Regular	-	-	-	-	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1188	Eucalyptus tereticornis	Forest Red Gum	220		220	19	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1189	Eucalyptus tereticornis	Forest Red Gum	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1190	Corymbia intermedia	Pink Bloodwood	220		220	17	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1191	Eucalyptus tereticornis	Forest Red Gum	240		240	17	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1192	Angophora leiocarpa	Smooth-barked Apple	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1193	Lophostemon suaveolens	Swamp Box	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1194	Eucalyptus saligna	Sydney Blue Gum	320		320	20	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1195	Lophostemon suaveolens	Swamp Box	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1196	Eucalyptus saligna	Sydney Blue Gum	300		300	18	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1197	Eucalyptus tereticornis	Forest Red Gum	220		220	20	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1198	Acacia disparrima	Hickory Wattle	150	160	219	10	4	2.6	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1199	Lophostemon suaveolens	Swamp Box	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	Termites	-		Remove for trunk sewer
1200	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1201	Eucalyptus saligna	Sydney Blue Gum	250		250	20	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1202	Corymbia tessellaris	Moreton Bay Ash	210		210	18	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1203	Eucalyptus saligna	Sydney Blue Gum	300		300	18	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1204	Eucalyptus saligna	Sydney Blue Gum	200		200	12	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1205	Eucalyptus saligna	Sydney Blue Gum	310		310	20	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1206	Eucalyptus saligna	Sydney Blue Gum	350		350	20	11	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1207	Eucalyptus saligna	Sydney Blue Gum	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1208	Eucalyptus saligna	Sydney Blue Gum	290		290	20	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1209	Eucalyptus saligna	Sydney Blue Gum	220		220	19	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1210	Acacia concurrens	Black Wattle	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1211	Eucalyptus saligna	Sydney Blue Gum	230		230	21	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1212	Eucalyptus saligna	Sydney Blue Gum	290		290	21	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1213	Eucalyptus saligna	Sydney Blue Gum	200		200	19	2	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1214	Eucalyptus saligna	Sydney Blue Gum	230		230	22	6	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1215	Eucalyptus saligna	Sydney Blue Gum	210		210	19	5	2.5	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1216	Eucalyptus tereticornis	Forest Red Gum	240	180	300	25	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1217	Eucalyptus saligna	Sydney Blue Gum	210		210	20	5	2.5	1.7	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1218	Eucalyptus saligna	Sydney Blue Gum	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1219	Eucalyptus saligna	Sydney Blue Gum	270		270	20	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1220	Eucalyptus saligna	Sydney Blue Gum	310		310	23	11	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1221	Acacia disparrima	Hickory Wattle	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1222	Eucalyptus saligna	Sydney Blue Gum	260		260	28	14	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1223	Eucalyptus saligna	Sydney Blue Gum	280		280	28	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1224	Eucalyptus saligna	Sydney Blue Gum	280		280	25	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1225	Eucalyptus saligna	Sydney Blue Gum	320		320	22	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1226	Eucalyptus saligna	Sydney Blue Gum	280		280	30	14	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1227	Eucalyptus saligna	Sydney Blue Gum	400		400	30	15	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1228	Eucalyptus tereticornis	Forest Red Gum	200		200	19	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1229	Eucalyptus saligna	Sydney Blue Gum	400		400	29	11	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1230	Eucalyptus tereticornis	Forest Red Gum	220		220	25	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1231	Eucalyptus saligna	Sydney Blue Gum	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1232	Eucalyptus saligna	Sydney Blue Gum	260		260	27	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1233	Eucalyptus saligna	Sydney Blue Gum	280		280	30	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1234	Eucalyptus saligna	Sydney Blue Gum	300		300	30	12	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1235	Angophora subvelutina	Broad-leaved Apple	220		220	20	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1236	Angophora subvelutina	Broad-leaved Apple	280		280	26	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1237	Angophora subvelutina	Broad-leaved Apple	290		290	29	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1238	Eucalyptus saligna	Sydney Blue Gum	400		400	28	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1239	Eucalyptus saligna	Sydney Blue Gum	220		220	19	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1240	Eucalyptus saligna	Sydney Blue Gum	270		270	25	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1241	Eucalyptus saligna	Sydney Blue Gum	210		210	25	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1242	Eucalyptus saligna	Sydney Blue Gum	200		200	18	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1243	Eucalyptus saligna	Sydney Blue Gum	210		210	17	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1244	Eucalyptus saligna	Sydney Blue Gum	320		320	22	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1245	Eucalyptus saligna	Sydney Blue Gum	320		320	20	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1246	Eucalyptus saligna	Sydney Blue Gum	200		200	23	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1247	Eucalyptus saligna	Sydney Blue Gum	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1248	Eucalyptus saligna	Sydney Blue Gum	370		370	24	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1249	Eucalyptus saligna	Sydney Blue Gum	310		310	20	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1250	Eucalyptus saligna	Sydney Blue Gum	280		280	21	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1251	Eucalyptus saligna	Sydney Blue Gum	300		300	20	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1252	Eucalyptus saligna	Sydney Blue Gum	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1253	Eucalyptus saligna	Sydney Blue Gum	280		280	20	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1254	Eucalyptus saligna	Sydney Blue Gum	320		320	21	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1255	Eucalyptus saligna	Sydney Blue Gum	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1256	Eucalyptus saligna	Sydney Blue Gum	270		270	21	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1257	Eucalyptus saligna	Sydney Blue Gum	370		370	18	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1258	Corymbia citriodora	Spotted Gum	350		350	17	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1259	Petalostigma pubescens	Quinine Bush	240	150	283	8	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1260	Petalostigma pubescens	Quinine Bush	210		210	7	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1261	Eucalyptus tereticornis	Forest Red Gum	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1262	Eucalyptus tereticornis	Forest Red Gum	220		220	17	3	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1263	Corymbia tessellaris	Moreton Bay Ash	410		410	21	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1264	Corymbia citriodora	Spotted Gum	510		510	22	7	6.1	2.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove for basin works
1265	Corymbia citriodora	Spotted Gum	460		460	23	7	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1266	Corymbia citriodora	Spotted Gum	420		420	23	5	5.0	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1267	Corymbia citriodora	Spotted Gum	320		320	22	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1268	Eucalyptus tereticornis	Forest Red Gum	380		380	22	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1269	Angophora leiocarpa	Smooth-barked Apple	220		220	13	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1270	Corymbia citriodora	Spotted Gum	250		250	18	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1271	Lophostemon suaveolens	Swamp Box	260		260	14	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1272	Corymbia citriodora	Spotted Gum	380		380	19	5	4.6	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1273	Corymbia intermedia	Pink Bloodwood	260		260	15	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1274	Acacia disparrima	Hickory Wattle	320	180	367	12	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1275	Corymbia tessellaris	Moreton Bay Ash	300		300	21	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1276	Eucalyptus saligna	Sydney Blue Gum	200		200	13	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1277	Eucalyptus saligna	Sydney Blue Gum	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1278	Corymbia trachyphloia	Brown Bloodwood	370		370	23	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1279	Angophora leiocarpa	Smooth-barked Apple	230		230	16	6	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1280	Angophora leiocarpa	Smooth-barked Apple	250		250	17	3	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1281	Angophora leiocarpa	Smooth-barked Apple	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1282	Eucalyptus tereticornis	Forest Red Gum	300		300	21	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1283	Eucalyptus siderophloia	Grey Ironbark	320		320	17	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1284	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1285	Lophostemon suaveolens	Swamp Box	320		320	14	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1286	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1287	Corymbia tessellaris	Moreton Bay Ash	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1288	Lophostemon suaveolens	Swamp Box	200		200	13	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1289	Lophostemon suaveolens	Swamp Box	220		220	14	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1290	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1291	Acacia disparrima	Hickory Wattle	280	200	344	12	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1292	Angophora leiocarpa	Smooth-barked Apple	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1293	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1294	Angophora leiocarpa	Smooth-barked Apple	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1295	Angophora leiocarpa	Smooth-barked Apple	300	220	372	19	7	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1296	Eucalyptus tereticornis	Forest Red Gum	340		340	21	6	4.1	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1297	Corymbia trachyphloia	Brown Bloodwood	300		300	16	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1298	Petalostigma pubescens	Quinine Bush	240		240	9	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1299	Corymbia citriodora	Spotted Gum	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1300	Corymbia citriodora	Spotted Gum	420		420	24	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1301	Corymbia intermedia	Pink Bloodwood	220	240	326	18	6	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1302	Angophora leiocarpa	Smooth-barked Apple	380		380	17	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1303	Angophora leiocarpa	Smooth-barked Apple	240		240	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1304	Eucalyptus tereticornis	Forest Red Gum	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1305	Corymbia tessellaris	Moreton Bay Ash	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1306	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1307	Angophora leiocarpa	Smooth-barked Apple	200		200	15	6	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1308	Eucalyptus tereticornis	Forest Red Gum	330		330	21	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1309	Eucalyptus siderophloia	Grey Ironbark	220		220	14	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
1310	Alphitonia excelsa	Soap Tree	220		220	7	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1311	Acacia disparrima	Hickory Wattle	210	180	277	9	4	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1312	Corymbia intermedia	Pink Bloodwood	270		270	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1313	Eucalyptus tereticornis	Forest Red Gum	220		220	18	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1314	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	21	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1315	Corymbia intermedia	Pink Bloodwood	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1316	Acacia disparrima	Hickory Wattle	210		210	14	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1317	Eucalyptus crebra	Narrow-leaved Ironbark	370		370	23	7	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1318	Angophora leiocarpa	Smooth-barked Apple	210		210	14	2	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1319	Corymbia intermedia	Pink Bloodwood	270	210	342	18	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1320	Eucalyptus crebra	Narrow-leaved Ironbark	490		490	24	9	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1321	Acacia disparrima	Hickory Wattle	220		220	13	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1322	Corymbia intermedia	Pink Bloodwood	200	90	219	16	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1323	Angophora leiocarpa	Smooth-barked Apple	230		230	24	6	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1324	Angophora leiocarpa	Smooth-barked Apple	430		430	18	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1325	Corymbia citriodora	Spotted Gum	280	230	362	23	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1326	Angophora leiocarpa	Smooth-barked Apple	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1327	Corymbia tessellaris	Moreton Bay Ash	260		260	19	4	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1328	Eucalyptus tereticornis	Forest Red Gum	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1329	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	19	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1330	Corymbia intermedia	Pink Bloodwood	270	140	304	16	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1331	Eucalyptus tereticornis	Forest Red Gum	320		320	20	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1332	Eucalyptus tereticornis	Forest Red Gum	310	190	364	22	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1333	Corymbia citriodora	Spotted Gum	320		320	23	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1334	Corymbia citriodora	Spotted Gum	330		330	25	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1335	Eucalyptus tereticornis	Forest Red Gum	300	260	397	19	8	4.8	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1336	Corymbia intermedia	Pink Bloodwood	270		270	15	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1337	Corymbia citriodora	Spotted Gum	290		290	21	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1338	Corymbia henryi	Large-leaved Spotted Gum	240		240	22	5	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1339	Angophora leiocarpa	Smooth-barked Apple	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1340	Eucalyptus tereticornis	Forest Red Gum	410		410	23	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1341	Angophora leiocarpa	Smooth-barked Apple	260		260	19	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1342	Corymbia citriodora	Spotted Gum	490		490	23	6	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
1343	Eucalyptus acmenoides	White Mahogany	220		220	17	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1344	Eucalyptus tereticornis	Forest Red Gum	580		580	28	12	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1345	Eucalyptus acmenoides	White Mahogany	280	260, 200	431	17	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1346	Eucalyptus seeana	Narrow-leaved Red Gum	240		240	16	6	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1347	Corymbia intermedia	Pink Bloodwood	400		400	19	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1348	Corymbia intermedia	Pink Bloodwood	340		340	19	4	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1349	Corymbia intermedia	Pink Bloodwood	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1350	Corymbia intermedia	Pink Bloodwood	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1351	Eucalyptus tereticornis	Forest Red Gum	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1352	Corymbia citriodora	Spotted Gum	590		590	28	14	7.1	2.7	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1353	Corymbia intermedia	Pink Bloodwood	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1354	Eucalyptus saligna	Sydney Blue Gum	400		400	22	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1355	Eucalyptus tereticornis	Forest Red Gum	290		290	23	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1356	Eucalyptus tereticornis	Forest Red Gum	450		450	26	8	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1357	Eucalyptus tereticornis	Forest Red Gum	300		300	21	5	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1358	Corymbia citriodora	Spotted Gum	470		470	27	9	5.6	2.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1359	Corymbia citriodora	Spotted Gum	370		370	26	11	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1360	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	19	7	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1361	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	17	8	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
1362	Corymbia citriodora	Spotted Gum	630		630	30	12	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1363	Corymbia citriodora	Spotted Gum	200		200	15	8	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1364	Corymbia citriodora	Spotted Gum	290		290	18	7	3.5	2.0	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1365	Corymbia citriodora	Spotted Gum	210		210	14	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1366	Corymbia citriodora	Spotted Gum	310		310	26	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1367	Corymbia citriodora	Spotted Gum	220		220	24	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1368	Eucalyptus siderophloia	Grey Ironbark	260		260	20	10	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1369	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	26	13	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1370	Corymbia citriodora	Spotted Gum	240		240	23	8	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1371	Eucalyptus siderophloia	Grey Ironbark	220		220	23	10	2.6	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1372	Corymbia citriodora	Spotted Gum	380		380	27	11	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1373	Eucalyptus tereticornis	Forest Red Gum	320		320	25	8	3.8	2.1	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1374	Corymbia citriodora	Spotted Gum	340		340	26	13	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1375	Eucalyptus tereticornis	Forest Red Gum	330		330	25	13	4.0	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1376	Corymbia citriodora	Spotted Gum	240		240	22	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1377	Corymbia citriodora	Spotted Gum	360		360	31	8	4.3	2.2	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1378	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	22	7	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1379	Corymbia citriodora	Spotted Gum	650		650	30	16	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1380	Eucalyptus tereticornis	Forest Red Gum	350	110	367	26	12	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1381	Corymbia citriodora	Spotted Gum	230		230	26	8	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1382	Corymbia citriodora	Spotted Gum	370		370	27	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1383	Eucalyptus tereticornis	Forest Red Gum	220		220	25	8	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1384	Corymbia citriodora	Spotted Gum	510		510	31	11	6.1	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1385	Corymbia citriodora	Spotted Gum	430		430	26	9	5.2	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1386	Corymbia citriodora	Spotted Gum	230		230	19	10	2.8	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1387	Eucalyptus siderophloia	Grey Ironbark	440		440	22	14	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1388	Eucalyptus tereticornis	Forest Red Gum	380		380	19	10	4.6	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1389	Corymbia citriodora	Spotted Gum	350		350	24	12	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1390	Corymbia citriodora	Spotted Gum	230		230	17	9	2.8	1.8	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1391	Corymbia citriodora	Spotted Gum	250		250	16	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1392	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	18	10	3.7	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1393	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	15	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1394	Eucalyptus seeana	Narrow-leaved Red Gum	220		220	20	6	2.6	1.8	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1395	Eucalyptus moluccana	Gum Topped Box	360		360	24	10	4.3	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1396	Corymbia citriodora	Spotted Gum	180	160, 150	284	17	11	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1397	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	20	12	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1398	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	21	10	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1399	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	23	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1400	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	24	12	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1401	Corymbia citriodora	Spotted Gum	250		250	21	8	3.0	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1402	Eucalyptus moluccana	Gum Topped Box	480		480	25	16	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1403	Eucalyptus tereticornis	Forest Red Gum	230		230	23	9	2.8	1.8	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1404	Corymbia citriodora	Spotted Gum	270		270	24	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1405	Eucalyptus siderophloia	Grey Ironbark	200	110	228	15	8	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1406	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	25	16	3.1	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1407	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	25	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1408	Corymbia citriodora	Spotted Gum	210		210	22	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1409	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	22	5	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1410	Eucalyptus siderophloia	Grey Ironbark	360		360	24	13	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1411	Corymbia citriodora	Spotted Gum	200		200	20	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1412	Corymbia citriodora	Spotted Gum	210		210	22	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1413	Corymbia citriodora	Spotted Gum	200		200	21	5	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1414	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	25	11	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1415	Corymbia citriodora	Spotted Gum	310		310	25	13	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1416	Corymbia citriodora	Spotted Gum	250		250	24	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1417	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	25	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1418	Corymbia citriodora	Spotted Gum	270		270	26	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1419	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	21	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1420	Corymbia citriodora	Spotted Gum	230		230	22	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1421	Corymbia citriodora	Spotted Gum	200		200	15	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1422	Eucalyptus siderophloia	Grey Ironbark	200		200	17	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1423	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1424	Eucalyptus siderophloia	Grey Ironbark	310		310	22	12	3.7	2.0	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1425	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	22	10	3.6	2.0	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1426	Corymbia citriodora	Spotted Gum	260	190	322	22	12	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1427	Eucalyptus siderophloia	Grey Ironbark	330		330	24	13	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1428	Corymbia citriodora	Spotted Gum	200		200	20	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1429	Eucalyptus siderophloia	Grey Ironbark	230		230	21	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1430	Corymbia citriodora	Spotted Gum	200		200	19	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1431	Eucalyptus crebra	Narrow-leaved Ironbark	370		370	25	13	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1432	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	22	12	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1433	Eucalyptus siderophloia	Grey Ironbark	240	130	273	15	9	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1434	Eucalyptus tereticornis	Forest Red Gum	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1435	Eucalyptus siderophloia	Grey Ironbark	290		290	18	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1436	Corymbia citriodora	Spotted Gum	290		290	20	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1437	Corymbia citriodora	Spotted Gum	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1438	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	10	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1439	Corymbia citriodora	Spotted Gum	250		250	18	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1440	Corymbia citriodora	Spotted Gum	240		240	19	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1441	Eucalyptus siderophloia	Grey Ironbark	200		200	15	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1442	Eucalyptus siderophloia	Grey Ironbark	260		260	18	8	3.1	1.9	Regular	-	-	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1443	Corymbia citriodora	Spotted Gum	200		200	15	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1444	Eucalyptus siderophloia	Grey Ironbark	350		350	23	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1445	Eucalyptus tereticornis	Forest Red Gum	230		230	17	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1446	Corymbia citriodora	Spotted Gum	300		300	22	13	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1447	Eucalyptus crebra	Narrow-leaved Ironbark	580		580	25	12	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1448	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	22	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1449	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	25	13	4.2	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1450	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	27	8	3.6	2.0	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1451	Corymbia citriodora	Spotted Gum	640		640	32	16	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	Large	-	-		Remove
1452	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	25	13	3.5	2.0	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1453	Corymbia citriodora	Spotted Gum	200		200	15	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1454	Corymbia citriodora	Spotted Gum	220		220	16	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1455	Corymbia citriodora	Spotted Gum	270		270	25	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1456	Eucalyptus siderophloia	Grey Ironbark	210		210	17	9	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1457	Corymbia citriodora	Spotted Gum	320		320	18	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1458	Eucalyptus tereticornis	Forest Red Gum	280		280	23	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1459	Corymbia citriodora	Spotted Gum	350		350	25	13	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1460	Corymbia citriodora	Spotted Gum	270		270	20	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1461	Eucalyptus tereticornis	Forest Red Gum	200		200	15	7	2.4	1.7	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1462	Corymbia citriodora	Spotted Gum	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1463	Corymbia citriodora	Spotted Gum	360		360	23	10	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1464	Corymbia citriodora	Spotted Gum	430		430	25	12	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1465	Corymbia citriodora	Spotted Gum	300		300	23	12	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1466	Corymbia citriodora	Spotted Gum	230		230	14	6	2.8	1.8	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1467	Corymbia citriodora	Spotted Gum	310		310	19	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1468	Corymbia citriodora	Spotted Gum	270		270	17	8	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1469	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	16	11	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1470	Corymbia citriodora	Spotted Gum	270		270	17	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1471	Eucalyptus tereticornis	Forest Red Gum	200		200	18	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1472	Corymbia tessellaris	Moreton Bay Ash	220		220	17	2	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1473	Eucalyptus tereticornis	Forest Red Gum	230		230	15	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1474	Corymbia citriodora	Spotted Gum	200		200	19	8	2.4	1.7	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1475	Corymbia citriodora	Spotted Gum	330		330	22	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1476	Eucalyptus tereticornis	Forest Red Gum	480		480	25	8	5.8	2.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1477	Eucalyptus tereticornis	Forest Red Gum	350		350	26	7	4.2	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1478	Corymbia citriodora	Spotted Gum	550		550	30	15	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1479	Corymbia citriodora	Spotted Gum	420		420	27	9	5.0	2.3	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1480	Corymbia citriodora	Spotted Gum	300		300	28	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1481	Corymbia citriodora	Spotted Gum	410		410	27	8	4.9	2.3	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1482	Corymbia citriodora	Spotted Gum	340		340	17	9	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
1483	Corymbia citriodora	Spotted Gum	350		350	26	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1484	Eucalyptus tereticornis	Forest Red Gum	330		330	13	4	4.0	2.1	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	Major	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
1485	Corymbia citriodora	Spotted Gum	360		360	25	9	4.3	2.2	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1486	Eucalyptus tereticornis	Forest Red Gum	530		530	29	13	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1487	Corymbia citriodora	Spotted Gum	490		490	27	15	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1488	Eucalyptus siderophloia	Grey Ironbark	270		270	17	9	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1489	Corymbia citriodora	Spotted Gum	410		410	24	11	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1490	Corymbia citriodora	Spotted Gum	600		600	31	16	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1491	Corymbia citriodora	Spotted Gum	300		300	19	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1492	Angophora leiocarpa	Smooth-barked Apple	260		260	10	9	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
1493	Eucalyptus crebra	Narrow-leaved Ironbark	380		380	21	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1494	Eucalyptus crebra	Narrow-leaved Ironbark	510		510	24	13	6.1	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1495	Corymbia citriodora	Spotted Gum	330		330	16	14	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1496	Eucalyptus moluccana	Gum Topped Box	250		250	22	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1497	Eucalyptus moluccana	Gum Topped Box	200		200	12	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1498	Eucalyptus tereticornis	Forest Red Gum	220		220	18	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1499	Eucalyptus moluccana	Gum Topped Box	320		320	22	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1500	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	20	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1501	Corymbia citriodora	Spotted Gum	250		250	19	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
1502	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	21	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retain
1503	Corymbia citriodora	Spotted Gum	310		310	26	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1504	Eucalyptus moluccana	Gum Topped Box	250		250	19	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1505	Eucalyptus moluccana	Gum Topped Box	500		500	30	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1506	Eucalyptus moluccana	Gum Topped Box	370		370	31	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1507	Eucalyptus moluccana	Gum Topped Box	350		350	24	11	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1508	Eucalyptus moluccana	Gum Topped Box	260	190	322	24	10	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1509	Angophora leiocarpa	Smooth-barked Apple	200		200	14	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1510	Eucalyptus moluccana	Gum Topped Box	350		350	23	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retain
1511	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	20	8	3.1	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1512	Alphitonia excelsa	Soap Tree	200		200	12	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1513	Acacia disparrima	Hickory Wattle	200	130	239	13	6	2.9	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1514	Corymbia citriodora	Spotted Gum	250		250	21	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1515	Eucalyptus tereticornis	Forest Red Gum	290		290	23	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1516	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	19	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Retain
1517	Eucalyptus tereticornis	Forest Red Gum	270		270	23	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1518	Eucalyptus tereticornis	Forest Red Gum	280		280	21	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1519	Eucalyptus tereticornis	Forest Red Gum	230		230	14	5	2.8	1.8	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1520	Corymbia citriodora	Spotted Gum	210		210	15	7	2.5	1.7	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1521	Corymbia intermedia	Pink Bloodwood	210		210	19	9	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1522	Eucalyptus tereticornis	Forest Red Gum	250		250	25	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1523	Eucalyptus tereticornis	Forest Red Gum	250		250	27	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1524	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	24	12	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1525	Lophostemon suaveolens	Swamp Box	230		230	13	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1526	Lophostemon suaveolens	Swamp Box	220	180	284	12	9	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1527	Eucalyptus tereticornis	Forest Red Gum	480		480	29	13	5.8	2.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1528	Corymbia tessellaris	Moreton Bay Ash	260		260	24	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1529	Eucalyptus saligna	Sydney Blue Gum	270		270	18	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1530	Angophora leiocarpa	Smooth-barked Apple	250		250	18	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1531	Eucalyptus saligna	Sydney Blue Gum	310		310	18	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1532	Eucalyptus saligna	Sydney Blue Gum	210		210	14	7	2.5	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
1533	Corymbia intermedia	Pink Bloodwood	140	140, 90	217	15	8	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1534	Corymbia citriodora	Spotted Gum	230		230	19	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1535	Lophostemon suaveolens	Swamp Box	230		230	12	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1536	Eucalyptus saligna	Sydney Blue Gum	220		220	17	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1537	Eucalyptus saligna	Sydney Blue Gum	270		270	22	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1538	Lophostemon suaveolens	Swamp Box	200		200	11	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1539	Corymbia intermedia	Pink Bloodwood	210		210	18	9	2.5	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1540	Lophostemon suaveolens	Swamp Box	200		200	13	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1541	Corymbia intermedia	Pink Bloodwood	230		230	19	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1542	Angophora leiocarpa	Smooth-barked Apple	250		250	22	11	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1543	Eucalyptus saligna	Sydney Blue Gum	290		290	23	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1544	Eucalyptus saligna	Sydney Blue Gum	220		220	18	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1545	Eucalyptus saligna	Sydney Blue Gum	310		310	18	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1546	Eucalyptus saligna	Sydney Blue Gum	200		200	16	5	2.4	1.7	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1547	Eucalyptus siderophloia	Grey Ironbark	290		290	17	11	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1548	Corymbia citriodora	Spotted Gum	240		240	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1549	Eucalyptus tereticornis	Forest Red Gum	230		230	14	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1550	Corymbia citriodora	Spotted Gum	520		520	22	8	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1551	Acacia disparrima	Hickory Wattle	270		270	10	5	3.2	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
1552	Corymbia citriodora	Spotted Gum	320		320	17	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1553	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1554	Angophora leiocarpa	Smooth-barked Apple	240		240	16	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1555	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1556	Corymbia intermedia	Pink Bloodwood	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1557	Eucalyptus crebra	Narrow-leaved Ironbark	180	200	269	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1558	Alphitonia excelsa	Soap Tree	220		220	11	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1559	Eucalyptus crebra	Narrow-leaved Ironbark	200	90	219	15	3	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1560	Eucalyptus tereticornis	Forest Red Gum	330		330	19	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1561	Eucalyptus seeana	Narrow-leaved Red Gum	360		360	18	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1562	Alphitonia excelsa	Soap Tree	200		200	9	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1563	Corymbia tessellaris	Moreton Bay Ash	220		220	15	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1564	Corymbia intermedia	Pink Bloodwood	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1565	Corymbia tessellaris	Moreton Bay Ash	220		220	14	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1566	Corymbia tessellaris	Moreton Bay Ash	220		220	14	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1567	Angophora subvelutina	Broad-leaved Apple	230		230	13	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1568	Eucalyptus crebra	Narrow-leaved Ironbark	540		540	24	11	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1569	Eucalyptus tereticornis	Forest Red Gum	220	200	297	17	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1570	Eucalyptus crebra	Narrow-leaved Ironbark	460		460	22	7	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1571	Eucalyptus crebra	Narrow-leaved Ironbark	660		660	22	8	7.9	2.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1572	Corymbia intermedia	Pink Bloodwood	240		240	15	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1573	Acacia disparrima	Hickory Wattle	280		280	13	6	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1574	Acacia concurrens	Black Wattle	210		210	9	5	2.5	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1575	Acacia disparrima	Hickory Wattle	240		240	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1576	Lophostemon suaveolens	Swamp Box	220		220	11	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1577	Eucalyptus crebra	Narrow-leaved Ironbark	680		680	24	9	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1578	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	22	6	4.0	2.1	One-sided	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1579	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	17	6	4.0	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1580	Corymbia intermedia	Pink Bloodwood	340		340	16	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1581	Corymbia intermedia	Pink Bloodwood	280		280	16	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1582	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	17	6	4.0	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1583	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	22	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1584	Petalostigma pubescens	Quinine Bush	220		220	10	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1585	Eucalyptus crebra	Narrow-leaved Ironbark	590		590	25	9	7.1	2.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1586	Corymbia tessellaris	Moreton Bay Ash	320		320	19	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1587	Corymbia intermedia	Pink Bloodwood	350		350	21	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1588	Corymbia tessellaris	Moreton Bay Ash	250		250	17	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1589	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1590	Corymbia tessellaris	Moreton Bay Ash	200		200	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1591	Lophostemon suaveolens	Swamp Box	290		290	14	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1592	Lophostemon suaveolens	Swamp Box	200	160, 130	287	13	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1593	Eucalyptus tereticornis	Forest Red Gum	430		430	26	9	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1594	Lophostemon suaveolens	Swamp Box	320	160	358	15	6	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1595	Lophostemon suaveolens	Swamp Box	200	170	262	12	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1596	Lophostemon suaveolens	Swamp Box	290	150	326	12	5	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1597	Lophostemon suaveolens	Swamp Box	310		310	12	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1598	Lophostemon suaveolens	Swamp Box	200	170	262	10	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove for basin works
1599	Eucalyptus tereticornis	Forest Red Gum	210		210	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1600	Angophora subvelutina	Broad-leaved Apple	240		240	11	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1601	Angophora subvelutina	Broad-leaved Apple	260		260	11	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1602	Acacia concurrens	Black Wattle	270	260, 230, 230	496	12	8	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1603	Eucalyptus tereticornis	Forest Red Gum	690		690	29	9	8.3	2.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1604	Lophostemon suaveolens	Swamp Box	230	140, 120	295	13	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1605	Lophostemon suaveolens	Swamp Box	210		210	11	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1606	Eucalyptus tereticornis	Forest Red Gum	200		200	13	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1607	Eucalyptus tereticornis	Forest Red Gum	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
1608	Corymbia tessellaris	Moreton Bay Ash	170	150, 150, 150	310	14	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1609	Acacia melanoxylon	Australian Blackwood	220	240, 220, 180, 160	461	12	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1610	Lophostemon suaveolens	Swamp Box	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1611	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1612	Lophostemon suaveolens	Swamp Box	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1613	Corymbia citriodora	Spotted Gum	280		280	17	5	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1614	Corymbia intermedia	Pink Bloodwood	210		210	13	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1615	Eucalyptus saligna	Sydney Blue Gum	240		240	14	6	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1616	Corymbia citriodora	Spotted Gum	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1617	Lophostemon suaveolens	Swamp Box	240		240	13	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1618	Eucalyptus tereticornis	Forest Red Gum	230		230	15	4	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1619	Eucalyptus saligna	Sydney Blue Gum	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1620	Angophora leiocarpa	Smooth-barked Apple	200	170	262	18	5	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1621	Corymbia intermedia	Pink Bloodwood	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1622	Corymbia intermedia	Pink Bloodwood	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1623	Corymbia citriodora	Spotted Gum	250		250	18	2	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1624	Eucalyptus saligna	Sydney Blue Gum	350		350	19	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1625	Angophora leiocarpa	Smooth-barked Apple	260		260	17	5	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1626	Lophostemon suaveolens	Swamp Box	240	190	306	12	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1627	Eucalyptus saligna	Sydney Blue Gum	210		210	12	3	2.5	1.7	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1628	Lophostemon suaveolens	Swamp Box	200	80	215	10	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1629	Corymbia citriodora	Spotted Gum	210		210	17	3	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1630	Angophora leiocarpa	Smooth-barked Apple	220		220	17	4	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1631	Lophostemon suaveolens	Swamp Box	230	190	298	11	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1632	Angophora leiocarpa	Smooth-barked Apple	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1633	Corymbia intermedia	Pink Bloodwood	220		220	14	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1634	Angophora leiocarpa	Smooth-barked Apple	230	190	298	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1635	Angophora leiocarpa	Smooth-barked Apple	210		210	14	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1636	Corymbia citriodora	Spotted Gum	290		290	17	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1637	Corymbia intermedia	Pink Bloodwood	250		250	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1638	Corymbia intermedia	Pink Bloodwood	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1639	Angophora leiocarpa	Smooth-barked Apple	300	200	361	16	6	4.3	2.2	Regular	-	-	-	-	-	Typical	Major	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
1640	Corymbia intermedia	Pink Bloodwood	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1641	Angophora leiocarpa	Smooth-barked Apple	220		220	12	4	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1642	Corymbia citriodora	Spotted Gum	280		280	18	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1643	Angophora leiocarpa	Smooth-barked Apple	230		230	14	4	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1644	Lophostemon suaveolens	Swamp Box	230		230	12	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1645	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1646	Lophostemon suaveolens	Swamp Box	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1647	Angophora leiocarpa	Smooth-barked Apple	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1648	Angophora leiocarpa	Smooth-barked Apple	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1649	Angophora leiocarpa	Smooth-barked Apple	370		370	21	10	4.4	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1650	Lophostemon suaveolens	Swamp Box	280		280	12	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1651	Lophostemon suaveolens	Swamp Box	290		290	13	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1652	Corymbia intermedia	Pink Bloodwood	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
1653	Lophostemon suaveolens	Swamp Box	210		210	11	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1654	Angophora leiocarpa	Smooth-barked Apple	220		220	17	5	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1655	Lophostemon suaveolens	Swamp Box	240		240	11	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1656	Eucalyptus tereticornis	Forest Red Gum	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1657	Corymbia tessellaris	Moreton Bay Ash	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1658	Angophora leiocarpa	Smooth-barked Apple	320		320	16	7	3.8	2.1	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1659	Lophostemon suaveolens	Swamp Box	210		210	13	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1660	Corymbia intermedia	Pink Bloodwood	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1661	Angophora leiocarpa	Smooth-barked Apple	200		200	17	6	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1662	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1663	Corymbia intermedia	Pink Bloodwood	250		250	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1664	Angophora leiocarpa	Smooth-barked Apple	200		200	14	4	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1665	Angophora leiocarpa	Smooth-barked Apple	210		210	14	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1666	Angophora leiocarpa	Smooth-barked Apple	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1667	Lophostemon suaveolens	Swamp Box	200	160	256	11	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1668	Angophora leiocarpa	Smooth-barked Apple	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1669	Angophora leiocarpa	Smooth-barked Apple	230		230	14	3	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1670	Angophora leiocarpa	Smooth-barked Apple	260		260	14	5	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1671	Corymbia intermedia	Pink Bloodwood	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1672	Corymbia citriodora	Spotted Gum	330		330	18	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1673	Corymbia citriodora	Spotted Gum	280		280	17	3	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1674	Corymbia citriodora	Spotted Gum	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1675	Corymbia citriodora	Spotted Gum	350		350	18	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1676	Corymbia intermedia	Pink Bloodwood	250		250	15	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1677	Corymbia citriodora	Spotted Gum	250		250	18	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1678	Eucalyptus tereticornis	Forest Red Gum	210	190	283	17	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1679	Angophora leiocarpa	Smooth-barked Apple	280		280	15	7	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1680	Eucalyptus crebra	Narrow-leaved Ironbark	420		420	22	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1681	Angophora leiocarpa	Smooth-barked Apple	230		230	14	5	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1682	Angophora leiocarpa	Smooth-barked Apple	240		240	14	5	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1683	Angophora leiocarpa	Smooth-barked Apple	240		240	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1684	Corymbia citriodora	Spotted Gum	290		290	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1685	Corymbia intermedia	Pink Bloodwood	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1686	Angophora leiocarpa	Smooth-barked Apple	200		200	13	4	2.4	1.7	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1687	Angophora leiocarpa	Smooth-barked Apple	240		240	17	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1688	Corymbia intermedia	Pink Bloodwood	200	140, 140	281	16	3	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1689	Eucalyptus tereticornis	Forest Red Gum	240		240	18	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1690	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1691	Angophora leiocarpa	Smooth-barked Apple	270		270	18	6	3.2	1.9	One-sided	-	Thinning	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1692	Corymbia intermedia	Pink Bloodwood	210		210	15	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1693	Lophostemon suaveolens	Swamp Box	250		250	13	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1694	Lophostemon suaveolens	Swamp Box	330		330	13	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1695	Alphitonia excelsa	Soap Tree	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1696	Angophora leiocarpa	Smooth-barked Apple	220		220	17	3	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1697	Eucalyptus tereticornis	Forest Red Gum	530		530	24	8	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1698	Corymbia intermedia	Pink Bloodwood	320	150	353	17	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1699	Eucalyptus tereticornis	Forest Red Gum	220		220	15	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1700	Acacia disparrima	Hickory Wattle	220		220	8	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1701	Corymbia intermedia	Pink Bloodwood	390		390	18	7	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1702	Corymbia intermedia	Pink Bloodwood	300		300	14	4	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1703	Casuarina cunninghamiana	River Sheoak	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1704	Corymbia intermedia	Pink Bloodwood	280		280	17	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1705	Petalostigma pubescens	Quinine Bush	200		200	9	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1706	Corymbia tessellaris	Moreton Bay Ash	200		200	18	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1707	Eucalyptus saligna	Sydney Blue Gum	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1708	Corymbia intermedia	Pink Bloodwood	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1709	Corymbia intermedia	Pink Bloodwood	200		200	13	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1710	Eucalyptus saligna	Sydney Blue Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1711	Eucalyptus saligna	Sydney Blue Gum	210		210	16	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1712	Eucalyptus saligna	Sydney Blue Gum	280		280	17	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1713	Eucalyptus saligna	Sydney Blue Gum	230		230	14	6	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1714	Eucalyptus saligna	Sydney Blue Gum	290		290	19	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1715	Eucalyptus saligna	Sydney Blue Gum	240		240	15	4	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1716	Eucalyptus saligna	Sydney Blue Gum	390		390	21	7	4.7	2.2	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1717	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1718	Corymbia tessellaris	Moreton Bay Ash	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1719	Eucalyptus tereticornis	Forest Red Gum	250		250	17	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1720	Eucalyptus saligna	Sydney Blue Gum	330		330	19	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1721	Corymbia tessellaris	Moreton Bay Ash	280		280	18	6	3.4	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1722	Eucalyptus saligna	Sydney Blue Gum	340		340	19	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1723	Eucalyptus saligna	Sydney Blue Gum	270		270	18	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1724	Eucalyptus saligna	Sydney Blue Gum	330		330	21	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1725	Eucalyptus saligna	Sydney Blue Gum	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1726	Eucalyptus saligna	Sydney Blue Gum	330		330	18	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1727	Eucalyptus saligna	Sydney Blue Gum	240		240	19	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1728	Eucalyptus saligna	Sydney Blue Gum	340		340	19	3	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1729	Eucalyptus saligna	Sydney Blue Gum	310		310	21	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1730	Eucalyptus saligna	Sydney Blue Gum	200		200	17	4	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1731	Eucalyptus saligna	Sydney Blue Gum	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1732	Eucalyptus saligna	Sydney Blue Gum	230		230	14	4	2.8	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1733	Eucalyptus saligna	Sydney Blue Gum	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1734	Eucalyptus saligna	Sydney Blue Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1735	Eucalyptus saligna	Sydney Blue Gum	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1736	Eucalyptus saligna	Sydney Blue Gum	320		320	19	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1737	Eucalyptus saligna	Sydney Blue Gum	230		230	19	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1738	Eucalyptus saligna	Sydney Blue Gum	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1739	Petalostigma pubescens	Quinine Bush	210		210	9	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1740	Eucalyptus saligna	Sydney Blue Gum	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1741	Eucalyptus saligna	Sydney Blue Gum	320		320	19	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1742	Eucalyptus saligna	Sydney Blue Gum	340		340	19	6	4.1	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1743	Corymbia intermedia	Pink Bloodwood	240		240	16	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1744	Eucalyptus saligna	Sydney Blue Gum	390		390	22	7	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1745	Eucalyptus saligna	Sydney Blue Gum	210		210	17	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1746	Eucalyptus saligna	Sydney Blue Gum	420		420	18	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1747	Eucalyptus saligna	Sydney Blue Gum	330		330	19	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1748	Eucalyptus tereticornis	Forest Red Gum	400	260	477	19	7	5.7	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1749	Acacia disparrima	Hickory Wattle	240	270	361	12	8	4.3	2.2	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1750	Eucalyptus saligna	Sydney Blue Gum	270		270	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1751	Eucalyptus saligna	Sydney Blue Gum	420		420	23	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1752	Eucalyptus saligna	Sydney Blue Gum	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1753	Eucalyptus saligna	Sydney Blue Gum	410		410	21	9	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1754	Lophostemon suaveolens	Swamp Box	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1755	Eucalyptus saligna	Sydney Blue Gum	350		350	17	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1756	Eucalyptus saligna	Sydney Blue Gum	340		340	18	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1757	Eucalyptus saligna	Sydney Blue Gum	270		270	17	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1758	Eucalyptus saligna	Sydney Blue Gum	290		290	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1759	Eucalyptus saligna	Sydney Blue Gum	300		300	15	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1760	Eucalyptus saligna	Sydney Blue Gum	270		270	19	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1761	Acacia disparrima	Hickory Wattle	230	150	275	12	7	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1762	Eucalyptus tereticornis	Forest Red Gum	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1763	Eucalyptus saligna	Sydney Blue Gum	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1764	Eucalyptus saligna	Sydney Blue Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1765	Eucalyptus saligna	Sydney Blue Gum	310		310	19	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1766	Eucalyptus saligna	Sydney Blue Gum	240		240	19	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1767	Acacia disparrima	Hickory Wattle	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1768	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1769	Corymbia intermedia	Pink Bloodwood	260		260	16	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
1770	Corymbia intermedia	Pink Bloodwood	330		330	27	11	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1771	Corymbia intermedia	Pink Bloodwood	270		270	21	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1772	Lophostemon suaveolens	Swamp Box	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1773	Corymbia intermedia	Pink Bloodwood	240		240	19	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1774	Lophostemon suaveolens	Swamp Box	220		220	10	5	2.6	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1775	Corymbia intermedia	Pink Bloodwood	290		290	15	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1776	Lophostemon suaveolens	Swamp Box	230		230	12	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1777	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1778	Lophostemon suaveolens	Swamp Box	230		230	13	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1779	Lophostemon suaveolens	Swamp Box	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1780	Eucalyptus tereticornis	Forest Red Gum	380		380	22	10	4.6	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
1781	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	24	10	3.1	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1782	Corymbia citriodora	Spotted Gum	500		500	32	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1783	Corymbia citriodora	Spotted Gum	290		290	18	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1784	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	17	9	2.5	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1785	Eucalyptus crebra	Narrow-leaved Ironbark	420		420	32	13	5.0	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1786	Corymbia citriodora	Spotted Gum	360		360	24	14	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1787	Corymbia citriodora	Spotted Gum	430		430	27	10	5.2	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1788	Eucalyptus tereticornis	Forest Red Gum	280		280	25	9	3.4	1.9	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1789	Angophora leiocarpa	Smooth-barked Apple	240		240	16	6	2.9	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1790	Angophora leiocarpa	Smooth-barked Apple	390		390	28	13	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1791	Eucalyptus tereticornis	Forest Red Gum	270		270	21	11	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1792	Corymbia citriodora	Spotted Gum	470		470	25	13	5.6	2.4	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1793	Eucalyptus tereticornis	Forest Red Gum	520		520	26	16	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1794	Corymbia trachyphloia	Brown Bloodwood	350		350	25	8	4.2	2.1	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1795	Corymbia citriodora	Spotted Gum	350		350	28	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1796	Angophora leiocarpa	Smooth-barked Apple	240		240	13	12	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1797	Eucalyptus tereticornis	Forest Red Gum	280		280	26	14	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1798	Angophora leiocarpa	Smooth-barked Apple	200		200	22	4	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
1799	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	16	5	3.2	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1800	Corymbia citriodora	Spotted Gum	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1801	Angophora leiocarpa	Smooth-barked Apple	210		210	18	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1802	Corymbia citriodora	Spotted Gum	330		330	21	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1803	Corymbia citriodora	Spotted Gum	350		350	32	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1804	Corymbia citriodora	Spotted Gum	250		250	25	8	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1805	Corymbia citriodora	Spotted Gum	280		280	28	8	3.4	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1806	Corymbia citriodora	Spotted Gum	210		210	20	3	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1807	Corymbia citriodora	Spotted Gum	310		310	24	14	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1808	Eucalyptus tereticornis	Forest Red Gum	290		290	20	10	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1809	Eucalyptus tereticornis	Forest Red Gum	230		230	26	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1810	Corymbia citriodora	Spotted Gum	390		390	31	15	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1811	Corymbia citriodora	Spotted Gum	300		300	24	12	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1812	Corymbia citriodora	Spotted Gum	310		310	25	8	3.7	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1813	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	28	11	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1814	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	23	12	3.8	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1815	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	15	7	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1816	Corymbia citriodora	Spotted Gum	360		360	26	13	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1817	Corymbia citriodora	Spotted Gum	320		320	22	14	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1818	Corymbia citriodora	Spotted Gum	430		430	30	16	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1819	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	14	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1820	Corymbia citriodora	Spotted Gum	260		260	21	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1821	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	23	11	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1822	Eucalyptus tereticornis	Forest Red Gum	280		280	21	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1823	Corymbia citriodora	Spotted Gum	820		820	31	15	9.8	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Retain
1824	Eucalyptus tereticornis	Forest Red Gum	340		340	20	12	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1825	Corymbia intermedia	Pink Bloodwood	210		210	13	12	2.5	1.7	One-sided	-	-	-	Epicormic	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
1826	Corymbia citriodora	Spotted Gum	230		230	22	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1827	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	14	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1828	Eucalyptus tereticornis	Forest Red Gum	290		290	20	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1829	Lophostemon suaveolens	Swamp Box	200		200	12	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1830	Lophostemon suaveolens	Swamp Box	210		210	8	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1831	Eucalyptus tereticornis	Forest Red Gum	350		350	22	10	4.2	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1832	Lophostemon suaveolens	Swamp Box	260		260	12	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1833	Eucalyptus tereticornis	Forest Red Gum	250		250	18	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1834	Eucalyptus tereticornis	Forest Red Gum	220		220	15	5	2.6	1.8	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1835	Corymbia intermedia	Pink Bloodwood	200		200	14	2	2.4	1.7	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1836	Lophostemon suaveolens	Swamp Box	300		300	10	5	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1837	Petalostigma pubescens	Quinine Bush	210		210	10	6	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1838	Lophostemon suaveolens	Swamp Box	220		220	12	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1839	Corymbia intermedia	Pink Bloodwood	220		220	15	6	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1840	Angophora leiocarpa	Smooth-barked Apple	320		320	15	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1841	Eucalyptus tereticornis	Forest Red Gum	410		410	25	12	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1842	Lophostemon suaveolens	Swamp Box	300	290, 200	463	12	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1843	Eucalyptus tereticornis	Forest Red Gum	240		240	18	8	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
1844	Corymbia citriodora	Spotted Gum	340		340	25	12	4.1	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1845	Lophostemon suaveolens	Swamp Box	210		210	10	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1846	Angophora leiocarpa	Smooth-barked Apple	270		270	18	7	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1847	Lophostemon suaveolens	Swamp Box	240		240	13	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1848	Eucalyptus tereticornis	Forest Red Gum	230		230	19	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1849	Lophostemon suaveolens	Swamp Box	210		210	13	5	2.5	1.7	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1850	Lophostemon suaveolens	Swamp Box	220		220	14	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1851	Lophostemon suaveolens	Swamp Box	240		240	11	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1852	Eucalyptus siderophloia	Grey Ironbark	360		360	24	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1853	Corymbia citriodora	Spotted Gum	230		230	26	10	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1854	Lophostemon suaveolens	Swamp Box	370		370	15	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Retain
1855	Corymbia citriodora	Spotted Gum	400		400	29	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1856	Corymbia intermedia	Pink Bloodwood	250		250	20	7	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1857	Eucalyptus tereticornis	Forest Red Gum	300		300	21	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1858	Lophostemon suaveolens	Swamp Box	250		250	12	6	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1859	Lophostemon suaveolens	Swamp Box	270		270	12	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1860	Eucalyptus tereticornis	Forest Red Gum	200		200	15	4	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1861	Corymbia tessellaris	Moreton Bay Ash	250		250	21	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1862	Lophostemon suaveolens	Swamp Box	270		270	12	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1863	Eucalyptus tereticornis	Forest Red Gum	400		400	20	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1864	Eucalyptus tereticornis	Forest Red Gum	520		520	22	11	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1865	Corymbia tessellaris	Moreton Bay Ash	200	200	283	16	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1866	Corymbia citriodora	Spotted Gum	360		360	26	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1867	Corymbia citriodora	Spotted Gum	360		360	27	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1868	Eucalyptus tereticornis	Forest Red Gum	230	170	286	16	8	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1869	Corymbia citriodora	Spotted Gum	250		250	17	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	fence around base	Retain
1870	Corymbia citriodora	Spotted Gum	470		470	20	15	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1871	Eucalyptus tereticornis	Forest Red Gum	530		530	26	13	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1872	Corymbia citriodora	Spotted Gum	440		440	24	12	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1873	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	16	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1874	Eucalyptus tereticornis	Forest Red Gum	300		300	20	8	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1875	Eucalyptus tereticornis	Forest Red Gum	220	220	311	15	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1876	Eucalyptus tereticornis	Forest Red Gum	160		160	15	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1877	Eucalyptus crebra	Narrow-leaved Ironbark	210	200, 160	331	13	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
1878	Corymbia citriodora	Spotted Gum	470		470	26	9	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1879	Angophora leiocarpa	Smooth-barked Apple	430		430	28	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1880	Eucalyptus siderophloia	Grey Ironbark	370		370	22	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1881	Eucalyptus tereticornis	Forest Red Gum	230		230	18	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1882	Corymbia intermedia	Pink Bloodwood	260		260	20	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1883	Eucalyptus siderophloia	Grey Ironbark	290		290	23	7	3.5	2.0	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1884	Eucalyptus siderophloia	Grey Ironbark	370		370	21	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1885	Angophora leiocarpa	Smooth-barked Apple	270		270	13	6	3.2	1.9	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1886	Eucalyptus tereticornis	Forest Red Gum	310		310	23	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1887	Eucalyptus siderophloia	Grey Ironbark	300		300	22	10	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1888	Corymbia citriodora	Spotted Gum	440		440	29	13	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1889	Corymbia citriodora	Spotted Gum	300		300	23	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1890	Eucalyptus tereticornis	Forest Red Gum	310		310	24	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1891	Eucalyptus siderophloia	Grey Ironbark	260		260	15	10	3.1	1.9	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1892	Corymbia citriodora	Spotted Gum	210		210	18	6	2.5	1.7	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1893	Eucalyptus tereticornis	Forest Red Gum	190		190	26	5	2.3	1.6	One-sided	-	Thinning	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1894	Corymbia citriodora	Spotted Gum	320		320	28	12	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1895	Eucalyptus siderophloia	Grey Ironbark	210		210	18	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1896	Corymbia citriodora	Spotted Gum	240		240	20	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1897	Eucalyptus siderophloia	Grey Ironbark	300		300	26	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1898	Eucalyptus siderophloia	Grey Ironbark	260		260	13	4	3.1	1.9	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1899	Eucalyptus siderophloia	Grey Ironbark	220		220	15	6	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1900	Eucalyptus siderophloia	Grey Ironbark	330		330	13	5	4.0	2.1	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1901	Eucalyptus tereticornis	Forest Red Gum	220		220	13	6	2.6	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1902	Alphitonia excelsa	Soap Tree	260		260	9	4	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retention TBC by CPTED
1903	Corymbia citriodora	Spotted Gum	240		240	16	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1904	Corymbia citriodora	Spotted Gum	340		340	22	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1905	Corymbia citriodora	Spotted Gum	250		250	21	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1906	Eucalyptus siderophloia	Grey Ironbark	230		230	18	5	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1907	Corymbia citriodora	Spotted Gum	230		230	22	5	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1908	Corymbia citriodora	Spotted Gum	240		240	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1909	Corymbia citriodora	Spotted Gum	290		290	22	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1910	Corymbia citriodora	Spotted Gum	330		330	22	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1911	Corymbia citriodora	Spotted Gum	200		200	22	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1912	Corymbia citriodora	Spotted Gum	210		210	14	5	2.5	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1913	Corymbia citriodora	Spotted Gum	310		310	22	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1914	Corymbia citriodora	Spotted Gum	270		270	15	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1915	Corymbia citriodora	Spotted Gum	430		430	29	12	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1916	Eucalyptus moluccana	Gum Topped Box	280		280	15	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
1917	Corymbia citriodora	Spotted Gum	240		240	16	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1918	Corymbia citriodora	Spotted Gum	230	230	325	24	9	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1919	Eucalyptus tereticornis	Forest Red Gum	330		330	27	11	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1920	Corymbia citriodora	Spotted Gum	290		290	24	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
1921	Corymbia citriodora	Spotted Gum	330		330	25	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1922	Corymbia citriodora	Spotted Gum	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1923	Angophora leiocarpa	Smooth-barked Apple	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1924	Corymbia citriodora	Spotted Gum	200		200	18	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1925	Corymbia citriodora	Spotted Gum	390		390	27	12	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1926	Corymbia citriodora	Spotted Gum	230		230	24	10	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1927	Corymbia citriodora	Spotted Gum	300		300	24	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1928	Eucalyptus tereticornis	Forest Red Gum	830		830	26	15	10.0	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1929	Corymbia citriodora	Spotted Gum	360		360	23	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1930	Eucalyptus siderophloia	Grey Ironbark	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1931	Eucalyptus tereticornis	Forest Red Gum	310		310	25	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1932	Eucalyptus tereticornis	Forest Red Gum	310		310	24	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1933	Eucalyptus tereticornis	Forest Red Gum	400		400	26	14	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	New	-	-	-	-		Retention TBC by CPTED
1934	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	20	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1935	Acacia disparrima	Hickory Wattle	260	180	316	12	10	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1936	Eucalyptus tereticornis	Forest Red Gum	400		400	29	13	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1937	Eucalyptus tereticornis	Forest Red Gum	350		350	28	8	4.2	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1938	Eucalyptus tereticornis	Forest Red Gum	310		310	25	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1939	Eucalyptus tereticornis	Forest Red Gum	320		320	20	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1940	Corymbia citriodora	Spotted Gum	230		230	21	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1941	Corymbia citriodora	Spotted Gum	280		280	17	8	3.4	1.9	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
1942	Eucalyptus tereticornis	Forest Red Gum	430		430	24	10	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1943	Corymbia citriodora	Spotted Gum	370		370	26	14	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1944	Eucalyptus tereticornis	Forest Red Gum	310		310	24	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Retention TBC by CPTED
1945	Corymbia citriodora	Spotted Gum	260		260	21	7	3.1	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1946	Corymbia citriodora	Spotted Gum	450		450	27	16	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1947	Angophora leiocarpa	Smooth-barked Apple	220		220	17	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1948	Eucalyptus tereticornis	Forest Red Gum	510		510	28	14	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1949	Corymbia intermedia	Pink Bloodwood	260		260	18	8	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1950	Eucalyptus tereticornis	Forest Red Gum	500		500	25	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1951	Corymbia citriodora	Spotted Gum	350		350	26	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1952	Eucalyptus tereticornis	Forest Red Gum	260		260	16	6	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1953	Corymbia citriodora	Spotted Gum	710		710	30	15	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1954	Eucalyptus tereticornis	Forest Red Gum	280		280	24	12	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1955	Corymbia citriodora	Spotted Gum	240		240	18	8	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1956	Corymbia citriodora	Spotted Gum	510		510	26	12	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1957	Corymbia citriodora	Spotted Gum	200		200	12	7	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1958	Corymbia citriodora	Spotted Gum	300		300	27	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1959	Eucalyptus tereticornis	Forest Red Gum	320		320	23	9	3.8	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1960	Corymbia citriodora	Spotted Gum	240		240	23	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1961	Eucalyptus tereticornis	Forest Red Gum	210		210	18	5	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
1962	Petalostigma pubescens	Quinine Bush	260		260	8	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1963	Corymbia intermedia	Pink Bloodwood	250		250	22	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1964	Corymbia citriodora	Spotted Gum	260		260	25	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1965	Corymbia citriodora	Spotted Gum	320		320	23	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1966	Corymbia citriodora	Spotted Gum	270		270	23	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1967	Corymbia citriodora	Spotted Gum	230		230	21	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1968	Eucalyptus tereticornis	Forest Red Gum	340		340	24	12	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1969	Corymbia citriodora	Spotted Gum	250		250	25	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1970	Corymbia citriodora	Spotted Gum	240		240	25	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1971	Corymbia citriodora	Spotted Gum	380		380	27	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1972	Corymbia citriodora	Spotted Gum	210		210	22	9	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1973	Corymbia citriodora	Spotted Gum	210		210	22	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1974	Corymbia citriodora	Spotted Gum	480		480	29	12	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1975	Corymbia citriodora	Spotted Gum	330		330	26	14	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1976	Corymbia citriodora	Spotted Gum	310		310	23	16	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
1977	Eucalyptus tereticornis	Forest Red Gum	330		330	26	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1978	Eucalyptus tereticornis	Forest Red Gum	360		360	27	13	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1979	Eucalyptus tereticornis	Forest Red Gum	220		220	19	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1980	Corymbia citriodora	Spotted Gum	300		300	24	11	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1981	Corymbia citriodora	Spotted Gum	280		280	22	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1982	Eucalyptus siderophloia	Grey Ironbark	320	240	400	24	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1983	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	23	15	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1984	Corymbia citriodora	Spotted Gum	430		430	30	17	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1985	Corymbia citriodora	Spotted Gum	390		390	29	17	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1986	Corymbia citriodora	Spotted Gum	450		450	24	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1987	Corymbia citriodora	Spotted Gum	240		240	16	7	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1988	Eucalyptus crebra	Narrow-leaved Ironbark	500		500	26	12	6.0	2.5	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1989	Corymbia citriodora	Spotted Gum	240		240	16	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
1990	Eucalyptus tereticornis	Forest Red Gum	550		550	26	8	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1991	Corymbia citriodora	Spotted Gum	230		230	19	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1992	Corymbia citriodora	Spotted Gum	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1993	Corymbia citriodora	Spotted Gum	220		220	23	5	2.6	1.8	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1994	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	21	6	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1995	Corymbia citriodora	Spotted Gum	240		240	18	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1996	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	19	4	2.5	1.7	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1997	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	14	6	2.9	1.8	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
1998	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	17	12	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termites	-		Remove
1999	Corymbia citriodora	Spotted Gum	240		240	15	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2000	Eucalyptus moluccana	Gum Topped Box	330		330	22	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2001	Eucalyptus moluccana	Gum Topped Box	480		480	31	11	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2002	Corymbia citriodora	Spotted Gum	240		240	18	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2003	Corymbia citriodora	Spotted Gum	410		410	23	8	4.9	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2004	Corymbia citriodora	Spotted Gum	250		250	21	7	3.0	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2005	Eucalyptus moluccana	Gum Topped Box	530		530	30	13	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2006	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	13	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2007	Corymbia citriodora	Spotted Gum	320	280	425	24	12	5.1	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2008	Corymbia citriodora	Spotted Gum	300		300	28	8	3.6	2.0	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2009	Eucalyptus moluccana	Gum Topped Box	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2010	Corymbia citriodora	Spotted Gum	260		260	25	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2011	Corymbia citriodora	Spotted Gum	300		300	26	15	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2012	Corymbia citriodora	Spotted Gum	300		300	28	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2013	Corymbia citriodora	Spotted Gum	230		230	25	5	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2014	Eucalyptus moluccana	Gum Topped Box	360		360	29	12	4.3	2.2	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
2015	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	24	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2016	Corymbia citriodora	Spotted Gum	260		260	17	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2017	Corymbia citriodora	Spotted Gum	200		200	24	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2018	Corymbia citriodora	Spotted Gum	210		210	22	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2019	Corymbia citriodora	Spotted Gum	410		410	29	14	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2020	Corymbia citriodora	Spotted Gum	360		360	26	15	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2021	Corymbia citriodora	Spotted Gum	390		390	32	13	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2022	Corymbia citriodora	Spotted Gum	370		370	28	11	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2023	Eucalyptus crebra	Narrow-leaved Ironbark	200	170	262	15	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2024	Corymbia citriodora	Spotted Gum	370		370	29	17	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2025	Corymbia citriodora	Spotted Gum	380		380	30	16	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2026	Corymbia citriodora	Spotted Gum	270		270	23	11	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2027	Corymbia citriodora	Spotted Gum	420		420	26	12	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2028	Corymbia citriodora	Spotted Gum	210		210	19	5	2.5	1.7	One-sided	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2029	Corymbia citriodora	Spotted Gum	330		330	31	15	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2030	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	14	9	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2031	Corymbia citriodora	Spotted Gum	250		250	22	9	3.0	1.8	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
2032	Corymbia citriodora	Spotted Gum	280		280	25	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2033	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	21	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2034	Corymbia citriodora	Spotted Gum	290		290	27	11	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2035	Corymbia citriodora	Spotted Gum	240		240	16	8	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2036	Corymbia citriodora	Spotted Gum	210		210	15	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2037	Corymbia citriodora	Spotted Gum	250		250	28	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2038	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	29	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2039	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	21	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2040	Eucalyptus moluccana	Gum Topped Box	220		220	22	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2041	Corymbia citriodora	Spotted Gum	350		350	28	16	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2042	Corymbia citriodora	Spotted Gum	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2043	Corymbia citriodora	Spotted Gum	330		330	26	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2044	Corymbia citriodora	Spotted Gum	250		250	26	5	3.0	1.8	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2045	Eucalyptus moluccana	Gum Topped Box	400		400	29	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2046	Corymbia citriodora	Spotted Gum	290		290	20	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2047	Corymbia citriodora	Spotted Gum	290		290	19	8	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2048	Eucalyptus tereticornis	Forest Red Gum	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2049	Corymbia citriodora	Spotted Gum	470		470	19	7	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2050	Eucalyptus siderophloia	Grey Ironbark	230		230	16	3	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2051	Alphitonia excelsa	Soap Tree	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2052	Angophora leiocarpa	Smooth-barked Apple	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2053	Lophostemon suaveolens	Swamp Box	430		430	16	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2054	Corymbia citriodora	Spotted Gum	210		210	16	6	2.5	1.7	Irregular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2055	Eucalyptus siderophloia	Grey Ironbark	260		260	15	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2056	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	20	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2057	Lophostemon suaveolens	Swamp Box	180	210	277	12	4	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2058	Corymbia citriodora	Spotted Gum	460		460	22	5	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2059	Corymbia intermedia	Pink Bloodwood	550		550	23	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2060	Corymbia tessellaris	Moreton Bay Ash	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2061	Lophostemon suaveolens	Swamp Box	230		230	9	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2062	Lophostemon suaveolens	Swamp Box	290		290	10	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2063	Lophostemon suaveolens	Swamp Box	230		230	10	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2064	Corymbia citriodora	Spotted Gum	340		340	22	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2065	Lophostemon suaveolens	Swamp Box	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2066	Acacia concurrens	Black Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2067	Alphitonia excelsa	Soap Tree	220		220	10	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2068	Corymbia intermedia	Pink Bloodwood	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2069	Corymbia citriodora	Spotted Gum	340		340	19	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2070	Corymbia citriodora	Spotted Gum	320		320	16	5	3.8	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2071	Eucalyptus tereticornis	Forest Red Gum	470		470	22	6	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2072	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	15	4	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2073	Eucalyptus siderophloia	Grey Ironbark	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2074	Corymbia citriodora	Spotted Gum	210		210	14	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2075	Eucalyptus tereticornis	Forest Red Gum	320		320	17	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2076	Corymbia citriodora	Spotted Gum	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2077	Corymbia citriodora	Spotted Gum	350		350	17	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2078	Lophostemon suaveolens	Swamp Box	240		240	10	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2079	Corymbia citriodora	Spotted Gum	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2080	Eucalyptus siderophloia	Grey Ironbark	210		210	11	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2081	Corymbia citriodora	Spotted Gum	550		550	20	7	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2082	Corymbia citriodora	Spotted Gum	260		260	16	5	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2083	Eucalyptus siderophloia	Grey Ironbark	230		230	16	2	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2084	Corymbia citriodora	Spotted Gum	290		290	20	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2085	Corymbia intermedia	Pink Bloodwood	270		270	17	3	3.2	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2086	Corymbia citriodora	Spotted Gum	350		350	20	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2087	Corymbia citriodora	Spotted Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2088	Eucalyptus siderophloia	Grey Ironbark	330		330	14	4	4.0	2.1	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2089	Eucalyptus siderophloia	Grey Ironbark	200		200	12	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2090	Corymbia citriodora	Spotted Gum	220	190	291	12	2	3.5	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2091	Corymbia citriodora	Spotted Gum	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2092	Corymbia citriodora	Spotted Gum	380		380	23	8	4.6	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2093	Corymbia citriodora	Spotted Gum	420		420	24	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2094	Eucalyptus siderophloia	Grey Ironbark	230		230	14	4	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2095	Eucalyptus siderophloia	Grey Ironbark	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2096	Corymbia citriodora	Spotted Gum	200		200	10	3	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2097	Eucalyptus siderophloia	Grey Ironbark	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2098	Corymbia citriodora	Spotted Gum	290		290	18	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2099	Corymbia citriodora	Spotted Gum	350		350	22	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2100	Eucalyptus siderophloia	Grey Ironbark	580		580	22	4	7.0	2.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2101	Eucalyptus siderophloia	Grey Ironbark	350		350	18	4	4.2	2.1	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2102	Eucalyptus tereticornis	Forest Red Gum	460		460	22	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2103	Corymbia citriodora	Spotted Gum	300		300	20	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2104	Eucalyptus crebra	Narrow-leaved Ironbark	530		530	23	7	6.4	2.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2105	Eucalyptus siderophloia	Grey Ironbark	260		260	19	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2106	Corymbia citriodora	Spotted Gum	550	440	704	29	14	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2107	Eucalyptus siderophloia	Grey Ironbark	460		460	20	6	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2108	Eucalyptus tereticornis	Forest Red Gum	430		430	20	5	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2109	Corymbia citriodora	Spotted Gum	200		200	12	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2110	Corymbia citriodora	Spotted Gum	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2111	Corymbia citriodora	Spotted Gum	470		470	26	9	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2112	Eucalyptus tereticornis	Forest Red Gum	430		430	23	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2113	Corymbia citriodora	Spotted Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2114	Corymbia citriodora	Spotted Gum	450		450	30	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2115	Eucalyptus siderophloia	Grey Ironbark	350		350	18	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2116	Eucalyptus tereticornis	Forest Red Gum	210		210	14	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2117	Eucalyptus tereticornis	Forest Red Gum	250		250	14	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2118	Corymbia citriodora	Spotted Gum	270		270	14	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2119	Eucalyptus moluccana	Gum Topped Box	390		390	23	7	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2120	Corymbia citriodora	Spotted Gum	450		450	18	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2121	Eucalyptus moluccana	Gum Topped Box	330		330	23	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2122	Eucalyptus moluccana	Gum Topped Box	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2123	Eucalyptus tereticornis	Forest Red Gum	370		370	17	5	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2124	Eucalyptus tereticornis	Forest Red Gum	310		310	19	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2125	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2126	Acacia concurrens	Black Wattle	220		220	9	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2127	Corymbia citriodora	Spotted Gum	310		310	21	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2128	Eucalyptus tereticornis	Forest Red Gum	470		470	20	9	5.6	2.4	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2129	Eucalyptus tereticornis	Forest Red Gum	460		460	20	7	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2130	Corymbia citriodora	Spotted Gum	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2131	Corymbia citriodora	Spotted Gum	300		300	18	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2132	Eucalyptus tereticornis	Forest Red Gum	340		340	23	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2133	Eucalyptus tereticornis	Forest Red Gum	360		360	18	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2134	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2135	Angophora leiocarpa	Smooth-barked Apple	270		270	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2136	Angophora leiocarpa	Smooth-barked Apple	400		400	18	7	4.8	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
2137	Corymbia tessellaris	Moreton Bay Ash	220		220	14	4	2.6	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2138	Lophostemon suaveolens	Swamp Box	350		350	12	4	4.2	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2139	Lophostemon suaveolens	Swamp Box	230		230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2140	Eucalyptus tereticornis	Forest Red Gum	290		290	17	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2141	Eucalyptus tereticornis	Forest Red Gum	290		290	18	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2142	Angophora leiocarpa	Smooth-barked Apple	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2143	Acacia concurrens	Black Wattle	170	150	227	14	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2144	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2145	Corymbia intermedia	Pink Bloodwood	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2146	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2147	Lophostemon suaveolens	Swamp Box	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2148	Lophostemon suaveolens	Swamp Box	210		210	12	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2149	Corymbia intermedia	Pink Bloodwood	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2150	Eucalyptus tereticornis	Forest Red Gum	350		350	16	3	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2151	Corymbia intermedia	Pink Bloodwood	210		210	12	2	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2152	Eucalyptus tereticornis	Forest Red Gum	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2153	Corymbia citriodora	Spotted Gum	390		390	22	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2154	Angophora leiocarpa	Smooth-barked Apple	280		280	16	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2155	Eucalyptus tereticornis	Forest Red Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2156	Lophostemon suaveolens	Swamp Box	190	210	283	16	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2157	Corymbia intermedia	Pink Bloodwood	330		330	20	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2158	Angophora leiocarpa	Smooth-barked Apple	290		290	24	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2159	Corymbia intermedia	Pink Bloodwood	330	200, 190	430	20	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2160	Eucalyptus tereticornis	Forest Red Gum	490		490	26	10	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2161	Corymbia citriodora	Spotted Gum	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2162	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2163	Corymbia intermedia	Pink Bloodwood	260		260	20	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2164	Lophostemon suaveolens	Swamp Box	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2165	Eucalyptus tereticornis	Forest Red Gum	200		200	16	6	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2166	Lophostemon suaveolens	Swamp Box	380		380	13	3	4.6	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2167	Lophostemon suaveolens	Swamp Box	180	150	234	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2168	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2169	Corymbia intermedia	Pink Bloodwood	400		400	20	5	4.8	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2170	Lophostemon suaveolens	Swamp Box	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2171	Angophora leiocarpa	Smooth-barked Apple	370		370	18	8	4.4	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
2172	Lophostemon suaveolens	Swamp Box	290		290	16	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2173	Acacia disparrima	Hickory Wattle	210		210	10	3	2.5	1.7	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
2174	Lophostemon suaveolens	Swamp Box	270		270	12	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2175	Lophostemon suaveolens	Swamp Box	250		250	15	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2176	Eucalyptus tereticornis	Forest Red Gum	470		470	20	9	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2177	Eucalyptus tereticornis	Forest Red Gum	380		380	21	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2178	Eucalyptus tereticornis	Forest Red Gum	400		400	22	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2179	Eucalyptus tereticornis	Forest Red Gum	320		320	22	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2180	Angophora leiocarpa	Smooth-barked Apple	300		300	20	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2181	Eucalyptus tereticornis	Forest Red Gum	880		880	26	10	10.6	3.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2182	Corymbia citriodora	Spotted Gum	300		300	20	5	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2183	Lophostemon suaveolens	Swamp Box	350		350	17	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2184	Eucalyptus tereticornis	Forest Red Gum	360		360	23	4	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2185	Eucalyptus tereticornis	Forest Red Gum	330		330	18	5	4.0	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2186	Corymbia intermedia	Pink Bloodwood	330		330	20	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2187	Corymbia citriodora	Spotted Gum	270		270	22	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2188	Lophostemon suaveolens	Swamp Box	220		220	14	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2189	Corymbia citriodora	Spotted Gum	550		550	27	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2190	Eucalyptus tereticornis	Forest Red Gum	320		320	24	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2191	Eucalyptus tereticornis	Forest Red Gum	320		320	20	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2192	Corymbia citriodora	Spotted Gum	340		340	20	7	4.1	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2193	Corymbia citriodora	Spotted Gum	290		290	21	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2194	Corymbia citriodora	Spotted Gum	640	300	707	23	12	8.5	2.9	One-sided	-	Thinning	-	Epicormic	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	Small	-	-	-		Retain
2195	Eucalyptus crebra	Narrow-leaved Ironbark	830		830	26	10	10.0	3.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
2196	Corymbia citriodora	Spotted Gum	540		540	27	10	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2197	Eucalyptus crebra	Narrow-leaved Ironbark	880		880	26	14	10.6	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2198	Corymbia citriodora	Spotted Gum	200	140	244	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2199	Eucalyptus crebra	Narrow-leaved Ironbark	500		500	24	8	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2200	Eucalyptus crebra	Narrow-leaved Ironbark	400		400	20	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2201	Corymbia citriodora	Spotted Gum	340		340	20	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2202	Eucalyptus siderophloia	Grey Ironbark	400		400	21	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2203	Eucalyptus tereticornis	Forest Red Gum	280		280	19	3	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2204	Angophora leiocarpa	Smooth-barked Apple	320		320	16	6	3.8	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2205	Corymbia intermedia	Pink Bloodwood	590		590	25	10	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2206	Corymbia citriodora	Spotted Gum	430		430	20	9	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2207	Corymbia citriodora	Spotted Gum	600		600	24	14	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2208	Eucalyptus siderophloia	Grey Ironbark	260		260	18	6	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2209	Eucalyptus siderophloia	Grey Ironbark	260		260	17	3	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2210	Angophora leiocarpa	Smooth-barked Apple	340		340	18	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2211	Eucalyptus siderophloia	Grey Ironbark	330		330	18	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2212	Corymbia citriodora	Spotted Gum	420		420	20	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2213	Eucalyptus tereticornis	Forest Red Gum	400		400	20	5	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2214	Eucalyptus siderophloia	Grey Ironbark	500		500	19	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2215	Corymbia citriodora	Spotted Gum	260		260	8	3	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2216	Eucalyptus siderophloia	Grey Ironbark	240		240	19	3	2.9	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2217	Eucalyptus siderophloia	Grey Ironbark	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2218	Angophora leiocarpa	Smooth-barked Apple	640		640	22	9	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2219	Eucalyptus siderophloia	Grey Ironbark	230		230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
2220	Eucalyptus tereticornis	Forest Red Gum	230		230	19	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2221	Eucalyptus tereticornis	Forest Red Gum	290	320	432	18	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2222	Corymbia citriodora	Spotted Gum	580		580	28	10	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2223	Eucalyptus tereticornis	Forest Red Gum	240		240	17	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2224	Eucalyptus siderophloia	Grey Ironbark	270		270	18	6	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2225	Eucalyptus siderophloia	Grey Ironbark	280		280	18	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2226	Eucalyptus siderophloia	Grey Ironbark	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2227	Eucalyptus siderophloia	Grey Ironbark	280		280	18	4	3.4	1.9	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2228	Eucalyptus tereticornis	Forest Red Gum	450		450	24	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2229	Corymbia intermedia	Pink Bloodwood	250	180	308	17	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2230	Eucalyptus siderophloia	Grey Ironbark	380		380	18	7	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2231	Corymbia intermedia	Pink Bloodwood	290		290	17	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2232	Eucalyptus siderophloia	Grey Ironbark	260	160	305	16	4	3.7	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2233	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	18	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2234	Corymbia citriodora	Spotted Gum	520		520	28	12	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2235	Eucalyptus siderophloia	Grey Ironbark	370		370	16	6	4.4	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2236	Corymbia citriodora	Spotted Gum	300		300	17	5	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2237	Corymbia citriodora	Spotted Gum	500		500	22	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2238	Corymbia citriodora	Spotted Gum	540		540	28	7	6.5	2.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2239	Corymbia citriodora	Spotted Gum	450		450	26	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2240	Corymbia citriodora	Spotted Gum	250		250	18	5	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2241	Eucalyptus moluccana	Gum Topped Box	540		540	29	9	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2242	Corymbia citriodora	Spotted Gum	240		240	14	5	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2243	Corymbia citriodora	Spotted Gum	220		220	18	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2244	Corymbia citriodora	Spotted Gum	490		490	22	8	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2245	Corymbia citriodora	Spotted Gum	200		200	18	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2246	Corymbia citriodora	Spotted Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2247	Corymbia citriodora	Spotted Gum	345		345	17	5	4.1	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2248	Corymbia citriodora	Spotted Gum	260		260	16	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2249	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2250	Eucalyptus siderophloia	Grey Ironbark	310		310	19	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2251	Eucalyptus moluccana	Gum Topped Box	710		710	26	12	8.5	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2252	Corymbia citriodora	Spotted Gum	520		520	26	9	6.2	2.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2253	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	16	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2254	Corymbia citriodora	Spotted Gum	350		350	18	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2255	Eucalyptus siderophloia	Grey Ironbark	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
2256	Corymbia citriodora	Spotted Gum	390		390	22	6	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2257	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	20	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2258	Alphitonia excelsa	Soap Tree	200		200	9	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2259	Corymbia intermedia	Pink Bloodwood	330		330	16	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2260	Eucalyptus tereticornis	Forest Red Gum	560		560	19	8	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2261	Corymbia citriodora	Spotted Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2262	Corymbia citriodora	Spotted Gum	470		470	18	5	5.6	2.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	Small	-	-	-		Remove
2263	Corymbia citriodora	Spotted Gum	395		395	19	7	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2264	Eucalyptus tereticornis	Forest Red Gum	420	410	587	23	14	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2265	Eucalyptus tereticornis	Forest Red Gum	650		650	24	8	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2266	Corymbia citriodora	Spotted Gum	540		540	23	11	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2267	Corymbia citriodora	Spotted Gum	225		225	16	4	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2268	Corymbia citriodora	Spotted Gum	305		305	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2269	Corymbia citriodora	Spotted Gum	230		230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2270	Corymbia citriodora	Spotted Gum	270		270	16	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2271	Corymbia citriodora	Spotted Gum	260		260	15	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2272	Eucalyptus tereticornis	Forest Red Gum	310		310	17	5	3.7	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2273	Eucalyptus siderophloia	Grey Ironbark	380	120	398	18	6	4.8	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2274	Eucalyptus tereticornis	Forest Red Gum	250		250	17	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2275	Acacia concurrens	Black Wattle	250		250	11	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2276	Angophora leiocarpa	Smooth-barked Apple	460		460	20	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2277	Eucalyptus tereticornis	Forest Red Gum	195		195	16	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2278	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	17	3	2.9	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2279	Eucalyptus tereticornis	Forest Red Gum	280		280	15	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2280	Alphitonia excelsa	Soap Tree	230		230	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2281	Acacia concurrens	Black Wattle	400		400	10	4	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2282	Corymbia intermedia	Pink Bloodwood	280	250, 200	425	16	5	5.1	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2283	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	19	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2284	Eucalyptus tereticornis	Forest Red Gum	310		310	16	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2285	Angophora leiocarpa	Smooth-barked Apple	150	240	283	14	3	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2286	Eucalyptus tereticornis	Forest Red Gum	210		210	10	2	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2287	Corymbia citriodora	Spotted Gum	320		320	18	7	3.8	2.1	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2288	Eucalyptus tereticornis	Forest Red Gum	500		500	16	7	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2289	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	17	3	3.1	1.9	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	Termites	-		Remove
2290	Corymbia citriodora	Spotted Gum	295		295	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2291	Eucalyptus tereticornis	Forest Red Gum	200	120	233	14	2	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2292	Eucalyptus tereticornis	Forest Red Gum	270		270	16	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2293	Eucalyptus tereticornis	Forest Red Gum	250		250	15	3	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2294	Eucalyptus tereticornis	Forest Red Gum	290		290	16	3	3.5	2.0	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2295	Corymbia citriodora	Spotted Gum	255		255	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2296	Eucalyptus siderophloia	Grey Ironbark	220		220	16	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2297	Eucalyptus siderophloia	Grey Ironbark	460		460	19	4	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
2298	Eucalyptus siderophloia	Grey Ironbark	500		500	22	9	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2299	Eucalyptus tereticornis	Forest Red Gum	800		800	24	9	9.6	3.0	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Remove
2300	Corymbia citriodora	Spotted Gum	480		480	27	10	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2301	Eucalyptus tereticornis	Forest Red Gum	440		440	25	10	5.3	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2302	Corymbia citriodora	Spotted Gum	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2303	Corymbia citriodora	Spotted Gum	370		370	22	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2304	Corymbia citriodora	Spotted Gum	220		220	15	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2305	Corymbia citriodora	Spotted Gum	320		320	18	3	3.8	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2306	Eucalyptus tereticornis	Forest Red Gum	560		560	16	8	6.7	2.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	Old	Small	-	-	-		Approved to remove
2307	Eucalyptus tereticornis	Forest Red Gum	410		410	20	4	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2308	Corymbia tessellaris	Moreton Bay Ash	400		400	23	6	4.8	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2309	Corymbia citriodora	Spotted Gum	520		520	26	10	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2310	Corymbia citriodora	Spotted Gum	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2311	Eucalyptus crebra	Narrow-leaved Ironbark	420		420	26	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2312	Corymbia citriodora	Spotted Gum	340		340	18	2	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2313	Eucalyptus siderophloia	Grey Ironbark	245		245	16	4	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2314	Corymbia citriodora	Spotted Gum	215	230, 150, 100	363	17	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2315	Corymbia citriodora	Spotted Gum	480		480	24	10	5.8	2.4	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2316	Eucalyptus siderophloia	Grey Ironbark	195		195	15	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2317	Eucalyptus siderophloia	Grey Ironbark	460		460	25	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2318	Eucalyptus siderophloia	Grey Ironbark	280		280	19	2	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2319	Eucalyptus siderophloia	Grey Ironbark	255		255	16	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2320	Corymbia citriodora	Spotted Gum	220		220	15	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2321	Corymbia citriodora	Spotted Gum	215		215	16	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2322	Corymbia citriodora	Spotted Gum	310		310	18	5	3.7	2.0	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2323	Corymbia tessellaris	Moreton Bay Ash	260		260	17	3	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2324	Eucalyptus crebra	Narrow-leaved Ironbark	530		530	26	10	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2325	Eucalyptus crebra	Narrow-leaved Ironbark	440		440	22	5	5.3	2.3	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2326	Corymbia citriodora	Spotted Gum	215		215	16	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2327	Corymbia citriodora	Spotted Gum	390		390	17	5	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2328	Corymbia citriodora	Spotted Gum	530		530	24	14	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2329	Corymbia citriodora	Spotted Gum	400		400	20	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2330	Eucalyptus siderophloia	Grey Ironbark	240	120	268	16	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2331	Eucalyptus siderophloia	Grey Ironbark	330		330	18	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2332	Corymbia citriodora	Spotted Gum	300		300	17	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Remove
2333	Eucalyptus crebra	Narrow-leaved Ironbark	400		400	18	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2334	Corymbia citriodora	Spotted Gum	480		480	24	8	5.8	2.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2335	Corymbia citriodora	Spotted Gum	380		380	23	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2336	Eucalyptus siderophloia	Grey Ironbark	300		300	18	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2337	Eucalyptus moluccana	Gum Topped Box	520		520	27	9	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2338	Eucalyptus tereticornis	Forest Red Gum	285		285	20	5	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2339	Eucalyptus siderophloia	Grey Ironbark	240		240	17	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2340	Eucalyptus siderophloia	Grey Ironbark	245		245	16	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2341	Corymbia citriodora	Spotted Gum	195		195	10	2	2.3	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2342	Angophora leiocarpa	Smooth-barked Apple	450		450	24	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2343	Eucalyptus moluccana	Gum Topped Box	475		475	28	10	5.7	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2344	Corymbia citriodora	Spotted Gum	270		270	18	3	3.2	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2345	Eucalyptus moluccana	Gum Topped Box	540		540	26	8	6.5	2.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2346	Eucalyptus moluccana	Gum Topped Box	315		315	20	5	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2347	Corymbia citriodora	Spotted Gum	255		255	18	3	3.1	1.9	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2348	Eucalyptus moluccana	Gum Topped Box	315		315	15	4	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2349	Eucalyptus moluccana	Gum Topped Box	320		320	19	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2350	Eucalyptus moluccana	Gum Topped Box	640		640	27	14	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2351	Corymbia citriodora	Spotted Gum	350		350	27	5	4.2	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2352	Corymbia citriodora	Spotted Gum	230		230	18	3	2.8	1.8	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2353	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2354	Corymbia citriodora	Spotted Gum	230		230	22	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2355	Corymbia citriodora	Spotted Gum	270		270	23	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2356	Corymbia citriodora	Spotted Gum	260		260	22	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2357	Corymbia citriodora	Spotted Gum	220		220	20	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2358	Corymbia citriodora	Spotted Gum	340		340	20	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2359	Corymbia citriodora	Spotted Gum	200		200	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2360	Eucalyptus moluccana	Gum Topped Box	330		330	23	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2361	Corymbia citriodora	Spotted Gum	230		230	20	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2362	Corymbia citriodora	Spotted Gum	230		230	14	4	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2363	Eucalyptus siderophloia	Grey Ironbark	385		385	21	4	4.6	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
2364	Corymbia citriodora	Spotted Gum	230		230	23	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2365	Corymbia citriodora	Spotted Gum	265		265	21	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2366	Corymbia citriodora	Spotted Gum	240		240	20	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2367	Corymbia citriodora	Spotted Gum	280		280	23	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2368	Corymbia citriodora	Spotted Gum	280		280	20	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2369	Eucalyptus moluccana	Gum Topped Box	220		220	14	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2370	Corymbia citriodora	Spotted Gum	200	180, 100	287	20	4	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2371	Corymbia citriodora	Spotted Gum	200		200	21	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2372	Corymbia citriodora	Spotted Gum	200	180	269	20	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2373	Corymbia citriodora	Spotted Gum	295		295	24	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2374	Corymbia citriodora	Spotted Gum	375		375	23	7	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2375	Eucalyptus moluccana	Gum Topped Box	250		250	25	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2376	Corymbia citriodora	Spotted Gum	280		280	23	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2377	Corymbia citriodora	Spotted Gum	230		230	24	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2378	Corymbia citriodora	Spotted Gum	210		210	20	3	2.5	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2379	Corymbia citriodora	Spotted Gum	220		220	20	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2380	Corymbia citriodora	Spotted Gum	220		220	19	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2381	Eucalyptus siderophloia	Grey Ironbark	255		255	24	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2382	Corymbia citriodora	Spotted Gum	215		215	24	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2383	Corymbia citriodora	Spotted Gum	260		260	17	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
2384	Corymbia citriodora	Spotted Gum	200		200	17	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2385	Corymbia citriodora	Spotted Gum	210		210	20	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2386	Eucalyptus siderophloia	Grey Ironbark	250		250	20	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2387	Eucalyptus crebra	Narrow-leaved Ironbark	235		235	22	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2388	Corymbia citriodora	Spotted Gum	650		650	34	15	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2389	Corymbia citriodora	Spotted Gum	330		330	15	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2390	Corymbia citriodora	Spotted Gum	330		330	17	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2391	Corymbia citriodora	Spotted Gum	280		280	21	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2392	Lophostemon suaveolens	Swamp Box	210		210	11	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2393	Corymbia intermedia	Pink Bloodwood	265		265	15	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2394	Acacia disparrima	Hickory Wattle	250		250	10	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2395	Acacia disparrima	Hickory Wattle	260		260	11	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2396	Corymbia intermedia	Pink Bloodwood	265		265	9	3	3.2	1.9	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2397	Lophostemon suaveolens	Swamp Box	275		275	11	4	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2398	Acacia disparrima	Hickory Wattle	270		270	11	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2399	Lophostemon suaveolens	Swamp Box	285	210	354	12	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2400	Lophostemon suaveolens	Swamp Box	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2401	Angophora floribunda	Rough-barked Apple	365		365	18	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2402	Acacia disparrima	Hickory Wattle	210	150	258	13	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2403	Corymbia intermedia	Pink Bloodwood	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2404	Angophora floribunda	Rough-barked Apple	310		310	17	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2405	Acacia disparrima	Hickory Wattle	250		250	13	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2406	Eucalyptus tereticornis	Forest Red Gum	630		630	26	12	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2407	Casuarina cunninghamiana	River Sheoak	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2408	Casuarina cunninghamiana	River Sheoak	220		220	9	7	2.6	1.8	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2409	Casuarina cunninghamiana	River Sheoak	460		460	26	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2410	Euodia elleryana	corkwood	300		300	12	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2411	Euodia elleryana	corkwood	230		230	9	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2412	Casuarina cunninghamiana	River Sheoak	270		270	12	9	3.2	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2413	Casuarina cunninghamiana	River Sheoak	490		490	22	9	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2414	Acacia disparrima	Hickory Wattle	230		230	9	7	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2415	Angophora floribunda	Rough-barked Apple	220		220	16	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2416	Angophora floribunda	Rough-barked Apple	370	230	436	15	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2417	Casuarina cunninghamiana	River Sheoak	420		420	17	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2418	Melaleuca viminalis	Weeping Bottlebrush	220		220	12	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2419	Melaleuca viminalis	Weeping Bottlebrush	240		240	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2420	Lophostemon suaveolens	Swamp Box	280		280	14	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2421	Casuarina cunninghamiana	River Sheoak	250		250	21	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2422	Casuarina cunninghamiana	River Sheoak	240		240	20	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2423	Casuarina cunninghamiana	River Sheoak	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2424	Casuarina cunninghamiana	River Sheoak	400		400	24	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2425	Casuarina cunninghamiana	River Sheoak	460	260	528	22	9	6.3	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2426	Casuarina cunninghamiana	River Sheoak	420		420	23	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2427	Casuarina cunninghamiana	River Sheoak	420		420	19	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2428	Casuarina cunninghamiana	River Sheoak	270		270	18	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2429	Casuarina cunninghamiana	River Sheoak	360		360	19	7	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2430	Casuarina cunninghamiana	River Sheoak	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2431	Casuarina cunninghamiana	River Sheoak	460		460	23	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2432	Euodia elleryana	corkwood	310		310	10	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2433	Casuarina cunninghamiana	River Sheoak	270		270	14	4	3.2	1.9	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2434	Casuarina cunninghamiana	River Sheoak	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2435	Casuarina cunninghamiana	River Sheoak	420		420	21	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2436	Casuarina cunninghamiana	River Sheoak	360		360	18	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2437	Acacia disparrima	Hickory Wattle	200	190, 150	314	13	7	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2438	Eucalyptus tereticornis	Forest Red Gum	265		265	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2439	Eucalyptus tereticornis	Forest Red Gum	485		485	19	7	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2440	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2441	Lophostemon suaveolens	Swamp Box	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2442	Lophostemon suaveolens	Swamp Box	320		320	13	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2443	Corymbia citriodora	Spotted Gum	270		270	17	11	3.2	1.9	Regular	-	-	-	-	-	Typical		-		-	Typical	-	-	-	-	-	-		Approved to remove
2444	Eucalyptus siderophloia	Grey Ironbark	390		390	22	12	4.7	2.2	Regular	-	-	-	-	-	Typical		-		-	Typical	-	-	-	-	-	-		Approved to remove
2445	Corymbia citriodora	Spotted Gum	310		310	15	12	3.7	2.0	Regular	-	-	-	-	-	Typical		-		-	Typical	-	-	-	-	-	-		Approved to remove
2446	Corymbia intermedia	Pink Bloodwood	360		360	17	11	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2447	Corymbia intermedia	Pink Bloodwood	240		240	16	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2448	Eucalyptus tereticornis	Forest Red Gum	340		340	18	12	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2449	Eucalyptus siderophloia	Grey Ironbark	470		470	20	11	5.6	2.4	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2450	Acacia leiocalyx	Early-flowering Black Wattle	160	170, 90	250	8	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2451	Corymbia citriodora	Spotted Gum	190		190	17	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2452	Corymbia citriodora	Spotted Gum	130		130	16	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2453	Acacia disparrima	Hickory Wattle	140		140	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2454	Corymbia citriodora	Spotted Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2455	Corymbia citriodora	Spotted Gum	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2456	Acacia disparrima	Hickory Wattle	110	70	130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2457	Corymbia citriodora	Spotted Gum	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2458	Corymbia citriodora	Spotted Gum	160		160	17	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2459	Acacia disparrima	Hickory Wattle	100	70	122	4	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2460	Corymbia citriodora	Spotted Gum	270		270	19	11	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2461	Acacia concurrens	Black Wattle	130		130	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2462	Corymbia citriodora	Spotted Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2463	Acacia concurrens	Black Wattle	110		110	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2464	Corymbia citriodora	Spotted Gum	340		340	23	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2465	Acacia concurrens	Black Wattle	170		170	5	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2466	Acacia concurrens	Black Wattle	160		160	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2467	Corymbia citriodora	Spotted Gum	260		260	19	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2468	Eucalyptus tereticornis	Forest Red Gum	250		250	16	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2469	Corymbia citriodora	Spotted Gum	220		220	21	10	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2470	Corymbia citriodora	Spotted Gum	240		240	21	11	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2471	Corymbia citriodora	Spotted Gum	260		260	16	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2472	Corymbia citriodora	Spotted Gum	260		260	20	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2473	Eucalyptus siderophloia	Grey Ironbark	290		290	21	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2474	Angophora leiocarpa	Smooth-barked Apple	280		280	18	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2475	Eucalyptus tereticornis	Forest Red Gum	260		260	18	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2476	Corymbia citriodora	Spotted Gum	220		220	19	10	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2477	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	18	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2478	Corymbia citriodora	Spotted Gum	170		170	18	9	2.0	1.6	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2479	Corymbia intermedia	Pink Bloodwood	160	50	168	16	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2480	Corymbia citriodora	Spotted Gum	460		460	21	14	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2481	Corymbia citriodora	Spotted Gum	280		280	21	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2482	Corymbia citriodora	Spotted Gum	160		160	15	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2483	Corymbia citriodora	Spotted Gum	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2484	Allocasuarina littoralis	Black She Oak	130		130	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2485	Allocasuarina littoralis	Black She Oak	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2486	Eucalyptus tereticornis	Forest Red Gum	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2487	Eucalyptus tereticornis	Forest Red Gum	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2488	Acacia disparrima	Hickory Wattle	130		130	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2489	Eucalyptus siderophloia	Grey Ironbark	220		220	11	6	2.6	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2490	Acacia disparrima	Hickory Wattle	140		140	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2491	Corymbia citriodora	Spotted Gum	260		260	19	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2492	Corymbia citriodora	Spotted Gum	260		260	16	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2493	Acacia concurrens	Black Wattle	150		150	5	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2494	Acacia concurrens	Black Wattle	150		150	5	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Approved to remove
2495	Acacia leiocalyx	Early-flowering Black Wattle	160	120	200	5	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2496	Acacia concurrens	Black Wattle	110		110	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2497	Acacia leiocalyx	Early-flowering Black Wattle	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2498	Acacia leiocalyx	Early-flowering Black Wattle	130	60	143	5	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2499	Acacia leiocalyx	Early-flowering Black Wattle	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2500	Acacia leiocalyx	Early-flowering Black Wattle	100	80	128	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2501	Acacia leiocalyx	Early-flowering Black Wattle	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2502	Acacia leiocalyx	Early-flowering Black Wattle	140		140	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2503	Acacia leiocalyx	Early-flowering Black Wattle	100	90	135	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2504	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2505	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2506	Acacia leiocalyx	Early-flowering Black Wattle	110		110	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2507	Acacia leiocalyx	Early-flowering Black Wattle	140		140	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2508	Corymbia citriodora	Spotted Gum	310		310	24	13	3.7	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2509	Corymbia citriodora	Spotted Gum	300		300	16	11	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2510	Eucalyptus siderophloia	Grey Ironbark	300		300	24	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2511	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	21	11	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2512	Corymbia citriodora	Spotted Gum	290		290	17	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2513	Corymbia citriodora	Spotted Gum	230		230	21	10	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2514	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	19	10	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2515	Eucalyptus siderophloia	Grey Ironbark	240		240	17	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2516	Corymbia citriodora	Spotted Gum	270		270	18	9	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2517	Corymbia citriodora	Spotted Gum	250		250	14	5	3.0	1.8	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2518	Alphitonia excelsa	Soap Tree	100		100	4	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2519	Eucalyptus tereticornis	Forest Red Gum	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2520	Eucalyptus tereticornis	Forest Red Gum	100	80	128	5	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2521	Corymbia citriodora	Spotted Gum	280		280	17	10	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2522	Angophora leiocarpa	Smooth-barked Apple	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2523	Acacia concurrens	Black Wattle	220		220	7	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2524	Acacia concurrens	Black Wattle	250		250	6	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2525	Eucalyptus tereticornis	Forest Red Gum	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2526	Acacia concurrens	Black Wattle	170		170	6	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2527	Corymbia citriodora	Spotted Gum	300		300	17	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2528	Eucalyptus tereticornis	Forest Red Gum	520		520	25	15	6.2	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
2529	Eucalyptus tereticornis	Forest Red Gum	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2530	Corymbia citriodora	Spotted Gum	270		270	17	10	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2531	Corymbia citriodora	Spotted Gum	270		270	23	12	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2532	Eucalyptus carnea	Thick-leaved Mahogany	160	150	219	15	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2533	Eucalyptus carnea	Thick-leaved Mahogany	220	150	266	14	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2534	Eucalyptus tereticornis	Forest Red Gum	140		140	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2535	Eucalyptus carnea	Thick-leaved Mahogany	210		210	14	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2536	Eucalyptus carnea	Thick-leaved Mahogany	230	130	264	14	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2537	Eucalyptus carnea	Thick-leaved Mahogany	230		230	13	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2538	DEAD/STAG		180		180	13	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2539	DEAD/STAG		140		140	7	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2540	DEAD/STAG		230		230	17	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2541	DEAD/STAG		100		100	5	3	2.0	1.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2542	DEAD/STAG		260		260	18	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2543	Eucalyptus siderophloia	Grey Ironbark	270		270	10	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2544	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	25	15	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2545	Lophostemon suaveolens	Swamp Box	220		220	9	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2546	Corymbia citriodora	Spotted Gum	450		450	28	15	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2547	Acacia concurrens	Black Wattle	120		120	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2548	Acacia concurrens	Black Wattle	120		120	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2549	Acacia concurrens	Black Wattle	120		120	4	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2550	Acacia leiocalyx	Early-flowering Black Wattle	130	110, 100	197	5	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2551	Acacia concurrens	Black Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2552	Acacia concurrens	Black Wattle	180		180	6	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2553	Acacia concurrens	Black Wattle	160	140	213	5	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2554	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	21	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2555	Eucalyptus tereticornis	Forest Red Gum	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2556	Acacia concurrens	Black Wattle	180		180	6	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2557	Eucalyptus seeana	Narrow-leaved Red Gum	450		450	18	11	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2558	Eucalyptus crebra	Narrow-leaved Ironbark	390		390	18	10	4.7	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2559	Corymbia citriodora	Spotted Gum	130		130	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2560	Acacia concurrens	Black Wattle	160		160	6	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2561	Acacia concurrens	Black Wattle	140		140	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2562	Acacia leiocalyx	Early-flowering Black Wattle	130		130	5	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2563	Eucalyptus crebra	Narrow-leaved Ironbark	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2564	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	13	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2565	Corymbia citriodora	Spotted Gum	130		130	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2566	Acacia concurrens	Black Wattle	150		150	6	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2567	Corymbia citriodora	Spotted Gum	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2568	Acacia concurrens	Black Wattle	130		130	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2569	Corymbia citriodora	Spotted Gum	70		70	5	2	2.0	1.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2570	Corymbia citriodora	Spotted Gum	80		80	5	2	2.0	1.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2571	Acacia leiocalyx	Early-flowering Black Wattle	100	70	122	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2572	Alphitonia excelsa	Soap Tree	140		140	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2573	Alphitonia excelsa	Soap Tree	120		120	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2574	Angophora subvelutina	Broad-leaved Apple	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2575	Angophora subvelutina	Broad-leaved Apple	290		290	16	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2576	Angophora subvelutina	Broad-leaved Apple	260		260	16	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2577	Angophora subvelutina	Broad-leaved Apple	400		400	17	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2578	Eucalyptus seeana	Narrow-leaved Red Gum	430		430	26	16	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2579	Lophostemon suaveolens	Swamp Box	120		120	16	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2580	Aphananthe philippinensis	Native Elm	540		540	20	14	6.5	2.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2581	Angophora subvelutina	Broad-leaved Apple	430		430	21	11	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2582	Eucalyptus tereticornis	Forest Red Gum	190		190	17	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2583	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2584	Lophostemon suaveolens	Swamp Box	270		270	16	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2585	Lophostemon suaveolens	Swamp Box	380		380	20	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2586	Corymbia tessellaris	Moreton Bay Ash	380		380	22	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2587	Corymbia tessellaris	Moreton Bay Ash	420		420	22	12	5.0	2.3	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2588	Aphananthe philippinensis	Native Elm	470		470	17	13	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2589	Lophostemon suaveolens	Swamp Box	290		290	17	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2590	Aphananthe philippinensis	Native Elm	370		370	16	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2591	Corymbia tessellaris	Moreton Bay Ash	660		660	29	17	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2592	Aphananthe philippinensis	Native Elm	380		380	16	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2593	Aphananthe philippinensis	Native Elm	200		200	14	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2594	Allocasuarina littoralis	Black She Oak	340		340	18	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2595	Eucalyptus tereticornis	Forest Red Gum	360		360	19	11	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2596	Eucalyptus tereticornis	Forest Red Gum	250		250	17	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2597	Lophostemon suaveolens	Swamp Box	300		300	17	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2598	Alphitonia excelsa	Soap Tree	300		300	14	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2599	Eucalyptus tereticornis	Forest Red Gum	270		270	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2600	Lophostemon suaveolens	Swamp Box	330		330	16	9	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2601	Acacia disparrima	Hickory Wattle	160	110	194	8	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2602	Acacia disparrima	Hickory Wattle	170	160, 80	247	10	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2603	Acacia disparrima	Hickory Wattle	190		190	13	7	2.3	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2604	Corymbia tessellaris	Moreton Bay Ash	510		510	27	17	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2605	Eucalyptus tereticornis	Forest Red Gum	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2606	Acacia disparrima	Hickory Wattle	180		180	10	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2607	Eucalyptus tereticornis	Forest Red Gum	800		800	26	16	9.6	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2608	Corymbia tessellaris	Moreton Bay Ash	160	90	184	16	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2609	Acacia disparrima	Hickory Wattle	110		110	13	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2610	Angophora subvelutina	Broad-leaved Apple	120		120	13	2	2.0	1.4	Regular	-	-	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2611	Melaleuca viminalis	Weeping Bottlebrush	340	160, 180	417	14	9	5.0	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2612	Melaleuca viminalis	Weeping Bottlebrush	130	60	143	5	5	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2613	Melaleuca viminalis	Weeping Bottlebrush	160	90, 60	193	7	6	2.3	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2614	Melaleuca viminalis	Weeping Bottlebrush	110		110	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2615	Melaleuca viminalis	Weeping Bottlebrush	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2616	Melaleuca viminalis	Weeping Bottlebrush	150	120, 80, 80	223	8	6	2.7	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2617	Melaleuca viminalis	Weeping Bottlebrush	180	140	228	6	4	2.7	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2618	Melaleuca viminalis	Weeping Bottlebrush	150	140	205	7	5	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2619	Casuarina cunninghamiana	River Sheoak	290		290	17	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2620	Casuarina cunninghamiana	River Sheoak	170		170	16	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2621	Acacia disparrima	Hickory Wattle	160		160	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2622	Alphitonia excelsa	Soap Tree	170		170	14	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2623	Casuarina cunninghamiana	River Sheoak	400		400	24	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2624	Melaleuca viminalis	Weeping Bottlebrush	150	130	198	7	4	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2625	Casuarina cunninghamiana	River Sheoak	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2626	Melaleuca viminalis	Weeping Bottlebrush	250	250, 250	433	7	5	5.2	2.3	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2627	Casuarina cunninghamiana	River Sheoak	480		480	16	9	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2628	Lophostemon suaveolens	Swamp Box	120		120	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2629	Corymbia tessellaris	Moreton Bay Ash	120		120	16	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2630	Casuarina cunninghamiana	River Sheoak	260		260	17	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2631	Casuarina cunninghamiana	River Sheoak	360	260, 130	463	18	11	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2632	Casuarina cunninghamiana	River Sheoak	450		450	20	11	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2633	Eucalyptus tereticornis	Forest Red Gum	690		690	27	15	8.3	2.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
2634	Eucalyptus tereticornis	Forest Red Gum	380		380	26	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2635	Eucalyptus tereticornis	Forest Red Gum	320		320	23	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2636	Corymbia tessellaris	Moreton Bay Ash	240		240	14	5	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2637	Corymbia tessellaris	Moreton Bay Ash	240		240	22	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2638	Corymbia tessellaris	Moreton Bay Ash	140		140	13	8	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2639	Eucalyptus tereticornis	Forest Red Gum	350		350	20	12	4.2	2.1	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
2640	Eucalyptus tereticornis	Forest Red Gum	140		140	13	5	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2641	Eucalyptus tereticornis	Forest Red Gum	500		500	27	15	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2642	Alphitonia excelsa	Soap Tree	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2643	Acacia disparrima	Hickory Wattle	200		200	12	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2644	Corymbia tessellaris	Moreton Bay Ash	440		440	24	12	5.3	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2645	Acacia disparrima	Hickory Wattle	290		290	16	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2646	Angophora subvelutina	Broad-leaved Apple	540		540	22	13	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2647	Corymbia citriodora	Spotted Gum	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2648	Corymbia citriodora	Spotted Gum	380		380	18	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2649	Acacia concurrens	Black Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Approved to remove
2650	Eucalyptus moluccana	Gum Topped Box	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2651	Acacia disparrima	Hickory Wattle	150		150	5	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2652	Corymbia citriodora	Spotted Gum	170		170	14	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2653	Angophora leiocarpa	Smooth-barked Apple	100		100	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2654	Eucalyptus moluccana	Gum Topped Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2655	Corymbia intermedia	Pink Bloodwood	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2656	Eucalyptus moluccana	Gum Topped Box	700		700	24	12	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
2657	Corymbia citriodora	Spotted Gum	160		160	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2658	Lophostemon suaveolens	Swamp Box	180		180	13	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2659	Corymbia citriodora	Spotted Gum	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2660	Eucalyptus seeana	Narrow-leaved Red Gum	200		200	13	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2661	Lophostemon suaveolens	Swamp Box	280		280	16	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2662	Lophostemon suaveolens	Swamp Box	180		180	13	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2663	Corymbia citriodora	Spotted Gum	320		320	23	12	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2664	Lophostemon suaveolens	Swamp Box	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2665	Corymbia citriodora	Spotted Gum	110		110	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2666	Lophostemon suaveolens	Swamp Box	100		100	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2667	Eucalyptus seeana	Narrow-leaved Red Gum	450		450	23	13	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2668	Corymbia citriodora	Spotted Gum	270		270	22	12	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2669	Corymbia citriodora	Spotted Gum	190		190	16	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2670	Corymbia tessellaris	Moreton Bay Ash	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2671	Corymbia citriodora	Spotted Gum	120		120	14	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2672	Corymbia citriodora	Spotted Gum	130		130	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
2673	Corymbia citriodora	Spotted Gum	270		270	21	11	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2674	Corymbia citriodora	Spotted Gum	340		340	18	11	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2675	Eucalyptus seeana	Narrow-leaved Red Gum	270		270	18	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2676	Angophora subvelutina	Broad-leaved Apple	280		280	21	11	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2677	Angophora subvelutina	Broad-leaved Apple	150		150	15	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2678	Angophora subvelutina	Broad-leaved Apple	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2679	Angophora subvelutina	Broad-leaved Apple	350		350	21	13	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2680	Angophora subvelutina	Broad-leaved Apple	140		140	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2681	Acacia disparrima	Hickory Wattle	150		150	11	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2682	Angophora subvelutina	Broad-leaved Apple	380		380	21	11	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2683	Angophora subvelutina	Broad-leaved Apple	130		130	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2684	Corymbia tessellaris	Moreton Bay Ash	200		200	10	3	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2685	Alphitonia excelsa	Soap Tree	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2686	Casuarina cunninghamiana	River Sheoak	310		310	15	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2687	Angophora subvelutina	Broad-leaved Apple	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2688	Eucalyptus seeana	Narrow-leaved Red Gum	680		680	26	16	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2689	Melaleuca viminalis	Weeping Bottlebrush	120	100	156	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2690	Melaleuca viminalis	Weeping Bottlebrush	180		180	6	4	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2691	Melaleuca viminalis	Weeping Bottlebrush	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2692	Casuarina cunninghamiana	River Sheoak	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2693	Acacia concurrens	Black Wattle	100		100	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2694	Lophostemon suaveolens	Swamp Box	120		120	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2695	Alphitonia excelsa	Soap Tree	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2696	Angophora subvelutina	Broad-leaved Apple	230		230	12	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2697	Angophora subvelutina	Broad-leaved Apple	300		300	18	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2698	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2699	Acacia disparrima	Hickory Wattle	150		150	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2700	Melaleuca viminalis	Weeping Bottlebrush	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2701	Angophora subvelutina	Broad-leaved Apple	260		260	17	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2702	Casuarina cunninghamiana	River Sheoak	240		240	17	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2703	Melaleuca viminalis	Weeping Bottlebrush	110	100, 100, 100	205	6	6	2.5	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2704	Casuarina cunninghamiana	River Sheoak	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2705	Casuarina cunninghamiana	River Sheoak	180		180	14	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2706	Casuarina cunninghamiana	River Sheoak	130		130	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2707	Casuarina cunninghamiana	River Sheoak	140		140	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2708	Casuarina cunninghamiana	River Sheoak	110		110	11	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2709	Casuarina cunninghamiana	River Sheoak	130		130	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2710	Casuarina cunninghamiana	River Sheoak	190		190	11	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2711	Acacia disparrima	Hickory Wattle	190	170	255	11	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2712	Casuarina cunninghamiana	River Sheoak	170		170	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2713	Casuarina cunninghamiana	River Sheoak	260		260	13	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2714	Casuarina cunninghamiana	River Sheoak	430		430	18	10	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2715	Casuarina cunninghamiana	River Sheoak	240		240	13	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2716	Acacia disparrima	Hickory Wattle	200		200	15	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2717	Acacia disparrima	Hickory Wattle	200		200	15	7	2.4	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2718	Angophora subvelutina	Broad-leaved Apple	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2719	Acacia disparrima	Hickory Wattle	190	190	269	13	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2720	Acacia concurrens	Black Wattle	100		100	10	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2721	Acacia disparrima	Hickory Wattle	130	120	177	10	6	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2722	Acacia disparrima	Hickory Wattle	140		140	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2723	Acacia disparrima	Hickory Wattle	220		220	10	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2724	Acacia concurrens	Black Wattle	130		130	10	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2725	Casuarina cunninghamiana	River Sheoak	220	210	304	16	7	3.6	2.0	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2726	Casuarina cunninghamiana	River Sheoak	350		350	22	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2727	Eucalyptus seeana	Narrow-leaved Red Gum	890		890	25	15	10.7	3.2	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2728	Alphitonia excelsa	Soap Tree	270		270	10	7	3.2	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2729	Melaleuca viminalis	Weeping Bottlebrush	260		260	6	3	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2730	Melaleuca viminalis	Weeping Bottlebrush	120	110	163	5	5	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2731	Casuarina cunninghamiana	River Sheoak	150		150	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2732	Casuarina cunninghamiana	River Sheoak	260		260	15	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2733	Casuarina cunninghamiana	River Sheoak	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2734	Melaleuca viminalis	Weeping Bottlebrush	150	140	205	6	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2735	Corymbia tessellaris	Moreton Bay Ash	140		140	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2736	Casuarina cunninghamiana	River Sheoak	170		170	18	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2737	Casuarina cunninghamiana	River Sheoak	400		400	22	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2738	Casuarina cunninghamiana	River Sheoak	400		400	20	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2739	Lophostemon suaveolens	Swamp Box	180		180	12	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2740	Casuarina cunninghamiana	River Sheoak	140		140	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2741	Melaleuca viminalis	Weeping Bottlebrush	140		140	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2742	Casuarina cunninghamiana	River Sheoak	390		390	21	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2743	Casuarina cunninghamiana	River Sheoak	160		160	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2744	Melaleuca viminalis	Weeping Bottlebrush	160		160	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2745	Melaleuca viminalis	Weeping Bottlebrush	120	120	170	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2746	Alphitonia excelsa	Soap Tree	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2747	Eucalyptus seeana	Narrow-leaved Red Gum	410	400, 400	699	22	13	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2748	Casuarina cunninghamiana	River Sheoak	180	150	234	11	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2749	Casuarina cunninghamiana	River Sheoak	180		180	10	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2750	Casuarina cunninghamiana	River Sheoak	170		170	12	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2751	Melaleuca viminalis	Weeping Bottlebrush	120	110	163	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2752	Melaleuca viminalis	Weeping Bottlebrush	120	120	170	8	5	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
2753	Acacia concurrens	Black Wattle	100		100	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2754	Acacia disparrima	Hickory Wattle	220	160	272	8	5	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2755	Acacia disparrima	Hickory Wattle	180	160	241	10	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2756	Alphitonia excelsa	Soap Tree	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2757	Acacia disparrima	Hickory Wattle	190		190	8	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2758	Angophora subvelutina	Broad-leaved Apple	260		260	15	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2759	Lophostemon suaveolens	Swamp Box	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2760	Lophostemon suaveolens	Swamp Box	170		170	11	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2761	Lophostemon suaveolens	Swamp Box	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2762	Lophostemon suaveolens	Swamp Box	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2763	Lophostemon suaveolens	Swamp Box	170	140	220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2764	Alphitonia excelsa	Soap Tree	130		130	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2765	Lophostemon suaveolens	Swamp Box	130		130	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2766	Lophostemon suaveolens	Swamp Box	180		180	11	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2767	Eucalyptus tereticornis	Forest Red Gum	200		200	16	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2768	Eucalyptus seeana	Narrow-leaved Red Gum	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2769	Alphitonia excelsa	Soap Tree	150		150	11	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2770	Corymbia citriodora	Spotted Gum	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2771	Corymbia citriodora	Spotted Gum	140	135	194	10	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2772	Eucalyptus tereticornis	Forest Red Gum	150	130	198	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2773	Corymbia citriodora	Spotted Gum	130	70	148	11	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2774	Corymbia citriodora	Spotted Gum	170	60	180	11	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2775	Corymbia citriodora	Spotted Gum	115		115	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2776	Eucalyptus crebra	Narrow-leaved Ironbark	215		215	13	5	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2777	Eucalyptus crebra	Narrow-leaved Ironbark	530		530	23	12	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2778	Corymbia citriodora	Spotted Gum	165	125	207	12	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2779	Eucalyptus tereticornis	Forest Red Gum	100	80, 90	157	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2780	Eucalyptus tereticornis	Forest Red Gum	100	90, 90	162	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2781	Corymbia citriodora	Spotted Gum	145	140, 130	240	9	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2782	Corymbia citriodora	Spotted Gum	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2783	Acacia leiocalyx	Early-flowering Black Wattle	150	140	205	7	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2784	Eucalyptus tereticornis	Forest Red Gum	540		540	26	14	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2785	Eucalyptus tereticornis	Forest Red Gum	650		650	28	12	7.8	2.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2786	Eucalyptus tereticornis	Forest Red Gum	520		520	28	12	6.2	2.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2787	Eucalyptus tereticornis	Forest Red Gum	690		690	29	14	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2788	Corymbia intermedia	Pink Bloodwood	600		600	28	14	7.2	2.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2789	Eucalyptus tereticornis	Forest Red Gum	600		600	24	4	7.2	2.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
2790	Eucalyptus tereticornis	Forest Red Gum	470		470	20	12	5.6	2.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
2791	Eucalyptus tereticornis	Forest Red Gum	280		280	18	11	3.4	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2792	Corymbia citriodora	Spotted Gum	240		240	17	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2793	Eucalyptus tereticornis	Forest Red Gum	290		290	16	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2794	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	17	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2795	Eucalyptus tereticornis	Forest Red Gum	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2796	Corymbia citriodora	Spotted Gum	320		320	19	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2797	Eucalyptus tereticornis	Forest Red Gum	380		380	15	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2798	Eucalyptus tereticornis	Forest Red Gum	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2799	Eucalyptus tereticornis	Forest Red Gum	280		280	15	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2800	Eucalyptus moluccana	Gum Topped Box	500		500	27	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2801	Corymbia citriodora	Spotted Gum	345		345	27	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2802	Acacia disparrima	Hickory Wattle	140		140	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2803	Alphitonia excelsa	Soap Tree	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2804	Corymbia citriodora	Spotted Gum	230		230	17	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2805	Eucalyptus moluccana	Gum Topped Box	270		270	24	7	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2806	Alphitonia excelsa	Soap Tree	130		130	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2807	Alphitonia excelsa	Soap Tree	220		220	11	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2808	Alphitonia excelsa	Soap Tree	115		115	9	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2809	Acacia concurrens	Black Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2810	Alphitonia excelsa	Soap Tree	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2811	Acacia concurrens	Black Wattle	165		165	8	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2812	Eucalyptus crebra	Narrow-leaved Ironbark	255		255	19	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2813	Acacia disparrima	Hickory Wattle	105		105	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2814	Corymbia citriodora	Spotted Gum	420		420	24	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2815	Corymbia citriodora	Spotted Gum	170		170	18	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2816	Corymbia citriodora	Spotted Gum	190		190	18	7	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2817	Eucalyptus tereticornis	Forest Red Gum	125		125	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2818	Corymbia citriodora	Spotted Gum	130		130	15	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2819	Allocasuarina littoralis	Black She Oak	165		165	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2820	Corymbia citriodora	Spotted Gum	260		260	19	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2821	Corymbia citriodora	Spotted Gum	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2822	Corymbia citriodora	Spotted Gum	285		285	21	9	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2823	Acacia concurrens	Black Wattle	115		115	8	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2824	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	18	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2825	Corymbia citriodora	Spotted Gum	165		165	16	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2826	Corymbia citriodora	Spotted Gum	165		165	12	7	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2827	Corymbia citriodora	Spotted Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2828	Alphitonia excelsa	Soap Tree	145		145	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2829	Corymbia citriodora	Spotted Gum	125		125	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2830	Acacia concurrens	Black Wattle	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2831	Corymbia citriodora	Spotted Gum	275		275	17	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2832	Eucalyptus crebra	Narrow-leaved Ironbark	205		205	16	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2833	Acacia concurrens	Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2834	Corymbia citriodora	Spotted Gum	370		370	22	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2835	Corymbia citriodora	Spotted Gum	185		185	15	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2836	Corymbia citriodora	Spotted Gum	110		110	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2837	Corymbia citriodora	Spotted Gum	100		100	11	4	2.0	1.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2838	DEAD/STAG		295		295	19	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2839	Alphitonia excelsa	Soap Tree	130		130	8	3	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2840	Eucalyptus tereticornis	Forest Red Gum	285		285	17	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2841	Corymbia citriodora	Spotted Gum	325		325	22	10	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2842	Acacia disparrima	Hickory Wattle	160		160	6	3	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2843	DEAD/STAG		285		285	21	7	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2844	Corymbia citriodora	Spotted Gum	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2845	Acacia disparrima	Hickory Wattle	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2846	Acacia concurrens	Black Wattle	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2847	Eucalyptus crebra	Narrow-leaved Ironbark	285		285	19	7	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2848	Corymbia citriodora	Spotted Gum	120		120	14	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2849	Acacia disparrima	Hickory Wattle	130	130	184	8	3	2.2	1.6	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2850	Eucalyptus tereticornis	Forest Red Gum	285		285	19	7	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2851	Alphitonia excelsa	Soap Tree	175		175	8	4	2.1	1.6	Regular	-	Thinning	Die-back	-	-	Poor	Minor	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Approved to remove
2852	Corymbia citriodora	Spotted Gum	235		235	23	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2853	Corymbia citriodora	Spotted Gum	210	130	247	17	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2854	Eucalyptus tereticornis	Forest Red Gum	140		140	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2855	Eucalyptus crebra	Narrow-leaved Ironbark	285		285	19	9	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2856	Eucalyptus crebra	Narrow-leaved Ironbark	155		155	16	9	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2857	Corymbia citriodora	Spotted Gum	320		320	22	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2858	Corymbia citriodora	Spotted Gum	380		380	23	7	4.6	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2859	Acacia disparrima	Hickory Wattle	180		180	9	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2860	Corymbia citriodora	Spotted Gum	415		415	21	12	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2861	Corymbia citriodora	Spotted Gum	195		195	15	6	2.3	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2862	Eucalyptus tereticornis	Forest Red Gum	260		260	22	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2863	Eucalyptus tereticornis	Forest Red Gum	150		150	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2864	Corymbia citriodora	Spotted Gum	295		295	26	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2865	Corymbia citriodora	Spotted Gum	390		390	23	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2866	Corymbia citriodora	Spotted Gum	275		275	21	9	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2867	Corymbia citriodora	Spotted Gum	590		590	27	14	7.1	2.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2868	Eucalyptus crebra	Narrow-leaved Ironbark	245		245	15	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2869	Corymbia citriodora	Spotted Gum	295		295	15	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2870	Acacia concurrens	Black Wattle	120	120, 80	188	7	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2871	Acacia concurrens	Black Wattle	125		125	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2872	Acacia concurrens	Black Wattle	125		125	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2873	Acacia concurrens	Black Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2874	Acacia concurrens	Black Wattle	165		165	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2875	Acacia concurrens	Black Wattle	130	85	155	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2876	Acacia concurrens	Black Wattle	160	160	226	7	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2877	Acacia concurrens	Black Wattle	125	125	177	7	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2878	Acacia concurrens	Black Wattle	155	150	216	8	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2879	Acacia concurrens	Black Wattle	155		155	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2880	Acacia concurrens	Black Wattle	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2881	Acacia concurrens	Black Wattle	190		190	8	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2882	Acacia concurrens	Black Wattle	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2883	Acacia concurrens	Black Wattle	140		140	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2884	Acacia concurrens	Black Wattle	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2885	Acacia concurrens	Black Wattle	165	145	220	8	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2886	Corymbia citriodora	Spotted Gum	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2887	Corymbia citriodora	Spotted Gum	285		285	21	6	3.4	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2888	Corymbia citriodora	Spotted Gum	335		335	22	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2889	Eucalyptus crebra	Narrow-leaved Ironbark	380		380	21	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Remove
2890	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	21	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2891	Acacia concurrens	Black Wattle	240		240	8	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2892	Corymbia citriodora	Spotted Gum	165		165	11	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2893	Eucalyptus crebra	Narrow-leaved Ironbark	380		380	17	7	4.6	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2894	Acacia concurrens	Black Wattle	150	140, 100, 20	229	6	6	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2895	Acacia concurrens	Black Wattle	150	120, 100, 120	248	5	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2896	Corymbia citriodora	Spotted Gum	285		285	18	8	3.4	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
2897	Corymbia citriodora	Spotted Gum	245		245	17	8	2.9	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2898	Corymbia citriodora	Spotted Gum	310		310	19	6	3.7	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2899	Corymbia citriodora	Spotted Gum	310		310	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2900	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	17	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2901	Corymbia citriodora	Spotted Gum	295		295	16	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2902	Corymbia citriodora	Spotted Gum	290		290	17	5	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2903	Corymbia citriodora	Spotted Gum	155		155	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2904	Corymbia citriodora	Spotted Gum	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2905	Corymbia citriodora	Spotted Gum	170		170	11	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2906	Corymbia citriodora	Spotted Gum	370		370	21	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2907	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	17	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2908	Eucalyptus tereticornis	Forest Red Gum	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2909	Acacia concurrens	Black Wattle	185		185	7	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2910	Corymbia citriodora	Spotted Gum	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2911	Corymbia citriodora	Spotted Gum	500		500	24	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2912	Corymbia citriodora	Spotted Gum	365		365	21	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2913	Angophora leiocarpa	Smooth-barked Apple	285		285	17	8	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2914	Eucalyptus tereticornis	Forest Red Gum	145		145	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2915	Eucalyptus carnea	Thick-leaved Mahogany	320		320	15	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2916	Eucalyptus carnea	Thick-leaved Mahogany	240	125	271	17	6	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2917	Eucalyptus carnea	Thick-leaved Mahogany	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2918	Eucalyptus carnea	Thick-leaved Mahogany	280	185	336	18	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2919	Eucalyptus carnea	Thick-leaved Mahogany	330	240	408	18	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2920	Eucalyptus carnea	Thick-leaved Mahogany	200	170	262	18	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2921	DEAD/STAG		255		255	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2922	Eucalyptus carnea	Thick-leaved Mahogany	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2923	Eucalyptus carnea	Thick-leaved Mahogany	265		265	18	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2924	Eucalyptus tereticornis	Forest Red Gum	175		175	17	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2925	Eucalyptus carnea	Thick-leaved Mahogany	165		165	16	6	2.0	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2926	DEAD/STAG		230		230	9	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2927	Corymbia intermedia	Pink Bloodwood	270		270	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2928	Eucalyptus tereticornis	Forest Red Gum	290		290	18	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2929	Corymbia intermedia	Pink Bloodwood	285	125	311	17	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2930	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	13	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2931	Eucalyptus tereticornis	Forest Red Gum	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
2932	Corymbia citriodora	Spotted Gum	660		660	22	14	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2933	Acacia concurrens	Black Wattle	190		190	7	4	2.3	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2934	Acacia concurrens	Black Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2935	Acacia concurrens	Black Wattle	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2936	Acacia concurrens	Black Wattle	165		165	7	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2937	Acacia concurrens	Black Wattle	200		200	7	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2938	Eucalyptus crebra	Narrow-leaved Ironbark	125		125	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2939	Acacia concurrens	Black Wattle	120	100	156	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2940	Ficus obliqua	Small-leaved Fig	520		520	10	10	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2941	Eucalyptus tereticornis	Forest Red Gum	610		610	25	12	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2942	Alphitonia excelsa	Soap Tree	140		140	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2943	Acacia concurrens	Black Wattle	180		180	7	4	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2944	Corymbia citriodora	Spotted Gum	490		490	24	11	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2945	Acacia concurrens	Black Wattle	145		145	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2946	Acacia concurrens	Black Wattle	145		145	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2947	Corymbia citriodora	Spotted Gum	235		235	16	4	2.8	1.8	One-sided	-	Thinning	Die-back	-	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2948	Eucalyptus tereticornis	Forest Red Gum	490		490	22	9	5.9	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2949	Acacia concurrens	Black Wattle	220		220	7	5	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Typical	Minor	-	-	-	Poor	-	-	-	-	-	-		Retain
2950	Eucalyptus tereticornis	Forest Red Gum	320		320	21	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2951	Acacia concurrens	Black Wattle	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2952	Acacia disparrima	Hickory Wattle	180		180	5	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2953	Eucalyptus tereticornis	Forest Red Gum	385		385	19	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
2954	Acacia concurrens	Black Wattle	150		150	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2955	Acacia concurrens	Black Wattle	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2956	Acacia disparrima	Hickory Wattle	200		200	7	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2957	DEAD/STAG		360		360	8	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2958	Acacia concurrens	Black Wattle	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2959	Acacia concurrens	Black Wattle	125		125	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2960	Acacia concurrens	Black Wattle	145		145	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2961	Acacia concurrens	Black Wattle	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2962	Angophora subvelutina	Broad-leaved Apple	420		420	21	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2963	Alphitonia excelsa	Soap Tree	115		115	11	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2964	Alphitonia excelsa	Soap Tree	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2965	Lophostemon suaveolens	Swamp Box	245		245	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2966	Lophostemon suaveolens	Swamp Box	260		260	14	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
2967	Acacia disparrima	Hickory Wattle	215		215	13	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2968	Casuarina cunninghamiana	River Sheoak	265		265	21	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2969	Lophostemon suaveolens	Swamp Box	265		265	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2970	Lophostemon suaveolens	Swamp Box	275		275	15	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2971	Angophora subvelutina	Broad-leaved Apple	200		200	17	6	2.4	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
2972	Lophostemon suaveolens	Swamp Box	255		255	16	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2973	Lophostemon suaveolens	Swamp Box	130		130	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2974	Lophostemon suaveolens	Swamp Box	270		270	16	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
2975	Aphananthe philippinensis	Native Elm	320	260	412	15	8	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2976	Alphitonia excelsa	Soap Tree	430		430	17	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	nest box	Retain
2977	Lophostemon suaveolens	Swamp Box	155		155	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2978	Lophostemon suaveolens	Swamp Box	245		245	13	4	2.9	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2979	Ficus coronata	Sandpaper Fig	145	80	166	7	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2980	Corymbia tessellaris	Moreton Bay Ash	390		390	23	9	4.7	2.2	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2981	Acacia disparrima	Hickory Wattle	125		125	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2982	Eucalyptus tereticornis	Forest Red Gum	335		335	28	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2983	Lophostemon suaveolens	Swamp Box	105		105	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2984	Alphitonia excelsa	Soap Tree	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2985	Eucalyptus tereticornis	Forest Red Gum	400		400	27	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2986	Lophostemon suaveolens	Swamp Box	250		250	11	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2987	Acacia disparrima	Hickory Wattle	150		150	6	5	2.0	1.5	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2988	Acacia disparrima	Hickory Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2989	Lophostemon suaveolens	Swamp Box	250	220	333	14	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2990	Eucalyptus tereticornis	Forest Red Gum	385		385	26	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2991	Acacia disparrima	Hickory Wattle	125		125	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2992	Acacia disparrima	Hickory Wattle	190		190	10	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2993	Alphitonia excelsa	Soap Tree	130	115	174	11	5	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2994	Alphitonia excelsa	Soap Tree	165		165	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2995	Alphitonia excelsa	Soap Tree	155		155	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2996	Acacia disparrima	Hickory Wattle	155		155	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2997	Alphitonia excelsa	Soap Tree	185		185	11	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2998	Angophora subvelutina	Broad-leaved Apple	210		210	15	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
2999	Acacia disparrima	Hickory Wattle	280	255, 165	413	11	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3000	Lophostemon suaveolens	Swamp Box	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3001	Alphitonia excelsa	Soap Tree	180		180	12	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3002	Angophora subvelutina	Broad-leaved Apple	360		360	22	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3003	Acacia disparrima	Hickory Wattle	190		190	6	9	2.3	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3004	Casuarina cunninghamiana	River Sheoak	395		395	22	10	4.7	2.2	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
3005	Lophostemon suaveolens	Swamp Box	265		265	15	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
3006	Lophostemon suaveolens	Swamp Box	210		210	11	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
3007	Melaleuca linariifolia	Snow-in-summer	280		280	10	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
3008	Angophora subvelutina	Broad-leaved Apple	340		340	19	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Retain
3009	Angophora subvelutina	Broad-leaved Apple	240		240	12	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3010	Angophora subvelutina	Broad-leaved Apple	320		320	21	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3011	Casuarina cunninghamiana	River Sheoak	510		510	24	11	6.1	2.5	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3012	Angophora subvelutina	Broad-leaved Apple	390		390	23	11	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3013	Angophora subvelutina	Broad-leaved Apple	220		220	13	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3014	Lophostemon suaveolens	Swamp Box	220	165	275	14	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3015	Corymbia intermedia	Pink Bloodwood	300	260	397	19	9	4.8	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3016	Lophostemon suaveolens	Swamp Box	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3017	Alphitonia excelsa	Soap Tree	160		160	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3018	Angophora subvelutina	Broad-leaved Apple	130		130	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3019	Alphitonia excelsa	Soap Tree	230		230	13	7	2.8	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3020	Angophora subvelutina	Broad-leaved Apple	370		370	22	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3021	Angophora subvelutina	Broad-leaved Apple	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3022	Angophora subvelutina	Broad-leaved Apple	420		420	23	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3023	Corymbia tessellaris	Moreton Bay Ash	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3024	Alphitonia excelsa	Soap Tree	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3025	Melaleuca viminalis	Weeping Bottlebrush	150	100	180	4	7	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3026	Melaleuca viminalis	Weeping Bottlebrush	155		155	5	6	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3027	Eucalyptus tereticornis	Forest Red Gum	200		200	17	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3028	Melaleuca viminalis	Weeping Bottlebrush	165		165	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3029	Eucalyptus tereticornis	Forest Red Gum	460		460	22	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3030	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3031	Casuarina cunninghamiana	River Sheoak	350		350	18	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3032	Casuarina cunninghamiana	River Sheoak	350		350	21	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3033	Corymbia intermedia	Pink Bloodwood	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3034	Casuarina cunninghamiana	River Sheoak	190		190	15	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3035	Acacia disparrima	Hickory Wattle	150		150	9	3	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3036	Angophora subvelutina	Broad-leaved Apple	630		630	26	14	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3037	Eucalyptus tereticornis	Forest Red Gum	540		540	26	12	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3038	Casuarina cunninghamiana	River Sheoak	320		320	21	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3039	Casuarina cunninghamiana	River Sheoak	225		225	19	7	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3040	Casuarina cunninghamiana	River Sheoak	190		190	16	8	2.3	1.6	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3041	Casuarina cunninghamiana	River Sheoak	190		190	13	4	2.3	1.6	One-sided	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3042	Acacia concurrens	Black Wattle	125		125	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3043	Corymbia intermedia	Pink Bloodwood	170		170	12	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3044	Lophostemon suaveolens	Swamp Box	190	180	262	12	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3045	Corymbia tessellaris	Moreton Bay Ash	140		140	14	3	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3046	Corymbia intermedia	Pink Bloodwood	210		210	8	2	2.5	1.7	Regular	-	-	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3047	Corymbia intermedia	Pink Bloodwood	400		400	24	11	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3048	Corymbia tessellaris	Moreton Bay Ash	275		275	17	5	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3049	Eucalyptus tereticornis	Forest Red Gum	265		265	21	7	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3050	Eucalyptus tereticornis	Forest Red Gum	430		430	24	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3051	Angophora subvelutina	Broad-leaved Apple	430		430	23	12	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3052	Lophostemon suaveolens	Swamp Box	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3053	Eucalyptus tereticornis	Forest Red Gum	560		560	29	14	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3054	Lophostemon suaveolens	Swamp Box	265		265	14	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3055	Lophostemon suaveolens	Swamp Box	210		210	12	5	2.5	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3056	Lophostemon suaveolens	Swamp Box	165		165	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3057	Eucalyptus tereticornis	Forest Red Gum	300		300	22	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3058	Lophostemon suaveolens	Swamp Box	485		485	16	8	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3059	Casuarina cunninghamiana	River Sheoak	320	220, 185, 165	461	17	10	5.5	2.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3060	Casuarina cunninghamiana	River Sheoak	320		320	17	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3061	Casuarina cunninghamiana	River Sheoak	380		380	21	9	4.6	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3062	Casuarina cunninghamiana	River Sheoak	410		410	17	5	4.9	2.3	Regular	-	-	-	-	-	Typical	Minor	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
3063	Casuarina cunninghamiana	River Sheoak	720	590	931	23	16	11.2	3.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3064	Acacia leiocalyx	Early-flowering Black Wattle	185		185	13	6	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3065	Eucalyptus tereticornis	Forest Red Gum	295		295	20	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3066	Angophora subvelutina	Broad-leaved Apple	180		180	15	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3067	Acacia disparrima	Hickory Wattle	195		195	12	6	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3068	Angophora subvelutina	Broad-leaved Apple	185		185	16	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3069	Corymbia tessellaris	Moreton Bay Ash	155		155	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3070	Angophora subvelutina	Broad-leaved Apple	265		265	21	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3071	Angophora subvelutina	Broad-leaved Apple	300		300	22	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3072	Angophora subvelutina	Broad-leaved Apple	275		275	15	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3073	Angophora subvelutina	Broad-leaved Apple	245		245	16	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3074	Eucalyptus tereticornis	Forest Red Gum	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3075	Eucalyptus tereticornis	Forest Red Gum	195		195	17	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3076	Corymbia intermedia	Pink Bloodwood	125		125	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3077	Acacia concurrens	Black Wattle	165		165	11	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3078	Acacia disparrima	Hickory Wattle	170		170	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3079	Eucalyptus tereticornis	Forest Red Gum	220		220	21	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3080	Angophora subvelutina	Broad-leaved Apple	185		185	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3081	Angophora subvelutina	Broad-leaved Apple	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3082	Angophora subvelutina	Broad-leaved Apple	310		310	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3083	Acacia disparrima	Hickory Wattle	165		165	10	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3084	Eucalyptus tereticornis	Forest Red Gum	560		560	23	11	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3085	Acacia disparrima	Hickory Wattle	100		100	8	5	2.0	1.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3086	Casuarina cunninghamiana	River Sheoak	470		470	22	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3087	Acacia disparrima	Hickory Wattle	145		145	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
3088	Corymbia citriodora	Spotted Gum	520		520	32	16	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3089	Corymbia intermedia	Pink Bloodwood	170	130	214	11	3	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3090	Corymbia citriodora	Spotted Gum	195		195	11	2	2.3	1.7	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3091	Alphitonia excelsa	Soap Tree	120		120	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3092	Alphitonia excelsa	Soap Tree	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3093	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3094	Angophora leiocarpa	Smooth-barked Apple	100	90, 60	147	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3095	Eucalyptus moluccana	Gum Topped Box	320		320	21	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3096	Eucalyptus crebra	Narrow-leaved Ironbark	105		105	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3097	Alphitonia excelsa	Soap Tree	140		140	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3098	Corymbia citriodora	Spotted Gum	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3099	Corymbia citriodora	Spotted Gum	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3100	Eucalyptus tereticornis	Forest Red Gum	230		230	15	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3101	Corymbia citriodora	Spotted Gum	145		145	11	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3102	Eucalyptus tereticornis	Forest Red Gum	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3103	Allocasuarina littoralis	Black She Oak	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3104	Lophostemon suaveolens	Swamp Box	125		125	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3105	Alphitonia excelsa	Soap Tree	135		135	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3106	Corymbia citriodora	Spotted Gum	285		285	23	7	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3107	Corymbia citriodora	Spotted Gum	180		180	17	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3108	Corymbia citriodora	Spotted Gum	180		180	17	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3109	Eucalyptus moluccana	Gum Topped Box	320		320	19	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3110	Allocasuarina littoralis	Black She Oak	215		215	11	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3111	Allocasuarina littoralis	Black She Oak	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3112	Eucalyptus tereticornis	Forest Red Gum	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3113	Corymbia citriodora	Spotted Gum	130		130	16	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3114	Corymbia citriodora	Spotted Gum	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3115	Acacia concurrens	Black Wattle	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3116	Acacia disparrima	Hickory Wattle	140	85, 65	176	8	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3117	Corymbia citriodora	Spotted Gum	230		230	19	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3118	Corymbia citriodora	Spotted Gum	220		220	19	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3119	Corymbia citriodora	Spotted Gum	210		210	18	2	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3120	Corymbia citriodora	Spotted Gum	135		135	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3121	Acacia concurrens	Black Wattle	145		145	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3122	Eucalyptus tereticornis	Forest Red Gum	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3123	Melaleuca viminalis	Weeping Bottlebrush	280	270, 220, 200, 185	523	9	12	6.3	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3124	Alphitonia excelsa	Soap Tree	145		145	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3125	Angophora subvelutina	Broad-leaved Apple	105		105	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3126	Alphitonia excelsa	Soap Tree	110		110	10	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3127	Acacia concurrens	Black Wattle	130		130	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3128	Corymbia citriodora	Spotted Gum	310		310	19	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3129	Lophostemon suaveolens	Swamp Box	265		265	12	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3130	Lophostemon suaveolens	Swamp Box	125		125	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3131	Alphitonia excelsa	Soap Tree	165		165	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3132	Acacia disparrima	Hickory Wattle	165		165	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3133	Corymbia tessellaris	Moreton Bay Ash	220		220	19	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3134	Eucalyptus tereticornis	Forest Red Gum	320	260	412	21	8	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3135	Acacia disparrima	Hickory Wattle	200		200	10	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3136	Corymbia tessellaris	Moreton Bay Ash	185		185	17	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3137	Alphitonia excelsa	Soap Tree	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3138	Corymbia citriodora	Spotted Gum	375		375	22	8	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3139	Lophostemon suaveolens	Swamp Box	210		210	14	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3140	Angophora subvelutina	Broad-leaved Apple	420		420	21	12	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3141	Corymbia tessellaris	Moreton Bay Ash	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3142	Angophora subvelutina	Broad-leaved Apple	320		320	17	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3143	Acacia disparrima	Hickory Wattle	145		145	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3144	Acacia concurrens	Black Wattle	125		125	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3145	Lophostemon suaveolens	Swamp Box	240	240	339	13	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3146	Corymbia tessellaris	Moreton Bay Ash	125		125	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3147	Corymbia intermedia	Pink Bloodwood	200		200	15	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3148	Acacia disparrima	Hickory Wattle	160		160	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3149	Eucalyptus tereticornis	Forest Red Gum	320		320	23	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3150	Eucalyptus tereticornis	Forest Red Gum	220		220	21	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3151	Corymbia citriodora	Spotted Gum	180		180	15	7	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
3152	Corymbia intermedia	Pink Bloodwood	180		180	15	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3153	Acacia concurrens	Black Wattle	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3154	Angophora subvelutina	Broad-leaved Apple	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3155	Eucalyptus crebra	Narrow-leaved Ironbark	170		170	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3156	Corymbia citriodora	Spotted Gum	220		220	17	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3157	Corymbia citriodora	Spotted Gum	125		125	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3158	Corymbia citriodora	Spotted Gum	155		155	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3159	Corymbia citriodora	Spotted Gum	115		115	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3160	Corymbia citriodora	Spotted Gum	160		160	11	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3161	Eucalyptus crebra	Narrow-leaved Ironbark	180		180	17	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3162	Acacia concurrens	Black Wattle	180		180	9	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3163	Corymbia tessellaris	Moreton Bay Ash	185		185	16	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3164	Corymbia citriodora	Spotted Gum	125		125	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3165	Lophostemon suaveolens	Swamp Box	145		145	10	3	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3166	Corymbia citriodora	Spotted Gum	125		125	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3167	Corymbia tessellaris	Moreton Bay Ash	360		360	17	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3168	Corymbia tessellaris	Moreton Bay Ash	140		140	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3169	Eucalyptus crebra	Narrow-leaved Ironbark	185	170	251	14	5	3.0	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3170	Angophora subvelutina	Broad-leaved Apple	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
3171	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	19	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3172	Eucalyptus crebra	Narrow-leaved Ironbark	195		195	18	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3173	Angophora subvelutina	Broad-leaved Apple	255		255	13	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3174	Eucalyptus tereticornis	Forest Red Gum	420		420	19	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3175	Corymbia intermedia	Pink Bloodwood	145		145	9	4	2.0	1.5	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3176	Alphitonia excelsa	Soap Tree	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3177	Corymbia citriodora	Spotted Gum	105		105	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3178	Corymbia citriodora	Spotted Gum	105		105	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3179	Corymbia citriodora	Spotted Gum	130		130	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3180	Alphitonia excelsa	Soap Tree	190		190	11	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3181	Alphitonia excelsa	Soap Tree	135		135	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3182	Acacia disparrima	Hickory Wattle	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3183	Acacia concurrens	Black Wattle	175		175	9	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3184	Corymbia citriodora	Spotted Gum	125		125	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3185	Acacia disparrima	Hickory Wattle	120	100	156	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3186	Corymbia citriodora	Spotted Gum	120		120	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3187	Lophostemon suaveolens	Swamp Box	180		180	11	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3188	Corymbia citriodora	Spotted Gum	190		190	17	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3189	Acacia concurrens	Black Wattle	105		105	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3190	Acacia disparrima	Hickory Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3191	Acacia disparrima	Hickory Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3192	Lophostemon suaveolens	Swamp Box	210	190	283	12	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3193	Acacia concurrens	Black Wattle	135		135	7	3	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3194	Lophostemon suaveolens	Swamp Box	185		185	12	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3195	Eucalyptus crebra	Narrow-leaved Ironbark	165	160	230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3196	Acacia disparrima	Hickory Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3197	Lophostemon suaveolens	Swamp Box	420		420	12	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3198	Casuarina cunninghamiana	River Sheoak	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3199	Lophostemon suaveolens	Swamp Box	230		230	13	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3200	Eucalyptus crebra	Narrow-leaved Ironbark	125		125	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3201	Eucalyptus tereticornis	Forest Red Gum	585		585	26	12	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3202	Lophostemon suaveolens	Swamp Box	320		320	13	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3203	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3204	Eucalyptus crebra	Narrow-leaved Ironbark	185		185	17	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3205	Melaleuca viminalis	Weeping Bottlebrush	220		220	9	6	2.6	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3206	Casuarina cunninghamiana	River Sheoak	310		310	19	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3207	Melaleuca viminalis	Weeping Bottlebrush	350		350	9	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3208	Melaleuca viminalis	Weeping Bottlebrush	200	145	247	8	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3209	Melaleuca viminalis	Weeping Bottlebrush	170		170	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3210	Melaleuca viminalis	Weeping Bottlebrush	110	65	128	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3211	Acacia disparrima	Hickory Wattle	130		130	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3212	Acacia disparrima	Hickory Wattle	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3213	Lophostemon suaveolens	Swamp Box	125	105, 70	178	6	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3214	Lophostemon suaveolens	Swamp Box	170		170	9	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3215	Acacia disparrima	Hickory Wattle	100	90, 70	152	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3216	Corymbia tessellaris	Moreton Bay Ash	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3217	Lophostemon suaveolens	Swamp Box	340		340	17	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3218	Lophostemon suaveolens	Swamp Box	155		155	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3219	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3220	Lophostemon suaveolens	Swamp Box	460		460	17	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3221	Lophostemon suaveolens	Swamp Box	125		125	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3222	Lophostemon suaveolens	Swamp Box	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3223	Lophostemon suaveolens	Swamp Box	125		125	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3224	Lophostemon suaveolens	Swamp Box	150		150	11	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3225	Lophostemon suaveolens	Swamp Box	205		205	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3226	Acacia disparrima	Hickory Wattle	155		155	8	2	2.0	1.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3227	Casuarina cunninghamiana	River Sheoak	300		300	17	9	3.6	2.0	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3228	Eucalyptus tereticornis	Forest Red Gum	120		120	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3229	Acacia concurrens	Black Wattle	145		145	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3230	Casuarina cunninghamiana	River Sheoak	220		220	17	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3231	Eucalyptus tereticornis	Forest Red Gum	120		120	14	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3232	Casuarina cunninghamiana	River Sheoak	365		365	17	10	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3233	Alphitonia excelsa	Soap Tree	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3234	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3235	Corymbia tessellaris	Moreton Bay Ash	320		320	23	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3236	Acacia disparrima	Hickory Wattle	165		165	10	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3237	Lophostemon suaveolens	Swamp Box	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3238	Angophora subvelutina	Broad-leaved Apple	540		540	21	12	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3239	Acacia disparrima	Hickory Wattle	135		135	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3240	Lophostemon suaveolens	Swamp Box	320		320	14	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3241	Acacia concurrens	Black Wattle	145		145	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3242	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3243	Corymbia intermedia	Pink Bloodwood	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3244	Lophostemon suaveolens	Swamp Box	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3245	Angophora subvelutina	Broad-leaved Apple	420	380	566	22	14	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3246	Corymbia intermedia	Pink Bloodwood	280		280	21	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3247	Alphitonia excelsa	Soap Tree	125		125	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3248	Eucalyptus crebra	Narrow-leaved Ironbark	295		295	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3249	Acacia disparrima	Hickory Wattle	165		165	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3250	Lophostemon suaveolens	Swamp Box	185		185	12	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3251	Corymbia tessellaris	Moreton Bay Ash	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3252	Acacia disparrima	Hickory Wattle	165	145, 120	250	10	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3253	Acacia disparrima	Hickory Wattle	185		185	7	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
3254	Acacia disparrima	Hickory Wattle	165	125, 100	230	8	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3255	Lophostemon suaveolens	Swamp Box	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3256	Alphitonia excelsa	Soap Tree	145		145	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3257	Eucalyptus tereticornis	Forest Red Gum	135		135	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3258	Corymbia intermedia	Pink Bloodwood	330		330	21	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3259	Corymbia tessellaris	Moreton Bay Ash	190		190	13	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3260	Acacia concurrens	Black Wattle	125		125	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3261	Acacia disparrima	Hickory Wattle	145		145	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
3262	Lophostemon suaveolens	Swamp Box	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3263	Eucalyptus tereticornis	Forest Red Gum	420		420	23	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3264	Lophostemon suaveolens	Swamp Box	230		230	13	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3265	Lophostemon suaveolens	Swamp Box	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3266	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3267	Corymbia tessellaris	Moreton Bay Ash	245		245	19	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3268	Corymbia citriodora	Spotted Gum	300	200	361	17	11	4.3	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
3269	Corymbia citriodora	Spotted Gum	300	200	361	17	11	4.3	2.2	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
3270	Acacia disparrima	Hickory Wattle	100	80	128	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3271	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	16	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3272	Acacia concurrens	Black Wattle	165		165	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3273	Lophostemon suaveolens	Swamp Box	105		105	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3274	Eucalyptus tereticornis	Forest Red Gum	255		255	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3275	Acacia concurrens	Black Wattle	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3276	Acacia concurrens	Black Wattle	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3277	Lophostemon suaveolens	Swamp Box	100	90	135	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3278	Lophostemon suaveolens	Swamp Box	280		280	17	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3279	Eucalyptus tereticornis	Forest Red Gum	460		460	18	7	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3280	Melaleuca viminalis	Weeping Bottlebrush	200		200	11	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3281	Melaleuca viminalis	Weeping Bottlebrush	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3282	Allocasuarina littoralis	Black She Oak	260	230	347	14	6	4.2	2.1	Irregular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3283	Melaleuca viminalis	Weeping Bottlebrush	220		220	5	2	2.6	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3284	Allocasuarina littoralis	Black She Oak	280	280	396	19	7	4.8	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3285	Allocasuarina littoralis	Black She Oak	240	90, 110, 90, 200	355	20	5	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3286	Allocasuarina littoralis	Black She Oak	210		210	23	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3287	Allocasuarina littoralis	Black She Oak	730		730	23	8	8.8	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3288	Lophostemon suaveolens	Swamp Box	310		310	12	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3289	Allocasuarina littoralis	Black She Oak	470		470	24	10	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3290	Lophostemon suaveolens	Swamp Box	270		270	10	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3291	Allocasuarina littoralis	Black She Oak	240	290	376	20	10	4.5	2.2	Irregular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3292	Melaleuca viminalis	Weeping Bottlebrush	210	200	290	10	8	3.5	2.0	Irregular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3293	Eucalyptus tereticornis	Forest Red Gum	480		480	27	9	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3294	Corymbia tessellaris	Moreton Bay Ash	460		460	25	9	5.5	2.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3295	Corymbia tessellaris	Moreton Bay Ash	540		540	26	12	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3296	Casuarina cunninghamiana	River Sheoak	470		470	23	6	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3297	Casuarina cunninghamiana	River Sheoak	440		440	18	6	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3298	Eucalyptus tereticornis	Forest Red Gum	690		690	32	12	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3299	Casuarina cunninghamiana	River Sheoak	480		480	23	9	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3300	Angophora subvelutina	Broad-leaved Apple	630		630	27	12	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3301	Angophora subvelutina	Broad-leaved Apple	660		660	26	12	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3302	Eucalyptus tereticornis	Forest Red Gum	590		590	26	11	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3303	Angophora subvelutina	Broad-leaved Apple	750		750	28	14	9.0	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3304	Angophora subvelutina	Broad-leaved Apple	390		390	23	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3305	Eucalyptus tereticornis	Forest Red Gum	490		490	25	12	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3306	DEAD/STAG		1250		1250	12	1	15.0	3.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	High		Approved to remove
3307	Eucalyptus tereticornis	Forest Red Gum	370		370	22	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3308	Angophora subvelutina	Broad-leaved Apple	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3309	Corymbia intermedia	Pink Bloodwood	450		450	21	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3310	Corymbia intermedia	Pink Bloodwood	560		560	20	8	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3311	Eucalyptus tereticornis	Forest Red Gum	650		650	27	14	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3312	Eucalyptus tereticornis	Forest Red Gum	510		510	23	9	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3313	Corymbia tessellaris	Moreton Bay Ash	210		210	17	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3314	Angophora subvelutina	Broad-leaved Apple	280		280	17	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3315	Angophora subvelutina	Broad-leaved Apple	480		480	25	14	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3316	Casuarina cunninghamiana	River Sheoak	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3317	Lophostemon suaveolens	Swamp Box	310		310	14	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3318	Lophostemon suaveolens	Swamp Box	220		220	8	2	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3319	Corymbia citriodora	Spotted Gum	310		310	19	2	3.7	2.0	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3320	Casuarina cunninghamiana	River Sheoak	280		280	17	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3321	Casuarina cunninghamiana	River Sheoak	280		280	14	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3322	Casuarina cunninghamiana	River Sheoak	220		220	13	4	2.6	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3323	Melaleuca viminalis	Weeping Bottlebrush	200		200	8	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3324	Eucalyptus tereticornis	Forest Red Gum	610		610	29	11	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3325	Acacia concurrens	Black Wattle	170		170	9	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3326	Eucalyptus tereticornis	Forest Red Gum	640		640	20	8	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3327	Eucalyptus tereticornis	Forest Red Gum	530		530	21	9	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3328	Lophostemon confertus	Brush Box	220	200	297	13	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3329	Eucalyptus tereticornis	Forest Red Gum	380		380	19	5	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3330	Eucalyptus tereticornis	Forest Red Gum	500		500	21	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3331	Lophostemon confertus	Brush Box	230		230	13	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3332	Corymbia tessellaris	Moreton Bay Ash	180		180	16	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3333	Corymbia tessellaris	Moreton Bay Ash	190		190	16	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3334	Corymbia tessellaris	Moreton Bay Ash	180		180	14	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3335	Lophostemon suaveolens	Swamp Box	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3336	Acacia disparrima	Hickory Wattle	130	100	164	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3337	Acacia disparrima	Hickory Wattle	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3338	Lophostemon suaveolens	Swamp Box	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3339	Angophora subvelutina	Broad-leaved Apple	230		230	17	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3340	Lophostemon suaveolens	Swamp Box	140		140	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3341	Lophostemon suaveolens	Swamp Box	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3342	Corymbia tessellaris	Moreton Bay Ash	150		150	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3343	Lophostemon suaveolens	Swamp Box	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3344	Lophostemon suaveolens	Swamp Box	160		160	14	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Retain
3345	Lophostemon suaveolens	Swamp Box	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3346	Acacia disparrima	Hickory Wattle	120	70	139	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3347	Acacia disparrima	Hickory Wattle	80	80, 80, 80	160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3348	Lophostemon suaveolens	Swamp Box	170		170	14	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3349	Lophostemon suaveolens	Swamp Box	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3350	Lophostemon suaveolens	Swamp Box	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3351	Eucalyptus tereticornis	Forest Red Gum	110		110	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3352	Corymbia citriodora	Spotted Gum	500		500	20	8	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3353	Corymbia citriodora	Spotted Gum	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3354	Corymbia citriodora	Spotted Gum	340		340	22	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3355	Corymbia citriodora	Spotted Gum	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3356	Corymbia citriodora	Spotted Gum	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3357	Corymbia citriodora	Spotted Gum	220	140	261	16	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3358	Corymbia citriodora	Spotted Gum	130		130	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3359	Corymbia citriodora	Spotted Gum	250		250	17	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3360	Corymbia citriodora	Spotted Gum	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3361	Corymbia tessellaris	Moreton Bay Ash	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3362	Corymbia citriodora	Spotted Gum	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3363	Corymbia citriodora	Spotted Gum	270		270	19	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3364	Corymbia tessellaris	Moreton Bay Ash	160	160	226	15	6	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3365	Eucalyptus tereticornis	Forest Red Gum	220		220	17	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3366	Eucalyptus tereticornis	Forest Red Gum	160		160	13	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3367	Corymbia tessellaris	Moreton Bay Ash	170		170	14	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3368	Corymbia citriodora	Spotted Gum	290		290	19	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3369	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3370	Corymbia citriodora	Spotted Gum	150	140, 110, 110, 100	276	15	7	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3371	Corymbia tessellaris	Moreton Bay Ash	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3372	Corymbia citriodora	Spotted Gum	320		320	19	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3373	Corymbia citriodora	Spotted Gum	230		230	18	9	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3374	Corymbia citriodora	Spotted Gum	570	220	611	20	11	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3375	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	16	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3376	Corymbia citriodora	Spotted Gum	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3377	Corymbia citriodora	Spotted Gum	270		270	18	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3378	Corymbia citriodora	Spotted Gum	230		230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3379	Corymbia citriodora	Spotted Gum	220		220	18	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3380	Corymbia citriodora	Spotted Gum	110		110	11	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3381	Corymbia citriodora	Spotted Gum	230		230	16	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3382	Corymbia citriodora	Spotted Gum	330		330	19	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3383	Corymbia citriodora	Spotted Gum	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3384	Corymbia citriodora	Spotted Gum	110		110	7	2	2.0	1.3	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3385	Corymbia citriodora	Spotted Gum	250		250	16	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3386	Corymbia citriodora	Spotted Gum	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3387	Corymbia citriodora	Spotted Gum	140		140	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3388	Corymbia citriodora	Spotted Gum	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3389	Corymbia citriodora	Spotted Gum	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3390	Corymbia citriodora	Spotted Gum	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3391	Corymbia citriodora	Spotted Gum	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3392	Corymbia citriodora	Spotted Gum	250		250	20	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3393	Corymbia citriodora	Spotted Gum	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3394	Corymbia citriodora	Spotted Gum	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3395	Corymbia citriodora	Spotted Gum	450		450	22	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3396	Lophostemon suaveolens	Swamp Box	140		140	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3397	Corymbia citriodora	Spotted Gum	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3398	Corymbia citriodora	Spotted Gum	160		160	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3399	Eucalyptus crebra	Narrow-leaved Ironbark	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3400	Eucalyptus crebra	Narrow-leaved Ironbark	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3401	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	17	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3402	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3403	Corymbia citriodora	Spotted Gum	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3404	Corymbia citriodora	Spotted Gum	180		180	10	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3405	Corymbia citriodora	Spotted Gum	300		300	22	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3406	Corymbia citriodora	Spotted Gum	110		110	14	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3407	Alphitonia excelsa	Soap Tree	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3408	Corymbia citriodora	Spotted Gum	400		400	19	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3409	Corymbia citriodora	Spotted Gum	200	180	269	18	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3410	Corymbia citriodora	Spotted Gum	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3411	Corymbia citriodora	Spotted Gum	250		250	17	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3412	Eucalyptus tereticornis	Forest Red Gum	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3413	Eucalyptus tereticornis	Forest Red Gum	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3414	Corymbia citriodora	Spotted Gum	190		190	19	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3415	Eucalyptus tereticornis	Forest Red Gum	250		250	19	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3416	Corymbia citriodora	Spotted Gum	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3417	Corymbia citriodora	Spotted Gum	160		160	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3418	Alphitonia excelsa	Soap Tree	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3419	Corymbia citriodora	Spotted Gum	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3420	Corymbia citriodora	Spotted Gum	400		400	21	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3421	Corymbia citriodora	Spotted Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3422	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	17	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3423	Corymbia tessellaris	Moreton Bay Ash	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3424	Corymbia tessellaris	Moreton Bay Ash	140		140	14	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3425	Alphitonia excelsa	Soap Tree	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3426	Lophostemon suaveolens	Swamp Box	270		270	10	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3427	Eucalyptus tereticornis	Forest Red Gum	170	80	188	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3428	Acacia disparrima	Hickory Wattle	150	130	198	9	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3429	Eucalyptus tereticornis	Forest Red Gum	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3430	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	18	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3431	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	19	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3432	Eucalyptus crebra	Narrow-leaved Ironbark	190	80	206	14	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3433	Eucalyptus tereticornis	Forest Red Gum	300		300	18	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3434	Eucalyptus tereticornis	Forest Red Gum	270		270	17	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3435	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3436	Acacia disparrima	Hickory Wattle	180	110, 100	233	9	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3437	Corymbia tessellaris	Moreton Bay Ash	230		230	17	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3438	Corymbia intermedia	Pink Bloodwood	250		250	18	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3439	Allocasuarina littoralis	Black She Oak	200	160	256	9	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3440	Corymbia citriodora	Spotted Gum	280		280	16	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3441	Eucalyptus crebra	Narrow-leaved Ironbark	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3442	Eucalyptus tereticornis	Forest Red Gum	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3443	Corymbia citriodora	Spotted Gum	190		190	16	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3444	Corymbia citriodora	Spotted Gum	210	160, 90	279	17	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3445	Corymbia citriodora	Spotted Gum	260		260	14	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3446	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Approved to remove
3447	Corymbia citriodora	Spotted Gum	220		220	17	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3448	Corymbia citriodora	Spotted Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3449	Acacia disparrima	Hickory Wattle	170		170	7	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3450	Corymbia citriodora	Spotted Gum	270		270	15	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3451	Corymbia citriodora	Spotted Gum	250		250	16	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3452	Corymbia citriodora	Spotted Gum	390		390	18	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3453	Eucalyptus tereticornis	Forest Red Gum	260		260	16	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3454	Eucalyptus tereticornis	Forest Red Gum	290		290	16	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3455	Eucalyptus tereticornis	Forest Red Gum	290		290	18	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3456	Corymbia citriodora	Spotted Gum	260		260	16	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3457	Corymbia citriodora	Spotted Gum	230		230	15	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3458	Corymbia intermedia	Pink Bloodwood	330		330	18	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3459	Lophostemon suaveolens	Swamp Box	270		270	14	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3460	Corymbia intermedia	Pink Bloodwood	260		260	16	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3461	Eucalyptus tereticornis	Forest Red Gum	420		420	19	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3462	Corymbia intermedia	Pink Bloodwood	300		300	16	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3463	Corymbia intermedia	Pink Bloodwood	280		280	17	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3464	Corymbia intermedia	Pink Bloodwood	450		450	18	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3465	Angophora leiocarpa	Smooth-barked Apple	360		360	14	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3466	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	16	4	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3467	Acacia disparrima	Hickory Wattle	160		160	10	4	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3468	Eucalyptus tereticornis	Forest Red Gum	310		310	17	6	3.7	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3469	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3470	Eucalyptus tereticornis	Forest Red Gum	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3471	Eucalyptus tereticornis	Forest Red Gum	290		290	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3472	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	17	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3473	Corymbia tessellaris	Moreton Bay Ash	110		110	13	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3474	Corymbia tessellaris	Moreton Bay Ash	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3475	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	18	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3476	Allocasuarina littoralis	Black She Oak	170		170	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3477	Corymbia citriodora	Spotted Gum	350		350	18	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3478	Corymbia citriodora	Spotted Gum	380		380	19	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3479	Corymbia citriodora	Spotted Gum	530		530	21	9	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3480	Eucalyptus tereticornis	Forest Red Gum	690		690	21	10	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3481	Acacia disparrima	Hickory Wattle	240		240	7	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3482	Corymbia citriodora	Spotted Gum	390		390	21	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3483	Corymbia intermedia	Pink Bloodwood	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3484	Corymbia tessellaris	Moreton Bay Ash	200	140	244	20	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3485	Corymbia citriodora	Spotted Gum	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3486	Corymbia citriodora	Spotted Gum	280		280	22	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3487	Corymbia citriodora	Spotted Gum	250		250	19	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3488	Corymbia citriodora	Spotted Gum	280		280	19	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3489	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	21	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3490	Corymbia intermedia	Pink Bloodwood	290		290	17	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3491	Alphitonia excelsa	Soap Tree	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3492	Angophora leiocarpa	Smooth-barked Apple	140		140	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3493	Alphitonia excelsa	Soap Tree	180		180	9	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3494	Acacia disparrima	Hickory Wattle	180		180	8	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3495	Lophostemon suaveolens	Swamp Box	80	80	113	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3496	Angophora leiocarpa	Smooth-barked Apple	700		700	18	8	8.4	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
3497	Angophora leiocarpa	Smooth-barked Apple	210		210	15	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3498	Corymbia citriodora	Spotted Gum	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3499	Corymbia citriodora	Spotted Gum	350		350	22	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3500	Acacia disparrima	Hickory Wattle	420		420	11	7	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3501	Corymbia intermedia	Pink Bloodwood	230	150	275	18	3	3.3	1.9	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3502	Angophora leiocarpa	Smooth-barked Apple	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3503	Corymbia citriodora	Spotted Gum	160		160	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3504	Angophora leiocarpa	Smooth-barked Apple	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3505	Angophora leiocarpa	Smooth-barked Apple	120		120	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3506	Corymbia citriodora	Spotted Gum	160		160	17	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3507	Corymbia citriodora	Spotted Gum	160		160	16	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3508	Lophostemon suaveolens	Swamp Box	160		160	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3509	Lophostemon suaveolens	Swamp Box	120		120	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3510	Corymbia citriodora	Spotted Gum	240	170	294	22	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3511	Lophostemon suaveolens	Swamp Box	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3512	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	20	3	2.6	1.8	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3513	Acacia disparrima	Hickory Wattle	240		240	16	6	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3514	Acacia concurrens	Black Wattle	120		120	9	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3515	Corymbia citriodora	Spotted Gum	100	90, 70, 50	160	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3516	Corymbia citriodora	Spotted Gum	130		130	16	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3517	Lophostemon suaveolens	Swamp Box	180		180	15	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3518	Lophostemon suaveolens	Swamp Box	110		110	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3519	Corymbia citriodora	Spotted Gum	90	90	127	16	2	2.0	1.4	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3520	Eucalyptus tereticornis	Forest Red Gum	90	80	120	16	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3521	Corymbia intermedia	Pink Bloodwood	120		120	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3522	Corymbia intermedia	Pink Bloodwood	310		310	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3523	Acacia disparrima	Hickory Wattle	100	80	128	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3524	Acacia disparrima	Hickory Wattle	140		140	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3525	Corymbia intermedia	Pink Bloodwood	190		190	16	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3526	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3527	Corymbia intermedia	Pink Bloodwood	170		170	18	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3528	Eucalyptus tereticornis	Forest Red Gum	490		490	22	10	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3529	Angophora leiocarpa	Smooth-barked Apple	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3530	Lophostemon suaveolens	Swamp Box	220		220	16	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3531	Angophora leiocarpa	Smooth-barked Apple	100		100	14	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3532	Corymbia intermedia	Pink Bloodwood	260	140	295	23	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3533	Corymbia intermedia	Pink Bloodwood	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3534	Angophora leiocarpa	Smooth-barked Apple	160		160	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3535	Acacia disparrima	Hickory Wattle	170		170	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3536	Lophostemon suaveolens	Swamp Box	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3537	Alphitonia excelsa	Soap Tree	220		220	14	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3538	Corymbia intermedia	Pink Bloodwood	110	110	156	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3539	Angophora leiocarpa	Smooth-barked Apple	260	230	347	20	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3540	Acacia disparrima	Hickory Wattle	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3541	Lophostemon suaveolens	Swamp Box	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3542	Lophostemon suaveolens	Swamp Box	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3543	Alphitonia excelsa	Soap Tree	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3544	Angophora leiocarpa	Smooth-barked Apple	140		140	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3545	Acacia disparrima	Hickory Wattle	140	100, 80	190	14	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3546	Corymbia intermedia	Pink Bloodwood	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3547	Acacia disparrima	Hickory Wattle	180		180	13	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3548	Alphitonia excelsa	Soap Tree	170		170	15	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3549	Angophora leiocarpa	Smooth-barked Apple	160		160	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3550	Eucalyptus tereticornis	Forest Red Gum	480		480	26	11	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3551	Angophora leiocarpa	Smooth-barked Apple	120		120	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3552	Acacia disparrima	Hickory Wattle	230		230	15	6	2.8	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3553	Angophora leiocarpa	Smooth-barked Apple	100		100	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3554	Angophora leiocarpa	Smooth-barked Apple	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3555	Alphitonia excelsa	Soap Tree	180		180	14	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3556	Angophora leiocarpa	Smooth-barked Apple	130		130	14	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3557	Acacia disparrima	Hickory Wattle	180		180	14	4	2.2	1.6	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3558	Acacia disparrima	Hickory Wattle	190		190	15	4	2.3	1.6	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3559	Lophostemon suaveolens	Swamp Box	180		180	14	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3560	Lophostemon suaveolens	Swamp Box	210		210	14	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3561	Lophostemon suaveolens	Swamp Box	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3562	Eucalyptus tereticornis	Forest Red Gum	530		530	22	7	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3563	Corymbia citriodora	Spotted Gum	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3564	Corymbia citriodora	Spotted Gum	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3565	Corymbia citriodora	Spotted Gum	360		360	19	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3566	Corymbia citriodora	Spotted Gum	280	220	356	19	9	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3567	Eucalyptus tereticornis	Forest Red Gum	220		220	18	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3568	Corymbia tessellaris	Moreton Bay Ash	190	130	230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3569	Angophora leiocarpa	Smooth-barked Apple	180		180	16	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3570	Corymbia intermedia	Pink Bloodwood	350		350	17	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3571	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	16	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3572	Acacia disparrima	Hickory Wattle	190		190	11	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3573	Acacia disparrima	Hickory Wattle	170		170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3574	Corymbia citriodora	Spotted Gum	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3575	Lophostemon suaveolens	Swamp Box	160		160	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3576	Angophora leiocarpa	Smooth-barked Apple	250		250	19	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3577	Alphitonia excelsa	Soap Tree	130		130	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3578	Acacia disparrima	Hickory Wattle	80	60, 60, 50	127	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3579	Corymbia citriodora	Spotted Gum	240		240	18	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3580	Corymbia citriodora	Spotted Gum	160		160	17	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3581	Lophostemon suaveolens	Swamp Box	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3582	Alphitonia excelsa	Soap Tree	140		140	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3583	Corymbia intermedia	Pink Bloodwood	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3584	Corymbia citriodora	Spotted Gum	110		110	13	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3585	Corymbia citriodora	Spotted Gum	310		310	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3586	Corymbia intermedia	Pink Bloodwood	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3587	Lophostemon suaveolens	Swamp Box	150		150	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3588	Corymbia intermedia	Pink Bloodwood	240	170, 100	311	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3589	Lophostemon suaveolens	Swamp Box	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3590	Lophostemon suaveolens	Swamp Box	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3591	Corymbia citriodora	Spotted Gum	180		180	16	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3592	Corymbia intermedia	Pink Bloodwood	250		250	17	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3593	Corymbia citriodora	Spotted Gum	250	130, 120, 80	317	17	8	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3594	Corymbia intermedia	Pink Bloodwood	220		220	14	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3595	Acacia disparrima	Hickory Wattle	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3596	Angophora leiocarpa	Smooth-barked Apple	150		150	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3597	Acacia disparrima	Hickory Wattle	240	180	300	16	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3598	Lophostemon suaveolens	Swamp Box	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3599	Lophostemon suaveolens	Swamp Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3600	Angophora leiocarpa	Smooth-barked Apple	110		110	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3601	Eucalyptus tereticornis	Forest Red Gum	360		360	20	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3602	Lophostemon suaveolens	Swamp Box	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3603	Lophostemon suaveolens	Swamp Box	170	160, 60	241	11	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3604	Eucalyptus tereticornis	Forest Red Gum	240		240	19	2	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3605	Acacia disparrima	Hickory Wattle	190		190	14	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3606	Acacia disparrima	Hickory Wattle	160		160	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3607	Alphitonia excelsa	Soap Tree	170		170	16	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3608	Corymbia intermedia	Pink Bloodwood	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3609	Eucalyptus tereticornis	Forest Red Gum	440		440	22	10	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3610	Acacia disparrima	Hickory Wattle	220		220	11	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3611	Corymbia intermedia	Pink Bloodwood	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3612	Angophora leiocarpa	Smooth-barked Apple	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3613	Angophora leiocarpa	Smooth-barked Apple	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3614	Angophora leiocarpa	Smooth-barked Apple	170		170	15	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3615	Lophostemon suaveolens	Swamp Box	240		240	13	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3616	Lophostemon suaveolens	Swamp Box	220		220	14	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3617	Acacia disparrima	Hickory Wattle	220		220	15	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3618	Lophostemon suaveolens	Swamp Box	290		290	16	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3619	Lophostemon suaveolens	Swamp Box	180		180	13	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3620	Lophostemon suaveolens	Swamp Box	170		170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3621	Lophostemon suaveolens	Swamp Box	190		190	12	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3622	Lophostemon suaveolens	Swamp Box	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3623	Lophostemon suaveolens	Swamp Box	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3624	Lophostemon suaveolens	Swamp Box	190	90, 90	229	14	4	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3625	Lophostemon suaveolens	Swamp Box	190		190	14	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3626	Lophostemon suaveolens	Swamp Box	120		120	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3627	Lophostemon suaveolens	Swamp Box	220		220	14	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3628	Angophora leiocarpa	Smooth-barked Apple	100		100	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3629	Lophostemon suaveolens	Swamp Box	210		210	10	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3630	Lophostemon suaveolens	Swamp Box	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3631	Lophostemon suaveolens	Swamp Box	200	150	250	12	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3632	Angophora leiocarpa	Smooth-barked Apple	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3633	Corymbia intermedia	Pink Bloodwood	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3634	Eucalyptus tereticornis	Forest Red Gum	240		240	20	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3635	Lophostemon suaveolens	Swamp Box	190	160	248	13	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3636	Alphitonia excelsa	Soap Tree	180		180	13	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3637	Lophostemon suaveolens	Swamp Box	220	180	284	18	8	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3638	Lophostemon suaveolens	Swamp Box	230		230	16	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3639	Lophostemon suaveolens	Swamp Box	220	170	278	14	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3640	Corymbia intermedia	Pink Bloodwood	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3641	Lophostemon suaveolens	Swamp Box	200	160	256	15	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3642	Lophostemon suaveolens	Swamp Box	220	150	266	17	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3643	Corymbia citriodora	Spotted Gum	360		360	19	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3644	Lophostemon suaveolens	Swamp Box	250		250	16	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3645	Eucalyptus tereticornis	Forest Red Gum	200		200	19	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3646	Lophostemon suaveolens	Swamp Box	270		270	17	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3647	Lophostemon suaveolens	Swamp Box	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3648	Lophostemon suaveolens	Swamp Box	220		220	16	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3649	Lophostemon suaveolens	Swamp Box	240		240	16	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3650	Lophostemon suaveolens	Swamp Box	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3651	Lophostemon suaveolens	Swamp Box	280		280	15	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3652	Corymbia intermedia	Pink Bloodwood	240		240	19	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3653	Eucalyptus tereticornis	Forest Red Gum	200		200	21	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3654	Corymbia intermedia	Pink Bloodwood	220		220	16	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3655	Eucalyptus tereticornis	Forest Red Gum	390		390	20	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3656	Lophostemon suaveolens	Swamp Box	240		240	15	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3657	Lophostemon suaveolens	Swamp Box	140		140	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3658	Lophostemon suaveolens	Swamp Box	140		140	16	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3659	Lophostemon suaveolens	Swamp Box	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3660	Corymbia intermedia	Pink Bloodwood	170		170	9	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3661	Lophostemon suaveolens	Swamp Box	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3662	Lophostemon suaveolens	Swamp Box	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3663	Alphitonia excelsa	Soap Tree	190		190	13	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3664	Lophostemon suaveolens	Swamp Box	190		190	16	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3665	Eucalyptus tereticornis	Forest Red Gum	200		200	19	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3666	Corymbia intermedia	Pink Bloodwood	210		210	20	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3667	Corymbia intermedia	Pink Bloodwood	290		290	20	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3668	Corymbia intermedia	Pink Bloodwood	240		240	22	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3669	Corymbia intermedia	Pink Bloodwood	240		240	22	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3670	Lophostemon suaveolens	Swamp Box	300		300	20	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3671	Lophostemon suaveolens	Swamp Box	240		240	18	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3672	Corymbia intermedia	Pink Bloodwood	150		150	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3673	Lophostemon suaveolens	Swamp Box	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3674	Lophostemon suaveolens	Swamp Box	130		130	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3675	Eucalyptus tereticornis	Forest Red Gum	350		350	22	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3676	Eucalyptus tereticornis	Forest Red Gum	320		320	20	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3677	Lophostemon suaveolens	Swamp Box	280		280	18	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3678	Lophostemon suaveolens	Swamp Box	280		280	17	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3679	Lophostemon suaveolens	Swamp Box	330		330	19	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3680	Eucalyptus tereticornis	Forest Red Gum	420		420	20	10	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3681	Lophostemon suaveolens	Swamp Box	230		230	16	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3682	Lophostemon suaveolens	Swamp Box	350	200	403	18	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3683	Lophostemon suaveolens	Swamp Box	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3684	Lophostemon suaveolens	Swamp Box	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3685	Lophostemon suaveolens	Swamp Box	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3686	Lophostemon suaveolens	Swamp Box	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3687	Lophostemon suaveolens	Swamp Box	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
3688	Lophostemon suaveolens	Swamp Box	360		360	19	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3689	Lophostemon suaveolens	Swamp Box	340	270, 230	491	18	9	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3690	Eucalyptus tereticornis	Forest Red Gum	750		750	27	12	9.0	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3691	Eucalyptus crebra	Narrow-leaved Ironbark	450		450	26	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Retain
3692	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	20	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3693	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	20	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3694	Corymbia citriodora	Spotted Gum	90	90	127	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3695	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	22	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3696	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	24	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3697	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	23	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3698	Eucalyptus crebra	Narrow-leaved Ironbark	330		330	22	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3699	Corymbia citriodora	Spotted Gum	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3700	Corymbia citriodora	Spotted Gum	340		340	22	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3701	Corymbia citriodora	Spotted Gum	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3702	Eucalyptus tereticornis	Forest Red Gum	270		270	21	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3703	Corymbia citriodora	Spotted Gum	130		130	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3704	Eucalyptus tereticornis	Forest Red Gum	180		180	18	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3705	Acacia disparrima	Hickory Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3706	Eucalyptus tereticornis	Forest Red Gum	60		60	10	3	2.0	1.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3707	Eucalyptus siderophloia	Grey Ironbark	280		280	21	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3708	Corymbia citriodora	Spotted Gum	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3709	Allocasuarina littoralis	Black She Oak	210		210	13	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3710	Corymbia citriodora	Spotted Gum	160		160	18	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
3711	Eucalyptus tereticornis	Forest Red Gum	300	290	417	18	6	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3712	Eucalyptus tereticornis	Forest Red Gum	320		320	20	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3713	Eucalyptus tereticornis	Forest Red Gum	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3714	Eucalyptus tereticornis	Forest Red Gum	280		280	17	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3715	Eucalyptus tereticornis	Forest Red Gum	230		230	17	3	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3716	Eucalyptus tereticornis	Forest Red Gum	510		510	20	9	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3717	Corymbia intermedia	Pink Bloodwood	240		240	15	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3718	Corymbia intermedia	Pink Bloodwood	260		260	17	3	3.1	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3719	Corymbia citriodora	Spotted Gum	370		370	21	7	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3720	Corymbia intermedia	Pink Bloodwood	320		320	23	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3721	Acacia concurrens	Black Wattle	230		230	8	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3722	Corymbia intermedia	Pink Bloodwood	310		310	19	4	3.7	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3723	Corymbia intermedia	Pink Bloodwood	330		330	19	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3724	Corymbia intermedia	Pink Bloodwood	280		280	19	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3725	Eucalyptus tereticornis	Forest Red Gum	300		300	17	3	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3726	Corymbia intermedia	Pink Bloodwood	320		320	19	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3727	Corymbia intermedia	Pink Bloodwood	330		330	21	3	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3728	Corymbia intermedia	Pink Bloodwood	390	200	438	18	5	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3729	Corymbia intermedia	Pink Bloodwood	300	290	417	17	6	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3730	Lophostemon suaveolens	Swamp Box	240		240	16	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3731	Lophostemon suaveolens	Swamp Box	210		210	9	3	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3732	Corymbia citriodora	Spotted Gum	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3733	Corymbia citriodora	Spotted Gum	320		320	22	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3734	Corymbia intermedia	Pink Bloodwood	520		520	19	5	6.2	2.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3735	Eucalyptus tereticornis	Forest Red Gum	330		330	21	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3736	Eucalyptus tereticornis	Forest Red Gum	380		380	17	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3737	Acacia concurrens	Black Wattle	200		200	8	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3738	Eucalyptus siderophloia	Grey Ironbark	320		320	19	8	3.8	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
3739	Corymbia citriodora	Spotted Gum	350		350	20	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3740	Corymbia intermedia	Pink Bloodwood	220	270	348	15	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3741	Corymbia citriodora	Spotted Gum	120		120	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3742	Corymbia citriodora	Spotted Gum	280		280	19	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3743	Angophora leiocarpa	Smooth-barked Apple	210		210	17	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3744	Acacia disparrima	Hickory Wattle	300		300	12	6	3.6	2.0	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3745	Angophora leiocarpa	Smooth-barked Apple	280		280	16	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3746	Corymbia citriodora	Spotted Gum	390		390	21	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3747	Acacia disparrima	Hickory Wattle	320		320	10	6	3.8	2.1	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3748	Corymbia citriodora	Spotted Gum	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3749	Lophostemon suaveolens	Swamp Box	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3750	Corymbia citriodora	Spotted Gum	120		120	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3751	Corymbia citriodora	Spotted Gum	120		120	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3752	Corymbia citriodora	Spotted Gum	130		130	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3753	Corymbia citriodora	Spotted Gum	150		150	15	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3754	Acacia disparrima	Hickory Wattle	150		150	10	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3755	Corymbia citriodora	Spotted Gum	150		150	14	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3756	Corymbia intermedia	Pink Bloodwood	300		300	23	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3757	Lophostemon suaveolens	Swamp Box	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3758	Corymbia citriodora	Spotted Gum	470		470	24	5	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3759	Eucalyptus seeana	Narrow-leaved Red Gum	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3760	Corymbia intermedia	Pink Bloodwood	310		310	19	4	3.7	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3761	Acacia disparrima	Hickory Wattle	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3762	Eucalyptus siderophloia	Grey Ironbark	160	90	184	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3763	Eucalyptus tereticornis	Forest Red Gum	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3764	Corymbia citriodora	Spotted Gum	140		140	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3765	Corymbia citriodora	Spotted Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3766	Lophostemon suaveolens	Swamp Box	320		320	14	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3767	Corymbia citriodora	Spotted Gum	120		120	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3768	Corymbia intermedia	Pink Bloodwood	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3769	Alphitonia excelsa	Soap Tree	200		200	8	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3770	Eucalyptus tereticornis	Forest Red Gum	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3771	Alphitonia excelsa	Soap Tree	250		250	9	2	3.0	1.8	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
3772	Corymbia intermedia	Pink Bloodwood	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3773	Corymbia citriodora	Spotted Gum	100		100	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3774	Corymbia intermedia	Pink Bloodwood	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3775	Corymbia citriodora	Spotted Gum	300		300	18	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3776	Angophora leiocarpa	Smooth-barked Apple	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3777	Corymbia intermedia	Pink Bloodwood	230		230	17	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	native bees	Remove
3778	Corymbia citriodora	Spotted Gum	250		250	17	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3779	Lophostemon suaveolens	Swamp Box	300		300	14	3	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3780	Corymbia citriodora	Spotted Gum	400		400	17	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3781	Corymbia citriodora	Spotted Gum	390		390	18	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3782	Alphitonia excelsa	Soap Tree	200	220	297	15	4	3.6	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3783	Angophora leiocarpa	Smooth-barked Apple	115		115	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3784	Corymbia citriodora	Spotted Gum	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3785	Corymbia citriodora	Spotted Gum	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3786	Acacia disparrima	Hickory Wattle	210		210	14	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3787	Corymbia citriodora	Spotted Gum	190		190	19	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3788	Corymbia citriodora	Spotted Gum	120		120	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3789	Corymbia citriodora	Spotted Gum	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3790	Corymbia intermedia	Pink Bloodwood	270		270	15	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3791	Corymbia citriodora	Spotted Gum	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3792	Corymbia intermedia	Pink Bloodwood	130		130	12	2	2.0	1.4	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3793	Acacia disparrima	Hickory Wattle	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3794	Corymbia citriodora	Spotted Gum	190	90	210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3795	Angophora leiocarpa	Smooth-barked Apple	220	140	261	16	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3796	Corymbia citriodora	Spotted Gum	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3797	Eucalyptus crebra	Narrow-leaved Ironbark	460		460	22	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3798	Corymbia intermedia	Pink Bloodwood	140		140	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3799	Corymbia citriodora	Spotted Gum	670		670	25	10	8.0	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3800	DEAD/STAG		870		870	19	6	10.4	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Remove
3801	Corymbia citriodora	Spotted Gum	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3802	Eucalyptus tereticornis	Forest Red Gum	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3803	Corymbia intermedia	Pink Bloodwood	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3804	Corymbia citriodora	Spotted Gum	220		220	15	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3805	Corymbia citriodora	Spotted Gum	390		390	17	6	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3806	Acacia disparrima	Hickory Wattle	150		150	10	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3807	Angophora leiocarpa	Smooth-barked Apple	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3808	Corymbia intermedia	Pink Bloodwood	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3809	Corymbia intermedia	Pink Bloodwood	320		320	20	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3810	Eucalyptus siderophloia	Grey Ironbark	220		220	12	2	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3811	Eucalyptus siderophloia	Grey Ironbark	190		190	14	2	2.3	1.6	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3812	Corymbia citriodora	Spotted Gum	130		130	14	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3813	Alphitonia excelsa	Soap Tree	270		270	16	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3814	Alphitonia excelsa	Soap Tree	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3815	Corymbia tessellaris	Moreton Bay Ash	200	150, 140	287	16	5	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3816	Angophora leiocarpa	Smooth-barked Apple	310	150	344	18	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3817	Angophora leiocarpa	Smooth-barked Apple	220		220	15	3	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3818	Corymbia intermedia	Pink Bloodwood	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3819	Corymbia intermedia	Pink Bloodwood	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3820	Eucalyptus tereticornis	Forest Red Gum	380		380	20	7	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3821	Lophostemon suaveolens	Swamp Box	160		160	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3822	Acacia disparrima	Hickory Wattle	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3823	Corymbia citriodora	Spotted Gum	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3824	Acacia disparrima	Hickory Wattle	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3825	Alphitonia excelsa	Soap Tree	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3826	Acacia disparrima	Hickory Wattle	300		300	15	5	3.6	2.0	One-sided	-	-	Die-back	-	-	Poor	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
3827	Angophora leiocarpa	Smooth-barked Apple	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3828	Angophora leiocarpa	Smooth-barked Apple	240		240	17	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3829	Acacia disparrima	Hickory Wattle	160		160	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3830	Eucalyptus tereticornis	Forest Red Gum	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3831	Alphitonia excelsa	Soap Tree	190		190	12	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3832	Alphitonia excelsa	Soap Tree	140		140	7	2	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3833	Corymbia tessellaris	Moreton Bay Ash	160	190	248	14	3	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3834	Acacia disparrima	Hickory Wattle	240		240	16	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3835	Acacia disparrima	Hickory Wattle	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3836	Lophostemon suaveolens	Swamp Box	160		160	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3837	Acacia disparrima	Hickory Wattle	250		250	13	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3838	Corymbia intermedia	Pink Bloodwood	320		320	19	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3839	Lophostemon suaveolens	Swamp Box	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3840	Alphitonia excelsa	Soap Tree	190		190	9	2	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3841	Eucalyptus tereticornis	Forest Red Gum	240		240	20	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3842	Corymbia citriodora	Spotted Gum	120		120	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3843	Acacia disparrima	Hickory Wattle	170		170	6	2	2.0	1.6	One-sided	-	-	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3844	DEAD/STAG		1300		1300	20	9	15.0	3.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Remove
3845	Alphitonia excelsa	Soap Tree	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3846	Alphitonia excelsa	Soap Tree	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3847	Alphitonia excelsa	Soap Tree	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3848	Alphitonia excelsa	Soap Tree	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3849	Alphitonia excelsa	Soap Tree	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3850	Alphitonia excelsa	Soap Tree	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3851	Corymbia citriodora	Spotted Gum	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3852	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3853	Alphitonia excelsa	Soap Tree	200		200	8	3	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3854	Alphitonia excelsa	Soap Tree	160		160	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3855	Alphitonia excelsa	Soap Tree	180		180	9	2	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3856	Eucalyptus tereticornis	Forest Red Gum	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3857	Corymbia citriodora	Spotted Gum	300		300	20	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3858	Corymbia citriodora	Spotted Gum	290		290	20	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3859	Lophostemon suaveolens	Swamp Box	210		210	9	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3860	Corymbia intermedia	Pink Bloodwood	160	130, 90, 90	242	10	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3861	Corymbia citriodora	Spotted Gum	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3862	Lophostemon suaveolens	Swamp Box	220		220	14	4	2.6	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3863	Lophostemon suaveolens	Swamp Box	130	100, 110	197	9	2	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3864	Eucalyptus tereticornis	Forest Red Gum	500		500	25	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3865	Lophostemon suaveolens	Swamp Box	180	120	216	10	3	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3866	Eucalyptus tereticornis	Forest Red Gum	130		130	13	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3867	Corymbia tessellaris	Moreton Bay Ash	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3868	Eucalyptus tereticornis	Forest Red Gum	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Poor	-	-	-	-	-	-		Remove for basin works
3869	Corymbia citriodora	Spotted Gum	150		150	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3870	Corymbia tessellaris	Moreton Bay Ash	180	180	255	16	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3871	Corymbia intermedia	Pink Bloodwood	230		230	16	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3872	Lophostemon suaveolens	Swamp Box	240		240	10	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3873	Eucalyptus crebra	Narrow-leaved Ironbark	460		460	23	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3874	Lophostemon suaveolens	Swamp Box	150		150	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3875	Lophostemon suaveolens	Swamp Box	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3876	Lophostemon suaveolens	Swamp Box	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3877	Corymbia citriodora	Spotted Gum	830		830	18	9	10.0	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3878	Corymbia citriodora	Spotted Gum	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3879	Corymbia tessellaris	Moreton Bay Ash	200	120	233	16	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3880	Corymbia citriodora	Spotted Gum	130	80	153	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3881	Corymbia citriodora	Spotted Gum	300		300	16	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3882	Corymbia citriodora	Spotted Gum	130		130	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3883	Corymbia citriodora	Spotted Gum	140		140	14	2	2.0	1.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3884	Corymbia citriodora	Spotted Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3885	Eucalyptus crebra	Narrow-leaved Ironbark	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3886	Corymbia citriodora	Spotted Gum	120		120	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3887	Angophora leiocarpa	Smooth-barked Apple	150		150	12	3	2.0	1.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3888	Corymbia citriodora	Spotted Gum	140		140	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3889	Corymbia citriodora	Spotted Gum	170	80, 60	197	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3890	Alphitonia excelsa	Soap Tree	150		150	9	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3891	Corymbia citriodora	Spotted Gum	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3892	Corymbia citriodora	Spotted Gum	160		160	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3893	Angophora leiocarpa	Smooth-barked Apple	160	80	179	14	2	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3894	Corymbia citriodora	Spotted Gum	310	180	358	18	4	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3895	Eucalyptus crebra	Narrow-leaved Ironbark	110		110	11	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3896	Alphitonia excelsa	Soap Tree	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3897	Alphitonia excelsa	Soap Tree	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3898	Alphitonia excelsa	Soap Tree	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3899	Corymbia citriodora	Spotted Gum	210		210	18	6	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3900	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	15	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3901	Alphitonia excelsa	Soap Tree	150		150	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3902	Corymbia citriodora	Spotted Gum	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3903	Alphitonia excelsa	Soap Tree	180		180	14	2	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3904	Corymbia intermedia	Pink Bloodwood	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3905	Acacia disparrima	Hickory Wattle	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3906	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	17	5	3.0	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3907	Acacia disparrima	Hickory Wattle	170		170	14	3	2.0	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3908	Eucalyptus crebra	Narrow-leaved Ironbark	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3909	Acacia disparrima	Hickory Wattle	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3910	Acacia disparrima	Hickory Wattle	160		160	12	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
3911	Corymbia intermedia	Pink Bloodwood	330	250	414	18	5	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3912	Corymbia citriodora	Spotted Gum	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3913	Eucalyptus tereticornis	Forest Red Gum	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3914	Lophostemon suaveolens	Swamp Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3915	Lophostemon suaveolens	Swamp Box	170		170	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3916	Corymbia tessellaris	Moreton Bay Ash	170		170	14	2	2.0	1.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3917	Eucalyptus siderophloia	Grey Ironbark	260		260	19	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3918	Corymbia intermedia	Pink Bloodwood	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3919	Lophostemon suaveolens	Swamp Box	190		190	14	2	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3920	Corymbia intermedia	Pink Bloodwood	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3921	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	17	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3922	Lophostemon suaveolens	Swamp Box	140	130	191	12	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3923	Corymbia citriodora	Spotted Gum	200	80, 100	237	18	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3924	Corymbia citriodora	Spotted Gum	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3925	Corymbia citriodora	Spotted Gum	150		150	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3926	Corymbia intermedia	Pink Bloodwood	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3927	Corymbia citriodora	Spotted Gum	220	230, 170, 100	374	18	7	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3928	Corymbia citriodora	Spotted Gum	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3929	Corymbia intermedia	Pink Bloodwood	270		270	16	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3930	Corymbia citriodora	Spotted Gum	100		100	15	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3931	Corymbia citriodora	Spotted Gum	260		260	20	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3932	Angophora leiocarpa	Smooth-barked Apple	210		210	14	2	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3933	Corymbia citriodora	Spotted Gum	130		130	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3934	Corymbia intermedia	Pink Bloodwood	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3935	Corymbia tessellaris	Moreton Bay Ash	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3936	Corymbia intermedia	Pink Bloodwood	190		190	12	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3937	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	23	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3938	Acacia disparrima	Hickory Wattle	150		150	9	2	2.0	1.5	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3939	Corymbia citriodora	Spotted Gum	330		330	22	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3940	Angophora leiocarpa	Smooth-barked Apple	190		190	14	2	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3941	Angophora leiocarpa	Smooth-barked Apple	290		290	15	3	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3942	Acacia concurrens	Black Wattle	150		150	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3943	Corymbia intermedia	Pink Bloodwood	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3944	Eucalyptus tereticornis	Forest Red Gum	400		400	25	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3945	Corymbia intermedia	Pink Bloodwood	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3946	Corymbia intermedia	Pink Bloodwood	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3947	Eucalyptus tereticornis	Forest Red Gum	220		220	17	3	2.6	1.8	One-sided	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3948	Angophora leiocarpa	Smooth-barked Apple	270		270	17	6	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3949	Eucalyptus tereticornis	Forest Red Gum	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3950	DEAD/STAG		780		780	12	1	9.4	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Remove
3951	Eucalyptus tereticornis	Forest Red Gum	280		280	18	3	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3952	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	19	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3953	Corymbia intermedia	Pink Bloodwood	310		310	16	5	3.7	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3954	Corymbia intermedia	Pink Bloodwood	460		460	22	11	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3955	Angophora leiocarpa	Smooth-barked Apple	160		160	12	3	2.0	1.5	One-sided	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3956	Acacia disparrima	Hickory Wattle	170		170	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
3957	Acacia disparrima	Hickory Wattle	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3958	Corymbia intermedia	Pink Bloodwood	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3959	Corymbia tessellaris	Moreton Bay Ash	100		100	11	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3960	Acacia disparrima	Hickory Wattle	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3961	Acacia disparrima	Hickory Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3962	Corymbia intermedia	Pink Bloodwood	510		510	23	12	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3963	Acacia disparrima	Hickory Wattle	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3964	Lophostemon suaveolens	Swamp Box	230		230	14	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3965	Lophostemon suaveolens	Swamp Box	250		250	16	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3966	Acacia disparrima	Hickory Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3967	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
3968	Corymbia tessellaris	Moreton Bay Ash	430		430	19	6	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3969	Lophostemon suaveolens	Swamp Box	140		140	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3970	Corymbia intermedia	Pink Bloodwood	350		350	17	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3971	Acacia disparrima	Hickory Wattle	220		220	11	3	2.6	1.8	One-sided	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3972	Angophora leiocarpa	Smooth-barked Apple	410		410	17	9	4.9	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3973	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	20	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3974	Acacia disparrima	Hickory Wattle	220		220	13	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3975	Eucalyptus tereticornis	Forest Red Gum	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3976	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3977	Eucalyptus tereticornis	Forest Red Gum	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3978	Lophostemon suaveolens	Swamp Box	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3979	Lophostemon suaveolens	Swamp Box	210		210	13	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3980	Lophostemon suaveolens	Swamp Box	240		240	12	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3981	Corymbia intermedia	Pink Bloodwood	280		280	18	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3982	Lophostemon suaveolens	Swamp Box	340		340	17	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3983	Corymbia tessellaris	Moreton Bay Ash	110		110	16	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3984	Lophostemon suaveolens	Swamp Box	160		160	14	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3985	Acacia disparrima	Hickory Wattle	150		150	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3986	Alphitonia excelsa	Soap Tree	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3987	Acacia disparrima	Hickory Wattle	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3988	Eucalyptus tereticornis	Forest Red Gum	290		290	16	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3989	Lophostemon suaveolens	Swamp Box	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3990	Lophostemon suaveolens	Swamp Box	240		240	13	3	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3991	Acacia disparrima	Hickory Wattle	250		250	12	5	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3992	Eucalyptus tereticornis	Forest Red Gum	150		150	12	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3993	Lophostemon suaveolens	Swamp Box	260		260	14	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3994	Eucalyptus tereticornis	Forest Red Gum	330		330	17	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3995	Lophostemon suaveolens	Swamp Box	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3996	Corymbia citriodora	Spotted Gum	290		290	9	5	3.5	2.0	Regular	-	-	-	-	-	Typical	Major	-	-	-	Poor	-	-	-	-	-	-		Remove for basin works
3997	Eucalyptus tereticornis	Forest Red Gum	620		620	22	14	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3998	Lophostemon suaveolens	Swamp Box	280		280	16	3	3.4	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
3999	Lophostemon suaveolens	Swamp Box	220		220	16	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4000	Lophostemon suaveolens	Swamp Box	250		250	16	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4001	Lophostemon suaveolens	Swamp Box	230		230	15	3	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4002	Lophostemon suaveolens	Swamp Box	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4003	Lophostemon suaveolens	Swamp Box	140		140	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4004	Alphitonia excelsa	Soap Tree	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4005	Eucalyptus tereticornis	Forest Red Gum	280		280	20	3	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4006	Lophostemon suaveolens	Swamp Box	220		220	15	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4007	Alphitonia excelsa	Soap Tree	240		240	15	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4008	Lophostemon suaveolens	Swamp Box	350		350	16	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4009	Lophostemon suaveolens	Swamp Box	280	270	389	18	6	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4010	Lophostemon suaveolens	Swamp Box	170		170	7	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4011	Lophostemon suaveolens	Swamp Box	250	260	361	16	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4012	Lophostemon suaveolens	Swamp Box	240		240	18	3	2.9	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4013	Lophostemon suaveolens	Swamp Box	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4014	Lophostemon suaveolens	Swamp Box	200	180	269	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4015	Lophostemon suaveolens	Swamp Box	150		150	14	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4016	Lophostemon suaveolens	Swamp Box	110		110	11	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4017	Lophostemon suaveolens	Swamp Box	150	110	186	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4018	Lophostemon suaveolens	Swamp Box	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4019	Alphitonia excelsa	Soap Tree	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4020	Lophostemon suaveolens	Swamp Box	180	150	234	15	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4021	Lophostemon suaveolens	Swamp Box	330		330	5	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4022	Lophostemon suaveolens	Swamp Box	130		130	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4023	Eucalyptus tereticornis	Forest Red Gum	290		290	17	6	3.5	2.0	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4024	Corymbia intermedia	Pink Bloodwood	340		340	19	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4025	Angophora leiocarpa	Smooth-barked Apple	110		110	13	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4026	Angophora leiocarpa	Smooth-barked Apple	110		110	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4027	Corymbia citriodora	Spotted Gum	120		120	14	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4028	Alphitonia excelsa	Soap Tree	150		150	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4029	Lophostemon suaveolens	Swamp Box	140		140	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4030	Alphitonia excelsa	Soap Tree	190		190	16	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4031	Acacia concurrens	Black Wattle	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4032	Corymbia intermedia	Pink Bloodwood	140		140	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4033	Acacia disparrima	Hickory Wattle	200		200	16	5	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4034	Corymbia intermedia	Pink Bloodwood	160		160	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4035	Allocasuarina littoralis	Black She Oak	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4036	Acacia disparrima	Hickory Wattle	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4037	Acacia concurrens	Black Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4038	Angophora leiocarpa	Smooth-barked Apple	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4039	Lophostemon suaveolens	Swamp Box	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4040	Lophostemon suaveolens	Swamp Box	270		270	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4041	Lophostemon suaveolens	Swamp Box	260	120	286	17	3	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4042	Lophostemon suaveolens	Swamp Box	380		380	19	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4043	Corymbia intermedia	Pink Bloodwood	570		570	25	12	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4044	Lophostemon suaveolens	Swamp Box	180		180	16	4	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4045	Eucalyptus tereticornis	Forest Red Gum	550		550	27	14	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4046	Lophostemon suaveolens	Swamp Box	400		400	21	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4047	Lophostemon suaveolens	Swamp Box	200		200	17	5	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4048	Lophostemon suaveolens	Swamp Box	240		240	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4049	Lophostemon suaveolens	Swamp Box	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4050	Lophostemon suaveolens	Swamp Box	120		120	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4051	Lophostemon suaveolens	Swamp Box	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4052	Lophostemon suaveolens	Swamp Box	140		140	11	3	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4053	Eucalyptus tereticornis	Forest Red Gum	630		630	28	16	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4054	Lophostemon suaveolens	Swamp Box	290		290	18	6	3.5	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4055	Lophostemon suaveolens	Swamp Box	200		200	14	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4056	Lophostemon suaveolens	Swamp Box	170		170	14	3	2.0	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4057	Corymbia intermedia	Pink Bloodwood	250		250	17	4	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4058	Eucalyptus tereticornis	Forest Red Gum	440		440	27	10	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4059	Lophostemon suaveolens	Swamp Box	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4060	Corymbia intermedia	Pink Bloodwood	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4061	Lophostemon suaveolens	Swamp Box	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4062	Corymbia intermedia	Pink Bloodwood	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4063	Alphitonia excelsa	Soap Tree	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4064	Lophostemon suaveolens	Swamp Box	190	110	220	15	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4065	Eucalyptus tereticornis	Forest Red Gum	430		430	28	16	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4066	Lophostemon suaveolens	Swamp Box	160		160	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4067	Eucalyptus tereticornis	Forest Red Gum	250		250	24	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4068	Lophostemon suaveolens	Swamp Box	240		240	19	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4069	Alphitonia excelsa	Soap Tree	190		190	18	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4070	Lophostemon suaveolens	Swamp Box	150		150	17	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4071	Alphitonia excelsa	Soap Tree	190		190	18	5	2.3	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4072	Lophostemon suaveolens	Swamp Box	240		240	21	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4073	Lophostemon suaveolens	Swamp Box	320	170	362	18	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4074	Lophostemon suaveolens	Swamp Box	250		250	19	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4075	Lophostemon suaveolens	Swamp Box	210	200	290	22	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4076	Eucalyptus tereticornis	Forest Red Gum	460		460	25	10	5.5	2.4	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4077	Lophostemon suaveolens	Swamp Box	320		320	26	10	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4078	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4079	Lophostemon suaveolens	Swamp Box	250		250	17	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4080	Lophostemon suaveolens	Swamp Box	120		120	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4081	Acacia disparrima	Hickory Wattle	160		160	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4082	Angophora leiocarpa	Smooth-barked Apple	250		250	27	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4083	Lophostemon suaveolens	Swamp Box	220		220	21	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4084	Corymbia intermedia	Pink Bloodwood	280		280	19	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4085	Acacia disparrima	Hickory Wattle	190		190	17	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4086	Alphitonia excelsa	Soap Tree	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4087	Corymbia intermedia	Pink Bloodwood	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4088	Lophostemon suaveolens	Swamp Box	190		190	16	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4089	Lophostemon suaveolens	Swamp Box	280		280	17	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4090	Acacia disparrima	Hickory Wattle	180		180	14	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4091	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4092	Lophostemon suaveolens	Swamp Box	290		290	18	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4093	Eucalyptus tereticornis	Forest Red Gum	360		360	27	12	4.3	2.2	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4094	Lophostemon suaveolens	Swamp Box	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4095	Alphitonia excelsa	Soap Tree	160		160	10	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
4096	Lophostemon suaveolens	Swamp Box	120		120	12	3	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4097	Eucalyptus tereticornis	Forest Red Gum	450		450	26	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4098	Lophostemon suaveolens	Swamp Box	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4099	Lophostemon suaveolens	Swamp Box	280		280	18	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4100	Lophostemon suaveolens	Swamp Box	170		170	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4101	Lophostemon suaveolens	Swamp Box	120		120	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4102	Lophostemon suaveolens	Swamp Box	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4103	Lophostemon suaveolens	Swamp Box	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4104	Eucalyptus tereticornis	Forest Red Gum	280		280	19	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4105	Lophostemon suaveolens	Swamp Box	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4106	Eucalyptus tereticornis	Forest Red Gum	290		290	26	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4107	Corymbia intermedia	Pink Bloodwood	330		330	18	6	4.0	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4108	Alphitonia excelsa	Soap Tree	150		150	10	3	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4109	Alphitonia excelsa	Soap Tree	280		280	14	5	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4110	Corymbia intermedia	Pink Bloodwood	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4111	Alphitonia excelsa	Soap Tree	270		270	15	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4112	Eucalyptus tereticornis	Forest Red Gum	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4113	Acacia disparrima	Hickory Wattle	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4114	Eucalyptus crebra	Narrow-leaved Ironbark	160	170	233	16	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4115	Lophostemon suaveolens	Swamp Box	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4116	Lophostemon suaveolens	Swamp Box	190		190	16	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4117	Lophostemon suaveolens	Swamp Box	270		270	20	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4118	Eucalyptus tereticornis	Forest Red Gum	760		760	27	14	9.1	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4119	Angophora leiocarpa	Smooth-barked Apple	150		150	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4120	Angophora leiocarpa	Smooth-barked Apple	750		750	26	12	9.0	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4121	Eucalyptus tereticornis	Forest Red Gum	110		110	11	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4122	Allocasuarina littoralis	Black She Oak	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4123	Eucalyptus tereticornis	Forest Red Gum	110		110	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4124	Eucalyptus tereticornis	Forest Red Gum	620		620	27	10	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4125	Eucalyptus tereticornis	Forest Red Gum	660		660	27	9	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4126	Eucalyptus tereticornis	Forest Red Gum	660		660	26	14	7.9	2.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4127	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	23	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4128	Eucalyptus tereticornis	Forest Red Gum	600		600	28	12	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4129	Corymbia citriodora	Spotted Gum	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4130	Eucalyptus siderophloia	Grey Ironbark	250		250	16	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4131	Eucalyptus siderophloia	Grey Ironbark	230		230	16	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4132	Eucalyptus siderophloia	Grey Ironbark	290		290	17	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4133	Eucalyptus siderophloia	Grey Ironbark	210		210	8	3	2.5	1.7	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4134	Eucalyptus siderophloia	Grey Ironbark	270		270	17	4	3.2	1.9	One-sided	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4135	Eucalyptus tereticornis	Forest Red Gum	250		250	17	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4136	Casuarina cunninghamiana	River Sheoak	300		300	22	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4137	Alphitonia excelsa	Soap Tree	230		230	13	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4138	Casuarina cunninghamiana	River Sheoak	360		360	25	12	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4139	Casuarina cunninghamiana	River Sheoak	275		275	22	9	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4140	Casuarina cunninghamiana	River Sheoak	280		280	22	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4141	Melia azedarach	White Cedar	180		180	12	8	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4142	DEAD/STAG		295		295	19	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4143	Lophostemon suaveolens	Swamp Box	190		190	16	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4144	Angophora subvelutina	Broad-leaved Apple	165		165	13	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4145	Casuarina cunninghamiana	River Sheoak	285	200	348	21	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4146	Casuarina cunninghamiana	River Sheoak	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4147	Angophora subvelutina	Broad-leaved Apple	255		255	16	7	3.1	1.9	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4148	Angophora subvelutina	Broad-leaved Apple	520		520	22	11	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4149	Alphitonia excelsa	Soap Tree	155		155	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4150	Angophora subvelutina	Broad-leaved Apple	640		640	23	11	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4151	Lophostemon suaveolens	Swamp Box	165		165	11	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4152	Lophostemon suaveolens	Swamp Box	150		150	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4153	Alphitonia excelsa	Soap Tree	155		155	11	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4154	Angophora subvelutina	Broad-leaved Apple	280		280	17	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4155	Corymbia tessellaris	Moreton Bay Ash	130		130	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4156	Angophora subvelutina	Broad-leaved Apple	430		430	22	9	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4157	Corymbia tessellaris	Moreton Bay Ash	195	100	219	16	5	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4158	Acacia melanoxylon	Australian Blackwood	175		175	12	5	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4159	Corymbia tessellaris	Moreton Bay Ash	280		280	17	8	3.4	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4160	Eucalyptus tereticornis	Forest Red Gum	275		275	18	4	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4161	Eucalyptus tereticornis	Forest Red Gum	295		295	21	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4162	Angophora subvelutina	Broad-leaved Apple	165		165	12	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4163	Alphitonia excelsa	Soap Tree	180		180	13	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4164	Corymbia tessellaris	Moreton Bay Ash	160	125	203	13	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4165	Angophora subvelutina	Broad-leaved Apple	390		390	19	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4166	Alphitonia excelsa	Soap Tree	165		165	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4167	Eucalyptus tereticornis	Forest Red Gum	400		400	24	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4168	Eucalyptus tereticornis	Forest Red Gum	230		230	21	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4169	Corymbia tessellaris	Moreton Bay Ash	140		140	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4170	Acacia disparrima	Hickory Wattle	130		130	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4171	Angophora subvelutina	Broad-leaved Apple	585		585	22	12	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4172	Acacia disparrima	Hickory Wattle	240		240	11	6	2.9	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
4173	Lophostemon suaveolens	Swamp Box	145		145	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4174	Alphitonia excelsa	Soap Tree	125		125	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4175	Angophora subvelutina	Broad-leaved Apple	420		420	24	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4176	Alphitonia excelsa	Soap Tree	265		265	12	7	3.2	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4177	Lophostemon suaveolens	Swamp Box	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4178	Acacia melanoxylon	Australian Blackwood	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4179	Alphitonia excelsa	Soap Tree	155	90	179	12	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4180	Lophostemon suaveolens	Swamp Box	275		275	14	5	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4181	Lophostemon suaveolens	Swamp Box	385		385	16	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4182	Acacia disparrima	Hickory Wattle	170		170	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4183	Corymbia tessellaris	Moreton Bay Ash	240		240	15	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
4184	Corymbia tessellaris	Moreton Bay Ash	220		220	17	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4185	Acacia disparrima	Hickory Wattle	165		165	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4186	Lophostemon suaveolens	Swamp Box	230		230	14	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4187	Lophostemon suaveolens	Swamp Box	265		265	11	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4188	Corymbia tessellaris	Moreton Bay Ash	180		180	11	8	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Poor	-	-	-	-	-	-		Retain
4189	Acacia disparrima	Hickory Wattle	195		195	9	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4190	Acacia disparrima	Hickory Wattle	175		175	9	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4191	Alphitonia excelsa	Soap Tree	175		175	12	5	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4192	Eucalyptus crebra	Narrow-leaved Ironbark	660		660	26	9	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
4193	Eucalyptus tereticornis	Forest Red Gum	185		185	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4194	Acacia disparrima	Hickory Wattle	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4195	Lophostemon suaveolens	Swamp Box	135		135	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4196	Angophora subvelutina	Broad-leaved Apple	275		275	16	7	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4197	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	17	7	4.3	2.2	Regular	-	-	-	-	Lopped	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
4198	Lophostemon suaveolens	Swamp Box	135		135	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4199	Lophostemon suaveolens	Swamp Box	165		165	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4200	Lophostemon suaveolens	Swamp Box	145		145	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4201	Lophostemon suaveolens	Swamp Box	265		265	11	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4202	Lophostemon suaveolens	Swamp Box	270		270	13	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4203	Alphitonia excelsa	Soap Tree	180		180	11	5	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4204	Alphitonia excelsa	Soap Tree	200		200	11	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4205	Melaleuca irbyana	Weeping Paperbark	275		275	7	5	3.3	1.9	One-sided	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4206	Allocasuarina littoralis	Black She Oak	160		160	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4207	Corymbia intermedia	Pink Bloodwood	210		210	10	3	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Approved to remove
4208	Corymbia citriodora	Spotted Gum	320		320	16	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4209	Corymbia citriodora	Spotted Gum	195		195	13	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4210	Corymbia citriodora	Spotted Gum	185		185	14	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4211	Alphitonia excelsa	Soap Tree	125		125	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4212	Alphitonia excelsa	Soap Tree	105		105	8	2	2.0	1.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4213	Corymbia citriodora	Spotted Gum	105		105	11	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4214	Alphitonia excelsa	Soap Tree	105	50	116	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4215	Corymbia citriodora	Spotted Gum	275		275	18	5	3.3	1.9	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4216	Corymbia citriodora	Spotted Gum	135		135	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4217	Corymbia citriodora	Spotted Gum	275		275	19	3	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4218	Corymbia citriodora	Spotted Gum	130		130	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4219	Corymbia citriodora	Spotted Gum	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4220	Alphitonia excelsa	Soap Tree	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4221	Corymbia citriodora	Spotted Gum	220		220	17	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4222	Corymbia citriodora	Spotted Gum	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4223	DEAD/STAG		275		275	18	3	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4224	Corymbia intermedia	Pink Bloodwood	275		275	17	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4225	Eucalyptus crebra	Narrow-leaved Ironbark	165		165	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4226	Eucalyptus crebra	Narrow-leaved Ironbark	170		170	14	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4227	Eucalyptus tereticornis	Forest Red Gum	280		280	16	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4228	Corymbia citriodora	Spotted Gum	340		340	21	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4229	Eucalyptus crebra	Narrow-leaved Ironbark	150		150	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4230	Corymbia citriodora	Spotted Gum	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4231	Eucalyptus moluccana	Gum Topped Box	290	180	341	17	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4232	Corymbia citriodora	Spotted Gum	195		195	16	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4233	Corymbia citriodora	Spotted Gum	195		195	17	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4234	Corymbia citriodora	Spotted Gum	175		175	15	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4235	Eucalyptus tereticornis	Forest Red Gum	320		320	19	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4236	Corymbia citriodora	Spotted Gum	420		420	21	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4237	Corymbia citriodora	Spotted Gum	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4238	Eucalyptus moluccana	Gum Topped Box	190	100	215	15	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4239	Corymbia citriodora	Spotted Gum	340	160, 105, 65	396	22	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4240	Eucalyptus moluccana	Gum Topped Box	230		230	12	5	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4241	Corymbia citriodora	Spotted Gum	160	80, 65, 95, 85	229	13	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4242	Corymbia citriodora	Spotted Gum	185		185	11	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4243	DEAD/STAG		360		360	24	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4244	Corymbia citriodora	Spotted Gum	205		205	16	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4245	Corymbia citriodora	Spotted Gum	165		165	11	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4246	Eucalyptus crebra	Narrow-leaved Ironbark	155		155	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4247	Eucalyptus tereticornis	Forest Red Gum	165		165	12	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4248	Corymbia citriodora	Spotted Gum	260	130	291	18	6	3.5	2.0	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4249	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	13	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Approved to remove
4250	Corymbia citriodora	Spotted Gum	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4251	Corymbia citriodora	Spotted Gum	295		295	18	6	3.5	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4252	Eucalyptus moluccana	Gum Topped Box	175		175	14	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4253	Corymbia citriodora	Spotted Gum	270		270	15	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4254	Corymbia citriodora	Spotted Gum	390		390	23	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4255	Corymbia citriodora	Spotted Gum	145		145	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4256	Eucalyptus crebra	Narrow-leaved Ironbark	165		165	12	4	2.0	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4257	Corymbia citriodora	Spotted Gum	325		325	18	5	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4258	Eucalyptus crebra	Narrow-leaved Ironbark	145		145	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4259	Eucalyptus tereticornis	Forest Red Gum	165		165	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4260	Corymbia citriodora	Spotted Gum	145		145	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4261	Eucalyptus tereticornis	Forest Red Gum	165		165	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4262	Eucalyptus crebra	Narrow-leaved Ironbark	345		345	22	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4263	Corymbia citriodora	Spotted Gum	365	170	403	18	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4264	Corymbia citriodora	Spotted Gum	185		185	14	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4265	Corymbia citriodora	Spotted Gum	390		390	24	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4266	Corymbia citriodora	Spotted Gum	165		165	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4267	Corymbia citriodora	Spotted Gum	310		310	19	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4268	Corymbia citriodora	Spotted Gum	185		185	15	3	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4269	Eucalyptus crebra	Narrow-leaved Ironbark	145		145	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4270	Corymbia tessellaris	Moreton Bay Ash	225		225	16	4	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4271	Alphitonia excelsa	Soap Tree	165		165	11	5	2.0	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4272	Angophora leiocarpa	Smooth-barked Apple	195		195	11	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4273	Eucalyptus tereticornis	Forest Red Gum	285		285	15	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4274	Corymbia citriodora	Spotted Gum	165		165	12	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4275	Eucalyptus tereticornis	Forest Red Gum	230		230	17	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4276	Acacia disparrima	Hickory Wattle	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4277	Alphitonia excelsa	Soap Tree	155		155	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4278	Eucalyptus crebra	Narrow-leaved Ironbark	175		175	15	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4279	Eucalyptus crebra	Narrow-leaved Ironbark	245		245	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4280	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	16	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4281	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	19	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4282	Alphitonia excelsa	Soap Tree	200		200	8	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4283	Alphitonia excelsa	Soap Tree	190		190	7	5	2.3	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4284	Alphitonia excelsa	Soap Tree	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4285	Eucalyptus crebra	Narrow-leaved Ironbark	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4286	Acacia disparrima	Hickory Wattle	140		140	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4287	Acacia disparrima	Hickory Wattle	240		240	9	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4288	Alphitonia excelsa	Soap Tree	165		165	12	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4289	Corymbia citriodora	Spotted Gum	165		165	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4290	Eucalyptus tereticornis	Forest Red Gum	155		155	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4291	Corymbia citriodora	Spotted Gum	125		125	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4292	Alphitonia excelsa	Soap Tree	235		235	12	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4293	Alphitonia excelsa	Soap Tree	205		205	12	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4294	Eucalyptus crebra	Narrow-leaved Ironbark	350	150	381	21	5	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4295	Corymbia citriodora	Spotted Gum	185		185	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4296	Corymbia citriodora	Spotted Gum	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4297	Corymbia citriodora	Spotted Gum	390		390	22	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4298	Alphitonia excelsa	Soap Tree	125	70	143	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4299	Alphitonia excelsa	Soap Tree	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4300	Corymbia citriodora	Spotted Gum	330		330	22	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4301	Eucalyptus crebra	Narrow-leaved Ironbark	300		300	16	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4302	Acacia disparrima	Hickory Wattle	140	80	161	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4303	Eucalyptus crebra	Narrow-leaved Ironbark	285		285	17	6	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4304	Corymbia citriodora	Spotted Gum	305		305	21	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4305	Corymbia citriodora	Spotted Gum	385		385	22	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4306	Corymbia citriodora	Spotted Gum	195		195	17	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4307	Eucalyptus tereticornis	Forest Red Gum	130		130	9	3	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4308	Eucalyptus tereticornis	Forest Red Gum	155		155	15	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4309	Corymbia citriodora	Spotted Gum	385		385	19	8	4.6	2.2	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4310	Corymbia citriodora	Spotted Gum	145		145	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4311	Corymbia citriodora	Spotted Gum	105		105	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4312	Corymbia citriodora	Spotted Gum	375		375	22	9	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4313	Corymbia citriodora	Spotted Gum	265		265	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4314	Eucalyptus tereticornis	Forest Red Gum	230		230	18	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4315	Corymbia citriodora	Spotted Gum	230		230	10	6	2.8	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4316	Eucalyptus tereticornis	Forest Red Gum	375		375	24	8	4.5	2.2	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4317	Corymbia citriodora	Spotted Gum	230		230	15	6	2.8	1.8	Regular	-	-	-	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4318	Acacia disparrima	Hickory Wattle	150	100	180	8	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4319	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	13	5	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4320	Lophostemon suaveolens	Swamp Box	105		105	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4321	Corymbia citriodora	Spotted Gum	185		185	16	4	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Approved to remove
4322	Corymbia citriodora	Spotted Gum	290		290	17	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4323	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	18	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4324	Eucalyptus tereticornis	Forest Red Gum	565		565	22	9	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4325	Corymbia citriodora	Spotted Gum	135		135	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4326	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4327	Corymbia citriodora	Spotted Gum	160	130	206	14	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4328	Eucalyptus tereticornis	Forest Red Gum	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4329	Eucalyptus tereticornis	Forest Red Gum	200		200	16	3	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4330	Alphitonia excelsa	Soap Tree	180		180	11	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4331	Eucalyptus crebra	Narrow-leaved Ironbark	205		205	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4332	Eucalyptus crebra	Narrow-leaved Ironbark	265		265	18	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4333	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	19	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4334	Eucalyptus siderophloia	Grey Ironbark	185		185	13	5	2.2	1.6	One-sided	-	-	-	-	-	Typical	Minor	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4335	Eucalyptus tereticornis	Forest Red Gum	390		390	16	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4336	Eucalyptus crebra	Narrow-leaved Ironbark	265		265	15	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4337	Acacia disparrima	Hickory Wattle	205		205	9	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4338	Eucalyptus tereticornis	Forest Red Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4339	Eucalyptus tereticornis	Forest Red Gum	320		320	17	4	3.8	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4340	Corymbia intermedia	Pink Bloodwood	205		205	16	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4341	Eucalyptus crebra	Narrow-leaved Ironbark	365		365	18	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4342	Eucalyptus tereticornis	Forest Red Gum	200		200	17	6	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4343	Eucalyptus tereticornis	Forest Red Gum	325		325	17	7	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4344	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	17	6	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4345	Corymbia intermedia	Pink Bloodwood	260	210	334	17	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4346	Corymbia citriodora	Spotted Gum	310		310	19	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4347	Corymbia citriodora	Spotted Gum	185		185	15	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4348	Corymbia citriodora	Spotted Gum	270	145	306	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4349	Corymbia citriodora	Spotted Gum	330		330	17	5	4.0	2.1	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4350	Alphitonia excelsa	Soap Tree	220		220	11	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4351	Corymbia citriodora	Spotted Gum	165		165	15	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4352	Eucalyptus tereticornis	Forest Red Gum	300		300	18	6	3.6	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4353	Alphitonia excelsa	Soap Tree	135		135	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4354	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	18	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4355	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	17	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Approved to remove
4356	Corymbia citriodora	Spotted Gum	330		330	17	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4357	Acacia leiocalyx	Early-flowering Black Wattle	185		185	6	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4358	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4359	Acacia leiocalyx	Early-flowering Black Wattle	180	80	197	6	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4360	Corymbia tessellaris	Moreton Bay Ash	195		195	16	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4361	Corymbia citriodora	Spotted Gum	300		300	17	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4362	Acacia leiocalyx	Early-flowering Black Wattle	220		220	7	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4363	Eucalyptus tereticornis	Forest Red Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4364	Corymbia citriodora	Spotted Gum	305		305	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4365	Eucalyptus tereticornis	Forest Red Gum	145		145	13	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4366	Corymbia citriodora	Spotted Gum	285		285	18	8	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4367	Eucalyptus tereticornis	Forest Red Gum	205		205	18	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4368	Eucalyptus crebra	Narrow-leaved Ironbark	205		205	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Remove
4369	Eucalyptus crebra	Narrow-leaved Ironbark	315		315	19	8	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4370	Corymbia henryi	Large-leaved Spotted Gum	285		285	17	7	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4371	Corymbia citriodora	Spotted Gum	345		345	18	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4372	Eucalyptus tereticornis	Forest Red Gum	360		360	21	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4373	Corymbia citriodora	Spotted Gum	330		330	19	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4374	Corymbia citriodora	Spotted Gum	265		265	18	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4375	Eucalyptus crebra	Narrow-leaved Ironbark	365		365	18	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4376	Eucalyptus tereticornis	Forest Red Gum	365		365	18	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4377	Corymbia citriodora	Spotted Gum	350		350	19	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4378	Eucalyptus tereticornis	Forest Red Gum	300		300	20	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4379	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4380	Eucalyptus tereticornis	Forest Red Gum	325		325	17	7	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4381	Corymbia citriodora	Spotted Gum	305		305	17	9	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4382	Acacia leiocalyx	Early-flowering Black Wattle	220	140	261	6	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4383	Eucalyptus tereticornis	Forest Red Gum	295		295	18	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4384	Eucalyptus tereticornis	Forest Red Gum	320		320	19	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4385	Acacia leiocalyx	Early-flowering Black Wattle	270		270	8	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4386	Eucalyptus tereticornis	Forest Red Gum	390		390	19	10	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4387	Corymbia intermedia	Pink Bloodwood	300	100, 90	329	19	8	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
4388	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	19	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4389	Allocasuarina littoralis	Black She Oak	155		155	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4390	Allocasuarina littoralis	Black She Oak	140	130	191	9	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4391	Eucalyptus tereticornis	Forest Red Gum	265		265	17	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4392	Corymbia intermedia	Pink Bloodwood	320		320	18	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4393	Corymbia intermedia	Pink Bloodwood	300		300	19	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4394	Corymbia citriodora	Spotted Gum	180		180	11	5	2.2	1.6	Regular	-	Thinning	-	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
4395	Corymbia citriodora	Spotted Gum	250		250	14	6	3.0	1.8	Regular	-	Thinning	-	-	-	Poor	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
4396	Eucalyptus tereticornis	Forest Red Gum	165	120	204	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4397	Acacia disparrima	Hickory Wattle	190		190	6	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4398	Eucalyptus tereticornis	Forest Red Gum	320	340, 230	520	18	7	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4399	Corymbia intermedia	Pink Bloodwood	270	230	355	14	6	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4400	Corymbia citriodora	Spotted Gum	125		125	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4401	Eucalyptus tereticornis	Forest Red Gum	270		270	17	5	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4402	Corymbia citriodora	Spotted Gum	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4403	Corymbia tessellaris	Moreton Bay Ash	270		270	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4404	Corymbia citriodora	Spotted Gum	240		240	16	3	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4405	Corymbia citriodora	Spotted Gum	160		160	13	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4406	Corymbia citriodora	Spotted Gum	250		250	16	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4407	Corymbia tessellaris	Moreton Bay Ash	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4408	Eucalyptus tereticornis	Forest Red Gum	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4409	Eucalyptus moluccana	Gum Topped Box	530	270	595	23	11	7.1	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4410	Corymbia citriodora	Spotted Gum	205		205	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4411	Eucalyptus tereticornis	Forest Red Gum	220		220	16	5	2.6	1.8	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4412	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	16	5	2.6	1.8	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4413	Angophora floribunda	Rough-barked Apple	200		200	13	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4414	Angophora subvelutina	Broad-leaved Apple	660		660	15	8	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Approved to remove
4415	Acacia disparrima	Hickory Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4416	Eucalyptus tereticornis	Forest Red Gum	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4417	Corymbia intermedia	Pink Bloodwood	360		360	22	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4418	Lophostemon suaveolens	Swamp Box	185		185	12	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4419	Eucalyptus crebra	Narrow-leaved Ironbark	400		400	26	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4420	Eucalyptus tereticornis	Forest Red Gum	400		400	23	8	4.8	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4421	Eucalyptus tereticornis	Forest Red Gum	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
4422	Eucalyptus crebra	Narrow-leaved Ironbark	550		550	27	12	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove for basin works
4423	Acacia leiocalyx	Early-flowering Black Wattle	170		170	11	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Remove
4424	Lophostemon suaveolens	Swamp Box	100	100, 80, 90	186	12	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Remove
4425	Lophostemon suaveolens	Swamp Box	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4426	Lophostemon suaveolens	Swamp Box	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4427	Acacia concurrens	Black Wattle	150		150	13	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4428	Acacia leiocalyx	Early-flowering Black Wattle	210		210	13	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4429	Lophostemon suaveolens	Swamp Box	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4430	Lophostemon suaveolens	Swamp Box	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4431	Corymbia intermedia	Pink Bloodwood	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4432	Acacia leiocalyx	Early-flowering Black Wattle	150		150	10	4	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4433	Acacia leiocalyx	Early-flowering Black Wattle	150		150	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4434	Corymbia citriodora	Spotted Gum	300		300	18	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4435	Acacia disparrima	Hickory Wattle	180		180	10	8	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
4436	Lophostemon suaveolens	Swamp Box	120	80	144	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4437	Acacia concurrens	Black Wattle	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4438	Lophostemon suaveolens	Swamp Box	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4439	Lophostemon suaveolens	Swamp Box	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4440	Eucalyptus tereticornis	Forest Red Gum	100		100	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4441	Lophostemon suaveolens	Swamp Box	70	70	99	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4442	Lophostemon suaveolens	Swamp Box	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4443	Eucalyptus tereticornis	Forest Red Gum	100		100	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4444	Lophostemon suaveolens	Swamp Box	100		100	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4445	Lophostemon suaveolens	Swamp Box	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4446	Eucalyptus tereticornis	Forest Red Gum	110		110	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4447	Lophostemon suaveolens	Swamp Box	110		110	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4448	Eucalyptus tereticornis	Forest Red Gum	120		120	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4449	Acacia leiocalyx	Early-flowering Black Wattle	160		160	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4450	Eucalyptus tereticornis	Forest Red Gum	115		115	11	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4451	Lophostemon suaveolens	Swamp Box	140	100	172	10	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4452	Acacia leiocalyx	Early-flowering Black Wattle	160		160	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4453	Lophostemon suaveolens	Swamp Box	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4454	Eucalyptus tereticornis	Forest Red Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4455	Lophostemon suaveolens	Swamp Box	100		100	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4456	Lophostemon suaveolens	Swamp Box	110		110	9	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4457	Lophostemon suaveolens	Swamp Box	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4458	Lophostemon suaveolens	Swamp Box	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4459	Acacia leiocalyx	Early-flowering Black Wattle	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4460	Eucalyptus tereticornis	Forest Red Gum	130		130	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4461	Lophostemon suaveolens	Swamp Box	160		160	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4462	Acacia leiocalyx	Early-flowering Black Wattle	150		150	9	6	2.0	1.5	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4463	Eucalyptus tereticornis	Forest Red Gum	120		120	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	New	-	-	-	-		Remove
4464	Eucalyptus tereticornis	Forest Red Gum	100		100	9	2	2.0	1.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4465	Lophostemon suaveolens	Swamp Box	160		160	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4466	Acacia leiocalyx	Early-flowering Black Wattle	150	110	186	9	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4467	Acacia leiocalyx	Early-flowering Black Wattle	150		150	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4468	Melaleuca viminalis	Weeping Bottlebrush	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4469	Eucalyptus tereticornis	Forest Red Gum	570		570	26	15	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove
4470	Eucalyptus tereticornis	Forest Red Gum	100		100	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4471	Angophora leiocarpa	Smooth-barked Apple	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4472	Eucalyptus tereticornis	Forest Red Gum	270		270	24	8	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4473	Acacia leiocalyx	Early-flowering Black Wattle	140	140	198	5	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4474	Corymbia intermedia	Pink Bloodwood	350		350	22	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4475	Eucalyptus tereticornis	Forest Red Gum	330	330	467	23	12	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4476	Eucalyptus tereticornis	Forest Red Gum	300		300	22	8	3.6	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4477	Eucalyptus siderophloia	Grey Ironbark	290		290	19	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4478	Corymbia intermedia	Pink Bloodwood	300		300	18	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4479	Acacia disparrima	Hickory Wattle	170		170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4480	Acacia disparrima	Hickory Wattle	130		130	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4481	Angophora leiocarpa	Smooth-barked Apple	170		170	20	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4482	Alphitonia excelsa	Soap Tree	120		120	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4483	Corymbia tessellaris	Moreton Bay Ash	160		160	17	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4484	Corymbia tessellaris	Moreton Bay Ash	150	100	180	18	5	2.2	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4485	Alphitonia excelsa	Soap Tree	120		120	11	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4486	Corymbia tessellaris	Moreton Bay Ash	170		170	16	6	2.0	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4487	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4488	Acacia disparrima	Hickory Wattle	150		150	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4489	Corymbia citriodora	Spotted Gum	100		100	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4490	Acacia disparrima	Hickory Wattle	140		140	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4491	Corymbia citriodora	Spotted Gum	370		370	28	14	4.4	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4492	Corymbia citriodora	Spotted Gum	100		100	13	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4493	Acacia disparrima	Hickory Wattle	180		180	8	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4494	Corymbia citriodora	Spotted Gum	390		390	28	13	4.7	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4495	Corymbia citriodora	Spotted Gum	300		300	23	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4496	Corymbia citriodora	Spotted Gum	610		610	31	16	7.3	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4497	Corymbia citriodora	Spotted Gum	140		140	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4498	Corymbia citriodora	Spotted Gum	420		420	30	15	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4499	Eucalyptus siderophloia	Grey Ironbark	370		370	24	10	4.4	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Retain
4500	Corymbia citriodora	Spotted Gum	430		430	32	15	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4501	Corymbia citriodora	Spotted Gum	450		450	32	14	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4502	Corymbia citriodora	Spotted Gum	260		260	26	8	3.1	1.9	Irregular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4503	Corymbia citriodora	Spotted Gum	360		360	29	9	4.3	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4504	Corymbia citriodora	Spotted Gum	290		290	21	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4505	Corymbia citriodora	Spotted Gum	400		400	30	13	4.8	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4506	Corymbia citriodora	Spotted Gum	390		390	31	10	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4507	Corymbia citriodora	Spotted Gum	340		340	29	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4508	Eucalyptus tereticornis	Forest Red Gum	330		330	28	14	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4509	Eucalyptus tereticornis	Forest Red Gum	480		480	30	15	5.8	2.4	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4510	Corymbia citriodora	Spotted Gum	320		320	26	14	3.8	2.1	Regular	-	-	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4511	Acacia disparrima	Hickory Wattle	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4512	Corymbia citriodora	Spotted Gum	390		390	28	18	4.7	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4513	Corymbia citriodora	Spotted Gum	440		440	27	18	5.3	2.3	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4514	Corymbia citriodora	Spotted Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4515	Corymbia citriodora	Spotted Gum	460		460	31	12	5.5	2.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4516	Corymbia citriodora	Spotted Gum	530		530	27	13	6.4	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4517	Acacia disparrima	Hickory Wattle	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4518	Corymbia citriodora	Spotted Gum	570		570	32	14	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4519	Corymbia citriodora	Spotted Gum	540		540	27	18	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4520	Corymbia citriodora	Spotted Gum	280		280	27	5	3.4	1.9	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4521	Eucalyptus tereticornis	Forest Red Gum	320		320	16	7	3.8	2.1	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4522	Corymbia citriodora	Spotted Gum	370		370	32	11	4.4	2.2	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4523	Corymbia citriodora	Spotted Gum	340		340	30	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4524	Corymbia citriodora	Spotted Gum	530		530	29	12	6.4	2.5	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4525	Corymbia citriodora	Spotted Gum	390		390	26	10	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4526	Corymbia citriodora	Spotted Gum	260		260	23	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4527	Corymbia citriodora	Spotted Gum	420		420	27	14	5.0	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4528	DEAD/STAG		440		440	25	9	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	potential hollows	Retain
4529	Corymbia citriodora	Spotted Gum	690		690	30	18	8.3	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4530	Corymbia citriodora	Spotted Gum	290		290	23	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4531	Corymbia citriodora	Spotted Gum	500		500	31	18	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-	potential sml hollows	Retain
4532	Alphitonia excelsa	Soap Tree	150		150	8	3	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4533	Corymbia citriodora	Spotted Gum	430		430	27	8	5.2	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4534	Corymbia intermedia	Pink Bloodwood	180		180	13	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4535	Alphitonia excelsa	Soap Tree	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4536	Eucalyptus tereticornis	Forest Red Gum	470		470	23	16	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4537	Corymbia citriodora	Spotted Gum	780		780	33	19	9.4	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4538	Corymbia citriodora	Spotted Gum	120		120	10	2	2.0	1.4	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4539	Alphitonia excelsa	Soap Tree	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4540	Alphitonia excelsa	Soap Tree	130	120	177	9	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4541	Alphitonia excelsa	Soap Tree	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4542	Acacia concurrens	Black Wattle	120	80	144	9	6	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
4543	Lophostemon suaveolens	Swamp Box	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4544	Acacia concurrens	Black Wattle	150	130	198	9	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4545	Lophostemon suaveolens	Swamp Box	120		120	7	2	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4546	Alphitonia excelsa	Soap Tree	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4547	Eucalyptus tereticornis	Forest Red Gum	650		650	27	12	7.8	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4548	Acacia disparrima	Hickory Wattle	160		160	9	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4549	Lophostemon suaveolens	Swamp Box	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4550	Acacia disparrima	Hickory Wattle	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4551	Corymbia intermedia	Pink Bloodwood	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4552	Eucalyptus crebra	Narrow-leaved Ironbark	380		380	22	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4553	Alphitonia excelsa	Soap Tree	210		210	12	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4554	Alphitonia excelsa	Soap Tree	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
4555	Alphitonia excelsa	Soap Tree	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4556	Alphitonia excelsa	Soap Tree	180		180	12	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-	Ants nest	Retain
4557	Eucalyptus tereticornis	Forest Red Gum	440		440	27	12	5.3	2.3	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4558	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	18	6	3.2	1.9	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4559	Eucalyptus tereticornis	Forest Red Gum	540		540	24	15	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4560	Eucalyptus tereticornis	Forest Red Gum	400		400	26	14	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4561	Eucalyptus crebra	Narrow-leaved Ironbark	410		410	27	10	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4562	Alphitonia excelsa	Soap Tree	180		180	12	4	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
4563	Alphitonia excelsa	Soap Tree	170		170	12	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4564	Alphitonia excelsa	Soap Tree	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4565	Corymbia intermedia	Pink Bloodwood	250		250	16	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4566	Corymbia intermedia	Pink Bloodwood	410		410	26	12	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4567	Alphitonia excelsa	Soap Tree	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4568	Corymbia intermedia	Pink Bloodwood	220		220	20	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4569	Eucalyptus crebra	Narrow-leaved Ironbark	480		480	26	16	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4570	Alphitonia excelsa	Soap Tree	150		150	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4571	Acacia disparrima	Hickory Wattle	160		160	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4572	Lophostemon suaveolens	Swamp Box	150		150	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4573	Petalostigma pubescens	Quinine Bush	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4574	Lophostemon suaveolens	Swamp Box	220		220	17	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4575	Acacia leiocalyx	Early-flowering Black Wattle	150		150	12	5	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4576	Lophostemon suaveolens	Swamp Box	140		140	16	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4577	Acacia leiocalyx	Early-flowering Black Wattle	200		200	12	7	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4578	Angophora subvelutina	Broad-leaved Apple	340		340	24	9	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4579	Corymbia intermedia	Pink Bloodwood	240		240	25	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4580	Eucalyptus tereticornis	Forest Red Gum	190		190	19	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4581	Eucalyptus tereticornis	Forest Red Gum	260		260	21	3	3.1	1.9	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4582	Eucalyptus tereticornis	Forest Red Gum	360	330	488	23	12	5.9	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4583	Corymbia intermedia	Pink Bloodwood	280		280	21	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4584	Acacia leiocalyx	Early-flowering Black Wattle	130		130	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4585	Corymbia intermedia	Pink Bloodwood	310		310	21	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4586	Acacia leiocalyx	Early-flowering Black Wattle	140		140	5	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4587	Eucalyptus tereticornis	Forest Red Gum	340		340	20	13	4.1	2.1	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4588	Acacia leiocalyx	Early-flowering Black Wattle	140	100, 110	204	4	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4589	Corymbia intermedia	Pink Bloodwood	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4590	Corymbia intermedia	Pink Bloodwood	290		290	15	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
4591	Corymbia intermedia	Pink Bloodwood	310		310	19	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4592	Corymbia intermedia	Pink Bloodwood	340		340	16	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4593	Eucalyptus siderophloia	Grey Ironbark	430		430	20	10	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4594	Allocasuarina littoralis	Black She Oak	200		200	8	3	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4595	Acacia leiocalyx	Early-flowering Black Wattle	130		130	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4596	Acacia leiocalyx	Early-flowering Black Wattle	140		140	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4597	Angophora leiocarpa	Smooth-barked Apple	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4598	Acacia leiocalyx	Early-flowering Black Wattle	160		160	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4599	Acacia leiocalyx	Early-flowering Black Wattle	170		170	8	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4600	Acacia leiocalyx	Early-flowering Black Wattle	120		120	5	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4601	Corymbia intermedia	Pink Bloodwood	330		330	14	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4602	Corymbia intermedia	Pink Bloodwood	350		350	16	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4603	Corymbia intermedia	Pink Bloodwood	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4604	Eucalyptus tereticornis	Forest Red Gum	420		420	22	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4605	Corymbia citriodora	Spotted Gum	370		370	22	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4606	Acacia leiocalyx	Early-flowering Black Wattle	130	120, 120, 140	256	6	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4607	Corymbia intermedia	Pink Bloodwood	310		310	26	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4608	Eucalyptus tereticornis	Forest Red Gum	300		300	22	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4609	Eucalyptus tereticornis	Forest Red Gum	320		320	25	8	3.8	2.1	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4610	Lophostemon suaveolens	Swamp Box	140	130	191	6	2	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4611	Eucalyptus tereticornis	Forest Red Gum	300		300	21	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4612	Eucalyptus tereticornis	Forest Red Gum	330		330	23	6	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4613	Corymbia intermedia	Pink Bloodwood	400		400	22	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4614	Corymbia intermedia	Pink Bloodwood	360		360	20	7	4.3	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4615	Corymbia intermedia	Pink Bloodwood	170		170	7	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4616	Eucalyptus tereticornis	Forest Red Gum	250		250	15	3	3.0	1.8	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4617	Corymbia intermedia	Pink Bloodwood	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4618	Eucalyptus siderophloia	Grey Ironbark	370		370	19	12	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4619	Eucalyptus tereticornis	Forest Red Gum	350		350	17	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4620	Lophostemon suaveolens	Swamp Box	220	170	278	14	3	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4621	Acacia leiocalyx	Early-flowering Black Wattle	250		250	10	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4622	Lophostemon suaveolens	Swamp Box	220		220	10	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4623	Corymbia intermedia	Pink Bloodwood	250		250	19	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4624	Eucalyptus tereticornis	Forest Red Gum	210	140	252	12	4	3.0	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4625	Corymbia intermedia	Pink Bloodwood	260		260	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4626	Corymbia intermedia	Pink Bloodwood	280		280	19	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4627	Eucalyptus tereticornis	Forest Red Gum	270		270	17	4	3.2	1.9	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4628	Eucalyptus tereticornis	Forest Red Gum	390		390	20	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4629	Lophostemon suaveolens	Swamp Box	270		270	10	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4630	Angophora leiocarpa	Smooth-barked Apple	290		290	17	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
4631	Corymbia intermedia	Pink Bloodwood	360		360	22	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4632	Corymbia intermedia	Pink Bloodwood	300		300	16	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4633	Angophora leiocarpa	Smooth-barked Apple	270		270	5	2	3.2	1.9	Regular	-	-	-	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4634	Eucalyptus tereticornis	Forest Red Gum	390		390	24	6	4.7	2.2	Regular	-	-	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4635	Lophostemon suaveolens	Swamp Box	300		300	12	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4636	Acacia leiocalyx	Early-flowering Black Wattle	230		230	8	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4637	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4638	Corymbia intermedia	Pink Bloodwood	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4639	Corymbia intermedia	Pink Bloodwood	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4640	Eucalyptus tereticornis	Forest Red Gum	380		380	20	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4641	Eucalyptus tereticornis	Forest Red Gum	160		160	12	2	2.0	1.5	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4642	Eucalyptus tereticornis	Forest Red Gum	280		280	15	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4643	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	16	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4644	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4645	Eucalyptus tereticornis	Forest Red Gum	270		270	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4646	Corymbia citriodora	Spotted Gum	260		260	17	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4647	Eucalyptus tereticornis	Forest Red Gum	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4648	Eucalyptus crebra	Narrow-leaved Ironbark	290		290	22	7	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4649	Eucalyptus carnea	Thick-leaved Mahogany	270		270	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4650	Eucalyptus tereticornis	Forest Red Gum	210		210	15	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4651	Eucalyptus carnea	Thick-leaved Mahogany	210		210	12	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4652	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	21	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4653	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4654	Corymbia citriodora	Spotted Gum	270		270	19	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
4655	Corymbia henryi	Large-leaved Spotted Gum	250		250	15	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4656	Corymbia henryi	Large-leaved Spotted Gum	310		310	20	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4657	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	18	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4658	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	14	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4659	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	Small	-	-		Remove
4660	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	18	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4661	Eucalyptus tereticornis	Forest Red Gum	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4662	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	18	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4663	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	20	4	3.8	2.1	Regular	-	-	Die-back	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4664	Corymbia citriodora	Spotted Gum	260		260	13	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4665	Corymbia citriodora	Spotted Gum	280		280	15	7	3.4	1.9	Irregular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4666	Eucalyptus crebra	Narrow-leaved Ironbark	320		320	18	8	3.8	2.1	One-sided	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4667	Acacia leiocalyx	Early-flowering Black Wattle	140		140	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4668	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4669	Alphitonia excelsa	Soap Tree	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4670	Acacia leiocalyx	Early-flowering Black Wattle	150	150, 100	235	8	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4671	Acacia leiocalyx	Early-flowering Black Wattle	150		150	5	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4672	Acacia leiocalyx	Early-flowering Black Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4673	Corymbia intermedia	Pink Bloodwood	130		130	5	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4674	Eucalyptus tereticornis	Forest Red Gum	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4675	Acacia leiocalyx	Early-flowering Black Wattle	160		160	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4676	Corymbia intermedia	Pink Bloodwood	130		130	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4677	Acacia leiocalyx	Early-flowering Black Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4678	Allocasuarina littoralis	Black She Oak	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4679	Corymbia citriodora	Spotted Gum	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4680	Allocasuarina littoralis	Black She Oak	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4681	Eucalyptus tereticornis	Forest Red Gum	340		340	20	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4682	Lophostemon suaveolens	Swamp Box	100	100	141	5	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4683	Lophostemon suaveolens	Swamp Box	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4684	DEAD/STAG		150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4685	Eucalyptus tereticornis	Forest Red Gum	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4686	Eucalyptus tereticornis	Forest Red Gum	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4687	Allocasuarina littoralis	Black She Oak	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4688	Lophostemon suaveolens	Swamp Box	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4689	Eucalyptus tereticornis	Forest Red Gum	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4690	Lophostemon suaveolens	Swamp Box	320		320	13	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4691	Corymbia intermedia	Pink Bloodwood	120	120	170	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4692	Acacia leiocalyx	Early-flowering Black Wattle	150		150	5	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4693	Eucalyptus tereticornis	Forest Red Gum	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4694	Corymbia citriodora	Spotted Gum	380		380	24	13	4.6	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove
4695	Acacia leiocalyx	Early-flowering Black Wattle	180		180	5	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4696	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4697	Acacia leiocalyx	Early-flowering Black Wattle	150		150	5	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4698	Eucalyptus tereticornis	Forest Red Gum	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4699	Lophostemon suaveolens	Swamp Box	270	260	375	13	7	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4700	Lophostemon suaveolens	Swamp Box	100		100	4	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4701	Lophostemon suaveolens	Swamp Box	180		180	7	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4702	Eucalyptus tereticornis	Forest Red Gum	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4703	Lophostemon suaveolens	Swamp Box	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4704	Eucalyptus tereticornis	Forest Red Gum	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4705	Eucalyptus tereticornis	Forest Red Gum	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4706	Lophostemon suaveolens	Swamp Box	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4707	Lophostemon suaveolens	Swamp Box	300	120	323	14	6	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4708	Lophostemon suaveolens	Swamp Box	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4709	Eucalyptus tereticornis	Forest Red Gum	110	110, 110	191	7	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4710	Corymbia citriodora	Spotted Gum	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4711	Corymbia citriodora	Spotted Gum	350		350	21	11	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4712	Eucalyptus tereticornis	Forest Red Gum	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4713	Lophostemon suaveolens	Swamp Box	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4714	Lophostemon suaveolens	Swamp Box	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4715	Lophostemon suaveolens	Swamp Box	100		100	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4716	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4717	Lophostemon suaveolens	Swamp Box	100		100	4	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4718	Corymbia intermedia	Pink Bloodwood	140		140	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4719	Lophostemon suaveolens	Swamp Box	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4720	Acacia leiocalyx	Early-flowering Black Wattle	160		160	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4721	Allocasuarina littoralis	Black She Oak	140		140	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4722	Acacia leiocalyx	Early-flowering Black Wattle	170		170	6	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4723	Alphitonia excelsa	Soap Tree	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4724	Acacia leiocalyx	Early-flowering Black Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4725	Lophostemon suaveolens	Swamp Box	140		140	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4726	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4727	Eucalyptus tereticornis	Forest Red Gum	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4728	Lophostemon suaveolens	Swamp Box	170		170	6	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4729	Lophostemon suaveolens	Swamp Box	170		170	6	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4730	Corymbia citriodora	Spotted Gum	160		160	16	5	2.0	1.5	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4731	Lophostemon suaveolens	Swamp Box	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4732	Eucalyptus tereticornis	Forest Red Gum	190		190	13	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4733	Eucalyptus crebra	Narrow-leaved Ironbark	200		200	11	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4734	Eucalyptus tereticornis	Forest Red Gum	140	100	172	8	2	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4735	Corymbia citriodora	Spotted Gum	250		250	25	12	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4736	Corymbia intermedia	Pink Bloodwood	390		390	24	12	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4737	Eucalyptus tereticornis	Forest Red Gum	360		360	27	13	4.3	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4738	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	24	14	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4739	Corymbia citriodora	Spotted Gum	380		380	26	13	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4740	Eucalyptus tereticornis	Forest Red Gum	280		280	20	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4741	Eucalyptus tereticornis	Forest Red Gum	320		320	26	16	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4742	Corymbia citriodora	Spotted Gum	630		630	31	17	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4743	Corymbia citriodora	Spotted Gum	170		170	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4744	Corymbia citriodora	Spotted Gum	230		230	15	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4745	Alphitonia excelsa	Soap Tree	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4746	Corymbia citriodora	Spotted Gum	150		150	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4747	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	12	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4748	Acacia disparrima	Hickory Wattle	200		200	7	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4749	Corymbia citriodora	Spotted Gum	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4750	Corymbia citriodora	Spotted Gum	150	80	170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4751	Corymbia citriodora	Spotted Gum	120	80	144	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4752	Eucalyptus crebra	Narrow-leaved Ironbark	170		170	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4753	Corymbia citriodora	Spotted Gum	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4754	Corymbia citriodora	Spotted Gum	180		180	12	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4755	Corymbia citriodora	Spotted Gum	260		260	16	8	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4756	Corymbia citriodora	Spotted Gum	150		150	13	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4757	Alphitonia excelsa	Soap Tree	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4758	Acacia disparrima	Hickory Wattle	110		110	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4759	Corymbia citriodora	Spotted Gum	160		160	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4760	Corymbia citriodora	Spotted Gum	120		120	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4761	Alphitonia excelsa	Soap Tree	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4762	Alphitonia excelsa	Soap Tree	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4763	Corymbia citriodora	Spotted Gum	290		290	25	14	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4764	Acacia disparrima	Hickory Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4765	Corymbia citriodora	Spotted Gum	150		150	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4766	Corymbia citriodora	Spotted Gum	240		240	22	12	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4767	Acacia disparrima	Hickory Wattle	150		150	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4768	Alphitonia excelsa	Soap Tree	100	100	141	6	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4769	Unknow spp.		140		140	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4770	Corymbia citriodora	Spotted Gum	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4771	Unknow spp.		130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4772	Acacia disparrima	Hickory Wattle	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4773	Corymbia citriodora	Spotted Gum	340		340	27	13	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4774	Corymbia citriodora	Spotted Gum	490		490	28	14	5.9	2.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4775	Alphitonia excelsa	Soap Tree	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4776	Acacia disparrima	Hickory Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4777	Corymbia citriodora	Spotted Gum	320		320	26	13	3.8	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4778	Corymbia tessellaris	Moreton Bay Ash	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4779	Corymbia tessellaris	Moreton Bay Ash	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4780	Acacia concurrens	Black Wattle	130		130	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4781	Acacia disparrima	Hickory Wattle	180		180	8	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4782	Acacia disparrima	Hickory Wattle	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4783	Corymbia intermedia	Pink Bloodwood	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4784	Acacia disparrima	Hickory Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4785	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4786	Alphitonia excelsa	Soap Tree	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4787	Corymbia citriodora	Spotted Gum	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4788	Alphitonia excelsa	Soap Tree	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4789	Corymbia citriodora	Spotted Gum	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4790	Acacia disparrima	Hickory Wattle	170		170	7	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4791	Alphitonia excelsa	Soap Tree	110		110	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4792	Eucalyptus tereticornis	Forest Red Gum	280		280	24	10	3.4	1.9	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4793	Acacia disparrima	Hickory Wattle	130		130	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4794	Corymbia intermedia	Pink Bloodwood	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4795	Corymbia citriodora	Spotted Gum	110		110	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4796	Alphitonia excelsa	Soap Tree	150		150	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4797	Alphitonia excelsa	Soap Tree	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4798	Corymbia citriodora	Spotted Gum	450		450	27	14	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4799	Corymbia intermedia	Pink Bloodwood	250		250	17	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4800	Corymbia citriodora	Spotted Gum	630		630	28	16	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4801	Corymbia intermedia	Pink Bloodwood	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4802	Corymbia citriodora	Spotted Gum	110		110	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4803	Corymbia citriodora	Spotted Gum	570		570	29	15	6.8	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4804	Corymbia citriodora	Spotted Gum	410		410	27	15	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4805	Lophostemon suaveolens	Swamp Box	100		100	4	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4806	Corymbia citriodora	Spotted Gum	100		100	11	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4807	DEAD/STAG		390		390	13	3	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-	hollow in trunk	Retain
4808	Corymbia citriodora	Spotted Gum	220		220	13	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4809	Alphitonia excelsa	Soap Tree	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4810	Corymbia citriodora	Spotted Gum	130		130	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4811	Alphitonia excelsa	Soap Tree	150		150	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4812	Corymbia citriodora	Spotted Gum	130		130	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4813	Corymbia citriodora	Spotted Gum	160		160	20	8	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4814	Alphitonia excelsa	Soap Tree	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4815	Eucalyptus crebra	Narrow-leaved Ironbark	410		410	26	14	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4816	Alphitonia excelsa	Soap Tree	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4817	Alphitonia excelsa	Soap Tree	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4818	Acacia disparrima	Hickory Wattle	150		150	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4819	Alphitonia excelsa	Soap Tree	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4820	Alphitonia excelsa	Soap Tree	160		160	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4821	Lophostemon suaveolens	Swamp Box	120		120	5	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4822	Alphitonia excelsa	Soap Tree	190		190	10	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4823	Alphitonia excelsa	Soap Tree	150		150	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4824	Corymbia intermedia	Pink Bloodwood	340		340	27	14	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4825	Alphitonia excelsa	Soap Tree	190		190	10	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4826	Acacia disparrima	Hickory Wattle	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4827	Eucalyptus tereticornis	Forest Red Gum	510		510	28	17	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4828	Angophora leiocarpa	Smooth-barked Apple	230		230	20	6	2.8	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4829	Eucalyptus tereticornis	Forest Red Gum	470		470	26	14	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4830	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4831	Acacia leiocalyx	Early-flowering Black Wattle	120	120	170	8	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4832	Eucalyptus tereticornis	Forest Red Gum	380		380	24	13	4.6	2.2	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
4833	Acacia disparrima	Hickory Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4834	Eucalyptus tereticornis	Forest Red Gum	400		400	27	13	4.8	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4835	Corymbia intermedia	Pink Bloodwood	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4836	Corymbia intermedia	Pink Bloodwood	110		110	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4837	Alphitonia excelsa	Soap Tree	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4838	Alphitonia excelsa	Soap Tree	110		110	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4839	Corymbia intermedia	Pink Bloodwood	410		410	26	16	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4840	Angophora leiocarpa	Smooth-barked Apple	310		310	16	8	3.7	2.0	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	Old	-	-	-	-		Retain
4841	Alphitonia excelsa	Soap Tree	110		110	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4842	Acacia leiocalyx	Early-flowering Black Wattle	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4843	Corymbia intermedia	Pink Bloodwood	280	260	382	22	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4844	Corymbia intermedia	Pink Bloodwood	130		130	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4845	Acacia leiocalyx	Early-flowering Black Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4846	Lophostemon suaveolens	Swamp Box	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4847	Eucalyptus tereticornis	Forest Red Gum	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4848	Corymbia tessellaris	Moreton Bay Ash	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4849	Eucalyptus crebra	Narrow-leaved Ironbark	210		210	19	10	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4850	Eucalyptus tereticornis	Forest Red Gum	350		350	24	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4851	Alphitonia excelsa	Soap Tree	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4852	Eucalyptus crebra	Narrow-leaved Ironbark	160		160	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4853	Eucalyptus crebra	Narrow-leaved Ironbark	180		180	16	8	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4854	Eucalyptus crebra	Narrow-leaved Ironbark	180		180	12	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4855	Corymbia intermedia	Pink Bloodwood	160	180	241	17	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4856	Corymbia intermedia	Pink Bloodwood	180		180	10	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4857	Eucalyptus crebra	Narrow-leaved Ironbark	110		110	5	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4858	Angophora leiocarpa	Smooth-barked Apple	140		140	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4859	Acacia leiocalyx	Early-flowering Black Wattle	240	230	332	6	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4860	Eucalyptus tereticornis	Forest Red Gum	220		220	6	4	2.6	1.8	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4861	Eucalyptus siderophloia	Grey Ironbark	380		380	26	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4862	Eucalyptus tereticornis	Forest Red Gum	560		560	26	15	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove
4863	Eucalyptus tereticornis	Forest Red Gum	260		260	22	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4864	Eucalyptus siderophloia	Grey Ironbark	320	320	453	23	13	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4865	Eucalyptus tereticornis	Forest Red Gum	360		360	25	10	4.3	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4866	Angophora leiocarpa	Smooth-barked Apple	260		260	20	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4867	Eucalyptus tereticornis	Forest Red Gum	490		490	24	14	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4868	Eucalyptus tereticornis	Forest Red Gum	290		290	22	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4869	Corymbia intermedia	Pink Bloodwood	280		280	22	10	3.4	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
4870	Acacia leiocalyx	Early-flowering Black Wattle	160	120	200	7	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4871	Allocasuarina littoralis	Black She Oak	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4872	Acacia leiocalyx	Early-flowering Black Wattle	210	110	237	7	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4873	Acacia leiocalyx	Early-flowering Black Wattle	160		160	5	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4874	Allocasuarina littoralis	Black She Oak	140		140	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4875	Lophostemon suaveolens	Swamp Box	320		320	12	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4876	Eucalyptus saligna	Sydney Blue Gum	260		260	14	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4877	Lophostemon suaveolens	Swamp Box	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4878	Corymbia intermedia	Pink Bloodwood	270		270	14	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4879	Lophostemon suaveolens	Swamp Box	270		270	11	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4880	Corymbia intermedia	Pink Bloodwood	260		260	24	12	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4881	Acacia leiocalyx	Early-flowering Black Wattle	170	170	240	7	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4882	Acacia leiocalyx	Early-flowering Black Wattle	150	150, 120	244	8	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4883	Acacia leiocalyx	Early-flowering Black Wattle	280		280	8	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4884	Acacia leiocalyx	Early-flowering Black Wattle	210		210	8	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4885	Lophostemon suaveolens	Swamp Box	370		370	10	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4886	Corymbia intermedia	Pink Bloodwood	360		360	18	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4887	Corymbia intermedia	Pink Bloodwood	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4888	Corymbia intermedia	Pink Bloodwood	190		190	9	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4889	Eucalyptus tereticornis	Forest Red Gum	260		260	16	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4890	Eucalyptus acmenoides	White Mahogany	270		270	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4891	Eucalyptus tereticornis	Forest Red Gum	270		270	17	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4892	Eucalyptus acmenoides	White Mahogany	280		280	13	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4893	Eucalyptus carnea	Thick-leaved Mahogany	270	250	368	15	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4894	Eucalyptus acmenoides	White Mahogany	320		320	15	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4895	Eucalyptus tereticornis	Forest Red Gum	200		200	18	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4896	Corymbia intermedia	Pink Bloodwood	130	130	184	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4897	Lophostemon suaveolens	Swamp Box	260		260	16	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4898	Eucalyptus tereticornis	Forest Red Gum	270		270	21	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4899	Corymbia intermedia	Pink Bloodwood	250		250	14	9	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4900	Corymbia intermedia	Pink Bloodwood	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4901	Lophostemon suaveolens	Swamp Box	320		320	17	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4902	Eucalyptus siderophloia	Grey Ironbark	420		420	22	14	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4903	Eucalyptus acmenoides	White Mahogany	270		270	14	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4904	Eucalyptus acmenoides	White Mahogany	260		260	14	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4905	Corymbia intermedia	Pink Bloodwood	160	160	226	14	6	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4906	Eucalyptus carnea	Thick-leaved Mahogany	330		330	12	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4907	Eucalyptus carnea	Thick-leaved Mahogany	270		270	14	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4908	Eucalyptus carnea	Thick-leaved Mahogany	260		260	14	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4909	Eucalyptus acmenoides	White Mahogany	280	170	328	14	8	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4910	Corymbia citriodora	Spotted Gum	320	150	353	21	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4911	Eucalyptus tereticornis	Forest Red Gum	550		550	26	13	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4912	Eucalyptus tereticornis	Forest Red Gum	630		630	28	15	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4913	Eucalyptus tereticornis	Forest Red Gum	560		560	26	14	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
4914	Lophostemon suaveolens	Swamp Box	210		210	14	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4915	Lophostemon suaveolens	Swamp Box	180		180	13	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4916	Angophora leiocarpa	Smooth-barked Apple	680		680	17	9	8.2	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4917	Acacia disparrima	Hickory Wattle	240		240	9	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4918	Alphitonia excelsa	Soap Tree	160		160	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4919	Eucalyptus tereticornis	Forest Red Gum	760		760	27	16	9.1	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4920	Eucalyptus tereticornis	Forest Red Gum	600		600	28	15	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4921	Eucalyptus tereticornis	Forest Red Gum	720		720	31	18	8.6	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4922	Eucalyptus tereticornis	Forest Red Gum	560		560	23	12	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4923	Eucalyptus tereticornis	Forest Red Gum	490		490	25	12	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4924	Eucalyptus tereticornis	Forest Red Gum	540		540	26	14	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4925	Corymbia citriodora	Spotted Gum	260	200	328	20	8	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4926	Eucalyptus tereticornis	Forest Red Gum	390		390	24	14	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4927	Corymbia intermedia	Pink Bloodwood	170	160, 100	254	18	9	3.0	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4928	Eucalyptus tereticornis	Forest Red Gum	440		440	25	14	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4929	Eucalyptus tereticornis	Forest Red Gum	550		550	22	12	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4930	Corymbia torelliana	Cadaghi	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4931	Eucalyptus crebra	Narrow-leaved Ironbark	510		510	27	22	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4932	Eucalyptus crebra	Narrow-leaved Ironbark	350		350	27	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4933	Eucalyptus moluccana	Gum Topped Box	530		530	28	16	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4934	Eucalyptus crebra	Narrow-leaved Ironbark	540		540	28	14	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
4935	Corymbia intermedia	Pink Bloodwood	220		220	14	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4936	Lophostemon suaveolens	Swamp Box	200		200	10	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4937	Corymbia intermedia	Pink Bloodwood	300		300	20	14	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4938	Corymbia intermedia	Pink Bloodwood	160		160	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4939	Acacia disparrima	Hickory Wattle	150		150	6	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4940	Eucalyptus tereticornis	Forest Red Gum	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4941	Acacia disparrima	Hickory Wattle	200		200	6	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4942	Acacia disparrima	Hickory Wattle	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4943	Eucalyptus tereticornis	Forest Red Gum	500		500	23	9	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4944	Acacia concurrens	Black Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
4945	Angophora subvelutina	Broad-leaved Apple	300		300	19	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4946	Lophostemon suaveolens	Swamp Box	200		200	18	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4947	Lophostemon suaveolens	Swamp Box	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4948	Corymbia citriodora	Spotted Gum	150		150	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4949	Lophostemon suaveolens	Swamp Box	150		150	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4950	Lophostemon suaveolens	Swamp Box	190		190	13	2	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4951	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4952	Corymbia intermedia	Pink Bloodwood	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4953	Corymbia intermedia	Pink Bloodwood	270		270	20	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4954	Lophostemon suaveolens	Swamp Box	450		450	19	6	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4955	Corymbia citriodora	Spotted Gum	220		220	16	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4956	Acacia concurrens	Black Wattle	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4957	Lophostemon suaveolens	Swamp Box	190		190	16	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4958	Acacia concurrens	Black Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4959	Corymbia citriodora	Spotted Gum	150		150	12	3	2.0	1.5	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4960	Lophostemon suaveolens	Swamp Box	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4961	Corymbia citriodora	Spotted Gum	320		320	23	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4962	Corymbia intermedia	Pink Bloodwood	230		230	16	4	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4963	Corymbia intermedia	Pink Bloodwood	160		160	15	3	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4964	Acacia concurrens	Black Wattle	150		150	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4965	Eucalyptus tereticornis	Forest Red Gum	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4966	Corymbia citriodora	Spotted Gum	150		150	17	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4967	Corymbia intermedia	Pink Bloodwood	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4968	Corymbia citriodora	Spotted Gum	400		400	23	10	4.8	2.3	Irregular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4969	Corymbia intermedia	Pink Bloodwood	240		240	16	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4970	Corymbia intermedia	Pink Bloodwood	250		250	17	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4971	Acacia disparrima	Hickory Wattle	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4972	Corymbia intermedia	Pink Bloodwood	290		290	20	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4973	Corymbia intermedia	Pink Bloodwood	300		300	20	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4974	Petalostigma pubescens	Quinine Bush	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4975	Eucalyptus seeana	Narrow-leaved Red Gum	310		310	22	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4976	Corymbia intermedia	Pink Bloodwood	280		280	19	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4977	Eucalyptus tereticornis	Forest Red Gum	150		150	17	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4978	Lophostemon suaveolens	Swamp Box	160		160	17	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4979	Corymbia intermedia	Pink Bloodwood	270		270	20	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4980	Corymbia intermedia	Pink Bloodwood	260		260	17	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4981	Acacia disparrima	Hickory Wattle	190	160	248	12	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4982	Corymbia citriodora	Spotted Gum	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4983	Corymbia intermedia	Pink Bloodwood	190		190	13	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4984	Corymbia intermedia	Pink Bloodwood	300		300	22	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4985	Corymbia intermedia	Pink Bloodwood	280		280	17	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4986	Corymbia intermedia	Pink Bloodwood	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
4987	Alphitonia excelsa	Soap Tree	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4988	Lophostemon suaveolens	Swamp Box	230		230	16	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4989	Angophora subvelutina	Broad-leaved Apple	310		310	21	7	3.7	2.0	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4990	Melaleuca viminalis	Weeping Bottlebrush	160		160	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4991	Casuarina cunninghamiana	River Sheoak	220	260	341	18	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
4992	Melaleuca quinquenervia	Broad-leaved Paperbark	200	190, 140, 130, 170	376	12	6	4.5	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4993	Casuarina cunninghamiana	River Sheoak	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4994	Melaleuca viminalis	Weeping Bottlebrush	150	130, 150	249	8	4	3.0	1.8	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
4995	Casuarina cunninghamiana	River Sheoak	260		260	12	4	3.1	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
4996	Casuarina cunninghamiana	River Sheoak	300		300	17	2	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4997	Eucalyptus tereticornis	Forest Red Gum	580		580	25	12	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4998	Casuarina cunninghamiana	River Sheoak	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
4999	Acacia concurrens	Black Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5000	Corymbia intermedia	Pink Bloodwood	380		380	20	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5001	Corymbia tessellaris	Moreton Bay Ash	300		300	18	3	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5002	Acacia concurrens	Black Wattle	220		220	12	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5003	Corymbia intermedia	Pink Bloodwood	200	180	269	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5004	Angophora subvelutina	Broad-leaved Apple	230		230	17	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5005	Eucalyptus tereticornis	Forest Red Gum	600		600	25	12	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5006	Acacia disparrima	Hickory Wattle	180	160	241	12	3	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5007	Corymbia tessellaris	Moreton Bay Ash	500		500	24	12	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5008	Corymbia tessellaris	Moreton Bay Ash	180		180	18	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5009	Eucalyptus tereticornis	Forest Red Gum	150		150	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5010	Aphananthe philippinensis	Native Elm	200	240	312	18	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5011	Casuarina cunninghamiana	River Sheoak	230		230	17	4	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5012	Casuarina cunninghamiana	River Sheoak	350		350	20	8	4.2	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5013	Eucalyptus siderophloia	Grey Ironbark	300		300	16	3	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5014	Eucalyptus seeana	Narrow-leaved Red Gum	530		530	23	8	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5015	Eucalyptus seeana	Narrow-leaved Red Gum	400		400	23	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5016	Eucalyptus siderophloia	Grey Ironbark	330		330	23	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5017	Corymbia intermedia	Pink Bloodwood	180		180	14	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5018	Lophostemon suaveolens	Swamp Box	340		340	10	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5019	Eucalyptus tereticornis	Forest Red Gum	250		250	19	2	3.0	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5020	Corymbia intermedia	Pink Bloodwood	460		460	23	8	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5021	Petalostigma pubescens	Quinine Bush	310		310	10	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5022	Eucalyptus siderophloia	Grey Ironbark	290		290	23	5	3.5	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5023	Corymbia citriodora	Spotted Gum	450		450	23	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5024	Corymbia citriodora	Spotted Gum	270		270	21	5	3.2	1.9	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5025	Corymbia citriodora	Spotted Gum	300		300	22	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5026	Acacia concurrens	Black Wattle	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5027	Acacia concurrens	Black Wattle	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5028	Acacia concurrens	Black Wattle	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5029	Eucalyptus siderophloia	Grey Ironbark	160		160	13	2	2.0	1.5	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5030	Eucalyptus seeana	Narrow-leaved Red Gum	260		260	15	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5031	Corymbia citriodora	Spotted Gum	180		180	16	3	2.2	1.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5032	Acacia concurrens	Black Wattle	120		120	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5033	Acacia disparrima	Hickory Wattle	120		120	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5034	Corymbia citriodora	Spotted Gum	140		140	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5035	Acacia concurrens	Black Wattle	160		160	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5036	Acacia concurrens	Black Wattle	130		130	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5037	Corymbia citriodora	Spotted Gum	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5038	Acacia concurrens	Black Wattle	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5039	Corymbia citriodora	Spotted Gum	260		260	20	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5040	Eucalyptus tereticornis	Forest Red Gum	140		140	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5041	Eucalyptus tereticornis	Forest Red Gum	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5042	Acacia concurrens	Black Wattle	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5043	Acacia concurrens	Black Wattle	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5044	Acacia concurrens	Black Wattle	250		250	8	3	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5045	Acacia concurrens	Black Wattle	170		170	5	2	2.0	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5046	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	17	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5047	Petalostigma pubescens	Quinine Bush	260		260	10	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5048	Eucalyptus tereticornis	Forest Red Gum	130	130	184	10	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5049	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	17	5	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5050	Eucalyptus crebra	Narrow-leaved Ironbark	390		390	20	5	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5051	Petalostigma pubescens	Quinine Bush	190		190	5	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5052	Petalostigma pubescens	Quinine Bush	260		260	10	3	3.1	1.9	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5053	Eucalyptus crebra	Narrow-leaved Ironbark	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5054	Acacia concurrens	Black Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5055	Acacia concurrens	Black Wattle	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5056	Petalostigma pubescens	Quinine Bush	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5057	Petalostigma pubescens	Quinine Bush	150		150	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5058	Petalostigma pubescens	Quinine Bush	150	110	186	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5059	Petalostigma pubescens	Quinine Bush	210		210	7	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5060	Acacia concurrens	Black Wattle	140	150, 140, 120	276	8	3	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5061	Eucalyptus tereticornis	Forest Red Gum	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5062	Petalostigma pubescens	Quinine Bush	250		250	9	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5063	Petalostigma pubescens	Quinine Bush	180		180	8	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5064	Petalostigma pubescens	Quinine Bush	220		220	10	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5065	Petalostigma pubescens	Quinine Bush	220		220	9	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5066	Acacia concurrens	Black Wattle	160		160	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5067	Acacia concurrens	Black Wattle	140	130	191	8	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5068	Acacia concurrens	Black Wattle	160		160	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5069	Corymbia citriodora	Spotted Gum	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5070	Acacia concurrens	Black Wattle	250		250	10	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5071	Eucalyptus crebra	Narrow-leaved Ironbark	370		370	19	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
5072	Acacia concurrens	Black Wattle	150	140	205	8	2	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5073	Eucalyptus siderophloia	Grey Ironbark	290		290	17	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5074	Acacia concurrens	Black Wattle	190		190	7	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5075	Acacia concurrens	Black Wattle	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5076	Corymbia intermedia	Pink Bloodwood	250		250	16	3	3.0	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
5077	Corymbia intermedia	Pink Bloodwood	270		270	16	3	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5078	Corymbia citriodora	Spotted Gum	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5079	Acacia concurrens	Black Wattle	210		210	8	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5080	Eucalyptus tereticornis	Forest Red Gum	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5081	Lophostemon suaveolens	Swamp Box	280		280	16	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5082	Eucalyptus tereticornis	Forest Red Gum	380		380	20	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5083	Acacia disparrima	Hickory Wattle	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5084	Acacia concurrens	Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5085	Lophostemon suaveolens	Swamp Box	220		220	14	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5086	Eucalyptus tereticornis	Forest Red Gum	200	170	262	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5087	Eucalyptus tereticornis	Forest Red Gum	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5088	Lophostemon suaveolens	Swamp Box	280		280	13	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5089	Eucalyptus tereticornis	Forest Red Gum	140		140	8	2	2.0	1.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5090	Eucalyptus tereticornis	Forest Red Gum	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5091	Lophostemon suaveolens	Swamp Box	170		170	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5092	Eucalyptus tereticornis	Forest Red Gum	220		220	18	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5093	Eucalyptus tereticornis	Forest Red Gum	200	190	276	16	3	3.3	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5094	Eucalyptus tereticornis	Forest Red Gum	300		300	16	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5095	Eucalyptus tereticornis	Forest Red Gum	190		190	16	2	2.3	1.6	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5096	Eucalyptus tereticornis	Forest Red Gum	310		310	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5097	Eucalyptus tereticornis	Forest Red Gum	160		160	12	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5098	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5099	Eucalyptus tereticornis	Forest Red Gum	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5100	Eucalyptus tereticornis	Forest Red Gum	140		140	7	2	2.0	1.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5101	Eucalyptus tereticornis	Forest Red Gum	190		190	17	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5102	Eucalyptus tereticornis	Forest Red Gum	220		220	16	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5103	Eucalyptus tereticornis	Forest Red Gum	360		360	18	5	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5104	Eucalyptus tereticornis	Forest Red Gum	260		260	17	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5105	Eucalyptus tereticornis	Forest Red Gum	400		400	20	5	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5106	Corymbia tessellaris	Moreton Bay Ash	350		350	22	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5107	Eucalyptus siderophloia	Grey Ironbark	250		250	18	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5108	Eucalyptus siderophloia	Grey Ironbark	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5109	Corymbia tessellaris	Moreton Bay Ash	150	130	198	10	2	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5110	Acacia disparrima	Hickory Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5111	Acacia disparrima	Hickory Wattle	200		200	17	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5112	Angophora subvelutina	Broad-leaved Apple	300		300	18	6	3.6	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5113	Angophora subvelutina	Broad-leaved Apple	300		300	19	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5114	Angophora leiocarpa	Smooth-barked Apple	150		150	11	3	2.0	1.5	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5115	Lophostemon suaveolens	Swamp Box	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5116	Eucalyptus tereticornis	Forest Red Gum	300		300	23	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5117	Eucalyptus tereticornis	Forest Red Gum	170		170	18	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5118	Angophora subvelutina	Broad-leaved Apple	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5119	Eucalyptus siderophloia	Grey Ironbark	200		200	17	3	2.4	1.7	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5120	Acacia concurrens	Black Wattle	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5121	Corymbia citriodora	Spotted Gum	350		350	25	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5122	Angophora subvelutina	Broad-leaved Apple	200		200	15	3	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5123	Angophora subvelutina	Broad-leaved Apple	320		320	18	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5124	Angophora subvelutina	Broad-leaved Apple	250		250	17	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5125	Angophora subvelutina	Broad-leaved Apple	180		180	13	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
5126	Angophora subvelutina	Broad-leaved Apple	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5127	Lophostemon suaveolens	Swamp Box	220		220	13	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5128	Corymbia tessellaris	Moreton Bay Ash	130		130	12	3	2.0	1.4	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5129	Lophostemon suaveolens	Swamp Box	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5130	Eucalyptus siderophloia	Grey Ironbark	140		140	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5131	Eucalyptus tereticornis	Forest Red Gum	200		200	19	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5132	Angophora subvelutina	Broad-leaved Apple	190		190	12	3	2.3	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5133	Angophora subvelutina	Broad-leaved Apple	250		250	18	3	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5134	Acacia disparrima	Hickory Wattle	200		200	15	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5135	Acacia disparrima	Hickory Wattle	260		260	15	4	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5136	Acacia disparrima	Hickory Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5137	Eucalyptus tereticornis	Forest Red Gum	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5138	Acacia concurrens	Black Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5139	Angophora subvelutina	Broad-leaved Apple	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5140	Corymbia intermedia	Pink Bloodwood	400		400	19	5	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5141	Corymbia tessellaris	Moreton Bay Ash	300		300	20	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5142	Eucalyptus siderophloia	Grey Ironbark	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5143	Acacia disparrima	Hickory Wattle	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5144	Acacia disparrima	Hickory Wattle	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5145	Corymbia citriodora	Spotted Gum	130		130	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5146	Eucalyptus siderophloia	Grey Ironbark	200		200	9	2	2.4	1.7	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5147	Corymbia citriodora	Spotted Gum	280		280	15	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5148	Acacia disparrima	Hickory Wattle	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5149	Corymbia tessellaris	Moreton Bay Ash	280	160	322	18	5	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5150	Alphitonia excelsa	Soap Tree	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5151	Acacia disparrima	Hickory Wattle	130		130	7	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5152	Alphitonia excelsa	Soap Tree	170		170	11	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5153	Eucalyptus tereticornis	Forest Red Gum	220		220	17	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5154	Eucalyptus crebra	Narrow-leaved Ironbark	190		190	17	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5155	Eucalyptus siderophloia	Grey Ironbark	170		170	13	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5156	Eucalyptus tereticornis	Forest Red Gum	280		280	18	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5157	Angophora leiocarpa	Smooth-barked Apple	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5158	Eucalyptus crebra	Narrow-leaved Ironbark	220		220	16	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5159	Corymbia citriodora	Spotted Gum	150	100	180	16	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5160	Acacia disparrima	Hickory Wattle	100	120	156	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5161	Corymbia citriodora	Spotted Gum	170	110, 90, 80	236	17	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5162	Corymbia citriodora	Spotted Gum	310	150	344	17	4	4.1	2.1	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5163	Corymbia intermedia	Pink Bloodwood	300		300	16	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5164	Corymbia intermedia	Pink Bloodwood	310		310	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5165	Eucalyptus tereticornis	Forest Red Gum	340		340	20	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5166	Lophostemon suaveolens	Swamp Box	280		280	12	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5167	Eucalyptus tereticornis	Forest Red Gum	380		380	20	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5168	Eucalyptus tereticornis	Forest Red Gum	460		460	22	6	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5169	Angophora leiocarpa	Smooth-barked Apple	390		390	16	6	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5170	Corymbia citriodora	Spotted Gum	310		310	17	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5171	Eucalyptus siderophloia	Grey Ironbark	410		410	16	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5172	Acacia disparrima	Hickory Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5173	Acacia concurrens	Black Wattle	180	180	255	9	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5174	Eucalyptus siderophloia	Grey Ironbark	280		280	18	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5175	Acacia concurrens	Black Wattle	230		230	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5176	Acacia concurrens	Black Wattle	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5177	Eucalyptus tereticornis	Forest Red Gum	320		320	17	2	3.8	2.1	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5178	Eucalyptus tereticornis	Forest Red Gum	260		260	16	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5179	Corymbia intermedia	Pink Bloodwood	330		330	14	4	4.0	2.1	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5180	Eucalyptus tereticornis	Forest Red Gum	300		300	18	2	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
5181	Corymbia intermedia	Pink Bloodwood	280		280	16	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5182	Lophostemon suaveolens	Swamp Box	260		260	14	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5183	Corymbia intermedia	Pink Bloodwood	380		380	16	5	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5184	Corymbia intermedia	Pink Bloodwood	330		330	17	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5185	Eucalyptus tereticornis	Forest Red Gum	380		380	20	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5186	Eucalyptus tereticornis	Forest Red Gum	320		320	21	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5187	Corymbia intermedia	Pink Bloodwood	280		280	15	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5188	Acacia concurrens	Black Wattle	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5189	Corymbia intermedia	Pink Bloodwood	330		330	17	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5190	Acacia concurrens	Black Wattle	180		180	6	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5191	Eucalyptus tereticornis	Forest Red Gum	300		300	18	2	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5192	Corymbia intermedia	Pink Bloodwood	320		320	21	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5193	Eucalyptus crebra	Narrow-leaved Ironbark	360		360	19	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5194	Corymbia citriodora	Spotted Gum	300		300	20	5	3.6	2.0	Regular	-	Thinning	-	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5195	Acacia concurrens	Black Wattle	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5196	Acacia concurrens	Black Wattle	220	190	291	10	3	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5197	Acacia concurrens	Black Wattle	230	140	269	11	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5198	Acacia concurrens	Black Wattle	170		170	11	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5199	Acacia concurrens	Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5200	Acacia concurrens	Black Wattle	150	100	180	11	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5201	Acacia concurrens	Black Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5202	Acacia concurrens	Black Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5203	Eucalyptus tereticornis	Forest Red Gum	390		390	17	5	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5204	Acacia concurrens	Black Wattle	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5205	Acacia concurrens	Black Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5206	Acacia concurrens	Black Wattle	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5207	Acacia concurrens	Black Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5208	Acacia concurrens	Black Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5209	Acacia concurrens	Black Wattle	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5210	Acacia concurrens	Black Wattle	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5211	Acacia concurrens	Black Wattle	210		210	9	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5212	Acacia concurrens	Black Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5213	Acacia concurrens	Black Wattle	170	120	208	11	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5214	Acacia concurrens	Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5215	Acacia concurrens	Black Wattle	150	110	186	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5216	Acacia concurrens	Black Wattle	170		170	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5217	Corymbia citriodora	Spotted Gum	150		150	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5218	Lophostemon suaveolens	Swamp Box	230		230	12	2	2.8	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5219	Acacia concurrens	Black Wattle	140	140	198	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5220	Acacia concurrens	Black Wattle	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5221	Eucalyptus tereticornis	Forest Red Gum	330		330	18	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5222	Acacia concurrens	Black Wattle	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5223	Acacia concurrens	Black Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5224	Acacia concurrens	Black Wattle	150	130	198	9	2	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5225	Angophora subvelutina	Broad-leaved Apple	210		210	16	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5226	Angophora subvelutina	Broad-leaved Apple	190		190	16	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5227	Angophora subvelutina	Broad-leaved Apple	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5228	Corymbia intermedia	Pink Bloodwood	500		500	18	7	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5229	Lophostemon suaveolens	Swamp Box	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5230	Lophostemon suaveolens	Swamp Box	260		260	16	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5231	Lophostemon suaveolens	Swamp Box	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5232	Lophostemon suaveolens	Swamp Box	180		180	17	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5233	Lophostemon suaveolens	Swamp Box	180		180	16	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5234	Corymbia tessellaris	Moreton Bay Ash	250		250	20	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5235	Lophostemon suaveolens	Swamp Box	150		150	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5236	Lophostemon suaveolens	Swamp Box	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5237	Lophostemon suaveolens	Swamp Box	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5238	Casuarina cunninghamiana	River Sheoak	290		290	17	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5239	Casuarina cunninghamiana	River Sheoak	290		290	16	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5240	Corymbia trachyphloia	Brown Bloodwood	300		300	17	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5241	Acacia concurrens	Black Wattle	190		190	10	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5242	Corymbia citriodora	Spotted Gum	160		160	16	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5243	Petalostigma pubescens	Quinine Bush	180	150, 110	259	14	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5244	Casuarina cunninghamiana	River Sheoak	270	160	314	19	7	3.8	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5245	Corymbia intermedia	Pink Bloodwood	180		180	17	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5246	Corymbia intermedia	Pink Bloodwood	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5247	Acacia disparrima	Hickory Wattle	160		160	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5248	Lophostemon suaveolens	Swamp Box	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5249	Lophostemon suaveolens	Swamp Box	150		150	16	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5250	Lophostemon suaveolens	Swamp Box	150		150	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5251	Casuarina cunninghamiana	River Sheoak	380		380	20	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5252	Casuarina cunninghamiana	River Sheoak	200		200	17	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5253	Lophostemon suaveolens	Swamp Box	200		200	14	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5254	Lophostemon suaveolens	Swamp Box	150		150	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5255	Casuarina cunninghamiana	River Sheoak	640		640	25	10	7.7	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5256	Casuarina cunninghamiana	River Sheoak	260		260	17	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5257	Casuarina cunninghamiana	River Sheoak	350		350	21	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5258	Casuarina cunninghamiana	River Sheoak	330		330	26	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5259	Acacia disparrima	Hickory Wattle	220		220	12	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5260	Eucalyptus tereticornis	Forest Red Gum	190		190	17	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5261	Acacia disparrima	Hickory Wattle	230		230	12	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5262	Corymbia tessellaris	Moreton Bay Ash	250		250	20	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5263	Corymbia tessellaris	Moreton Bay Ash	170	80	188	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5264	Corymbia tessellaris	Moreton Bay Ash	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5265	Eucalyptus tereticornis	Forest Red Gum	440		440	25	8	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5266	Eucalyptus seeana	Narrow-leaved Red Gum	350		350	20	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5267	Eucalyptus siderophloia	Grey Ironbark	260		260	19	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5268	Acacia disparrima	Hickory Wattle	180		180	16	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5269	Eucalyptus siderophloia	Grey Ironbark	190		190	17	3	2.3	1.6	Regular	-	Thinning	Die-back	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5270	Eucalyptus seeana	Narrow-leaved Red Gum	270		270	18	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5271	Lophostemon suaveolens	Swamp Box	260		260	16	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5272	Eucalyptus seeana	Narrow-leaved Red Gum	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5273	Eucalyptus siderophloia	Grey Ironbark	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5274	Eucalyptus siderophloia	Grey Ironbark	360		360	20	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5275	Eucalyptus tereticornis	Forest Red Gum	280		280	19	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5276	Corymbia citriodora	Spotted Gum	330		330	19	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5277	Corymbia citriodora	Spotted Gum	290		290	20	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5278	Eucalyptus siderophloia	Grey Ironbark	340		340	20	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5279	Corymbia citriodora	Spotted Gum	250		250	21	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5280	Acacia disparrima	Hickory Wattle	260		260	10	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5281	Corymbia citriodora	Spotted Gum	290		290	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5282	Eucalyptus siderophloia	Grey Ironbark	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5283	Acacia disparrima	Hickory Wattle	170		170	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5284	Acacia disparrima	Hickory Wattle	190		190	9	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5285	Acacia concurrens	Black Wattle	180		180	9	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5286	Acacia concurrens	Black Wattle	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5287	Acacia concurrens	Black Wattle	140	130	191	9	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5288	Acacia disparrima	Hickory Wattle	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5289	Eucalyptus siderophloia	Grey Ironbark	200		200	16	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5290	Eucalyptus siderophloia	Grey Ironbark	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5291	Eucalyptus siderophloia	Grey Ironbark	330		330	22	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5292	Acacia concurrens	Black Wattle	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5293	Acacia disparrima	Hickory Wattle	160		160	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5294	Eucalyptus siderophloia	Grey Ironbark	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5295	Petalostigma pubescens	Quinine Bush	240		240	14	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5296	Eucalyptus siderophloia	Grey Ironbark	230		230	22	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5297	Eucalyptus siderophloia	Grey Ironbark	280		280	23	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5298	Acacia disparrima	Hickory Wattle	200		200	9	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5299	Eucalyptus siderophloia	Grey Ironbark	330		330	21	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5300	Eucalyptus siderophloia	Grey Ironbark	230		230	21	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5301	Acacia concurrens	Black Wattle	170		170	8	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5302	Acacia disparrima	Hickory Wattle	190		190	11	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5303	Lophostemon suaveolens	Swamp Box	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5304	Lophostemon suaveolens	Swamp Box	180		180	10	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5305	Lophostemon suaveolens	Swamp Box	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5306	Acacia concurrens	Black Wattle	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5307	Acacia disparrima	Hickory Wattle	180		180	9	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5308	Lophostemon suaveolens	Swamp Box	140	130	191	12	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5309	Lophostemon suaveolens	Swamp Box	270		270	17	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5310	Eucalyptus tereticornis	Forest Red Gum	330		330	21	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5311	Eucalyptus seeana	Narrow-leaved Red Gum	180		180	20	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5312	Lophostemon suaveolens	Swamp Box	160		160	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5313	Angophora subvelutina	Broad-leaved Apple	270	200	336	19	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5314	Eucalyptus tereticornis	Forest Red Gum	250		250	20	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5315	Lophostemon suaveolens	Swamp Box	150		150	12	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5316	Eucalyptus tereticornis	Forest Red Gum	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5317	Lophostemon suaveolens	Swamp Box	120		120	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5318	Corymbia citriodora	Spotted Gum	120		120	16	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5319	Eucalyptus seeana	Narrow-leaved Red Gum	230		230	19	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5320	Eucalyptus seeana	Narrow-leaved Red Gum	320		320	22	9	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5321	Eucalyptus seeana	Narrow-leaved Red Gum	120	90, 80, 50	177	12	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5322	Eucalyptus tereticornis	Forest Red Gum	300		300	21	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5323	Lophostemon suaveolens	Swamp Box	170		170	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5324	Eucalyptus seeana	Narrow-leaved Red Gum	160		160	16	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5325	Eucalyptus tereticornis	Forest Red Gum	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5326	Eucalyptus tereticornis	Forest Red Gum	170		170	16	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5327	Eucalyptus tereticornis	Forest Red Gum	200		200	17	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5328	Lophostemon suaveolens	Swamp Box	190		190	15	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5329	Corymbia tessellaris	Moreton Bay Ash	230	190	298	22	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5330	Lophostemon suaveolens	Swamp Box	120		120	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5331	Lophostemon suaveolens	Swamp Box	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5332	Acacia disparrima	Hickory Wattle	200		200	16	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5333	Angophora subvelutina	Broad-leaved Apple	220		220	18	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5334	Angophora subvelutina	Broad-leaved Apple	190		190	20	7	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5335	Eucalyptus tereticornis	Forest Red Gum	150		150	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5336	Angophora subvelutina	Broad-leaved Apple	150		150	14	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5337	Acacia concurrens	Black Wattle	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5338	Angophora subvelutina	Broad-leaved Apple	240		240	17	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5339	Angophora subvelutina	Broad-leaved Apple	450		450	19	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5340	Eucalyptus tereticornis	Forest Red Gum	200		200	23	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5341	Angophora subvelutina	Broad-leaved Apple	270		270	20	9	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5342	Acacia disparrima	Hickory Wattle	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5343	Angophora subvelutina	Broad-leaved Apple	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5344	Acacia disparrima	Hickory Wattle	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5345	Angophora subvelutina	Broad-leaved Apple	180		180	19	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5346	Angophora subvelutina	Broad-leaved Apple	300		300	20	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5347	Angophora subvelutina	Broad-leaved Apple	240		240	19	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5348	Angophora subvelutina	Broad-leaved Apple	300	210	366	22	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5349	Acacia concurrens	Black Wattle	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5350	Acacia concurrens	Black Wattle	170		170	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5351	Corymbia citriodora	Spotted Gum	140		140	16	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5352	Acacia disparrima	Hickory Wattle	120		120	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5353	Eucalyptus tereticornis	Forest Red Gum	300		300	21	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5354	Eucalyptus siderophloia	Grey Ironbark	160		160	16	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5355	Acacia disparrima	Hickory Wattle	150		150	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5356	Corymbia citriodora	Spotted Gum	230		230	22	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5357	Acacia disparrima	Hickory Wattle	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5358	Eucalyptus siderophloia	Grey Ironbark	160		160	17	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5359	Corymbia citriodora	Spotted Gum	280		280	21	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5360	Corymbia citriodora	Spotted Gum	190	100, 100, 70	247	19	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5361	Eucalyptus siderophloia	Grey Ironbark	110		110	14	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5362	Corymbia citriodora	Spotted Gum	110		110	14	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5363	Eucalyptus tereticornis	Forest Red Gum	320		320	21	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5364	Eucalyptus tereticornis	Forest Red Gum	420		420	19	6	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5365	Eucalyptus tereticornis	Forest Red Gum	180		180	17	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5366	Corymbia intermedia	Pink Bloodwood	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5367	Corymbia citriodora	Spotted Gum	170	110, 100, 90	243	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5368	Eucalyptus siderophloia	Grey Ironbark	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5369	Acacia concurrens	Black Wattle	110	100	149	5	3	2.0	1.5	Regular	-	Thinning	Die-back	-	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5370	Acacia concurrens	Black Wattle	150	140, 140	248	9	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5371	Eucalyptus tereticornis	Forest Red Gum	170		170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5372	Eucalyptus tereticornis	Forest Red Gum	140		140	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5373	Acacia disparrima	Hickory Wattle	220		220	11	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5374	Acacia disparrima	Hickory Wattle	160		160	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5375	Acacia disparrima	Hickory Wattle	170		170	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5376	Acacia disparrima	Hickory Wattle	160		160	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5377	Acacia concurrens	Black Wattle	170		170	9	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5378	Acacia concurrens	Black Wattle	240		240	11	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5379	Acacia concurrens	Black Wattle	180		180	11	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5380	Acacia concurrens	Black Wattle	150		150	11	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5381	Acacia concurrens	Black Wattle	190		190	10	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5382	Acacia concurrens	Black Wattle	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5383	Acacia concurrens	Black Wattle	170		170	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5384	Lophostemon suaveolens	Swamp Box	170		170	14	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5385	Acacia disparrima	Hickory Wattle	140	130	191	10	5	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5386	Acacia concurrens	Black Wattle	170		170	10	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5387	Acacia concurrens	Black Wattle	120	120	170	11	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5388	Acacia concurrens	Black Wattle	200		200	11	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5389	Acacia concurrens	Black Wattle	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5390	Acacia concurrens	Black Wattle	210		210	12	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5391	Acacia concurrens	Black Wattle	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5392	Lophostemon suaveolens	Swamp Box	140		140	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5393	Eucalyptus tereticornis	Forest Red Gum	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5394	Acacia concurrens	Black Wattle	180		180	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5395	Eucalyptus tereticornis	Forest Red Gum	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5396	Acacia concurrens	Black Wattle	170		170	9	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5397	Eucalyptus siderophloia	Grey Ironbark	280		280	18	6	3.4	1.9	Regular	-	Thinning	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5398	Acacia concurrens	Black Wattle	140	130	191	9	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5399	Acacia concurrens	Black Wattle	160		160	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5400	Acacia concurrens	Black Wattle	190		190	13	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5401	Eucalyptus siderophloia	Grey Ironbark	280		280	19	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5402	Acacia concurrens	Black Wattle	200		200	10	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5403	Acacia concurrens	Black Wattle	170		170	13	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5404	Acacia concurrens	Black Wattle	150	130	198	12	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5405	Acacia concurrens	Black Wattle	140	120	184	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5406	Corymbia intermedia	Pink Bloodwood	240		240	17	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5407	Acacia concurrens	Black Wattle	170		170	10	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5408	Petalostigma pubescens	Quinine Bush	280		280	16	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5409	Acacia concurrens	Black Wattle	210		210	9	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5410	Acacia concurrens	Black Wattle	160		160	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5411	Corymbia intermedia	Pink Bloodwood	230		230	19	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5412	Corymbia citriodora	Spotted Gum	370		370	22	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5413	Lophostemon suaveolens	Swamp Box	290		290	18	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5414	Eucalyptus tereticornis	Forest Red Gum	310		310	21	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5415	Acacia concurrens	Black Wattle	200		200	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5416	Acacia concurrens	Black Wattle	160	130	206	13	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5417	Acacia concurrens	Black Wattle	210	170	270	13	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5418	Acacia concurrens	Black Wattle	160		160	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5419	Eucalyptus seeana	Narrow-leaved Red Gum	150		150	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5420	Acacia concurrens	Black Wattle	170		170	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5421	Acacia concurrens	Black Wattle	180		180	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5422	Acacia concurrens	Black Wattle	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5423	Eucalyptus tereticornis	Forest Red Gum	380		380	18	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5424	Acacia disparrima	Hickory Wattle	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5425	Corymbia citriodora	Spotted Gum	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5426	Acacia leiocalyx	Early-flowering Black Wattle	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5427	Eucalyptus seeana	Narrow-leaved Red Gum	500		500	25	13	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	Old	Old	-	-	-	-		Remove
5428	Corymbia intermedia	Pink Bloodwood	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5429	Acacia disparrima	Hickory Wattle	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5430	Acacia disparrima	Hickory Wattle	130		130	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5431	Corymbia tessellaris	Moreton Bay Ash	120		120	11	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5432	Acacia disparrima	Hickory Wattle	130	130	184	7	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5433	Acacia disparrima	Hickory Wattle	100		100	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5434	Acacia disparrima	Hickory Wattle	200		200	10	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5435	Corymbia intermedia	Pink Bloodwood	630		630	25	13	7.6	2.7	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5436	Corymbia intermedia	Pink Bloodwood	380		380	20	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5437	Acacia concurrens	Black Wattle	100		100	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5438	Acacia disparrima	Hickory Wattle	160		160	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5439	Acacia disparrima	Hickory Wattle	160		160	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5440	Corymbia intermedia	Pink Bloodwood	260		260	11	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5441	Acacia disparrima	Hickory Wattle	100		100	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5442	Corymbia intermedia	Pink Bloodwood	260		260	24	13	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5443	Corymbia intermedia	Pink Bloodwood	270		270	22	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5444	Acacia disparrima	Hickory Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5445	Lophostemon suaveolens	Swamp Box	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5446	Banksia integrifolia	Coast Banksia	120		120	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5447	Acacia concurrens	Black Wattle	100		100	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5448	Banksia integrifolia	Coast Banksia	100		100	4	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5449	Corymbia intermedia	Pink Bloodwood	260		260	22	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5450	Lophostemon suaveolens	Swamp Box	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5451	Eucalyptus crebra	Narrow-leaved Ironbark	160		160	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5452	Acacia concurrens	Black Wattle	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5453	Corymbia intermedia	Pink Bloodwood	480		480	25	14	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5454	Corymbia intermedia	Pink Bloodwood	300		300	25	13	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5455	Corymbia intermedia	Pink Bloodwood	230		230	20	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5456	Corymbia intermedia	Pink Bloodwood	220		220	20	10	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5457	Corymbia intermedia	Pink Bloodwood	370		370	25	14	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5458	Acacia concurrens	Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5459	Corymbia intermedia	Pink Bloodwood	140		140	16	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5460	Lophostemon suaveolens	Swamp Box	300		300	16	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5461	Allocasuarina littoralis	Black She-oak	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5462	Lophostemon suaveolens	Swamp Box	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5463	Acacia concurrens	Black Wattle	130		130	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5464	Angophora leiocarpa	Smooth-barked Apple	180		180	14	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5465	Eucalyptus tereticornis	Forest Red Gum	310		310	25	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5466	Lophostemon suaveolens	Swamp Box	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5467	Eucalyptus tereticornis	Forest Red Gum	400		400	25	15	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retention TBC by CPTED
5468	Petalostigma pubescens	Quinine Bush	190		190	6	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5469	Acacia concurrens	Black Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5470	Acacia disparrima	Hickory Wattle	160		160	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5471	Acacia disparrima	Hickory Wattle	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5472	Corymbia intermedia	Pink Bloodwood	220		220	18	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5473	Acacia concurrens	Black Wattle	100		100	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5474	Acacia concurrens	Black Wattle	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5475	Corymbia intermedia	Pink Bloodwood	400		400	26	14	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5476	Corymbia intermedia	Pink Bloodwood	280		280	25	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5477	Corymbia intermedia	Pink Bloodwood	460		460	26	14	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5478	Acacia disparrima	Hickory Wattle	100		100	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5479	Acacia concurrens	Black Wattle	130	100	164	9	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5480	Acacia concurrens	Black Wattle	130		130	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5481	Eucalyptus seeana	Narrow-leaved Red Gum	250		250	25	12	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5482	Eucalyptus seeana	Narrow-leaved Red Gum	400		400	25	14	4.8	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5483	Acacia leiocalyx	Early-flowering Black Wattle	130		130	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5484	Petalostigma pubescens	Quinine Bush	230		230	7	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5485	Corymbia intermedia	Pink Bloodwood	340		340	20	10	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5486	Corymbia intermedia	Pink Bloodwood	510		510	26	14	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5487	Corymbia intermedia	Pink Bloodwood	340		340	26	14	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5488	Alphitonia excelsa	Soap Tree	430		430	13	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5489	Corymbia intermedia	Pink Bloodwood	300		300	25	12	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5490	Acacia concurrens	Black Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5491	Corymbia intermedia	Pink Bloodwood	320		320	24	8	3.8	2.1	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5492	Acacia concurrens	Black Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5493	Corymbia intermedia	Pink Bloodwood	150		150	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5494	Acacia concurrens	Black Wattle	110		110	8	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5495	Petalostigma pubescens	Quinine Bush	230		230	10	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5496	Corymbia intermedia	Pink Bloodwood	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5497	Corymbia intermedia	Pink Bloodwood	400		400	26	10	4.8	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5498	Acacia disparrima	Hickory Wattle	110		110	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5499	Acacia disparrima	Hickory Wattle	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5500	Corymbia intermedia	Pink Bloodwood	270		270	24	14	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5501	Acacia concurrens	Black Wattle	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5502	Corymbia intermedia	Pink Bloodwood	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5503	Petalostigma pubescens	Quinine Bush	150		150	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5504	Corymbia intermedia	Pink Bloodwood	200		200	16	7	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5505	Corymbia intermedia	Pink Bloodwood	250		250	25	14	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5506	Acacia concurrens	Black Wattle	110		110	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5507	Angophora leiocarpa	Smooth-barked Apple	300		300	26	14	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5508	Corymbia intermedia	Pink Bloodwood	120		120	7	3	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5509	Corymbia intermedia	Pink Bloodwood	170		170	14	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5510	Petalostigma pubescens	Quinine Bush	140		140	8	5	2.0	1.4	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5511	Lophostemon suaveolens	Swamp Box	150		150	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5512	Corymbia intermedia	Pink Bloodwood	160		160	12	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5513	Petalostigma pubescens	Quinine Bush	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5514	Petalostigma pubescens	Quinine Bush	130		130	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5515	Alphitonia excelsa	Soap Tree	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5516	Alphitonia excelsa	Soap Tree	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5517	Corymbia intermedia	Pink Bloodwood	140		140	10	7	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5518	Petalostigma pubescens	Quinine Bush	110		110	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5519	Alphitonia excelsa	Soap Tree	200		200	10	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5520	Lophostemon suaveolens	Swamp Box	170		170	14	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5521	Angophora leiocarpa	Smooth-barked Apple	340		340	25	14	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5522	Alphitonia excelsa	Soap Tree	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5523	Alphitonia excelsa	Soap Tree	180		180	11	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5524	Alphitonia excelsa	Soap Tree	190		190	7	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5525	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5526	Acacia disparrima	Hickory Wattle	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5527	Acacia disparrima	Hickory Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5528	Acacia disparrima	Hickory Wattle	180		180	10	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5529	Alphitonia excelsa	Soap Tree	340		340	12	7	4.1	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5530	Allocasuarina littoralis	Black She-oak	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5531	Petalostigma pubescens	Quinine Bush	210		210	7	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5532	Petalostigma pubescens	Quinine Bush	200		200	7	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5533	Petalostigma pubescens	Quinine Bush	180		180	6	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5534	Petalostigma pubescens	Quinine Bush	220		220	7	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5535	Eucalyptus tereticornis	Forest Red Gum	330		330	25	14	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retention TBC by CPTED
5536	Acacia leiocalyx	Early-flowering Black Wattle	100		100	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5537	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5538	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5539	Corymbia intermedia	Pink Bloodwood	230		230	24	10	2.8	1.8	Regular	-	Thinning	Die-back	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5540	Acacia disparrima	Hickory Wattle	120		120	5	3	2.0	1.4	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5541	Acacia disparrima	Hickory Wattle	120	100	156	7	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5542	Acacia disparrima	Hickory Wattle	120		120	7	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5543	Acacia leiocalyx	Early-flowering Black Wattle	170		170	7	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5544	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5545	Acacia leiocalyx	Early-flowering Black Wattle	170		170	8	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5546	Eucalyptus tereticornis	Forest Red Gum	330		330	25	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove for trunk sewer
5547	Acacia disparrima	Hickory Wattle	120		120	7	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5548	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5549	Petalostigma pubescens	Quinine Bush	240		240	10	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5550	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5551	Corymbia citriodora	Spotted Gum	520		520	27	16	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5552	Alphitonia excelsa	Soap Tree	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5553	Angophora leiocarpa	Smooth-barked Apple	420		420	22	14	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5554	Acacia disparrima	Hickory Wattle	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5555	Alphitonia excelsa	Soap Tree	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5556	Corymbia intermedia	Pink Bloodwood	250		250	20	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5557	Angophora leiocarpa	Smooth-barked Apple	150		150	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5558	Eucalyptus tereticornis	Forest Red Gum	420		420	25	14	5.0	2.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5559	Angophora leiocarpa	Smooth-barked Apple	430		430	25	14	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5560	Angophora leiocarpa	Smooth-barked Apple	220		220	14	6	2.6	1.8	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5561	Alphitonia excelsa	Soap Tree	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5562	Acacia disparrima	Hickory Wattle	200		200	10	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5563	Eucalyptus tereticornis	Forest Red Gum	210		210	16	5	2.5	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5564	Angophora leiocarpa	Smooth-barked Apple	140		140	14	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5565	Corymbia intermedia	Pink Bloodwood	250		250	25	13	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5566	Acacia disparrima	Hickory Wattle	130		130	8	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5567	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5568	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5569	Lophostemon suaveolens	Swamp Box	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5570	Acacia leiocalyx	Early-flowering Black Wattle	160		160	9	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5571	Acacia disparrima	Hickory Wattle	170		170	9	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5572	Allocasuarina littoralis	Black She-oak	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5573	Lophostemon suaveolens	Swamp Box	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5574	Acacia leiocalyx	Early-flowering Black Wattle	180		180	9	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5575	Angophora leiocarpa	Smooth-barked Apple	110		110	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5576	Angophora leiocarpa	Smooth-barked Apple	100		100	6	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5577	Acacia disparrima	Hickory Wattle	110		110	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5578	Angophora leiocarpa	Smooth-barked Apple	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5579	Acacia disparrima	Hickory Wattle	100		100	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5580	Acacia disparrima	Hickory Wattle	140		140	9	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5581	Alphitonia excelsa	Soap Tree	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5582	Acacia disparrima	Hickory Wattle	200	100, 140	264	7	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5583	Lophostemon suaveolens	Swamp Box	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5584	Acacia leiocalyx	Early-flowering Black Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5585	Allocasuarina littoralis	Black She-oak	120	80	144	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5586	Corymbia intermedia	Pink Bloodwood	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5587	Acacia leiocalyx	Early-flowering Black Wattle	220		220	8	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5588	Acacia leiocalyx	Early-flowering Black Wattle	150		150	8	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5589	Acacia disparrima	Hickory Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5590	Corymbia intermedia	Pink Bloodwood	330		330	20	11	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5591	Acacia disparrima	Hickory Wattle	160		160	9	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5592	Acacia disparrima	Hickory Wattle	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5593	Petalostigma pubescens	Quinine Bush	220		220	7	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5594	Acacia leiocalyx	Early-flowering Black Wattle	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5595	Acacia leiocalyx	Early-flowering Black Wattle	130		130	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5596	Corymbia intermedia	Pink Bloodwood	320		320	25	12	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5597	Acacia leiocalyx	Early-flowering Black Wattle	140		140	7	5	2.0	1.4	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5598	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5599	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5600	Allocasuarina littoralis	Black She-oak	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
5601	Eucalyptus tereticornis	Forest Red Gum	530		530	25	14	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5602	Allocasuarina littoralis	Black She-oak	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5603	Allocasuarina littoralis	Black She-oak	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5604	Angophora leiocarpa	Smooth-barked Apple	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5605	Corymbia intermedia	Pink Bloodwood	320		320	25	14	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5606	Acacia disparrima	Hickory Wattle	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5607	Corymbia intermedia	Pink Bloodwood	320		320	22	12	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5608	Acacia disparrima	Hickory Wattle	100	80	128	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5609	Acacia disparrima	Hickory Wattle	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5610	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5611	Allocasuarina littoralis	Black She-oak	120	60	134	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5612	Corymbia intermedia	Pink Bloodwood	500		500	25	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5613	Corymbia citriodora	Spotted Gum	380		380	25	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5614	Acacia disparrima	Hickory Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5615	Alphitonia excelsa	Soap Tree	140		140	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5616	Acacia leiocalyx	Early-flowering Black Wattle	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5617	Eucalyptus tereticornis	Forest Red Gum	440		440	25	14	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove
5618	Acacia disparrima	Hickory Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5619	Acacia leiocalyx	Early-flowering Black Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5620	Alphitonia excelsa	Soap Tree	210		210	9	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5621	Eucalyptus tereticornis	Forest Red Gum	420		420	25	13	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5622	Acacia leiocalyx	Early-flowering Black Wattle	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5623	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5624	Corymbia citriodora	Spotted Gum	110		110	11	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5625	Acacia disparrima	Hickory Wattle	160		160	8	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5626	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5627	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5628	Corymbia citriodora	Spotted Gum	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5629	Corymbia citriodora	Spotted Gum	140		140	11	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5630	Alphitonia excelsa	Soap Tree	300		300	10	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5631	DEAD/STAG		460		460	14	7	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5632	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5633	Alphitonia excelsa	Soap Tree	210		210	10	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5634	Acacia disparrima	Hickory Wattle	110	120	163	8	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5635	Corymbia citriodora	Spotted Gum	460		460	26	14	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5636	Eucalyptus crebra	Narrow-leaved Ironbark	340		340	26	14	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5637	Eucalyptus tereticornis	Forest Red Gum	200		200	20	4	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5638	Corymbia citriodora	Spotted Gum	360		360	25	14	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5639	Acacia leiocalyx	Early-flowering Black Wattle	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5640	Acacia leiocalyx	Early-flowering Black Wattle	120	100	156	6	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5641	Eucalyptus tereticornis	Forest Red Gum	440		440	26	14	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5642	Acacia leiocalyx	Early-flowering Black Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
5643	Acacia disparrima	Hickory Wattle	120		120	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5644	Lophostemon suaveolens	Swamp Box	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5645	Acacia disparrima	Hickory Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5646	Acacia leiocalyx	Early-flowering Black Wattle	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5647	Alphitonia excelsa	Soap Tree	280		280	12	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5648	Acacia disparrima	Hickory Wattle	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5649	Corymbia citriodora	Spotted Gum	450		450	24	13	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5650	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	25	12	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5651	Acacia disparrima	Hickory Wattle	100	80	128	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5652	Eucalyptus tereticornis	Forest Red Gum	240		240	24	8	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5653	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5654	Acacia leiocalyx	Early-flowering Black Wattle	180		180	7	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5655	Corymbia citriodora	Spotted Gum	470		470	27	15	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5656	Acacia disparrima	Hickory Wattle	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5657	Eucalyptus tereticornis	Forest Red Gum	380		380	24	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove for basin works
5658	Acacia disparrima	Hickory Wattle	130	120	177	6	5	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5659	Acacia leiocalyx	Early-flowering Black Wattle	150		150	6	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5660	Allocasuarina littoralis	Black She-oak	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5661	Acacia leiocalyx	Early-flowering Black Wattle	110		110	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5662	Petalostigma pubescens	Quinine Bush	120		120	5	4	2.0	1.4	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5663	Acacia disparrima	Hickory Wattle	110		110	5	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5664	Acacia leiocalyx	Early-flowering Black Wattle	190		190	7	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5665	Acacia leiocalyx	Early-flowering Black Wattle	130		130	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5666	Corymbia citriodora	Spotted Gum	410		410	25	10	4.9	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5667	Eucalyptus crebra	Narrow-leaved Ironbark	120		120	6	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5668	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5669	Corymbia citriodora	Spotted Gum	410		410	26	14	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5670	Eucalyptus tereticornis	Forest Red Gum	260		260	20	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5671	Corymbia citriodora	Spotted Gum	280		280	26	14	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5672	Eucalyptus tereticornis	Forest Red Gum	240		240	5	2	2.9	1.8	Regular	-	-	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5673	Acacia leiocalyx	Early-flowering Black Wattle	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5674	Corymbia intermedia	Pink Bloodwood	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5675	Acacia leiocalyx	Early-flowering Black Wattle	150		150	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5676	Acacia leiocalyx	Early-flowering Black Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5677	Acacia leiocalyx	Early-flowering Black Wattle	140		140	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5678	Acacia leiocalyx	Early-flowering Black Wattle	110		110	4	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5679	Allocasuarina littoralis	Black She-oak	260		260	8	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5680	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5681	Acacia leiocalyx	Early-flowering Black Wattle	130		130	5	2	2.0	1.4	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5682	Corymbia citriodora	Spotted Gum	400		400	26	14	4.8	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5683	Corymbia citriodora	Spotted Gum	380		380	24	10	4.6	2.2	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5684	Acacia leiocalyx	Early-flowering Black Wattle	100		100	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5685	Acacia leiocalyx	Early-flowering Black Wattle	150		150	8	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5686	Corymbia citriodora	Spotted Gum	340		340	24	12	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5687	Alphitonia excelsa	Soap Tree	200		200	10	5	2.4	1.7	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5688	Allocasuarina littoralis	Black She-oak	120		120	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5689	Eucalyptus tereticornis	Forest Red Gum	200		200	22	10	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5690	Corymbia intermedia	Pink Bloodwood	160		160	18	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5691	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5692	Allocasuarina littoralis	Black She-oak	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5693	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	24	8	2.9	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5694	Eucalyptus tereticornis	Forest Red Gum	280		280	24	14	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
5695	Petalostigma pubescens	Quinine Bush	220		220	8	7	2.6	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5696	Acacia leiocalyx	Early-flowering Black Wattle	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5697	Allocasuarina littoralis	Black She-oak	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5698	Allocasuarina littoralis	Black She-oak	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5699	Allocasuarina littoralis	Black She-oak	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5700	Acacia disparrima	Hickory Wattle	100		100	6	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5701	Alphitonia excelsa	Soap Tree	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5702	Allocasuarina littoralis	Black She-oak	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5703	Alphitonia excelsa	Soap Tree	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5704	Alphitonia excelsa	Soap Tree	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5705	Allocasuarina littoralis	Black She-oak	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5706	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5707	Allocasuarina littoralis	Black She-oak	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5708	Alphitonia excelsa	Soap Tree	170		170	9	5	2.0	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5709	Alphitonia excelsa	Soap Tree	170		170	8	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5710	Allocasuarina littoralis	Black She-oak	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5711	Corymbia citriodora	Spotted Gum	440		440	25	13	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5712	Acacia leiocalyx	Early-flowering Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5713	Angophora leiocarpa	Smooth-barked Apple	160		160	12	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5714	Corymbia citriodora	Spotted Gum	290		290	24	13	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5715	Corymbia citriodora	Spotted Gum	410		410	26	14	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5716	Eucalyptus tereticornis	Forest Red Gum	250		250	18	8	3.0	1.8	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5717	Acacia leiocalyx	Early-flowering Black Wattle	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5718	Alphitonia excelsa	Soap Tree	150		150	7	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5719	Acacia leiocalyx	Early-flowering Black Wattle	100		100	6	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5720	Acacia leiocalyx	Early-flowering Black Wattle	140		140	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5721	Corymbia citriodora	Spotted Gum	230		230	26	12	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5722	Acacia leiocalyx	Early-flowering Black Wattle	140		140	6	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5723	Corymbia citriodora	Spotted Gum	170		170	20	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5724	Corymbia citriodora	Spotted Gum	220		220	24	10	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5725	Eucalyptus crebra	Narrow-leaved Ironbark	170		170	18	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5726	Corymbia citriodora	Spotted Gum	380		380	26	13	4.6	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5727	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5728	Corymbia citriodora	Spotted Gum	420		420	26	14	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5729	Acacia leiocalyx	Early-flowering Black Wattle	130		130	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5730	Corymbia intermedia	Pink Bloodwood	200		200	22	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5731	Acacia leiocalyx	Early-flowering Black Wattle	130	130	184	9	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5732	Corymbia citriodora	Spotted Gum	140		140	5	3	2.0	0.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5733	Acacia disparrima	Hickory Wattle	130		130	9	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5734	Corymbia citriodora	Spotted Gum	430		430	26	14	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5735	Alphitonia excelsa	Soap Tree	210		210	13	7	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5736	Eucalyptus crebra	Narrow-leaved Ironbark	240		240	22	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5737	Corymbia intermedia	Pink Bloodwood	220		220	20	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5738	Acacia leiocalyx	Early-flowering Black Wattle	120	100	156	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5739	Allocasuarina littoralis	Black She-oak	170		170	8	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5740	Alphitonia excelsa	Soap Tree	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5741	Allocasuarina littoralis	Black She-oak	110		110	9	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5742	Allocasuarina littoralis	Black She-oak	120		120	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5743	Acacia leiocalyx	Early-flowering Black Wattle	140		140	10	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5744	Eucalyptus tereticornis	Forest Red Gum	560		560	26	14	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
5745	Alphitonia excelsa	Soap Tree	320		320	9	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5746	Allocasuarina littoralis	Black She-oak	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5747	Lophostemon suaveolens	Swamp Box	160		160	15	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5748	Allocasuarina littoralis	Black She-oak	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5749	Allocasuarina littoralis	Black She-oak	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
5750	Allocasuarina littoralis	Black She-oak	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
5751	Allocasuarina littoralis	Black She-oak	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5752	Corymbia intermedia	Pink Bloodwood	230		230	22	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5753	Eucalyptus tereticornis	Forest Red Gum	220		220	22	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	Introduced	-	-	Typical	-	-	-	-	-	-		Retain
5754	Alphitonia excelsa	Soap Tree	100		100	8	6	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5755	Allocasuarina littoralis	Black She-oak	100		100	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5756	Alphitonia excelsa	Soap Tree	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5757	Corymbia intermedia	Pink Bloodwood	200		200	16	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5758	Alphitonia excelsa	Soap Tree	230		230	14	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5759	Lophostemon suaveolens	Swamp Box	280		280	16	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5760	Corymbia intermedia	Pink Bloodwood	230		230	14	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5761	Allocasuarina littoralis	Black She-oak	110		110	6	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5762	Eucalyptus tereticornis	Forest Red Gum	440		440	26	14	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5763	Alphitonia excelsa	Soap Tree	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5764	Petalostigma pubescens	Quinine Bush	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5765	Petalostigma pubescens	Quinine Bush	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5766	Alphitonia excelsa	Soap Tree	210		210	16	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5767	Petalostigma pubescens	Quinine Bush	150		150	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5768	Corymbia citriodora	Spotted Gum	420		420	26	14	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5769	Eucalyptus tereticornis	Forest Red Gum	420		420	25	13	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
5770	Casuarina cunninghamiana	River She-oak	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5771	Casuarina cunninghamiana	River She-oak	150	130	198	18	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5772	Casuarina cunninghamiana	River She-oak	220		220	20	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5773	Grevillea robusta	Silky Oak	130		130	16	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5774	Casuarina cunninghamiana	River She-oak	180		180	18	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5775	Eucalyptus tereticornis	Forest Red Gum	250		250	22	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5776	Casuarina cunninghamiana	River She-oak	230		230	20	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5777	Alphitonia excelsa	Soap Tree	110		110	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5778	Casuarina cunninghamiana	River She-oak	430		430	22	10	5.2	2.3	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
5779	Alphitonia excelsa	Soap Tree	100		100	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5780	Casuarina cunninghamiana	River She-oak	240		240	20	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5781	Alphitonia excelsa	Soap Tree	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5782	Alphitonia excelsa	Soap Tree	110		110	11	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5783	Alphitonia excelsa	Soap Tree	110		110	12	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5784	Eucalyptus tereticornis	Forest Red Gum	180		180	16	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5785	Acacia disparrima	Hickory Wattle	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5786	Grevillea robusta	Silky Oak	240		240	18	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5787	Banksia integrifolia	Coast Banksia	150		150	10	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5788	Alphitonia excelsa	Soap Tree	120		120	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5789	Eucalyptus tereticornis	Forest Red Gum	340		340	24	12	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
5790	Alphitonia excelsa	Soap Tree	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5791	Eucalyptus saligna	Sydney Blue Gum	520		520	27	15	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5792	Casuarina cunninghamiana	River She-oak	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5793	Angophora leiocarpa	Smooth-barked Apple	230		230	20	10	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5794	Corymbia citriodora	Spotted Gum	260		260	22	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5795	Eucalyptus saligna	Sydney Blue Gum	260		260	22	12	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5796	Corymbia citriodora	Spotted Gum	170		170	18	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5797	Alphitonia excelsa	Soap Tree	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5798	Alphitonia excelsa	Soap Tree	170		170	10	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5799	Eucalyptus tereticornis	Forest Red Gum	280		280	18	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5800	Acacia fimbriata	Fringed Wattle	100		100	8	6	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5801	Corymbia intermedia	Pink Bloodwood	150		150	16	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5802	Alphitonia excelsa	Soap Tree	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5803	Alphitonia excelsa	Soap Tree	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5804	Corymbia citriodora	Spotted Gum	130		130	18	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5805	Acacia disparrima	Hickory Wattle	170		170	10	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5806	Corymbia citriodora	Spotted Gum	140		140	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5807	Corymbia intermedia	Pink Bloodwood	100		100	12	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5808	Angophora leiocarpa	Smooth-barked Apple	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5809	Angophora leiocarpa	Smooth-barked Apple	160		160	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5810	Corymbia intermedia	Pink Bloodwood	140		140	16	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5811	Corymbia citriodora	Spotted Gum	130		130	16	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5812	Corymbia intermedia	Pink Bloodwood	130		130	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5813	Corymbia intermedia	Pink Bloodwood	180		180	16	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5814	Corymbia citriodora	Spotted Gum	310		310	24	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5815	Corymbia intermedia	Pink Bloodwood	150		150	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5816	Eucalyptus tereticornis	Forest Red Gum	140		140	18	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5817	Angophora leiocarpa	Smooth-barked Apple	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5818	Corymbia citriodora	Spotted Gum	210		210	22	10	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5819	Angophora leiocarpa	Smooth-barked Apple	170		170	18	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5820	Corymbia citriodora	Spotted Gum	260	240	354	22	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5821	Corymbia citriodora	Spotted Gum	200		200	20	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5822	Angophora leiocarpa	Smooth-barked Apple	160	140	213	14	6	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5823	Corymbia intermedia	Pink Bloodwood	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5824	Corymbia intermedia	Pink Bloodwood	100		100	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5825	Corymbia citriodora	Spotted Gum	260		260	20	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5826	Angophora leiocarpa	Smooth-barked Apple	330	140	358	20	11	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5827	Angophora leiocarpa	Smooth-barked Apple	120		120	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5828	Corymbia intermedia	Pink Bloodwood	210		210	20	8	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5829	Eucalyptus tereticornis	Forest Red Gum	310		310	20	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5830	Angophora leiocarpa	Smooth-barked Apple	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5831	Corymbia citriodora	Spotted Gum	160		160	20	8	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5832	Corymbia intermedia	Pink Bloodwood	220		220	20	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5833	Lophostemon suaveolens	Swamp Box	200		200	14	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5834	Angophora leiocarpa	Smooth-barked Apple	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5835	Lophostemon suaveolens	Swamp Box	180		180	12	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5836	Lophostemon suaveolens	Swamp Box	150	150, 140	254	10	7	3.0	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5837	Lophostemon suaveolens	Swamp Box	180		180	16	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5838	Corymbia intermedia	Pink Bloodwood	230		230	22	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5839	Corymbia citriodora	Spotted Gum	160		160	20	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5840	Lophostemon suaveolens	Swamp Box	130		130	10	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5841	Lophostemon suaveolens	Swamp Box	120		120	8	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5842	Lophostemon suaveolens	Swamp Box	140	140	198	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5843	Lophostemon suaveolens	Swamp Box	170		170	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5844	Lophostemon suaveolens	Swamp Box	160		160	12	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5845	Corymbia intermedia	Pink Bloodwood	150		150	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5846	Eucalyptus tereticornis	Forest Red Gum	350		350	25	14	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5847	Lophostemon suaveolens	Swamp Box	150	150	212	12	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5848	Lophostemon suaveolens	Swamp Box	150		150	10	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5849	Lophostemon suaveolens	Swamp Box	180		180	9	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5850	Lophostemon suaveolens	Swamp Box	160		160	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5851	Lophostemon suaveolens	Swamp Box	140		140	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5852	Angophora leiocarpa	Smooth-barked Apple	140		140	18	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5853	Corymbia intermedia	Pink Bloodwood	220		220	20	8	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5854	Lophostemon suaveolens	Swamp Box	150		150	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5855	Angophora leiocarpa	Smooth-barked Apple	200		200	14	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5856	Lophostemon suaveolens	Swamp Box	130		130	13	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5857	Lophostemon suaveolens	Swamp Box	180		180	16	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5858	Lophostemon suaveolens	Swamp Box	140		140	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5859	Alphitonia excelsa	Soap Tree	150		150	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5860	Lophostemon suaveolens	Swamp Box	200		200	12	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5861	Angophora leiocarpa	Smooth-barked Apple	180		180	20	10	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5862	Corymbia intermedia	Pink Bloodwood	280	220	356	22	10	4.3	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5863	Eucalyptus seeana	Narrow-leaved Red Gum	250		250	20	10	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5864	Corymbia intermedia	Pink Bloodwood	180	140	228	14	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5865	Lophostemon suaveolens	Swamp Box	120		120	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5866	Lophostemon suaveolens	Swamp Box	140		140	12	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5867	Corymbia intermedia	Pink Bloodwood	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5868	Eucalyptus seeana	Narrow-leaved Red Gum	180		180	18	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5869	Lophostemon suaveolens	Swamp Box	160		160	16	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5870	Eucalyptus seeana	Narrow-leaved Red Gum	120		120	14	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5871	Eucalyptus seeana	Narrow-leaved Red Gum	140		140	14	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5872	Acacia disparrima	Hickory Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5873	Corymbia intermedia	Pink Bloodwood	180		180	18	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5874	Corymbia intermedia	Pink Bloodwood	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5875	Lophostemon suaveolens	Swamp Box	110		110	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5876	Lophostemon suaveolens	Swamp Box	110		110	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5877	Lophostemon suaveolens	Swamp Box	140		140	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5878	Corymbia intermedia	Pink Bloodwood	240		240	18	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5879	Alphitonia excelsa	Soap Tree	130		130	14	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5880	Lophostemon suaveolens	Swamp Box	160		160	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5881	Lophostemon suaveolens	Swamp Box	160		160	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5882	Alphitonia excelsa	Soap Tree	120		120	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5883	Lophostemon suaveolens	Swamp Box	180		180	12	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5884	Corymbia intermedia	Pink Bloodwood	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5885	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5886	Lophostemon suaveolens	Swamp Box	140		140	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5887	Alphitonia excelsa	Soap Tree	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5888	Acacia disparrima	Hickory Wattle	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5889	Lophostemon suaveolens	Swamp Box	220		220	10	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5890	Alphitonia excelsa	Soap Tree	100		100	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5891	Corymbia intermedia	Pink Bloodwood	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5892	Corymbia intermedia	Pink Bloodwood	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5893	Angophora leiocarpa	Smooth-barked Apple	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
5894	Corymbia tessellaris	Moreton Bay Ash	150		150	14	3	2.0	1.5	Regular	-	Thinning	-	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5895	Lophostemon suaveolens	Swamp Box	160	160, 160	277	12	5	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5896	Lophostemon suaveolens	Swamp Box	180		180	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5897	Lophostemon suaveolens	Swamp Box	170		170	10	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5898	Lophostemon suaveolens	Swamp Box	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5899	Corymbia intermedia	Pink Bloodwood	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5900	Angophora leiocarpa	Smooth-barked Apple	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5901	Lophostemon suaveolens	Swamp Box	200		200	11	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5902	Acacia leiocalyx	Early-flowering Black Wattle	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5903	Alphitonia excelsa	Soap Tree	180		180	10	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5904	Lophostemon suaveolens	Swamp Box	130	130	184	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5905	Corymbia citriodora	Spotted Gum	230		230	18	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5906	Eucalyptus tereticornis	Forest Red Gum	190		190	14	8	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5907	Lophostemon suaveolens	Swamp Box	160		160	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5908	Lophostemon suaveolens	Swamp Box	140		140	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5909	Corymbia citriodora	Spotted Gum	200		200	18	10	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5910	Corymbia intermedia	Pink Bloodwood	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5911	Acacia disparrima	Hickory Wattle	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5912	Corymbia citriodora	Spotted Gum	130		130	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5913	Corymbia citriodora	Spotted Gum	170		170	14	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5914	Alphitonia excelsa	Soap Tree	100		100	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5915	Angophora leiocarpa	Smooth-barked Apple	220		220	10	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5916	Eucalyptus tereticornis	Forest Red Gum	200		200	18	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5917	Corymbia intermedia	Pink Bloodwood	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5918	Corymbia tessellaris	Moreton Bay Ash	120		120	12	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5919	Eucalyptus siderophloia	Northern Grey Ironbark	310		310	15	4	3.7	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5920	Corymbia intermedia	Pink Bloodwood	360		360	18	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5921	Eucalyptus tereticornis	Forest Red Gum	270		270	20	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5922	Corymbia intermedia	Pink Bloodwood	210		210	15	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5923	Corymbia intermedia	Pink Bloodwood	220		220	22	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5924	Corymbia intermedia	Pink Bloodwood	270		270	16	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5925	Corymbia intermedia	Pink Bloodwood	340		340	18	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5926	Corymbia intermedia	Pink Bloodwood	290		290	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5927	Eucalyptus seeana	Narrow-leaved Red Gum	220		220	15	2	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5928	Corymbia intermedia	Pink Bloodwood	230		230	16	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5929	Acacia disparrima	Hickory Wattle	110	70, 80	153	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5930	Corymbia intermedia	Pink Bloodwood	270		270	20	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5931	Corymbia intermedia	Pink Bloodwood	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5932	Corymbia intermedia	Pink Bloodwood	150		150	15	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5933	Lophostemon suaveolens	Swamp Box	320		320	15	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5934	Eucalyptus seeana	Narrow-leaved Red Gum	300		300	25	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5935	Petalostigma pubescens	Quinine Bush	230		230	9	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5936	Acacia disparrima	Hickory Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5937	Corymbia tessellaris	Moreton Bay Ash	110		110	15	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5938	Petalostigma pubescens	Quinine Bush	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5939	Acacia disparrima	Hickory Wattle	130	70	148	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5940	Acacia disparrima	Hickory Wattle	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5941	Acacia disparrima	Hickory Wattle	130	120	177	12	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5942	Acacia leiocalyx	Early-flowering Black Wattle	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5943	Lophostemon suaveolens	Swamp Box	280		280	15	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5944	Corymbia intermedia	Pink Bloodwood	320		320	16	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5945	Acacia disparrima	Hickory Wattle	100	70	122	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5946	Acacia leiocalyx	Early-flowering Black Wattle	110		110	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5947	Corymbia intermedia	Pink Bloodwood	260		260	22	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5948	Acacia leiocalyx	Early-flowering Black Wattle	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5949	Corymbia intermedia	Pink Bloodwood	170		170	18	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5950	Corymbia intermedia	Pink Bloodwood	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5951	Corymbia intermedia	Pink Bloodwood	420		420	22	6	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5952	Corymbia intermedia	Pink Bloodwood	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5953	Acacia leiocalyx	Early-flowering Black Wattle	100		100	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5954	Petalostigma pubescens	Quinine Bush	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5955	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5956	Acacia disparrima	Hickory Wattle	120		120	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5957	Corymbia intermedia	Pink Bloodwood	170		170	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5958	Eucalyptus tereticornis	Forest Red Gum	280		280	25	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5959	Corymbia intermedia	Pink Bloodwood	220		220	18	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5960	Eucalyptus seeana	Narrow-leaved Red Gum	290		290	23	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5961	Corymbia intermedia	Pink Bloodwood	290		290	18	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5962	Acacia disparrima	Hickory Wattle	100	70, 40	128	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5963	Corymbia intermedia	Pink Bloodwood	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5964	Corymbia intermedia	Pink Bloodwood	170		170	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5965	Corymbia intermedia	Pink Bloodwood	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5966	Acacia disparrima	Hickory Wattle	110		110	12	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5967	Eucalyptus seeana	Narrow-leaved Red Gum	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
5968	Corymbia intermedia	Pink Bloodwood	260		260	16	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5969	Corymbia intermedia	Pink Bloodwood	260		260	22	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5970	Acacia leiocalyx	Early-flowering Black Wattle	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5971	Corymbia intermedia	Pink Bloodwood	300		300	18	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5972	Alphitonia excelsa	Soap Tree	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5973	Alphitonia excelsa	Soap Tree	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5974	Corymbia intermedia	Pink Bloodwood	250		250	18	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5975	Corymbia intermedia	Pink Bloodwood	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5976	Corymbia intermedia	Pink Bloodwood	260		260	15	2	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5977	Corymbia intermedia	Pink Bloodwood	310		310	18	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5978	Corymbia intermedia	Pink Bloodwood	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5979	Corymbia intermedia	Pink Bloodwood	290		290	22	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
5980	Corymbia intermedia	Pink Bloodwood	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5981	Corymbia intermedia	Pink Bloodwood	320		320	18	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
5982	Corymbia intermedia	Pink Bloodwood	210		210	15	2	2.5	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5983	Corymbia intermedia	Pink Bloodwood	160		160	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5984	Corymbia intermedia	Pink Bloodwood	180		180	18	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5985	Corymbia intermedia	Pink Bloodwood	120		120	8	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5986	Corymbia intermedia	Pink Bloodwood	340		340	25	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5987	Corymbia intermedia	Pink Bloodwood	320		320	22	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5988	Acacia leiocalyx	Early-flowering Black Wattle	110		110	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5989	Angophora leiocarpa	Smooth-barked Apple	220		220	20	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5990	Corymbia intermedia	Pink Bloodwood	320		320	22	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5991	Lophostemon suaveolens	Swamp Box	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5992	Corymbia intermedia	Pink Bloodwood	160		160	18	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5993	Alphitonia excelsa	Soap Tree	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5994	Corymbia intermedia	Pink Bloodwood	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5995	Corymbia intermedia	Pink Bloodwood	280		280	18	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5996	Corymbia intermedia	Pink Bloodwood	260		260	18	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5997	Alphitonia excelsa	Soap Tree	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5998	Acacia disparrima	Hickory Wattle	100	90, 50, 50, 50, 40	165	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
5999	Alphitonia excelsa	Soap Tree	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6000	Alphitonia excelsa	Soap Tree	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6001	Corymbia intermedia	Pink Bloodwood	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6002	Acacia disparrima	Hickory Wattle	130	50, 50, 30	151	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6003	Alphitonia excelsa	Soap Tree	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6004	Alphitonia excelsa	Soap Tree	210		210	15	2	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove for trunk sewer
6005	Melaleuca quinquenervia	Broad-leaved Paperbark	310		310	22	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6006	Melaleuca quinquenervia	Broad-leaved Paperbark	230		230	18	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6007	Corymbia intermedia	Pink Bloodwood	300		300	18	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6008	Alphitonia excelsa	Soap Tree	210		210	8	2	2.5	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6009	Angophora leiocarpa	Smooth-barked Apple	250		250	23	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6010	Acacia disparrima	Hickory Wattle	100		100	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6011	Corymbia intermedia	Pink Bloodwood	280		280	25	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6012	Alphitonia excelsa	Soap Tree	150		150	5	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6013	Lophostemon suaveolens	Swamp Box	230		230	18	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6014	Alphitonia excelsa	Soap Tree	150		150	3	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6015	Alphitonia excelsa	Soap Tree	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6016	Petalostigma pubescens	Quinine Bush	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6017	Angophora leiocarpa	Smooth-barked Apple	130		130	20	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6018	Petalostigma pubescens	Quinine Bush	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6019	Eucalyptus tereticornis	Forest Red Gum	320		320	22	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6020	Acacia leiocalyx	Early-flowering Black Wattle	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6021	Petalostigma pubescens	Quinine Bush	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6022	Corymbia intermedia	Pink Bloodwood	160		160	18	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6023	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6024	Alphitonia excelsa	Soap Tree	250		250	15	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6025	Alphitonia excelsa	Soap Tree	130		130	12	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6026	Lophostemon suaveolens	Swamp Box	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6027	Corymbia intermedia	Pink Bloodwood	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6028	Acacia disparrima	Hickory Wattle	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6029	Corymbia intermedia	Pink Bloodwood	330		330	18	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6030	Corymbia intermedia	Pink Bloodwood	320		320	20	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6031	Lophostemon suaveolens	Swamp Box	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6032	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6033	Acacia leiocalyx	Early-flowering Black Wattle	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6034	Corymbia intermedia	Pink Bloodwood	210		210	22	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6035	Acacia disparrima	Hickory Wattle	160	80	179	8	2	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6036	Corymbia intermedia	Pink Bloodwood	300		300	18	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6037	Acacia leiocalyx	Early-flowering Black Wattle	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6038	Corymbia citriodora	Spotted Gum	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6039	Acacia disparrima	Hickory Wattle	140		140	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6040	Angophora leiocarpa	Smooth-barked Apple	110		110	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6041	Eucalyptus siderophloia	Northern Grey Ironbark	100		100	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6042	Corymbia citriodora	Spotted Gum	130		130	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6043	Corymbia citriodora	Spotted Gum	120		120	18	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6044	Acacia leiocalyx	Early-flowering Black Wattle	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6045	Acacia disparrima	Hickory Wattle	140	50, 50	157	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6046	Acacia leiocalyx	Early-flowering Black Wattle	180		180	13	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6047	Acacia leiocalyx	Early-flowering Black Wattle	120		120	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6048	Acacia disparrima	Hickory Wattle	120		120	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6049	Acacia leiocalyx	Early-flowering Black Wattle	120		120	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6050	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6051	Alphitonia excelsa	Soap Tree	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6052	Corymbia intermedia	Pink Bloodwood	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6053	Acacia leiocalyx	Early-flowering Black Wattle	140		140	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6054	Corymbia citriodora	Spotted Gum	300		300	20	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6055	Acacia disparrima	Hickory Wattle	140		140	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6056	Acacia disparrima	Hickory Wattle	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6057	Acacia leiocalyx	Early-flowering Black Wattle	130	60	143	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6058	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6059	Corymbia citriodora	Spotted Gum	160		160	20	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6060	Acacia leiocalyx	Early-flowering Black Wattle	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6061	Corymbia citriodora	Spotted Gum	90	50	103	15	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6062	Corymbia citriodora	Spotted Gum	350		350	22	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6063	Corymbia citriodora	Spotted Gum	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6064	Corymbia citriodora	Spotted Gum	280		280	20	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6065	Corymbia citriodora	Spotted Gum	100		100	8	1	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6066	Eucalyptus siderophloia	Northern Grey Ironbark	130		130	10	1	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6067	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6068	Corymbia citriodora	Spotted Gum	110		110	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6069	Acacia leiocalyx	Early-flowering Black Wattle	90	60	108	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6070	Corymbia citriodora	Spotted Gum	100		100	13	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6071	Corymbia citriodora	Spotted Gum	130		130	16	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6072	Acacia leiocalyx	Early-flowering Black Wattle	120		120	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6073	Acacia leiocalyx	Early-flowering Black Wattle	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6074	Acacia leiocalyx	Early-flowering Black Wattle	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6075	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	25	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6076	Acacia leiocalyx	Early-flowering Black Wattle	120		120	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6077	Acacia leiocalyx	Early-flowering Black Wattle	100	90	135	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6078	Corymbia citriodora	Spotted Gum	260		260	18	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6079	Angophora leiocarpa	Smooth-barked Apple	320		320	20	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6080	Eucalyptus crebra	Narrow-leaved Ironbark	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6081	Acacia leiocalyx	Early-flowering Black Wattle	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6082	Corymbia citriodora	Spotted Gum	240		240	20	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6083	Acacia leiocalyx	Early-flowering Black Wattle	110		110	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6084	Angophora leiocarpa	Smooth-barked Apple	230		230	20	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6085	Corymbia citriodora	Spotted Gum	330		330	25	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6086	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	20	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6087	Acacia leiocalyx	Early-flowering Black Wattle	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6088	Corymbia intermedia	Pink Bloodwood	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6089	Corymbia citriodora	Spotted Gum	230		230	18	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6090	Allocasuarina littoralis	Black She-oak	130		130	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6091	Eucalyptus tereticornis	Forest Red Gum	160		160	20	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6092	Corymbia citriodora	Spotted Gum	340		340	20	5	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6093	Acacia disparrima	Hickory Wattle	240		240	10	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6094	Alphitonia excelsa	Soap Tree	210		210	13	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6095	Alphitonia excelsa	Soap Tree	100		100	13	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6096	Acacia disparrima	Hickory Wattle	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6097	Acacia leiocalyx	Early-flowering Black Wattle	110		110	13	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6098	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6099	Corymbia citriodora	Spotted Gum	280		280	22	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6100	Eucalyptus tereticornis	Forest Red Gum	270		270	25	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	New	-	-	-	-		Retain
6101	Acacia leiocalyx	Early-flowering Black Wattle	100		100	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6102	Corymbia citriodora	Spotted Gum	290		290	22	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6103	Eucalyptus siderophloia	Northern Grey Ironbark	130		130	18	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6104	Corymbia intermedia	Pink Bloodwood	240		240	22	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6105	Acacia leiocalyx	Early-flowering Black Wattle	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6106	Corymbia citriodora	Spotted Gum	240		240	18	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6107	Eucalyptus crebra	Narrow-leaved Ironbark	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6108	Corymbia citriodora	Spotted Gum	310		310	20	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6109	Acacia disparrima	Hickory Wattle	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6110	Angophora leiocarpa	Smooth-barked Apple	360		360	20	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6111	Alphitonia excelsa	Soap Tree	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6112	Acacia disparrima	Hickory Wattle	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6113	Eucalyptus tereticornis	Forest Red Gum	280		280	20	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6114	Eucalyptus siderophloia	Northern Grey Ironbark	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6115	Acacia disparrima	Hickory Wattle	100	70, 80	146	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6116	Corymbia intermedia	Pink Bloodwood	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6117	Acacia leiocalyx	Early-flowering Black Wattle	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6118	Eucalyptus seeana	Narrow-leaved Red Gum	130		130	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6119	Alphitonia excelsa	Soap Tree	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6120	Acacia leiocalyx	Early-flowering Black Wattle	130		130	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6121	Alphitonia excelsa	Soap Tree	170		170	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6122	Alphitonia excelsa	Soap Tree	230		230	15	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6123	Alphitonia excelsa	Soap Tree	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6124	Petalostigma pubescens	Quinine Bush	110	100	149	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6125	Eucalyptus crebra	Narrow-leaved Ironbark	310		310	25	7	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6126	Acacia leiocalyx	Early-flowering Black Wattle	110		110	13	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6127	Allocasuarina littoralis	Black She-oak	120		120	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6128	Acacia disparrima	Hickory Wattle	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6129	Corymbia intermedia	Pink Bloodwood	120		120	16	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6130	Alphitonia excelsa	Soap Tree	100		100	10	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6131	Acacia disparrima	Hickory Wattle	100	70	122	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6132	Allocasuarina littoralis	Black She-oak	120		120	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6133	Petalostigma pubescens	Quinine Bush	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6134	Allocasuarina littoralis	Black She-oak	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6135	Allocasuarina littoralis	Black She-oak	100		100	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6136	Corymbia citriodora	Spotted Gum	280		280	25	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6137	Casuarina cunninghamiana	River She-oak	120		120	18	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6138	Casuarina cunninghamiana	River She-oak	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6139	Corymbia intermedia	Pink Bloodwood	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6140	Eucalyptus seeana	Narrow-leaved Red Gum	420		420	25	4	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6141	Alphitonia excelsa	Soap Tree	130		130	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6142	Alphitonia excelsa	Soap Tree	110		110	12	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6143	Eucalyptus tereticornis	Forest Red Gum	240		240	18	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6144	Alphitonia excelsa	Soap Tree	150		150	18	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6145	Alphitonia excelsa	Soap Tree	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6146	Corymbia intermedia	Pink Bloodwood	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6147	Corymbia citriodora	Spotted Gum	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6148	Eucalyptus tereticornis	Forest Red Gum	180		180	18	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6149	Eucalyptus tereticornis	Forest Red Gum	260		260	22	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6150	Eucalyptus tereticornis	Forest Red Gum	310		310	20	4	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6151	Corymbia citriodora	Spotted Gum	180		180	18	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6152	Eucalyptus seeana	Narrow-leaved Red Gum	210		210	20	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6153	Eucalyptus seeana	Narrow-leaved Red Gum	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6154	Angophora leiocarpa	Smooth-barked Apple	190		190	18	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6155	Corymbia citriodora	Spotted Gum	240		240	20	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6156	Alphitonia excelsa	Soap Tree	120		120	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6157	Angophora leiocarpa	Smooth-barked Apple	130		130	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6158	Corymbia citriodora	Spotted Gum	120		120	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6159	Corymbia intermedia	Pink Bloodwood	120		120	18	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6160	Petalostigma pubescens	Quinine Bush	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6161	Alphitonia excelsa	Soap Tree	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6162	Corymbia citriodora	Spotted Gum	100		100	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6163	Lophostemon suaveolens	Swamp Box	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6164	Eucalyptus seeana	Narrow-leaved Red Gum	280		280	18	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6165	Angophora leiocarpa	Smooth-barked Apple	280		280	18	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6166	Alphitonia excelsa	Soap Tree	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6167	Eucalyptus seeana	Narrow-leaved Red Gum	160		160	18	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6168	Corymbia intermedia	Pink Bloodwood	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6169	Angophora leiocarpa	Smooth-barked Apple	150		150	18	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6170	Lophostemon suaveolens	Swamp Box	200		200	20	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6171	Lophostemon suaveolens	Swamp Box	190	110	220	18	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6172	Angophora leiocarpa	Smooth-barked Apple	180		180	22	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6173	Corymbia intermedia	Pink Bloodwood	180		180	20	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6174	Angophora leiocarpa	Smooth-barked Apple	160		160	18	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6175	Eucalyptus tereticornis	Forest Red Gum	140		140	18	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6176	Lophostemon suaveolens	Swamp Box	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6177	Angophora leiocarpa	Smooth-barked Apple	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6178	Petalostigma pubescens	Quinine Bush	170		170	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6179	Corymbia intermedia	Pink Bloodwood	190		190	18	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6180	Acacia disparrima	Hickory Wattle	160		160	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6181	Lophostemon suaveolens	Swamp Box	130	180	222	13	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6182	Eucalyptus seeana	Narrow-leaved Red Gum	230		230	22	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6183	Eucalyptus seeana	Narrow-leaved Red Gum	143		143	18	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6184	Corymbia intermedia	Pink Bloodwood	260		260	20	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6185	Corymbia intermedia	Pink Bloodwood	120		120	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6186	Angophora leiocarpa	Smooth-barked Apple	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6187	Eucalyptus tereticornis	Forest Red Gum	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6188	Lophostemon suaveolens	Swamp Box	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6189	Lophostemon suaveolens	Swamp Box	180		180	15	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6190	Eucalyptus tereticornis	Forest Red Gum	140		140	18	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6191	Lophostemon suaveolens	Swamp Box	210		210	15	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6192	Eucalyptus tereticornis	Forest Red Gum	210		210	20	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6193	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6194	Corymbia intermedia	Pink Bloodwood	180		180	18	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6195	Corymbia intermedia	Pink Bloodwood	130		130	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6196	Angophora leiocarpa	Smooth-barked Apple	230		230	20	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6197	Corymbia intermedia	Pink Bloodwood	130		130	18	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6198	Lophostemon suaveolens	Swamp Box	130		130	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6199	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6200	Acacia disparrima	Hickory Wattle	170		170	13	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6201	Angophora leiocarpa	Smooth-barked Apple	210		210	20	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6202	Lophostemon suaveolens	Swamp Box	180		180	18	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6203	Lophostemon suaveolens	Swamp Box	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6204	Lophostemon suaveolens	Swamp Box	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6205	Corymbia tessellaris	Moreton Bay Ash	130		130	20	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6206	Lophostemon suaveolens	Swamp Box	150		150	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6207	Corymbia intermedia	Pink Bloodwood	180		180	20	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6208	Lophostemon suaveolens	Swamp Box	120		120	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6209	Lophostemon suaveolens	Swamp Box	140		140	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6210	Corymbia intermedia	Pink Bloodwood	200		200	20	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6211	Lophostemon suaveolens	Swamp Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6212	Acacia disparrima	Hickory Wattle	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6213	Lophostemon suaveolens	Swamp Box	130		130	10	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6214	Lophostemon suaveolens	Swamp Box	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6215	Angophora leiocarpa	Smooth-barked Apple	200		200	20	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6216	Lophostemon suaveolens	Swamp Box	190	150	242	18	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6217	Lophostemon suaveolens	Swamp Box	220		220	15	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6218	Lophostemon suaveolens	Swamp Box	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6219	Acacia leiocalyx	Early-flowering Black Wattle	110		110	15	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6220	Lophostemon suaveolens	Swamp Box	110		110	15	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6221	Lophostemon suaveolens	Swamp Box	140	90	166	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6222	Lophostemon suaveolens	Swamp Box	210		210	15	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6223	Lophostemon suaveolens	Swamp Box	130		130	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6224	Allocasuarina littoralis	Black She-oak	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6225	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6226	Acacia leiocalyx	Early-flowering Black Wattle	140		140	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6227	Lophostemon suaveolens	Swamp Box	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6228	Lophostemon suaveolens	Swamp Box	110		110	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6229	Lophostemon suaveolens	Swamp Box	110		110	15	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6230	Corymbia intermedia	Pink Bloodwood	140		140	18	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6231	Corymbia citriodora	Spotted Gum	140		140	15	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6232	Lophostemon suaveolens	Swamp Box	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6233	Lophostemon suaveolens	Swamp Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6234	Corymbia intermedia	Pink Bloodwood	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6235	Eucalyptus tereticornis	Forest Red Gum	160	240	288	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6236	Corymbia intermedia	Pink Bloodwood	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6237	Lophostemon suaveolens	Swamp Box	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6238	Lophostemon suaveolens	Swamp Box	160	150	219	13	4	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6239	Lophostemon suaveolens	Swamp Box	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6240	Alphitonia excelsa	Soap Tree	100		100	10	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6241	Alphitonia excelsa	Soap Tree	90	90, 40	133	13	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6242	Eucalyptus tereticornis	Forest Red Gum	320		320	22	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6243	Lophostemon suaveolens	Swamp Box	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6244	Lophostemon suaveolens	Swamp Box	130	100, 60	175	13	4	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6245	Acacia leiocalyx	Early-flowering Black Wattle	120		120	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6246	Lophostemon suaveolens	Swamp Box	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6247	Corymbia intermedia	Pink Bloodwood	210	150	258	18	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6248	Alphitonia excelsa	Soap Tree	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6249	Lophostemon suaveolens	Swamp Box	110		110	8	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6250	Corymbia intermedia	Pink Bloodwood	200		200	18	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6251	Lophostemon suaveolens	Swamp Box	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6252	Acacia disparrima	Hickory Wattle	110		110	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6253	Alphitonia excelsa	Soap Tree	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6254	Casuarina cunninghamiana	River She-oak	130		130	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6255	Corymbia intermedia	Pink Bloodwood	160		160	18	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6256	Lophostemon suaveolens	Swamp Box	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6257	Corymbia citriodora	Spotted Gum	120		120	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6258	Lophostemon suaveolens	Swamp Box	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6259	Lophostemon suaveolens	Swamp Box	150		150	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6260	Corymbia citriodora	Spotted Gum	400	40	420	28	12	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6261	Eucalyptus crebra	Narrow-leaved Ironbark	500		500	26	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6262	Corymbia citriodora	Spotted Gum	400		400	24	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6263	Corymbia intermedia	Pink Bloodwood	440		440	18	6	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6264	Petalostigma pubescens	Quinine Bush	150	160	219	9	3	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6265	Corymbia intermedia	Pink Bloodwood	360		360	17	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6266	Corymbia intermedia	Pink Bloodwood	430		430	20	7	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6267	Eucalyptus tereticornis	Forest Red Gum	480		480	21	10	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6268	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6269	Acacia disparrima	Hickory Wattle	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6270	Petalostigma pubescens	Quinine Bush	290		290	13	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6271	Petalostigma pubescens	Quinine Bush	280		280	9	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6272	Petalostigma pubescens	Quinine Bush	270		270	13	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6273	Petalostigma pubescens	Quinine Bush	260		260	10	6	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6274	Petalostigma pubescens	Quinine Bush	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6275	Petalostigma pubescens	Quinine Bush	270		270	10	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6276	Alphitonia excelsa	Soap Tree	250		250	10	2	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6277	Acacia disparrima	Hickory Wattle	270		270	12	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6278	Acacia disparrima	Hickory Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6279	Acacia disparrima	Hickory Wattle	220		220	13	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6280	Acacia disparrima	Hickory Wattle	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6281	Acacia disparrima	Hickory Wattle	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6282	Petalostigma pubescens	Quinine Bush	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6283	Corymbia intermedia	Pink Bloodwood	250		250	16	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6284	Petalostigma pubescens	Quinine Bush	330		330	15	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6285	Petalostigma pubescens	Quinine Bush	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6286	Petalostigma pubescens	Quinine Bush	360		360	13	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6287	Acacia disparrima	Hickory Wattle	230		230	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6288	Acacia disparrima	Hickory Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6289	Acacia disparrima	Hickory Wattle	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6290	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6291	Alphitonia excelsa	Soap Tree	160		160	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6292	Acacia disparrima	Hickory Wattle	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6293	Acacia disparrima	Hickory Wattle	130		130	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6294	Acacia disparrima	Hickory Wattle	140		140	13	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6295	Acacia disparrima	Hickory Wattle	130		130	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6296	Eucalyptus tereticornis	Forest Red Gum	560		560	24	10	6.7	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6297	Acacia disparrima	Hickory Wattle	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6298	Acacia disparrima	Hickory Wattle	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6299	Acacia disparrima	Hickory Wattle	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6300	Corymbia intermedia	Pink Bloodwood	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6301	Acacia disparrima	Hickory Wattle	150		150	13	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6302	Petalostigma pubescens	Quinine Bush	280		280	13	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6303	Alphitonia excelsa	Soap Tree	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6304	Acacia disparrima	Hickory Wattle	150		150	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6305	Acacia disparrima	Hickory Wattle	170	150	227	10	3	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6306	Petalostigma pubescens	Quinine Bush	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6307	Corymbia intermedia	Pink Bloodwood	350		350	20	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6308	Acacia disparrima	Hickory Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6309	Corymbia intermedia	Pink Bloodwood	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6310	Acacia concurrens	Black Wattle	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6311	Acacia disparrima	Hickory Wattle	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6312	Eucalyptus tereticornis	Forest Red Gum	290		290	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6313	Acacia disparrima	Hickory Wattle	350		350	14	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6314	Acacia concurrens	Black Wattle	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6315	Acacia disparrima	Hickory Wattle	170		170	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6316	Alphitonia excelsa	Soap Tree	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6317	Eucalyptus tereticornis	Forest Red Gum	360		360	23	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6318	Eucalyptus tereticornis	Forest Red Gum	550		550	26	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6319	Petalostigma pubescens	Quinine Bush	180		180	9	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6320	Petalostigma pubescens	Quinine Bush	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6321	Petalostigma pubescens	Quinine Bush	250		250	10	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6322	Corymbia intermedia	Pink Bloodwood	290		290	20	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6323	Eucalyptus tereticornis	Forest Red Gum	380		380	21	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6324	Acacia disparrima	Hickory Wattle	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6325	Acacia disparrima	Hickory Wattle	210		210	14	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6326	Acacia disparrima	Hickory Wattle	160	100	189	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6327	Acacia disparrima	Hickory Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6328	Corymbia intermedia	Pink Bloodwood	280		280	19	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6329	Eucalyptus tereticornis	Forest Red Gum	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6330	Acacia disparrima	Hickory Wattle	170		170	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6331	Acacia disparrima	Hickory Wattle	130	140	191	10	4	2.3	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6332	Acacia disparrima	Hickory Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6333	Alphitonia excelsa	Soap Tree	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6334	Alphitonia excelsa	Soap Tree	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6335	Acacia disparrima	Hickory Wattle	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6336	Acacia disparrima	Hickory Wattle	180		180	13	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6337	Eucalyptus tereticornis	Forest Red Gum	330		330	22	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6338	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6339	Acacia disparrima	Hickory Wattle	160		160	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6340	Eucalyptus tereticornis	Forest Red Gum	330		330	26	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6341	Petalostigma pubescens	Quinine Bush	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6342	Petalostigma pubescens	Quinine Bush	220		220	12	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6343	Corymbia intermedia	Pink Bloodwood	290		290	23	6	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6344	Petalostigma pubescens	Quinine Bush	200		200	8	3	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6345	Petalostigma pubescens	Quinine Bush	280		280	10	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6346	Petalostigma pubescens	Quinine Bush	160		160	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6347	Alphitonia excelsa	Soap Tree	330		330	15	6	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6348	Alphitonia excelsa	Soap Tree	330		330	16	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6349	Petalostigma pubescens	Quinine Bush	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6350	Eucalyptus tereticornis	Forest Red Gum	350		350	25	10	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6351	Corymbia intermedia	Pink Bloodwood	310		310	18	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6352	Petalostigma pubescens	Quinine Bush	170	160	233	10	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6353	Petalostigma pubescens	Quinine Bush	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6354	Allocasuarina littoralis	Black She-oak	260		260	11	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6355	Petalostigma pubescens	Quinine Bush	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6356	Eucalyptus tereticornis	Forest Red Gum	540		540	23	9	6.5	2.6	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retain
6357	Allocasuarina littoralis	Black She-oak	180		180	8	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6358	Allocasuarina littoralis	Black She-oak	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6359	Allocasuarina littoralis	Black She-oak	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6360	Allocasuarina littoralis	Black She-oak	190		190	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6361	Acacia concurrens	Black Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6362	Allocasuarina littoralis	Black She-oak	200		200	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6363	Banksia integrifolia	Coast Banksia	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6364	Eucalyptus tereticornis	Forest Red Gum	460		460	23	9	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6365	Banksia integrifolia	Coast Banksia	210		210	9	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6366	Petalostigma pubescens	Quinine Bush	230		230	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6367	Allocasuarina littoralis	Black She-oak	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6368	Petalostigma pubescens	Quinine Bush	190		190	9	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6369	Petalostigma pubescens	Quinine Bush	280		280	11	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6370	Petalostigma pubescens	Quinine Bush	160	130	206	9	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6371	Acacia concurrens	Black Wattle	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6372	Corymbia intermedia	Pink Bloodwood	280		280	20	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6373	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6374	Acacia disparrima	Hickory Wattle	190		190	12	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6375	Petalostigma pubescens	Quinine Bush	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6376	Petalostigma pubescens	Quinine Bush	140		140	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6377	Acacia concurrens	Black Wattle	150		150	13	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6378	Petalostigma pubescens	Quinine Bush	330		330	9	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6379	Petalostigma pubescens	Quinine Bush	280		280	11	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6380	Petalostigma pubescens	Quinine Bush	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6381	Petalostigma pubescens	Quinine Bush	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6382	Petalostigma pubescens	Quinine Bush	350		350	10	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retention TBC by CPTED
6383	Petalostigma pubescens	Quinine Bush	170		170	8	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6384	Petalostigma pubescens	Quinine Bush	210		210	10	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6385	Eucalyptus tereticornis	Forest Red Gum	410		410	23	7	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6386	Corymbia intermedia	Pink Bloodwood	480		480	20	8	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6387	Petalostigma pubescens	Quinine Bush	230		230	10	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6388	Alphitonia excelsa	Soap Tree	170		170	9	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6389	Petalostigma pubescens	Quinine Bush	200		200	11	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6390	Petalostigma pubescens	Quinine Bush	260		260	14	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6391	Acacia disparrima	Hickory Wattle	140		140	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6392	Lophostemon suaveolens	Swamp Box	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6393	Allocasuarina littoralis	Black She-oak	230		230	12	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6394	Petalostigma pubescens	Quinine Bush	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6395	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6396	Petalostigma pubescens	Quinine Bush	170	100	197	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6397	Eucalyptus tereticornis	Forest Red Gum	300		300	21	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6398	Acacia disparrima	Hickory Wattle	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6399	Corymbia intermedia	Pink Bloodwood	370		370	17	7	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6400	Alphitonia excelsa	Soap Tree	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6401	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6402	Petalostigma pubescens	Quinine Bush	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6403	Petalostigma pubescens	Quinine Bush	220		220	11	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6404	Acacia concurrens	Black Wattle	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6405	Petalostigma pubescens	Quinine Bush	180		180	6	2	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6406	Alphitonia excelsa	Soap Tree	270		270	11	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6407	Corymbia intermedia	Pink Bloodwood	500		500	22	9	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6408	Acacia concurrens	Black Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6409	Petalostigma pubescens	Quinine Bush	300		300	10	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6410	Acacia disparrima	Hickory Wattle	180		180	11	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6411	Lophostemon suaveolens	Swamp Box	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6412	Petalostigma pubescens	Quinine Bush	240		240	8	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6413	Corymbia intermedia	Pink Bloodwood	360		360	23	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6414	Eucalyptus tereticornis	Forest Red Gum	270		270	22	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6415	Acacia disparrima	Hickory Wattle	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6416	Petalostigma pubescens	Quinine Bush	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6417	Petalostigma pubescens	Quinine Bush	190		190	8	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6418	Alphitonia excelsa	Soap Tree	300		300	17	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6419	Petalostigma pubescens	Quinine Bush	300	310	431	10	8	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6420	Eucalyptus tereticornis	Forest Red Gum	390		390	23	9	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6421	DEAD/STAG		770		770	14	5	9.2	3.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Remove for trunk sewer
6422	Acacia concurrens	Black Wattle	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6423	Petalostigma pubescens	Quinine Bush	240	190	306	5	3	3.7	2.0	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6424	Acacia disparrima	Hickory Wattle	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6425	Acacia disparrima	Hickory Wattle	200		200	10	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6426	Eucalyptus tereticornis	Forest Red Gum	510		510	23	12	6.1	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6427	Lophostemon suaveolens	Swamp Box	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6428	Corymbia intermedia	Pink Bloodwood	350		350	23	6	4.2	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6429	Acacia disparrima	Hickory Wattle	150	130	198	13	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6430	Eucalyptus tereticornis	Forest Red Gum	330		330	22	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6431	Eucalyptus tereticornis	Forest Red Gum	240		240	19	5	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6432	Corymbia intermedia	Pink Bloodwood	400		400	21	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6433	Acacia concurrens	Black Wattle	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6434	Allocasuarina littoralis	Black She-oak	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6435	Banksia integrifolia	Coast Banksia	140	120	184	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6436	Allocasuarina littoralis	Black She-oak	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6437	Allocasuarina littoralis	Black She-oak	120		120	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6438	Allocasuarina littoralis	Black She-oak	140	120	184	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6439	Allocasuarina littoralis	Black She-oak	160		160	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6440	Petalostigma pubescens	Quinine Bush	200		200	9	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6441	Corymbia intermedia	Pink Bloodwood	330		330	20	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6442	Allocasuarina littoralis	Black She-oak	140		140	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6443	Allocasuarina littoralis	Black She-oak	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6444	Allocasuarina littoralis	Black She-oak	150	120	192	12	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6445	Banksia integrifolia	Coast Banksia	200		200	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6446	Acacia disparrima	Hickory Wattle	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6447	Banksia integrifolia	Coast Banksia	150		150	7	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6448	Allocasuarina littoralis	Black She-oak	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6449	Alphitonia excelsa	Soap Tree	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6450	Acacia disparrima	Hickory Wattle	270		270	12	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6451	Eucalyptus tereticornis	Forest Red Gum	460		460	25	10	5.5	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6452	Banksia integrifolia	Coast Banksia	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6453	Eucalyptus tereticornis	Forest Red Gum	130		130	13	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6454	Corymbia tessellaris	Moreton Bay Ash	140		140	15	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6455	Banksia integrifolia	Coast Banksia	170	190	255	9	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6456	Acacia disparrima	Hickory Wattle	220		220	12	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6457	Allocasuarina littoralis	Black She-oak	120		120	5	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6458	Allocasuarina littoralis	Black She-oak	150		150	14	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6459	Allocasuarina littoralis	Black She-oak	130		130	13	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6460	Corymbia intermedia	Pink Bloodwood	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6461	Allocasuarina littoralis	Black She-oak	170		170	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6462	Banksia integrifolia	Coast Banksia	140		140	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6463	Banksia integrifolia	Coast Banksia	180	130	222	10	3	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6464	Acacia concurrens	Black Wattle	130		130	10	2	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6465	Allocasuarina littoralis	Black She-oak	130		130	6	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6466	Allocasuarina littoralis	Black She-oak	140		140	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6467	Allocasuarina littoralis	Black She-oak	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6468	Allocasuarina littoralis	Black She-oak	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6469	Allocasuarina littoralis	Black She-oak	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6470	Banksia integrifolia	Coast Banksia	300		300	10	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6471	Corymbia intermedia	Pink Bloodwood	290		290	18	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6472	Allocasuarina littoralis	Black She-oak	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6473	Allocasuarina littoralis	Black She-oak	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6474	Allocasuarina littoralis	Black She-oak	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6475	Allocasuarina littoralis	Black She-oak	190		190	12	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6476	Eucalyptus tereticornis	Forest Red Gum	400		400	20	8	4.8	2.3	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6477	Corymbia intermedia	Pink Bloodwood	400		400	19	7	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6478	Corymbia intermedia	Pink Bloodwood	410		410	23	10	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6479	Acacia disparrima	Hickory Wattle	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6480	Corymbia intermedia	Pink Bloodwood	430		430	20	7	5.2	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6481	Petalostigma pubescens	Quinine Bush	250	200	320	12	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6482	Petalostigma pubescens	Quinine Bush	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6483	Petalostigma pubescens	Quinine Bush	150	160	219	10	3	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6484	Allocasuarina littoralis	Black She-oak	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6485	Corymbia intermedia	Pink Bloodwood	420		420	20	8	5.0	2.3	Regular	-	-	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6486	Acacia disparrima	Hickory Wattle	230		230	13	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6487	Banksia integrifolia	Coast Banksia	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6488	Allocasuarina littoralis	Black She-oak	160		160	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6489	Corymbia intermedia	Pink Bloodwood	320		320	21	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6490	Acacia disparrima	Hickory Wattle	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6491	Corymbia intermedia	Pink Bloodwood	350		350	22	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6492	Allocasuarina littoralis	Black She-oak	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6493	Corymbia intermedia	Pink Bloodwood	500		500	23	11	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6494	Acacia disparrima	Hickory Wattle	270		270	13	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6495	Eucalyptus tereticornis	Forest Red Gum	320		320	20	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6496	Acacia disparrima	Hickory Wattle	170		170	10	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6497	Corymbia intermedia	Pink Bloodwood	420		420	25	10	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6498	Acacia disparrima	Hickory Wattle	180		180	11	2	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6499	Acacia disparrima	Hickory Wattle	340		340	13	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6500	Acacia disparrima	Hickory Wattle	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6501	Petalostigma pubescens	Quinine Bush	240		240	14	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6502	Acacia concurrens	Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6503	Corymbia intermedia	Pink Bloodwood	170		170	16	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6504	Allocasuarina littoralis	Black She-oak	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6505	Corymbia tessellaris	Moreton Bay Ash	150		150	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6506	Corymbia intermedia	Pink Bloodwood	370		370	22	9	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6507	Corymbia intermedia	Pink Bloodwood	340		340	20	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6508	Eucalyptus tereticornis	Forest Red Gum	280		280	18	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6509	Acacia disparrima	Hickory Wattle	120		120	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6510	Acacia concurrens	Black Wattle	120		120	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6511	Lophostemon suaveolens	Swamp Box	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6512	Lophostemon suaveolens	Swamp Box	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6513	Acacia disparrima	Hickory Wattle	200	160	256	12	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6514	Corymbia intermedia	Pink Bloodwood	350		350	20	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6515	Lophostemon suaveolens	Swamp Box	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6516	Lophostemon suaveolens	Swamp Box	150		150	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6517	Acacia disparrima	Hickory Wattle	170		170	11	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6518	Lophostemon suaveolens	Swamp Box	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6519	Lophostemon suaveolens	Swamp Box	190		190	12	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6520	Lophostemon suaveolens	Swamp Box	160		160	11	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6521	Acacia concurrens	Black Wattle	130		130	11	1	2.0	1.4	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6522	Acacia concurrens	Black Wattle	150		150	12	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6523	Acacia concurrens	Black Wattle	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6524	Allocasuarina littoralis	Black She-oak	220		220	9	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6525	Allocasuarina littoralis	Black She-oak	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6526	Allocasuarina littoralis	Black She-oak	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6527	Allocasuarina littoralis	Black She-oak	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6528	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
6529	Petalostigma pubescens	Quinine Bush	260		260	9	7	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6530	Corymbia tessellaris	Moreton Bay Ash	150		150	15	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6531	Acacia concurrens	Black Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6532	Lophostemon suaveolens	Swamp Box	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6533	Acacia disparrima	Hickory Wattle	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6534	Alphitonia excelsa	Soap Tree	180		180	12	2	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6535	Acacia disparrima	Hickory Wattle	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6536	Acacia disparrima	Hickory Wattle	140		140	14	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6537	Acacia disparrima	Hickory Wattle	130		130	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6538	Corymbia intermedia	Pink Bloodwood	320		320	19	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6539	Corymbia tessellaris	Moreton Bay Ash	130		130	16	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6540	Corymbia tessellaris	Moreton Bay Ash	200		200	20	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6541	Eucalyptus tereticornis	Forest Red Gum	220		220	19	3	2.6	1.8	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6542	Acacia disparrima	Hickory Wattle	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6543	Acacia disparrima	Hickory Wattle	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6544	Alphitonia excelsa	Soap Tree	280		280	12	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6545	Eucalyptus tereticornis	Forest Red Gum	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6546	Corymbia intermedia	Pink Bloodwood	360		360	22	8	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6547	Acacia disparrima	Hickory Wattle	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6548	Corymbia intermedia	Pink Bloodwood	330		330	20	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6549	Corymbia intermedia	Pink Bloodwood	280		280	17	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6550	Eucalyptus tereticornis	Forest Red Gum	360		360	19	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6551	Corymbia intermedia	Pink Bloodwood	320		320	20	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6552	Acacia disparrima	Hickory Wattle	240	140	278	14	6	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6553	Eucalyptus tereticornis	Forest Red Gum	450		450	23	9	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6554	Corymbia intermedia	Pink Bloodwood	380		380	18	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6555	Acacia disparrima	Hickory Wattle	190		190	13	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6556	Acacia disparrima	Hickory Wattle	200		200	13	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6557	Petalostigma pubescens	Quinine Bush	190		190	9	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6558	Petalostigma pubescens	Quinine Bush	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6559	Eucalyptus tereticornis	Forest Red Gum	630		630	26	12	7.6	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6560	Acacia disparrima	Hickory Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6561	Acacia disparrima	Hickory Wattle	130		130	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6562	Corymbia tessellaris	Moreton Bay Ash	140		140	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6563	Alphitonia excelsa	Soap Tree	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6564	Acacia disparrima	Hickory Wattle	230		230	15	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6565	Banksia integrifolia	Coast Banksia	130		130	6	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6566	Acacia disparrima	Hickory Wattle	150		150	12	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6567	Acacia disparrima	Hickory Wattle	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6568	Petalostigma pubescens	Quinine Bush	470		470	12	8	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6569	Petalostigma pubescens	Quinine Bush	270		270	10	6	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6570	Alphitonia excelsa	Soap Tree	150		150	9	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6571	Acacia disparrima	Hickory Wattle	190		190	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6572	Corymbia intermedia	Pink Bloodwood	120	100, 90	180	12	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6573	Acacia disparrima	Hickory Wattle	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6574	Corymbia intermedia	Pink Bloodwood	280		280	18	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6575	Acacia concurrens	Black Wattle	140		140	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6576	Acacia concurrens	Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6577	Corymbia intermedia	Pink Bloodwood	400		400	23	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6578	Petalostigma pubescens	Quinine Bush	270		270	8	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6579	Corymbia intermedia	Pink Bloodwood	400		400	19	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6580	Acacia disparrima	Hickory Wattle	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6581	Corymbia intermedia	Pink Bloodwood	260		260	17	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6582	Alphitonia excelsa	Soap Tree	260		260	16	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6583	Eucalyptus tereticornis	Forest Red Gum	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6584	Petalostigma pubescens	Quinine Bush	210		210	9	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6585	Corymbia intermedia	Pink Bloodwood	200		200	14	2	2.4	1.7	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6586	Corymbia intermedia	Pink Bloodwood	190		190	14	2	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6587	Acacia disparrima	Hickory Wattle	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6588	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6589	Acacia disparrima	Hickory Wattle	130	140	191	13	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6590	Corymbia intermedia	Pink Bloodwood	530		530	25	12	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6591	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6592	Eucalyptus tereticornis	Forest Red Gum	380		380	20	6	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6593	Corymbia intermedia	Pink Bloodwood	660		660	25	14	7.9	2.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6594	Acacia disparrima	Hickory Wattle	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6595	Corymbia intermedia	Pink Bloodwood	220		220	16	3	2.6	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6596	Corymbia intermedia	Pink Bloodwood	380		380	19	9	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6597	Eucalyptus tereticornis	Forest Red Gum	380		380	19	8	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6598	Corymbia intermedia	Pink Bloodwood	270		270	20	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6599	Eucalyptus tereticornis	Forest Red Gum	370		370	18	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6600	Corymbia intermedia	Pink Bloodwood	490		490	23	11	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6601	Petalostigma pubescens	Quinine Bush	280		280	10	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6602	Corymbia intermedia	Pink Bloodwood	260		260	17	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6603	Corymbia intermedia	Pink Bloodwood	370		370	20	7	4.4	2.2	Regular	-	Thinning	-	Epicormic	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6604	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6605	Corymbia intermedia	Pink Bloodwood	280		280	17	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6606	Corymbia tessellaris	Moreton Bay Ash	160	150, 120	250	14	2	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6607	Corymbia intermedia	Pink Bloodwood	400		400	20	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6608	Alphitonia excelsa	Soap Tree	270		270	16	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6609	Petalostigma pubescens	Quinine Bush	190		190	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6610	Petalostigma pubescens	Quinine Bush	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6611	Acacia disparrima	Hickory Wattle	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6612	Petalostigma pubescens	Quinine Bush	280		280	9	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6613	Petalostigma pubescens	Quinine Bush	120		120	11	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6614	Petalostigma pubescens	Quinine Bush	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6615	Petalostigma pubescens	Quinine Bush	160	180	241	6	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6616	Acacia disparrima	Hickory Wattle	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6617	Petalostigma pubescens	Quinine Bush	150		150	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6618	Acacia disparrima	Hickory Wattle	180		180	14	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6619	Corymbia intermedia	Pink Bloodwood	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6620	Corymbia intermedia	Pink Bloodwood	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6621	Corymbia intermedia	Pink Bloodwood	170		170	16	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6622	Corymbia intermedia	Pink Bloodwood	210		210	15	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6623	Acacia concurrens	Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6624	Allocasuarina littoralis	Black She-oak	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6625	Banksia integrifolia	Coast Banksia	170		170	9	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6626	Acacia disparrima	Hickory Wattle	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6627	Acacia concurrens	Black Wattle	120	130	177	11	3	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6628	Acacia disparrima	Hickory Wattle	150		150	15	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6629	Acacia disparrima	Hickory Wattle	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6630	Acacia disparrima	Hickory Wattle	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6631	Petalostigma pubescens	Quinine Bush	190		190	9	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6632	Acacia disparrima	Hickory Wattle	120		120	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6633	Acacia concurrens	Black Wattle	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6634	Corymbia intermedia	Pink Bloodwood	410		410	19	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6635	Petalostigma pubescens	Quinine Bush	340		340	12	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6636	Acacia disparrima	Hickory Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6637	Alphitonia excelsa	Soap Tree	310		310	16	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6638	Corymbia intermedia	Pink Bloodwood	290		290	18	8	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6639	Alphitonia excelsa	Soap Tree	190		190	6	5	2.3	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6640	Allocasuarina littoralis	Black She-oak	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6641	Eucalyptus tereticornis	Forest Red Gum	450		450	25	13	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6642	Eucalyptus tereticornis	Forest Red Gum	380		380	23	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6643	Eucalyptus tereticornis	Forest Red Gum	250		250	13	7	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6644	Corymbia intermedia	Pink Bloodwood	380		380	18	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6645	Acacia concurrens	Black Wattle	170		170	6	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6646	Acacia concurrens	Black Wattle	160		160	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6647	Acacia disparrima	Hickory Wattle	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6648	Alphitonia excelsa	Soap Tree	320		320	10	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6649	Angophora leiocarpa	Smooth-barked Apple	310		310	23	12	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
6650	Corymbia intermedia	Pink Bloodwood	360		360	25	14	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6651	Petalostigma pubescens	Quinine Bush	210	160	264	9	7	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6652	Acacia disparrima	Hickory Wattle	130		130	7	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6653	Eucalyptus tereticornis	Forest Red Gum	180		180	14	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6654	Corymbia intermedia	Pink Bloodwood	280		280	16	9	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6655	Corymbia intermedia	Pink Bloodwood	150		150	13	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6656	Acacia disparrima	Hickory Wattle	200		200	8	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6657	Petalostigma pubescens	Quinine Bush	220		220	5	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6658	Acacia disparrima	Hickory Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6659	Petalostigma pubescens	Quinine Bush	230		230	6	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6660	Acacia disparrima	Hickory Wattle	200		200	10	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6661	Petalostigma pubescens	Quinine Bush	150	150	212	7	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6662	Acacia disparrima	Hickory Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6663	Alphitonia excelsa	Soap Tree	140		140	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6664	Acacia disparrima	Hickory Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6665	Petalostigma pubescens	Quinine Bush	260		260	9	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6666	Eucalyptus seeana	Narrow-leaved Red Gum	390		390	23	12	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6667	Petalostigma pubescens	Quinine Bush	140	130	191	7	6	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6668	Petalostigma pubescens	Quinine Bush	180		180	7	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6669	Acacia concurrens	Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6670	Petalostigma pubescens	Quinine Bush	260		260	6	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6671	Alphitonia excelsa	Soap Tree	200		200	13	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6672	Alphitonia excelsa	Soap Tree	200		200	11	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6673	Petalostigma pubescens	Quinine Bush	170		170	8	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6674	Corymbia tessellaris	Moreton Bay Ash	240		240	23	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6675	Alphitonia excelsa	Soap Tree	220	140	261	12	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6676	Acacia disparrima	Hickory Wattle	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6677	Alphitonia excelsa	Soap Tree	400		400	13	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6678	Alphitonia excelsa	Soap Tree	160		160	10	6	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6679	Alphitonia excelsa	Soap Tree	200		200	11	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6680	Alphitonia excelsa	Soap Tree	160		160	14	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6681	Eucalyptus tereticornis	Forest Red Gum	290		290	20	10	3.5	2.0	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Retain
6682	Alphitonia excelsa	Soap Tree	230		230	14	8	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6683	Petalostigma pubescens	Quinine Bush	140		140	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6684	Alphitonia excelsa	Soap Tree	110		110	7	2	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6685	Acacia disparrima	Hickory Wattle	160		160	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6686	Eucalyptus grandis	Flooded Gum	230		230	14	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6687	Alphitonia excelsa	Soap Tree	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6688	Alphitonia excelsa	Soap Tree	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6689	Eucalyptus grandis	Flooded Gum	220		220	14	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6690	Petalostigma pubescens	Quinine Bush	110		110	8	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6691	Eucalyptus grandis	Flooded Gum	380		380	25	13	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
6692	Acacia concurrens	Black Wattle	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6693	Eucalyptus grandis	Flooded Gum	300		300	22	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
6694	Eucalyptus grandis	Flooded Gum	250		250	7	2	3.0	1.8	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6695	Alphitonia excelsa	Soap Tree	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6696	Eucalyptus grandis	Flooded Gum	240		240	22	10	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6697	Alphitonia excelsa	Soap Tree	120		120	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6698	Eucalyptus grandis	Flooded Gum	280		280	23	12	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6699	Alphitonia excelsa	Soap Tree	120	80	144	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6700	Eucalyptus grandis	Flooded Gum	230		230	12	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6701	Eucalyptus grandis	Flooded Gum	210		210	22	9	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6702	Acacia disparrima	Hickory Wattle	120	70	139	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6703	Eucalyptus grandis	Flooded Gum	220		220	14	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6704	Alphitonia excelsa	Soap Tree	130		130	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6705	Eucalyptus grandis	Flooded Gum	240		240	16	9	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6706	Eucalyptus grandis	Flooded Gum	220		220	18	10	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6707	Eucalyptus grandis	Flooded Gum	330		330	22	10	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6708	Alphitonia excelsa	Soap Tree	120		120	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6709	Eucalyptus grandis	Flooded Gum	220		220	18	9	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6710	Eucalyptus grandis	Flooded Gum	330		330	22	12	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6711	Eucalyptus grandis	Flooded Gum	200		200	20	10	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6712	Alphitonia excelsa	Soap Tree	140		140	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6713	Eucalyptus grandis	Flooded Gum	220		220	16	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6714	Alphitonia excelsa	Soap Tree	140		140	9	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6715	Eucalyptus grandis	Flooded Gum	370		370	22	13	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6716	Eucalyptus grandis	Flooded Gum	240		240	20	8	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6717	Eucalyptus grandis	Flooded Gum	260		260	22	10	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6718	Eucalyptus grandis	Flooded Gum	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6719	Eucalyptus grandis	Flooded Gum	200		200	13	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6720	Eucalyptus grandis	Flooded Gum	270		270	20	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6721	Eucalyptus grandis	Flooded Gum	260		260	20	9	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6722	Acacia disparrima	Hickory Wattle	100		100	9	4	2.0	0.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6723	Acacia concurrens	Black Wattle	140		140	10	5	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6724	Eucalyptus grandis	Flooded Gum	150		150	9	4	2.0	1.5	Regular	-	-	-	Epicormic	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6725	Alphitonia excelsa	Soap Tree	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6726	Eucalyptus grandis	Flooded Gum	310		310	22	10	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6727	Eucalyptus grandis	Flooded Gum	350		350	22	9	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6728	Acacia disparrima	Hickory Wattle	160		160	10	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6729	Alphitonia excelsa	Soap Tree	110		110	9	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6730	Eucalyptus grandis	Flooded Gum	240		240	16	7	2.9	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6731	Eucalyptus grandis	Flooded Gum	140		140	16	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6732	Acacia concurrens	Black Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6733	Petalostigma pubescens	Quinine Bush	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6734	Alphitonia excelsa	Soap Tree	130		130	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6735	Petalostigma pubescens	Quinine Bush	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6736	Alphitonia excelsa	Soap Tree	140		140	10	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6737	Eucalyptus grandis	Flooded Gum	360		360	22	12	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6738	Corymbia intermedia	Pink Bloodwood	200		200	15	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6739	Corymbia intermedia	Pink Bloodwood	380		380	22	12	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6740	Petalostigma pubescens	Quinine Bush	200		200	8	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6741	Corymbia tessellaris	Moreton Bay Ash	300		300	22	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6742	Alphitonia excelsa	Soap Tree	110		110	9	6	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6743	Corymbia intermedia	Pink Bloodwood	390		390	22	12	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6744	Grevillea robusta	Silky Oak	170		170	8	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6745	Petalostigma pubescens	Quinine Bush	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6746	Lophostemon suaveolens	Swamp Box	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6747	Lophostemon suaveolens	Swamp Box	360	200	412	18	10	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6748	Grevillea robusta	Silky Oak	320		320	16	7	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6749	Alphitonia excelsa	Soap Tree	150		150	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6750	Alphitonia excelsa	Soap Tree	100		100	7	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6751	Alphitonia excelsa	Soap Tree	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6752	Melaleuca viminalis	Weeping Bottlebrush	200		200	9	7	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
6753	Alphitonia excelsa	Soap Tree	100		100	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6754	Lophostemon suaveolens	Swamp Box	270	240	361	16	10	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6755	Alphitonia excelsa	Soap Tree	130		130	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6756	Alphitonia excelsa	Soap Tree	120		120	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
6757	Corymbia intermedia	Pink Bloodwood	270		270	22	12	3.2	1.9	Regular	-	-	-	-	-	Typical	-	Native	-	-	Typical	-	-	-	-	-	-		Retain
6758	Lophostemon suaveolens	Swamp Box	210		210	12	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6759	Eucalyptus tereticornis	Forest Red Gum	330		330	16	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6760	Corymbia tessellaris	Moreton Bay Ash	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6761	Alphitonia excelsa	Soap Tree	110		110	7	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6762	Corymbia intermedia	Pink Bloodwood	250		250	22	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6763	Corymbia intermedia	Pink Bloodwood	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6764	Acacia concurrens	Black Wattle	150		150	9	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6765	Alphitonia excelsa	Soap Tree	120		120	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6766	Corymbia tessellaris	Moreton Bay Ash	270		270	20	10	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6767	Corymbia tessellaris	Moreton Bay Ash	210		210	18	9	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6768	Acacia disparrima	Hickory Wattle	200		200	11	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6769	Petalostigma pubescens	Quinine Bush	180		180	7	6	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6770	Petalostigma pubescens	Quinine Bush	120		120	5	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6771	Alphitonia excelsa	Soap Tree	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6772	Angophora subvelutina	Broad-leaved Apple	320		320	20	11	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6773	Acacia disparrima	Hickory Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6774	Acacia disparrima	Hickory Wattle	180		180	9	5	2.2	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6775	Banksia integrifolia	Coast Banksia	210		210	12	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6776	Alphitonia excelsa	Soap Tree	120		120	5	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6777	Corymbia intermedia	Pink Bloodwood	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6778	Corymbia intermedia	Pink Bloodwood	200		200	15	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6779	Corymbia intermedia	Pink Bloodwood	130		130	14	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6780	Acacia disparrima	Hickory Wattle	110		110	8	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6781	Corymbia intermedia	Pink Bloodwood	400		400	22	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6782	Eucalyptus tereticornis	Forest Red Gum	120		120	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6783	Corymbia tessellaris	Moreton Bay Ash	200		200	16	9	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6784	Corymbia tessellaris	Moreton Bay Ash	170		170	16	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6785	Corymbia tessellaris	Moreton Bay Ash	150		150	14	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6786	Acacia disparrima	Hickory Wattle	120		120	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6787	Corymbia tessellaris	Moreton Bay Ash	120		120	10	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6788	Eucalyptus tereticornis	Forest Red Gum	430		430	25	15	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6789	Eucalyptus tereticornis	Forest Red Gum	580		580	25	14	7.0	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6790	Alphitonia excelsa	Soap Tree	150		150	10	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6791	Acacia disparrima	Hickory Wattle	140		140	10	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6792	Corymbia tessellaris	Moreton Bay Ash	300		300	20	10	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6793	Alphitonia excelsa	Soap Tree	140		140	9	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6794	Corymbia intermedia	Pink Bloodwood	280		280	18	10	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6795	Alphitonia excelsa	Soap Tree	150		150	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6796	Alphitonia excelsa	Soap Tree	170		170	11	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6797	Eucalyptus tereticornis	Forest Red Gum	360		360	22	12	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
6798	Alphitonia excelsa	Soap Tree	180		180	12	7	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6799	DEAD/STAG		440		440	16	8	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
6800	Corymbia intermedia	Pink Bloodwood	220	200, 200	358	18	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6801	Alphitonia excelsa	Soap Tree	170		170	9	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6802	Casuarina cunninghamiana	River She-oak	220		220	16	7	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6803	Melaleuca viminalis	Weeping Bottlebrush	260	140, 140	327	9	6	3.9	2.1	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
6804	Melaleuca viminalis	Weeping Bottlebrush	270		270	9	6	3.2	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6805	Melaleuca viminalis	Weeping Bottlebrush	200		200	9	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6806	Alchornea ilicifolia	native holly	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6807	Melaleuca viminalis	Weeping Bottlebrush	240	110	264	10	7	3.2	1.9	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
6808	Alphitonia excelsa	Soap Tree	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6809	Lophostemon suaveolens	Swamp Box	250		250	12	8	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6810	Eucalyptus tereticornis	Forest Red Gum	280		280	14	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6811	Alphitonia excelsa	Soap Tree	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6812	Corymbia intermedia	Pink Bloodwood	140		140	13	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6813	Acacia disparrima	Hickory Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6814	Acacia concurrens	Black Wattle	120		120	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6815	Alphitonia excelsa	Soap Tree	150		150	8	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6816	Grevillea robusta	Silky Oak	110		110	9	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6817	Alphitonia excelsa	Soap Tree	100		100	7	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6818	Acacia disparrima	Hickory Wattle	120		120	9	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6819	Alphitonia excelsa	Soap Tree	160		160	11	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6820	Alphitonia excelsa	Soap Tree	110		110	6	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6821	Eucalyptus grandis	Flooded Gum	450		450	22	12	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6822	Acacia concurrens	Black Wattle	170		170	13	5	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6823	Alphitonia excelsa	Soap Tree	160		160	15	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6824	DEAD/STAG		450		450	16	5	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
6825	Lophostemon suaveolens	Swamp Box	120		120	12	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6826	Eucalyptus grandis	Flooded Gum	300		300	20	8	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6827	Alphitonia excelsa	Soap Tree	130		130	7	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6828	Eucalyptus grandis	Flooded Gum	400		400	14	4	4.8	2.3	Regular	-	-	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6829	Eucalyptus grandis	Flooded Gum	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6830	Eucalyptus grandis	Flooded Gum	340		340	24	13	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6831	Eucalyptus grandis	Flooded Gum	120		120	16	7	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6832	Alphitonia excelsa	Soap Tree	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6833	Eucalyptus tereticornis	Forest Red Gum	300		300	20	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6834	Alphitonia excelsa	Soap Tree	380		380	16	10	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6835	Corymbia intermedia	Pink Bloodwood	200		200	16	8	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6836	Eucalyptus tereticornis	Forest Red Gum	350		350	25	15	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6837	Acacia disparrima	Hickory Wattle	140		140	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6838	Eucalyptus tereticornis	Forest Red Gum	290		290	20	9	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6839	Eucalyptus tereticornis	Forest Red Gum	380		380	25	14	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6840	Corymbia intermedia	Pink Bloodwood	540		540	24	14	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6841	Corymbia intermedia	Pink Bloodwood	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6842	Corymbia intermedia	Pink Bloodwood	300		300	14	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6843	Corymbia intermedia	Pink Bloodwood	230		230	20	11	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6844	Corymbia intermedia	Pink Bloodwood	300		300	24	14	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6845	Corymbia intermedia	Pink Bloodwood	230		230	18	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6846	Corymbia intermedia	Pink Bloodwood	450		450	24	14	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6847	Corymbia intermedia	Pink Bloodwood	300		300	16	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6848	Corymbia intermedia	Pink Bloodwood	230		230	18	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6849	Corymbia intermedia	Pink Bloodwood	240		240	14	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6850	Corymbia intermedia	Pink Bloodwood	400		400	24	11	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6851	Corymbia intermedia	Pink Bloodwood	210		210	14	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6852	Petalostigma pubescens	Quinine Bush	200		200	8	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6853	Corymbia intermedia	Pink Bloodwood	280		280	14	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6854	Eucalyptus tereticornis	Forest Red Gum	250		250	24	12	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6855	Acacia disparrima	Hickory Wattle	120		120	11	6	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6856	Acacia concurrens	Black Wattle	120		120	6	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6857	Petalostigma pubescens	Quinine Bush	200		200	11	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6858	Eucalyptus tereticornis	Forest Red Gum	400		400	25	12	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6859	Acacia disparrima	Hickory Wattle	140		140	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6860	Banksia integrifolia	Coast Banksia	110		110	4	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6861	Petalostigma pubescens	Quinine Bush	170		170	6	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6862	Acacia concurrens	Black Wattle	140		140	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6863	Petalostigma pubescens	Quinine Bush	200	140	244	7	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6864	Petalostigma pubescens	Quinine Bush	140		140	10	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6865	Petalostigma pubescens	Quinine Bush	160		160	6	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6866	Petalostigma pubescens	Quinine Bush	110		110	4	4	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6867	Petalostigma pubescens	Quinine Bush	110		110	6	5	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6868	Petalostigma pubescens	Quinine Bush	170		170	10	7	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6869	Petalostigma pubescens	Quinine Bush	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6870	Petalostigma pubescens	Quinine Bush	160		160	9	5	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6871	Petalostigma pubescens	Quinine Bush	180		180	8	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6872	Acacia disparrima	Hickory Wattle	160		160	9	7	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6873	Acacia disparrima	Hickory Wattle	150		150	7	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6874	Petalostigma pubescens	Quinine Bush	250		250	10	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
6875	Acacia disparrima	Hickory Wattle	120	110	163	7	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6876	Acacia concurrens	Black Wattle	120		120	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6877	Acacia concurrens	Black Wattle	140		140	7	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6878	Petalostigma pubescens	Quinine Bush	170		170	6	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6879	Acacia concurrens	Black Wattle	110		110	5	3	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6880	Casuarina cunninghamiana	River She-oak	220		220	13	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6881	Casuarina cunninghamiana	River She-oak	220		220	14	6	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6882	Alphitonia excelsa	Soap Tree	140		140	6	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6883	Corymbia intermedia	Pink Bloodwood	200		200	14	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6884	Corymbia intermedia	Pink Bloodwood	420		420	22	14	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
6885	Eucalyptus crebra	Narrow-leaved Ironbark	500		500	23	10	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6886	Acacia leiocalyx	Early-flowering Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6887	Eucalyptus tereticornis	Forest Red Gum	360		360	23	8	4.3	2.2	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6888	Corymbia citriodora	Spotted Gum	160		160	18	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6889	Corymbia citriodora	Spotted Gum	500		500	25	16	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6890	Eucalyptus tereticornis	Forest Red Gum	260		260	17	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6891	Acacia leiocalyx	Early-flowering Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6892	Petalostigma pubescens	Quinine Bush	210		210	8	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6893	Corymbia citriodora	Spotted Gum	360		360	25	9	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6894	Eucalyptus tereticornis	Forest Red Gum	500		500	27	14	6.0	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6895	Eucalyptus siderophloia	Northern Grey Ironbark	620		620	18	5	7.4	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Large	-	-	-		Remove
6896	Alphitonia excelsa	Soap Tree	280		280	10	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Remove
6897	Alphitonia excelsa	Soap Tree	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6898	Eucalyptus tereticornis	Forest Red Gum	280		280	20	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6899	Eucalyptus tereticornis	Forest Red Gum	200		200	16	3	2.4	1.7	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6900	Eucalyptus tereticornis	Forest Red Gum	260		260	18	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6901	Acacia disparrima	Hickory Wattle	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6902	Alphitonia excelsa	Soap Tree	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6903	Melaleuca viminalis	Weeping Bottlebrush	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6904	Melaleuca viminalis	Weeping Bottlebrush	200		200	7	3	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6905	Eucalyptus tereticornis	Forest Red Gum	240		240	19	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6906	Corymbia intermedia	Pink Bloodwood	260		260	17	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6907	Alphitonia excelsa	Soap Tree	190		190	8	3	2.3	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6908	Melaleuca viminalis	Weeping Bottlebrush	180	160	241	5	3	2.9	1.8	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6909	Melaleuca viminalis	Weeping Bottlebrush	230		230	9	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6910	Melaleuca viminalis	Weeping Bottlebrush	140	130	191	8	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6911	Melaleuca viminalis	Weeping Bottlebrush	130	130	184	8	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6912	Melaleuca viminalis	Weeping Bottlebrush	200	180	269	9	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6913	Lophostemon suaveolens	Swamp Box	390		390	15	5	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6914	Alphitonia excelsa	Soap Tree	370		370	16	5	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6915	Acacia disparrima	Hickory Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6916	Corymbia intermedia	Pink Bloodwood	320		320	20	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6917	Acacia concurrens	Black Wattle	170		170	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6918	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6919	Acacia disparrima	Hickory Wattle	150	100, 90	201	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6920	Acacia concurrens	Black Wattle	130		130	12	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6921	Corymbia intermedia	Pink Bloodwood	210		210	16	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6922	Lophostemon suaveolens	Swamp Box	170		170	13	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6923	Corymbia intermedia	Pink Bloodwood	350		350	18	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6924	Acacia disparrima	Hickory Wattle	270		270	11	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6925	Acacia disparrima	Hickory Wattle	200		200	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6926	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	18	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6927	Corymbia intermedia	Pink Bloodwood	300		300	19	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6928	Acacia disparrima	Hickory Wattle	200		200	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6929	Corymbia intermedia	Pink Bloodwood	320		320	18	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6930	Lophostemon suaveolens	Swamp Box	260		260	16	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6931	Corymbia intermedia	Pink Bloodwood	160		160	16	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6932	Lophostemon suaveolens	Swamp Box	400		400	17	6	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6933	Eucalyptus tereticornis	Forest Red Gum	310		310	18	5	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6934	Corymbia intermedia	Pink Bloodwood	130		130	11	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6935	Lophostemon suaveolens	Swamp Box	160		160	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6936	Lophostemon suaveolens	Swamp Box	120		120	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6937	Corymbia intermedia	Pink Bloodwood	360		360	17	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6938	Lophostemon suaveolens	Swamp Box	270		270	14	3	3.2	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6939	Lophostemon suaveolens	Swamp Box	260		260	14	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6940	Lophostemon suaveolens	Swamp Box	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6941	Lophostemon suaveolens	Swamp Box	250		250	16	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6942	Lophostemon suaveolens	Swamp Box	270		270	14	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6943	Eucalyptus tereticornis	Forest Red Gum	400		400	23	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6944	Alphitonia excelsa	Soap Tree	260		260	14	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6945	Alphitonia excelsa	Soap Tree	320	220	388	16	7	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6946	Angophora leiocarpa	Smooth-barked Apple	270		270	17	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6947	Lophostemon suaveolens	Swamp Box	250		250	15	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6948	Eucalyptus tereticornis	Forest Red Gum	200		200	17	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6949	Eucalyptus tereticornis	Forest Red Gum	240		240	17	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6950	Lophostemon suaveolens	Swamp Box	330		330	14	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6951	Acacia disparrima	Hickory Wattle	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6952	Eucalyptus tereticornis	Forest Red Gum	350		350	18	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6953	Acacia disparrima	Hickory Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6954	Acacia disparrima	Hickory Wattle	180	160	241	12	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6955	Eucalyptus tereticornis	Forest Red Gum	300		300	17	4	3.6	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6956	Eucalyptus tereticornis	Forest Red Gum	550		550	25	10	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6957	Eucalyptus tereticornis	Forest Red Gum	480		480	27	12	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6958	Lophostemon suaveolens	Swamp Box	280		280	14	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6959	Eucalyptus tereticornis	Forest Red Gum	450		450	23	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6960	Eucalyptus tereticornis	Forest Red Gum	290		290	20	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6961	Acacia disparrima	Hickory Wattle	190		190	15	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6962	Acacia disparrima	Hickory Wattle	160		160	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6963	Corymbia intermedia	Pink Bloodwood	300		300	16	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6964	Acacia disparrima	Hickory Wattle	50		50	6	3	2.0	0.9	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6965	Corymbia intermedia	Pink Bloodwood	250		250	16	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6966	Lophostemon suaveolens	Swamp Box	150		150	14	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6967	Corymbia tessellaris	Moreton Bay Ash	350		350	18	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6968	Eucalyptus tereticornis	Forest Red Gum	200		200	16	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6969	Eucalyptus tereticornis	Forest Red Gum	520		520	20	8	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6970	Petalostigma pubescens	Quinine Bush	240		240	9	4	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6971	Petalostigma pubescens	Quinine Bush	180	160	241	8	7	2.9	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
6972	Petalostigma pubescens	Quinine Bush	170	190, 120	282	9	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6973	Petalostigma pubescens	Quinine Bush	230		230	8	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6974	Angophora subvelutina	Broad-leaved Apple	290		290	16	5	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6975	Petalostigma pubescens	Quinine Bush	260		260	9	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6976	Petalostigma pubescens	Quinine Bush	330		330	10	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6977	Acacia leiocalyx	Early-flowering Black Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6978	Corymbia intermedia	Pink Bloodwood	350		350	17	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6979	Acacia disparrima	Hickory Wattle	170		170	11	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6980	Acacia disparrima	Hickory Wattle	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6981	Lophostemon suaveolens	Swamp Box	440		440	16	7	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6982	Acacia disparrima	Hickory Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6983	Eucalyptus tereticornis	Forest Red Gum	310		310	17	3	3.7	2.0	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6984	Acacia leiocalyx	Early-flowering Black Wattle	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6985	Petalostigma pubescens	Quinine Bush	360		360	10	4	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6986	Petalostigma pubescens	Quinine Bush	260		260	8	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6987	Petalostigma pubescens	Quinine Bush	320		320	9	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6988	Petalostigma pubescens	Quinine Bush	240	250	347	10	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6989	Petalostigma pubescens	Quinine Bush	300		300	10	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6990	Petalostigma pubescens	Quinine Bush	180		180	8	3	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
6991	Petalostigma pubescens	Quinine Bush	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6992	Petalostigma pubescens	Quinine Bush	160		160	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6993	Petalostigma pubescens	Quinine Bush	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6994	Corymbia intermedia	Pink Bloodwood	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6995	Petalostigma pubescens	Quinine Bush	350		350	11	5	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6996	Corymbia intermedia	Pink Bloodwood	270		270	18	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6997	Petalostigma pubescens	Quinine Bush	360		360	9	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
6998	Acacia leiocalyx	Early-flowering Black Wattle	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
6999	Allocasuarina littoralis	Black She-oak	300		300	14	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7000	Acacia leiocalyx	Early-flowering Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7001	Lophostemon suaveolens	Swamp Box	250		250	12	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	Termite nest	-		Remove
7002	Eucalyptus tereticornis	Forest Red Gum	600		600	27	12	7.2	2.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7003	Lophostemon suaveolens	Swamp Box	260		260	14	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7004	Angophora subvelutina	Broad-leaved Apple	360		360	17	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7005	Corymbia intermedia	Pink Bloodwood	420		420	22	9	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7006	Lophostemon suaveolens	Swamp Box	350		350	17	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7007	Acacia leiocalyx	Early-flowering Black Wattle	180		180	14	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7008	Allocasuarina littoralis	Black She-oak	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7009	Petalostigma pubescens	Quinine Bush	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7010	Petalostigma pubescens	Quinine Bush	190		190	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7011	Petalostigma pubescens	Quinine Bush	350	320	474	11	5	5.7	2.4	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Retain
7012	Corymbia intermedia	Pink Bloodwood	370		370	17	6	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7013	Petalostigma pubescens	Quinine Bush	270		270	9	4	3.2	1.9	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
7014	Petalostigma pubescens	Quinine Bush	230		230	8	4	2.8	1.8	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
7015	Petalostigma pubescens	Quinine Bush	240	170	294	8	3	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7016	Corymbia intermedia	Pink Bloodwood	360		360	16	6	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7017	Corymbia intermedia	Pink Bloodwood	200		200	15	3	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7018	Alphitonia excelsa	Soap Tree	230		230	14	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7019	Grevillea robusta	Silky Oak	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7020	Casuarina cunninghamiana	River She-oak	230		230	14	3	2.8	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7021	Corymbia intermedia	Pink Bloodwood	330		330	18	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7022	Melaleuca viminalis	Weeping Bottlebrush	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7023	Glochidion ferdinandi	Cheese Tree	180		180	7	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7024	Melaleuca cajuputi	Cajuputi	200	190	276	6	3	3.3	1.9	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7025	Melaleuca viminalis	Weeping Bottlebrush	130	150, 140, 150	285	5	4	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7026	Lophostemon suaveolens	Swamp Box	410		410	16	6	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7027	Grevillea robusta	Silky Oak	280		280	16	3	3.4	1.9	Regular	-	-	-	-	Lopped	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7028	Alphitonia excelsa	Soap Tree	230		230	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7029	Alphitonia excelsa	Soap Tree	160		160	11	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7030	Allocasuarina littoralis	Black She-oak	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7031	Alphitonia excelsa	Soap Tree	270		270	17	4	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7032	Alphitonia excelsa	Soap Tree	160		160	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7033	Corymbia intermedia	Pink Bloodwood	360		360	18	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7034	Petalostigma pubescens	Quinine Bush	170	70	184	9	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Remove
7035	Petalostigma pubescens	Quinine Bush	250	140	287	10	3	3.4	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7036	Petalostigma pubescens	Quinine Bush	240		240	10	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7037	Petalostigma pubescens	Quinine Bush	180	190	262	9	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7038	Alphitonia excelsa	Soap Tree	320		320	11	4	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Poor	-	-	-	-	-	-		Remove
7039	Petalostigma pubescens	Quinine Bush	180		180	8	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7040	Eucalyptus crebra	Narrow-leaved Ironbark	270		270	20	6	3.2	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7041	Petalostigma pubescens	Quinine Bush	180		180	9	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7042	Eucalyptus tereticornis	Forest Red Gum	340		340	16	2	4.1	2.1	Regular	-	Thinning	Die-back	Epicormic	Lopped	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7043	Corymbia tessellaris	Moreton Bay Ash	180		180	16	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7044	Corymbia intermedia	Pink Bloodwood	260		260	16	4	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7045	Corymbia intermedia	Pink Bloodwood	140		140	12	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7046	Eucalyptus tereticornis	Forest Red Gum	200		200	16	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7047	Corymbia citriodora	Spotted Gum	440		440	25	10	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7048	Petalostigma pubescens	Quinine Bush	210		210	9	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7049	Eucalyptus tereticornis	Forest Red Gum	240		240	17	5	2.9	1.8	Regular	-	Thinning	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7050	Alphitonia excelsa	Soap Tree	260		260	10	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7051	Corymbia citriodora	Spotted Gum	300		300	21	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7052	Petalostigma pubescens	Quinine Bush	200		200	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7053	Acacia disparrima	Hickory Wattle	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7054	Alphitonia excelsa	Soap Tree	240		240	11	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7055	Corymbia intermedia	Pink Bloodwood	340		340	18	7	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7056	Corymbia citriodora	Spotted Gum	220		220	19	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7057	Acacia leiocalyx	Early-flowering Black Wattle	160	170	233	9	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7058	Corymbia citriodora	Spotted Gum	140		140	17	1	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7059	Corymbia citriodora	Spotted Gum	270		270	17	5	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7060	Acacia disparrima	Hickory Wattle	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7061	Alphitonia excelsa	Soap Tree	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7062	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7063	Acacia disparrima	Hickory Wattle	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7064	Acacia disparrima	Hickory Wattle	190		190	12	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7065	Corymbia intermedia	Pink Bloodwood	360		360	19	7	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7066	Acacia disparrima	Hickory Wattle	240		240	15	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7067	Acacia disparrima	Hickory Wattle	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7068	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7069	Eucalyptus crebra	Narrow-leaved Ironbark	710		710	21	10	8.5	2.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7070	Alphitonia excelsa	Soap Tree	260		260	10	3	3.1	1.9	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7071	Acacia leiocalyx	Early-flowering Black Wattle	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7072	Eucalyptus crebra	Narrow-leaved Ironbark	230		230	17	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7073	Petalostigma pubescens	Quinine Bush	250	200	320	10	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7074	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	20	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7075	Acacia disparrima	Hickory Wattle	250		250	11	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7076	Grevillea robusta	Silky Oak	210		210	17	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7077	Corymbia intermedia	Pink Bloodwood	260		260	20	5	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7078	Alphitonia excelsa	Soap Tree	330		330	13	5	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7079	Acacia disparrima	Hickory Wattle	140		140	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7080	Petalostigma pubescens	Quinine Bush	250		250	11	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7081	Petalostigma pubescens	Quinine Bush	180		180	8	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7082	Alphitonia excelsa	Soap Tree	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7083	Petalostigma pubescens	Quinine Bush	280		280	12	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7084	Petalostigma pubescens	Quinine Bush	210		210	11	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7085	Acacia disparrima	Hickory Wattle	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7086	Petalostigma pubescens	Quinine Bush	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7087	Petalostigma pubescens	Quinine Bush	200		200	9	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7088	Petalostigma pubescens	Quinine Bush	170	160	233	9	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7089	Petalostigma pubescens	Quinine Bush	280		280	12	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7090	Eucalyptus tereticornis	Forest Red Gum	430		430	17	6	5.2	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7091	Petalostigma pubescens	Quinine Bush	300	180	350	8	4	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7092	Petalostigma pubescens	Quinine Bush	310		310	12	6	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7093	Allocasuarina littoralis	Black She-oak	180	90	201	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7094	Acacia leiocalyx	Early-flowering Black Wattle	180		180	11	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7095	Eucalyptus tereticornis	Forest Red Gum	470		470	16	5	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7096	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7097	Alphitonia excelsa	Soap Tree	330		330	12	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7098	Acacia leiocalyx	Early-flowering Black Wattle	160		160	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7099	Acacia disparrima	Hickory Wattle	200		200	12	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7100	Acacia leiocalyx	Early-flowering Black Wattle	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7101	Allocasuarina littoralis	Black She-oak	170		170	14	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7102	Lophostemon suaveolens	Swamp Box	240		240	14	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7103	Petalostigma pubescens	Quinine Bush	250	180, 150	343	11	4	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7104	Acacia leiocalyx	Early-flowering Black Wattle	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7105	Acacia disparrima	Hickory Wattle	160		160	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7106	Acacia leiocalyx	Early-flowering Black Wattle	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7107	Acacia disparrima	Hickory Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7108	Acacia disparrima	Hickory Wattle	170	140	220	11	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7109	Acacia disparrima	Hickory Wattle	140	130	191	12	3	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7110	Corymbia tessellaris	Moreton Bay Ash	160		160	13	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7111	Acacia disparrima	Hickory Wattle	160		160	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7112	Acacia leiocalyx	Early-flowering Black Wattle	140		140	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7113	Alphitonia excelsa	Soap Tree	250		250	13	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7114	Corymbia intermedia	Pink Bloodwood	350		350	17	6	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7115	Petalostigma pubescens	Quinine Bush	340		340	12	6	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7116	Alphitonia excelsa	Soap Tree	160		160	7	2	2.0	1.5	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7117	Acacia disparrima	Hickory Wattle	130		130	9	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7118	Corymbia intermedia	Pink Bloodwood	380		380	16	5	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7119	Alphitonia excelsa	Soap Tree	320		320	15	5	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7120	Alphitonia excelsa	Soap Tree	280		280	12	4	3.4	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7121	Acacia leiocalyx	Early-flowering Black Wattle	130		130	9	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7122	Acacia leiocalyx	Early-flowering Black Wattle	190	130	230	10	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7123	Corymbia intermedia	Pink Bloodwood	270		270	14	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7124	Alphitonia excelsa	Soap Tree	220		220	14	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7125	Casuarina cunninghamiana	River She-oak	200		200	9	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7126	Lophostemon suaveolens	Swamp Box	240		240	15	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7127	Lophostemon suaveolens	Swamp Box	250		250	12	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7128	Eucalyptus tereticornis	Forest Red Gum	490		490	17	8	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7129	Corymbia intermedia	Pink Bloodwood	300		300	17	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7130	Acacia disparrima	Hickory Wattle	220	100	242	10	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7131	Corymbia tessellaris	Moreton Bay Ash	400		400	17	5	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7132	Casuarina cunninghamiana	River She-oak	270		270	14	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7133	Melaleuca quinquenervia	Broad-leaved Paperbark	200		200	14	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7134	Casuarina cunninghamiana	River She-oak	270		270	15	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7135	Acacia leiocalyx	Early-flowering Black Wattle	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7136	Alphitonia excelsa	Soap Tree	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7137	Acacia disparrima	Hickory Wattle	180		180	12	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7138	Alphitonia excelsa	Soap Tree	210		210	10	3	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7139	Casuarina cunninghamiana	River She-oak	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7140	Casuarina cunninghamiana	River She-oak	360		360	12	3	4.3	2.2	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7141	Melaleuca quinquenervia	Broad-leaved Paperbark	180		180	9	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7142	Alphitonia excelsa	Soap Tree	260		260	11	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7143	Corymbia tessellaris	Moreton Bay Ash	250		250	15	3	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7144	Acacia disparrima	Hickory Wattle	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7145	Casuarina cunninghamiana	River She-oak	190		190	15	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7146	Melaleuca quinquenervia	Broad-leaved Paperbark	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7147	Angophora leiocarpa	Smooth-barked Apple	300		300	16	4	3.6	2.0	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7148	Melaleuca quinquenervia	Broad-leaved Paperbark	210	200, 140	322	15	4	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7149	Lophostemon suaveolens	Swamp Box	240		240	16	3	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7150	Alphitonia excelsa	Soap Tree	190		190	13	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7151	Melaleuca quinquenervia	Broad-leaved Paperbark	220		220	12	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7152	Angophora leiocarpa	Smooth-barked Apple	420		420	16	5	5.0	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7153	Casuarina cunninghamiana	River She-oak	230		230	9	3	2.8	1.8	One-sided	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7154	Melaleuca quinquenervia	Broad-leaved Paperbark	270		270	14	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7155	Melaleuca quinquenervia	Broad-leaved Paperbark	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7156	Melaleuca quinquenervia	Broad-leaved Paperbark	160		160	16	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7157	Acacia disparrima	Hickory Wattle	170		170	13	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7158	Eucalyptus tereticornis	Forest Red Gum	240		240	16	4	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7159	Alphitonia excelsa	Soap Tree	230		230	14	3	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7160	Eucalyptus tereticornis	Forest Red Gum	300		300	17	4	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7161	Corymbia intermedia	Pink Bloodwood	250		250	17	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7162	Alphitonia excelsa	Soap Tree	250		250	16	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7163	Petalostigma pubescens	Quinine Bush	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7164	Corymbia intermedia	Pink Bloodwood	400		400	17	6	4.8	2.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7165	Corymbia intermedia	Pink Bloodwood	430		430	17	5	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7166	Eucalyptus tereticornis	Forest Red Gum	190		190	14	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7167	Alphitonia excelsa	Soap Tree	360		360	18	4	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7168	Alphitonia excelsa	Soap Tree	360		360	13	5	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7169	Acacia disparrima	Hickory Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7170	Petalostigma pubescens	Quinine Bush	260		260	10	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7171	Petalostigma pubescens	Quinine Bush	180		180	7	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7172	Petalostigma pubescens	Quinine Bush	200		200	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7173	Petalostigma pubescens	Quinine Bush	200		200	11	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7174	Petalostigma pubescens	Quinine Bush	200		200	9	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7175	Petalostigma pubescens	Quinine Bush	250		250	9	3	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7176	Petalostigma pubescens	Quinine Bush	220		220	9	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7177	Petalostigma pubescens	Quinine Bush	180		180	8	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7178	Acacia disparrima	Hickory Wattle	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7179	Petalostigma pubescens	Quinine Bush	250		250	8	3	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7180	Petalostigma pubescens	Quinine Bush	200		200	9	4	2.4	1.7	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7181	Petalostigma pubescens	Quinine Bush	250		250	10	4	3.0	1.8	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7182	Alphitonia excelsa	Soap Tree	150		150	9	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7183	Petalostigma pubescens	Quinine Bush	190		190	9	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7184	Petalostigma pubescens	Quinine Bush	160		160	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7185	Alphitonia excelsa	Soap Tree	330		330	14	3	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7186	Petalostigma pubescens	Quinine Bush	260		260	10	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7187	Petalostigma pubescens	Quinine Bush	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7188	Petalostigma pubescens	Quinine Bush	190		190	11	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7189	Corymbia intermedia	Pink Bloodwood	300		300	19	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7190	Petalostigma pubescens	Quinine Bush	290		290	10	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7191	Acacia disparrima	Hickory Wattle	150	130	198	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7192	Petalostigma pubescens	Quinine Bush	180		180	8	3	2.2	1.6	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7193	Corymbia citriodora	Spotted Gum	370		370	25	8	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7194	Eucalyptus tereticornis	Forest Red Gum	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7195	Corymbia intermedia	Pink Bloodwood	200		200	15	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7196	Corymbia citriodora	Spotted Gum	420		420	20	8	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7197	Alphitonia excelsa	Soap Tree	200		200	14	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7198	Acacia disparrima	Hickory Wattle	150		150	8	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7199	Alphitonia excelsa	Soap Tree	190		190	14	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7200	Eucalyptus tereticornis	Forest Red Gum	180		180	15	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7201	Petalostigma pubescens	Quinine Bush	180	150, 150, 160	321	8	5	3.9	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7202	Corymbia intermedia	Pink Bloodwood	260		260	22	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7203	Eucalyptus crebra	Narrow-leaved Ironbark	400		400	25	10	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7204	Alphitonia excelsa	Soap Tree	200		200	10	7	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7205	Alphitonia excelsa	Soap Tree	150		150	15	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7206	Eucalyptus tereticornis	Forest Red Gum	200		200	20	5	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7207	Corymbia intermedia	Pink Bloodwood	400		400	20	9	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7208	Acacia disparrima	Hickory Wattle	160		160	10	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7209	Alphitonia excelsa	Soap Tree	180		180	15	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7210	Eucalyptus tereticornis	Forest Red Gum	320		320	22	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7211	Alphitonia excelsa	Soap Tree	190		190	15	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7212	Eucalyptus tereticornis	Forest Red Gum	320		320	25	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7213	Lophostemon suaveolens	Swamp Box	250		250	15	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7214	Melaleuca viminalis	Weeping Bottlebrush	180		180	8	4	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7215	Melaleuca viminalis	Weeping Bottlebrush	170		170	5	2	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7216	Casuarina cunninghamiana	River She-oak	320		320	20	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7217	Lophostemon suaveolens	Swamp Box	260		260	14	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7218	Lophostemon suaveolens	Swamp Box	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7219	Lophostemon suaveolens	Swamp Box	230		230	15	4	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7220	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7221	Acacia disparrima	Hickory Wattle	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7222	Corymbia intermedia	Pink Bloodwood	230		230	20	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7223	Acacia disparrima	Hickory Wattle	210		210	10	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7224	Corymbia intermedia	Pink Bloodwood	260		260	20	4	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7225	Corymbia intermedia	Pink Bloodwood	240		240	20	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7226	Allocasuarina littoralis	Black She-oak	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7227	Corymbia intermedia	Pink Bloodwood	180		180	15	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7228	Acacia leiocalyx	Early-flowering Black Wattle	150		150	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7229	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	24	4	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7230	Eucalyptus tereticornis	Forest Red Gum	330		330	23	4	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7231	Eucalyptus tereticornis	Forest Red Gum	350		350	24	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7232	Eucalyptus tereticornis	Forest Red Gum	330		330	25	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7233	Eucalyptus tereticornis	Forest Red Gum	270		270	22	3	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7234	Eucalyptus tereticornis	Forest Red Gum	330		330	22	7	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7235	Lophostemon suaveolens	Swamp Box	320		320	10	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7236	Lophostemon suaveolens	Swamp Box	250		250	15	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7237	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7238	Lophostemon suaveolens	Swamp Box	280		280	15	3	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7239	Corymbia intermedia	Pink Bloodwood	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7240	Corymbia intermedia	Pink Bloodwood	250		250	15	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7241	Lophostemon suaveolens	Swamp Box	280		280	15	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7242	Lophostemon suaveolens	Swamp Box	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7243	Corymbia intermedia	Pink Bloodwood	210		210	18	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7244	Alphitonia excelsa	Soap Tree	210		210	15	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7245	Corymbia intermedia	Pink Bloodwood	270		270	20	8	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7246	Angophora leiocarpa	Smooth-barked Apple	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7247	Alphitonia excelsa	Soap Tree	160	160	226	15	5	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7248	Eucalyptus crebra	Narrow-leaved Ironbark	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7249	Corymbia intermedia	Pink Bloodwood	450		450	22	10	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7250	Eucalyptus tereticornis	Forest Red Gum	240		240	18	7	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7251	Acacia disparrima	Hickory Wattle	190	70	202	10	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7252	Lophostemon suaveolens	Swamp Box	280		280	15	5	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7253	Corymbia intermedia	Pink Bloodwood	210		210	15	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7254	Acacia disparrima	Hickory Wattle	190		190	10	4	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7255	Eucalyptus tereticornis	Forest Red Gum	260		260	25	7	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7256	Corymbia intermedia	Pink Bloodwood	300		300	18	5	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7257	Alphitonia excelsa	Soap Tree	150		150	18	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7258	Alphitonia excelsa	Soap Tree	140		140	15	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7259	Corymbia tessellaris	Moreton Bay Ash	300		300	24	7	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7260	Petalostigma pubescens	Quinine Bush	220		220	15	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7261	Petalostigma pubescens	Quinine Bush	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7262	Eucalyptus tereticornis	Forest Red Gum	470		470	28	9	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7263	Acacia disparrima	Hickory Wattle	210		210	10	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7264	Corymbia intermedia	Pink Bloodwood	210		210	16	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7265	Corymbia intermedia	Pink Bloodwood	280		280	20	7	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7266	Alphitonia excelsa	Soap Tree	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7267	Corymbia intermedia	Pink Bloodwood	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7268	Eucalyptus tereticornis	Forest Red Gum	440		440	23	7	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7269	Acacia disparrima	Hickory Wattle	170		170	10	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7270	Petalostigma pubescens	Quinine Bush	200		200	12	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7271	Petalostigma pubescens	Quinine Bush	210		210	15	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7272	Corymbia tessellaris	Moreton Bay Ash	330		330	22	9	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7273	Petalostigma pubescens	Quinine Bush	140	100, 90	194	9	4	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7274	Petalostigma pubescens	Quinine Bush	150		150	5	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7275	Corymbia intermedia	Pink Bloodwood	400		400	20	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7276	Lophostemon suaveolens	Swamp Box	220		220	15	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7277	Eucalyptus crebra	Narrow-leaved Ironbark	250		250	20	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7278	Acacia disparrima	Hickory Wattle	180		180	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7279	Acacia leiocalyx	Early-flowering Black Wattle	170		170	10	6	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7280	Corymbia intermedia	Pink Bloodwood	330		330	21	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7281	Alphitonia excelsa	Soap Tree	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7282	Alphitonia excelsa	Soap Tree	150		150	15	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7283	Eucalyptus crebra	Narrow-leaved Ironbark	260		260	22	6	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7284	Alphitonia excelsa	Soap Tree	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7285	Acacia disparrima	Hickory Wattle	190		190	15	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7286	Corymbia intermedia	Pink Bloodwood	450		450	20	7	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7287	Alphitonia excelsa	Soap Tree	190		190	15	6	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7288	Alphitonia excelsa	Soap Tree	150		150	15	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7289	Lophostemon suaveolens	Swamp Box	200		200	15	4	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7290	Alphitonia excelsa	Soap Tree	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7291	Petalostigma pubescens	Quinine Bush	150		150	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7292	Melaleuca viminalis	Weeping Bottlebrush	180		180	10	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7293	Lophostemon suaveolens	Swamp Box	210		210	10	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7294	Lophostemon suaveolens	Swamp Box	230		230	15	5	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7295	Melaleuca viminalis	Weeping Bottlebrush	170		170	4	2	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7296	Melaleuca viminalis	Weeping Bottlebrush	160		160	5	2	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7297	Alphitonia excelsa	Soap Tree	250		250	15	5	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7298	Corymbia citriodora	Spotted Gum	410		410	25	10	4.9	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7299	Alphitonia excelsa	Soap Tree	230		230	15	6	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7300	Acacia disparrima	Hickory Wattle	150		150	12	5	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7301	Alphitonia excelsa	Soap Tree	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7302	Petalostigma pubescens	Quinine Bush	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7303	Alphitonia excelsa	Soap Tree	170		170	10	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7304	Corymbia citriodora	Spotted Gum	330		330	25	8	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7305	Corymbia intermedia	Pink Bloodwood	350		350	20	7	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7306	Petalostigma pubescens	Quinine Bush	170		170	8	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7307	Corymbia intermedia	Pink Bloodwood	210		210	18	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7308	Alphitonia excelsa	Soap Tree	160		160	15	6	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7309	Alphitonia excelsa	Soap Tree	220		220	12	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7310	Corymbia intermedia	Pink Bloodwood	140		140	18	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7311	Petalostigma pubescens	Quinine Bush	130		130	8	5	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7312	Corymbia citriodora	Spotted Gum	390		390	21	8	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7313	Petalostigma pubescens	Quinine Bush	150		150	6	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7314	Alphitonia excelsa	Soap Tree	240		240	18	6	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7315	Corymbia citriodora	Spotted Gum	220		220	20	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7316	Corymbia citriodora	Spotted Gum	280		280	21	6	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7317	Alphitonia excelsa	Soap Tree	200		200	10	3	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7318	Corymbia citriodora	Spotted Gum	320		320	28	8	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7319	Corymbia citriodora	Spotted Gum	340		340	22	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7320	Acacia disparrima	Hickory Wattle	150		150	8	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7321	Acacia disparrima	Hickory Wattle	180		180	9	2	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7322	Acacia disparrima	Hickory Wattle	150		150	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7323	Acacia disparrima	Hickory Wattle	160		160	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7324	Acacia disparrima	Hickory Wattle	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7325	Acacia disparrima	Hickory Wattle	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7326	Acacia disparrima	Hickory Wattle	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7327	Corymbia intermedia	Pink Bloodwood	300		300	23	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7328	Alphitonia excelsa	Soap Tree	380		380	18	7	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7329	Acacia leiocalyx	Early-flowering Black Wattle	210		210	8	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7330	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7331	Acacia disparrima	Hickory Wattle	180	170	248	8	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7332	Corymbia tessellaris	Moreton Bay Ash	210		210	20	6	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7333	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7334	Acacia leiocalyx	Early-flowering Black Wattle	130		130	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7335	Petalostigma pubescens	Quinine Bush	160		160	10	2	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7336	Alphitonia excelsa	Soap Tree	290		290	10	4	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7337	Alphitonia excelsa	Soap Tree	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7338	Acacia leiocalyx	Early-flowering Black Wattle	170		170	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7339	Lophostemon suaveolens	Swamp Box	120		120	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7340	Petalostigma pubescens	Quinine Bush	130		130	8	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7341	Corymbia intermedia	Pink Bloodwood	320		320	23	6	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7342	Alphitonia excelsa	Soap Tree	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7343	Petalostigma pubescens	Quinine Bush	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7344	Acacia disparrima	Hickory Wattle	140		140	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7345	Acacia disparrima	Hickory Wattle	130		130	8	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7346	Corymbia intermedia	Pink Bloodwood	150		150	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7347	Corymbia intermedia	Pink Bloodwood	170		170	15	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7348	Corymbia intermedia	Pink Bloodwood	420		420	20	10	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7349	Eucalyptus tereticornis	Forest Red Gum	310		310	20	8	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7350	Corymbia citriodora	Spotted Gum	400		400	23	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7351	Corymbia intermedia	Pink Bloodwood	220		220	18	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7352	Alphitonia excelsa	Soap Tree	160		160	5	2	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7353	Acacia disparrima	Hickory Wattle	190		190	18	5	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7354	Acacia disparrima	Hickory Wattle	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7355	Acacia disparrima	Hickory Wattle	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7356	Acacia disparrima	Hickory Wattle	160		160	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7357	Acacia disparrima	Hickory Wattle	150		150	8	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7358	Petalostigma pubescens	Quinine Bush	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7359	Acacia disparrima	Hickory Wattle	190		190	10	3	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7360	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7361	Acacia disparrima	Hickory Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7362	Eucalyptus tereticornis	Forest Red Gum	150		150	20	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7363	Petalostigma pubescens	Quinine Bush	260		260	4	3	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7364	Alphitonia excelsa	Soap Tree	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7365	Acacia disparrima	Hickory Wattle	170	140	220	10	3	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7366	Acacia disparrima	Hickory Wattle	180		180	10	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7367	Acacia disparrima	Hickory Wattle	130		130	10	2	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7368	Petalostigma pubescens	Quinine Bush	200		200	8	6	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7369	Eucalyptus tereticornis	Forest Red Gum	350		350	20	8	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7370	Alphitonia excelsa	Soap Tree	140		140	8	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7371	Alphitonia excelsa	Soap Tree	250		250	18	6	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7372	Alphitonia excelsa	Soap Tree	180		180	10	5	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7373	Alphitonia excelsa	Soap Tree	180		180	8	4	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7374	Alphitonia excelsa	Soap Tree	150		150	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7375	Casuarina cunninghamiana	River She-oak	170		170	20	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7376	Alphitonia excelsa	Soap Tree	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7377	Acacia disparrima	Hickory Wattle	360		360	10	4	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7378	Alphitonia excelsa	Soap Tree	170		170	8	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7379	Casuarina cunninghamiana	River She-oak	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7380	Melaleuca quinquenervia	Broad-leaved Paperbark	170		170	15	4	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7381	Melaleuca quinquenervia	Broad-leaved Paperbark	230		230	15	7	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7382	Melaleuca quinquenervia	Broad-leaved Paperbark	330		330	18	6	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7383	Corymbia intermedia	Pink Bloodwood	210		210	18	4	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7384	Alphitonia excelsa	Soap Tree	240		240	15	5	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7385	Acacia disparrima	Hickory Wattle	210		210	15	5	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7386	Eucalyptus tereticornis	Forest Red Gum	220		220	20	5	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7387	Alphitonia excelsa	Soap Tree	140		140	15	4	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7388	Alphitonia excelsa	Soap Tree	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7389	Melaleuca quinquenervia	Broad-leaved Paperbark	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7390	Alphitonia excelsa	Soap Tree	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7391	Corymbia intermedia	Pink Bloodwood	300		300	20	6	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7392	Acacia disparrima	Hickory Wattle	160		160	10	3	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7393	Corymbia intermedia	Pink Bloodwood	400		400	22	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7394	Alphitonia excelsa	Soap Tree	340		340	18	8	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7395	Corymbia intermedia	Pink Bloodwood	400		400	20	8	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7396	Alphitonia excelsa	Soap Tree	280		280	20	8	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7397	Acacia disparrima	Hickory Wattle	180		180	18	3	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7398	Acacia disparrima	Hickory Wattle	170		170	12	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7399	Petalostigma pubescens	Quinine Bush	250		250	18	4	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7400	Acacia leiocalyx	Early-flowering Black Wattle	160		160	10	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7401	Eucalyptus tereticornis	Forest Red Gum	300		300	22	9	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7402	Corymbia torelliana	Cadaghi	160		160	15	4	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7403	Alphitonia excelsa	Soap Tree	220		220	10	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7404	Alphitonia excelsa	Soap Tree	220		220	10	4	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7405	Petalostigma pubescens	Quinine Bush	170		170	10	3	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7406	Petalostigma pubescens	Quinine Bush	140		140	10	3	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retention TBC by CPTED
7407	*Corymbia intermedia*	Pink Bloodwood	320		320	24.0	12.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7408	*Acacia disparrima*	Hickory Wattle	140		140	7.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7409	*Alphitonia excelsa*	Red Ash	170		170	12.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7410	*Eucalyptus tereticornis*	Forest Red Gum	160		160	14.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7411	*Alphitonia excelsa*	Red Ash	140		140	9.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7412	*Acacia disparrima*	Hickory Wattle	180		180	10.0	7.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7413	*Alphitonia excelsa*	Red Ash	130		130	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7414	*Alphitonia excelsa*	Red Ash	170		170	12.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7415	*Alphitonia excelsa*	Red Ash	170		170	12.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7416	*Alphitonia excelsa*	Red Ash	150		150	12.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7417	*Alphitonia excelsa*	Red Ash	150		150	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7418	*Grevillea robusta*	Silky Oak	480		480	24.0	12.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7419	*Grevillea robusta*	Silky Oak	260		260	24.0	10.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7420	*Lophostemon suaveolens*	Swamp Box	270		270	22.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7421	*Lophostemon suaveolens*	Swamp Box	170		170	20.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details						Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7422	*Alchornea ilicifolia*	Native Holly	130		130	9.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7423	*Grevillea robusta*	Silky Oak	140		140	16.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7424	*Eucalyptus tereticornis*	Forest Red Gum	330		330	24.0	14.0	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
7425	*Alchornea ilicifolia*	Native Holly	110		110	7.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7426	*Lophostemon suaveolens*	Swamp Box	240		240	18.0	8.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7427	*Allocasuarina littoralis*	Black Sheoak	180		180	12.0	7.0	2.2	1.6	Regular	-	Thinning	Die-back	-	-	Poor	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7428	*Casuarina cunninghamiana*	River Sheoak	340		340	22.0	8.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7429	*Casuarina cunninghamiana*	River Sheoak	210		210	14.0	6.0	2.5	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7430	*Acacia disparrima*	Hickory Wattle	190		190	10.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7431	*Casuarina cunninghamiana*	River Sheoak	270		270	20.0	6.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7432	*Grevillea robusta*	Silky Oak	210		210	18.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7433	*Alphitonia excelsa*	Red Ash	170		170	12.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7434	*Angophora subvelutina*	Broadleaf Apple	370		370	24.0	14.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7435	*Lophostemon suaveolens*	Swamp Box	150		150	14.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7436	*Grevillea robusta*	Silky Oak	220		220	18.0	7.0	2.6	1.8	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7437	*Casuarina cunninghamiana*	River Sheoak	120		120	18.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7438	*Corymbia intermedia*	Pink Bloodwood	420		420	26.0	14.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7439	*Alchornea ilicifolia*	Native Holly	220		220	12.0	7.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7440	*Alphitonia excelsa*	Red Ash	220		220	18.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7441	**DEAD/STAG**		550		550	16.0	4.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
7442	*Grevillea robusta*	Silky Oak	160		160	18.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7443	*Alchornea ilicifolia*	Native Holly	170		170	14.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7444	*Casuarina cunninghamiana*	River Sheoak	190		190	20.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7445	*Casuarina cunninghamiana*	River Sheoak	210		210	22.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7446	*Casuarina cunninghamiana*	River Sheoak	250		250	22.0	8.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7447	*Eucalyptus siderophloia*	Grey Ironbark	260		260	26.0	14.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7448	*Alphitonia excelsa*	Red Ash	270		270	22.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7449	*Eucalyptus tereticornis*	Forest Red Gum	450		450	26.0	14.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Remove for basin works
7450	*Allocasuarina littoralis*	Black Sheoak	140		140	10.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7451	*Corymbia intermedia*	Pink Bloodwood	280		280	24.0	14.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7452	*Petalostigma pubescens*	Quinine Bush	260		260	10.0	7.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7453	*Allocasuarina littoralis*	Black Sheoak	140		140	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7454	*Corymbia intermedia*	Pink Bloodwood	600		600	26.0	12.0	7.2	2.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7455	*Corymbia intermedia*	Pink Bloodwood	240		240	22.0	14.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7456	*Corymbia intermedia*	Pink Bloodwood	230		230	22.0	10.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7457	*Alphitonia excelsa*	Red Ash	180		180	10.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7458	*Acacia disparrima*	Hickory Wattle	150		150	8.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7459	*Petalostigma pubescens*	Quinine Bush	170		170	10.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7460	*Corymbia citriodora*	Spotted Gum	290		290	26.0	12.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7461	*Acacia disparrima*	Hickory Wattle	260		260	12.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7462	*Alphitonia excelsa*	Red Ash	120		120	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7463	*Eucalyptus tereticornis*	Forest Red Gum	210		210	22.0	12.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7464	*Lophostemon suaveolens*	Swamp Box	190		190	14.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7465	*Grevillea robusta*	Silky Oak	180		180	10.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7466	*Grevillea robusta*	Silky Oak	200		200	10.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7467	*Melaleuca viminalis*	Weeping Bottlebrush	200		200	14.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Remove
7468	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	8.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7469	*Corymbia intermedia*	Pink Bloodwood	230		230	16.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7470	*Corymbia intermedia*	Pink Bloodwood	270		270	16.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7471	*Corymbia intermedia*	Pink Bloodwood	340		340	24.0	12.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7472	*Corymbia tessellaris*	Moreton Bay Ash	120		120	16.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7473	*Eucalyptus tereticornis*	Forest Red Gum	260		260	26.0	12.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7474	*Acacia disparrima*	Hickory Wattle	130		130	8.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7475	*Corymbia tessellaris*	Moreton Bay Ash	190		190	18.0	3.0	2.3	1.6	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7476	*Eucalyptus tereticornis*	Forest Red Gum	270		270	24.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7477	*Corymbia tessellaris*	Moreton Bay Ash	140		140	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7478	*Corymbia tessellaris*	Moreton Bay Ash	130		130	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7479	*Corymbia tessellaris*	Moreton Bay Ash	130	130	184	22.0	8.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7480	*Alphitonia excelsa*	Red Ash	110		110	12.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7481	*Acacia disparrima*	Hickory Wattle	130		130	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7482	*Acacia disparrima*	Hickory Wattle	160		160	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7483	*Acacia disparrima*	Hickory Wattle	140		140	8.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7484	*Eucalyptus siderophloia*	Grey Ironbark	200		200	26.0	10.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7485	*Acacia disparrima*	Hickory Wattle	130		130	8.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7486	*Eucalyptus siderophloia*	Grey Ironbark	260		260	26.0	14.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7487	*Eucalyptus siderophloia*	Grey Ironbark	140		140	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7488	*Eucalyptus tereticornis*	Forest Red Gum	330		330	26.0	14.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7489	*Corymbia tessellaris*	Moreton Bay Ash	160		160	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7490	*Acacia disparrima*	Hickory Wattle	130		130	8.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7491	*Corymbia tessellaris*	Moreton Bay Ash	170		170	12.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7492	*Eucalyptus siderophloia*	Grey Ironbark	200		200	22.0	10.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7493	*Corymbia tessellaris*	Moreton Bay Ash	140		140	14.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7494	*Acacia disparrima*	Hickory Wattle	260		260	10.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7495	*Corymbia intermedia*	Pink Bloodwood	270		270	20.0	12.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7496	*Eucalyptus tereticornis*	Forest Red Gum	180		180	20.0	10.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7497	*Acacia disparrima*	Hickory Wattle	160		160	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7498	*Eucalyptus siderophloia*	Grey Ironbark	280		280	22.0	14.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7499	*Corymbia intermedia*	Pink Bloodwood	260		260	16.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7500	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	8.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7501	*Lophostemon suaveolens*	Swamp Box	190		190	10.0	7.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7502	*Eucalyptus tereticornis*	Forest Red Gum	280		280	22.0	12.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7503	*Alphitonia excelsa*	Red Ash	110		110	7.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7504	*Eucalyptus tereticornis*	Forest Red Gum	290		290	22.0	12.0	3.5	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7505	*Acacia disparrima*	Hickory Wattle	160		160	8.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7506	*Petalostigma pubescens*	Quinine Bush	260		260	12.0	8.0	3.1	1.9	Regular	-	Thinning	Die-back	-	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7507	*Acacia disparrima*	Hickory Wattle	130		130	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7508	*Eucalyptus tereticornis*	Forest Red Gum	240		240	22.0	12.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7509	*Melaleuca viminalis*	Weeping Bottlebrush	170		170	8.0	4.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
7510	*Ficus benjamina*	Weeping Fig	440		440	18.0	12.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7511	*Grevillea robusta*	Silky Oak	110		110	12.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7512	*Casuarina cunninghamiana*	River Sheoak	210		210	20.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7513	*Acacia disparrima*	Hickory Wattle	150		150	14.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
7514	*Alphitonia excelsa*	Red Ash	140		140	16.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7515	*Petalostigma pubescens*	Quinine Bush	250		250	8.0	6.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7516	*Alphitonia excelsa*	Red Ash	330		330	14.0	12.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7517	*Eucalyptus siderophloia*	Grey Ironbark	390		390	26.0	14.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	Trunk Dmg.	-	Typical	-	-	-	-	-	-		Retain
7518	**DEAD/STAG**		540		540	12.0	4.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
7519	*Eucalyptus tereticornis*	Forest Red Gum	220		220	20.0	10.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7520	*Corymbia intermedia*	Pink Bloodwood	270		270	20.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7521	*Corymbia citriodora*	Spotted Gum	330		330	26.0	12.0	4.0	2.1	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7522	**DEAD/STAG**		480		480	18.0	2.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
7523	*Alphitonia excelsa*	Red Ash	230		230	12.0	10.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7524	*Corymbia citriodora*	Spotted Gum	240		240	24.0	10.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7525	*Corymbia citriodora*	Spotted Gum	350		350	24.0	14.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7526	*Corymbia citriodora*	Spotted Gum	150		150	18.0	6.0	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7527	*Eucalyptus siderophloia*	Grey Ironbark	630		630	24.0	12.0	7.6	2.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-		Retain
7528	*Eucalyptus siderophloia*	Grey Ironbark	120		120	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7529	*Alphitonia excelsa*	Red Ash	240		240	18.0	10.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7530	*Eucalyptus siderophloia*	Grey Ironbark	130		130	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7531	*Corymbia citriodora*	Spotted Gum	340		340	26.0	14.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7532	*Eucalyptus siderophloia*	Grey Ironbark	130		130	16.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7533	*Eucalyptus tereticornis*	Forest Red Gum	200		200	20.0	10.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7534	*Eucalyptus siderophloia*	Grey Ironbark	220		220	26.0	12.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7535	*Corymbia citriodora*	Spotted Gum	170		170	20.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7536	*Alphitonia excelsa*	Red Ash	170		170	12.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7537	*Corymbia citriodora*	Spotted Gum	310		310	26.0	14.0	3.7	2.0	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7538	*Eucalyptus tereticornis*	Forest Red Gum	140		140	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7539	*Corymbia citriodora*	Spotted Gum	310		310	28.0	12.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7540	*Corymbia citriodora*	Spotted Gum	210		210	18.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7541	*Corymbia citriodora*	Spotted Gum	320		320	28.0	14.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7542	*Corymbia tessellaris*	Moreton Bay Ash	150		150	12.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7543	*Pinus elliotii*	Slash Pine	350		350	16.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7544	*Alphitonia excelsa*	Red Ash	120		120	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7545	*Corymbia tessellaris*	Moreton Bay Ash	160		160	12.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7546	*Alphitonia excelsa*	Red Ash	80		80	4.0	1.0	2.0	1.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7547	*Eucalyptus tereticornis*	Forest Red Gum	120		120	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7548	*Pinus elliotii*	Slash Pine	440		440	18.0	10.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7549	*Corymbia intermedia*	Pink Bloodwood	110		110	12.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7550	*Eucalyptus tereticornis*	Forest Red Gum	140		140	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7551	*Grevillea robusta*	Silky Oak	100		100	14.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7552	*Alphitonia excelsa*	Red Ash	110	110	156	8.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7553	*Casuarina cunninghamiana*	River Sheoak	150	150	212	18.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7554	*Eucalyptus tereticornis*	Forest Red Gum	150		150	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7555	*Angophora subvelutina*	Broadleaf Apple	180		180	12.0	5.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7556	*Corymbia intermedia*	Pink Bloodwood	170	130	214	14.0	5.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7557	*Lophostemon suaveolens*	Swamp Box	130		130	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7558	*Eucalyptus tereticornis*	Forest Red Gum	330		330	24.0	12.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7559	*Acacia concurrens*	Black Wattle	200		200	10.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7560	*Lophostemon suaveolens*	Swamp Box	320		320	14.0	8.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7561	*Grevillea robusta*	Silky Oak	110		110	8.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7562	*Acacia concurrens*	Black Wattle	150		150	10.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7563	*Pinus elliotii*	Slash Pine	160		160	12.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7564	*Casuarina cunninghamiana*	River Sheoak	200	180	269	20.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7565	*Casuarina cunninghamiana*	River Sheoak	210	180	277	20.0	8.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7566	*Casuarina cunninghamiana*	River Sheoak	160		160	18.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7567	*Acacia concurrens*	Black Wattle	180		180	11.0	7.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7568	*Eucalyptus tereticornis*	Forest Red Gum	260		260	24.0	12.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7569	*Lophostemon suaveolens*	Swamp Box	150	120, 120	226	16.0	7.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7570	*Acacia fimbriata*	Fringed Wattle	150		150	10.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7571	*Lophostemon suaveolens*	Swamp Box	120		120	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7572	*Lophostemon suaveolens*	Swamp Box	230		230	16.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7573	*Lophostemon suaveolens*	Swamp Box	130		130	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7574	*Corymbia citriodora*	Spotted Gum	120		120	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7575	*Lophostemon suaveolens*	Swamp Box	130		130	8.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7576	*Corymbia citriodora*	Spotted Gum	120		120	12.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7577	*Angophora leiocarpa*	Smooth Barked Apple	120		120	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7578	*Lophostemon suaveolens*	Swamp Box	230		230	18.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7579	*Lophostemon suaveolens*	Swamp Box	130		130	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7580	*Alphitonia excelsa*	Red Ash	130		130	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7581	*Corymbia citriodora*	Spotted Gum	520		520	28.0	14.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7582	*Corymbia citriodora*	Spotted Gum	110		110	10.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7583	*Corymbia citriodora*	Spotted Gum	440		440	28.0	14.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7584	*Corymbia citriodora*	Spotted Gum	140		140	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7585	*Corymbia citriodora*	Spotted Gum	120		120	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7586	*Eucalyptus tereticornis*	Forest Red Gum	280		280	26.0	12.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7587	*Corymbia citriodora*	Spotted Gum	480		480	26.0	14.0	5.8	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7588	*Corymbia citriodora*	Spotted Gum	370		370	28.0	14.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7589	*Corymbia citriodora*	Spotted Gum	450		450	28.0	14.0	5.4	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7590	*Corymbia citriodora*	Spotted Gum	330		330	26.0	10.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7591	*Eucalyptus tereticornis*	Forest Red Gum	130		130	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7592	*Corymbia citriodora*	Spotted Gum	370		370	28.0	16.0	4.4	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7593	*Angophora leiocarpa*	Smooth Barked Apple	440		440	22.0	14.0	5.3	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7594	*Corymbia citriodora*	Spotted Gum	110		110	10.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7595	*Alphitonia excelsa*	Red Ash	120		120	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7596	*Lophostemon suaveolens*	Swamp Box	240	130	273	15.0	6.0	3.3	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7597	*Lophostemon suaveolens*	Swamp Box	230		230	10.0	6.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7598	*Lophostemon suaveolens*	Swamp Box	190		190	8.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7599	*Eucalyptus tereticornis*	Forest Red Gum	230		230	24.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7600	*Eucalyptus tereticornis*	Forest Red Gum	470		470	26.0	12.0	5.6	2.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7601	*Eucalyptus tereticornis*	Forest Red Gum	390		390	28.0	14.0	4.7	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7602	*Corymbia citriodora*	Spotted Gum	520		520	26.0	12.0	6.2	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7603	*Corymbia citriodora*	Spotted Gum	380		380	28.0	14.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7604	*Alphitonia excelsa*	Red Ash	120		120	10.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7605	*Angophora leiocarpa*	Smooth Barked Apple	300		300	24.0	13.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7606	*Alphitonia excelsa*	Red Ash	130		130	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7607	*Angophora leiocarpa*	Smooth Barked Apple	530		530	28.0	16.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7608	*Corymbia citriodora*	Spotted Gum	550		550	28.0	16.0	6.6	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7609	*Eucalyptus tereticornis*	Forest Red Gum	300		300	24.0	10.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7610	*Eucalyptus tereticornis*	Forest Red Gum	360		360	28.0	14.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7611	*Corymbia intermedia*	Pink Bloodwood	250		250	22.0	14.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7612	*Corymbia intermedia*	Pink Bloodwood	150		150	16.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7613	*Eucalyptus tereticornis*	Forest Red Gum	160		160	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7614	*Eucalyptus tereticornis*	Forest Red Gum	420		420	28.0	14.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7615	*Corymbia intermedia*	Pink Bloodwood	160		160	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7616	*Alphitonia excelsa*	Red Ash	120		120	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7617	*Lophostemon suaveolens*	Swamp Box	350		350	14.0	8.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7618	*Eucalyptus tereticornis*	Forest Red Gum	870		870	32.0	16.0	10.4	3.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7619	*Eucalyptus tereticornis*	Forest Red Gum	720		720	26.0	14.0	8.6	2.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	Old	-	-	-	-		Retain
7620	*Corymbia tessellaris*	Moreton Bay Ash	230		230	14.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7621	*Acacia disparrima*	Hickory Wattle	130		130	12.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7622	*Acacia disparrima*	Hickory Wattle	220	150	266	12.0	9.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7623	*Acacia disparrima*	Hickory Wattle	140		140	7.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7624	*Acacia disparrima*	Hickory Wattle	140		140	8.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7625	*Acacia disparrima*	Hickory Wattle	240		240	8.0	6.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7626	*Acacia disparrima*	Hickory Wattle	140		140	7.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7627	*Acacia disparrima*	Hickory Wattle	120		120	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7628	*Alphitonia excelsa*	Red Ash	170		170	12.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7629	*Corymbia intermedia*	Pink Bloodwood	120	110	163	8.0	3.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7630	*Corymbia citriodora*	Spotted Gum	110		110	14.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7631	*Acacia disparrima*	Hickory Wattle	220		220	10.0	7.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7632	*Acacia disparrima*	Hickory Wattle	140		140	8.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7633	*Acacia disparrima*	Hickory Wattle	190		190	7.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7634	*Corymbia intermedia*	Pink Bloodwood	220	220	311	18.0	7.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7635	*Acacia disparrima*	Hickory Wattle	120	120	170	8.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7636	*Acacia disparrima*	Hickory Wattle	170		170	8.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	Minor	-	-	-	Typical	-	-	-	-	-	-		Retain
7637	*Lophostemon suaveolens*	Swamp Box	110		110	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7638	*Angophora leiocarpa*	Smooth Barked Apple	130		130	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7639	*Angophora leiocarpa*	Smooth Barked Apple	160		160	10.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7640	*Angophora leiocarpa*	Smooth Barked Apple	140		140	16.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7641	*Eucalyptus tereticornis*	Forest Red Gum	280		280	18.0	12.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7642	*Alphitonia excelsa*	Red Ash	160		160	12.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7643	*Angophora leiocarpa*	Smooth Barked Apple	160		160	12.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7644	*Eucalyptus tereticornis*	Forest Red Gum	220		220	18.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7645	*Lophostemon suaveolens*	Swamp Box	140		140	10.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7646	*Lophostemon suaveolens*	Swamp Box	140		140	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7647	*Angophora leiocarpa*	Smooth Barked Apple	200		200	22.0	12.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7648	*Alphitonia excelsa*	Red Ash	120		120	10.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7649	*Angophora leiocarpa*	Smooth Barked Apple	160		160	16.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7650	*Acacia disparrima*	Hickory Wattle	170		170	16.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7651	*Eucalyptus tereticornis*	Forest Red Gum	420		420	24.0	8.0	5.0	2.3	Regular	-	Thinning	Die-back	Epicormic	-	Poor	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7652	*Alphitonia excelsa*	Red Ash	160		160	22.0	10.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7653	*Acacia disparrima*	Hickory Wattle	130		130	12.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7654	*Lophostemon suaveolens*	Swamp Box	170		170	16.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7655	*Eucalyptus tereticornis*	Forest Red Gum	400		400	26.0	12.0	4.8	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7656	*Melaleuca quinquenervia*	Broad-leaved Paperbark	230		230	18.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7657	*Acacia disparrima*	Hickory Wattle	150		150	4.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7658	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	6.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7659	*Angophora subvelutina*	Broadleaf Apple	110		110	10.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7660	*Angophora subvelutina*	Broadleaf Apple	150		150	8.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7661	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	8.0	8.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7662	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	11.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7663	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	12.0	7.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7664	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	12.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7665	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	9.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7666	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	7.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7667	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	9.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7668	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	9.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7669	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	8.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7670	*Acacia leiocalyx*	Early Flowering Black Wattle	130	110	170	8.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7671	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	7.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7672	*Acacia leiocalyx*	Early Flowering Black Wattle	160		160	9.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7673	*Angophora subvelutina*	Broadleaf Apple	110		110	6.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7674	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	7.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7675	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	6.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7676	*Acacia leiocalyx*	Early Flowering Black Wattle	130	120	177	7.0	5.0	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7677	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	7.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7678	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	6.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7679	*Acacia leiocalyx*	Early Flowering Black Wattle	180	150	234	6.0	8.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7680	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	6.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7681	*Petalostigma pubescens*	Quinine Bush	140		140	6.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7682	*Acacia disparrima*	Hickory Wattle	140		140	5.0	9.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7683	*Petalostigma pubescens*	Quinine Bush	140		140	4.0	8.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7684	*Acacia disparrima*	Hickory Wattle	100		100	13.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7685	*Lophostemon suaveolens*	Swamp Box	310		310	20.0	12.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7686	*Petalostigma pubescens*	Quinine Bush	110		110	4.0	6.0	2.0	1.3	One-sided	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7687	*Petalostigma pubescens*	Quinine Bush	120	90	150	4.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7688	*Petalostigma pubescens*	Quinine Bush	200	170	262	14.0	10.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7689	*Petalostigma pubescens*	Quinine Bush	230		230	5.0	10.0	2.8	1.8	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7690	*Petalostigma pubescens*	Quinine Bush	100		100	5.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7691	*Alphitonia excelsa*	Red Ash	150		150	16.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7692	*Acacia disparrima*	Hickory Wattle	250		250	15.0	9.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7693	*Petalostigma pubescens*	Quinine Bush	100	60, 70	136	6.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7694	*Petalostigma pubescens*	Quinine Bush	200	130, 100	259	15.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7695	*Allocasuarina littoralis*	Black Sheoak	160		160	15.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7696	*Allocasuarina littoralis*	Black Sheoak	110		110	16.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7697	*Allocasuarina littoralis*	Black Sheoak	150	70	166	15.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7698	*Banksia integrifolia*	Coastal Banksia	130	70	148	14.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7699	*Allocasuarina littoralis*	Black Sheoak	170		170	15.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7700	*Allocasuarina littoralis*	Black Sheoak	100	70, 70	141	5.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7701	*Alphitonia excelsa*	Red Ash	120		120	14.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7702	*Alphitonia excelsa*	Red Ash	120		120	14.0	3.0	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7703	*Alphitonia excelsa*	Red Ash	150		150	17.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7704	*Petalostigma pubescens*	Quinine Bush	150		150	5.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7705	*Petalostigma pubescens*	Quinine Bush	140		140	6.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7706	*Petalostigma pubescens*	Quinine Bush	170		170	10.0	13.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7707	*Petalostigma pubescens*	Quinine Bush	110	90	142	4.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7708	*Petalostigma pubescens*	Quinine Bush	200		200	17.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7709	*Petalostigma pubescens*	Quinine Bush	110		110	7.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7710	*Corymbia intermedia*	Pink Bloodwood	180		180	16.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7711	*Corymbia intermedia*	Pink Bloodwood	490		490	25.0	14.0	5.9	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7712	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	16.0	8.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7713	*Eucalyptus tereticornis*	Forest Red Gum	380		380	26.0	17.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7714	*Allocasuarina littoralis*	Black Sheoak	180		180	16.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7715	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7716	*Acacia fimbriata*	Fringed Wattle	90	90, 90, 30	159	14.0	9.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7717	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	15.0	9.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7718	*Acacia leiocalyx*	Early Flowering Black Wattle	150		150	17.0	9.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7719	*Acacia disparrima*	Hickory Wattle	180		180	17.0	10.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7720	*Acacia disparrima*	Hickory Wattle	190	100	215	13.0	10.0	2.6	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7721	*Petalostigma pubescens*	Quinine Bush	220		220	6.0	15.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7722	*Corymbia citriodora*	Spotted Gum	200		200	20.0	13.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7723	*Petalostigma pubescens*	Quinine Bush	160	160	226	4.0	11.0	2.7	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7724	*Eucalyptus tereticornis*	Forest Red Gum	200		200	23.0	10.0	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7725	*Acacia disparrima*	Hickory Wattle	170		170	16.0	10.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7726	*Corymbia tessellaris*	Moreton Bay Ash	100	90	135	16.0	1.0	2.0	1.4	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7727	*Lophostemon suaveolens*	Swamp Box	180		180	16.0	8.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7728	*Lophostemon suaveolens*	Swamp Box	170		170	16.0	9.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7729	*Grevillea robusta*	Silky Oak	220		220	20.0	8.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7730	*Angophora subvelutina*	Broadleaf Apple	400	350	532	22.0	20.0	6.4	2.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7731	*Acacia disparrima*	Hickory Wattle	110		110	14.0	7.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7732	*Acacia disparrima*	Hickory Wattle	150		150	15.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7733	*Allocasuarina littoralis*	Black Sheoak	120		120	16.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7734	*Eucalyptus tereticornis*	Forest Red Gum	110		110	16.0	3.0	2.0	1.3	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7735	*Acacia disparrima*	Hickory Wattle	200		200	5.0	9.0	2.4	1.7	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7736	*Eucalyptus tereticornis*	Forest Red Gum	190		190	22.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7737	*Eucalyptus tereticornis*	Forest Red Gum	210		210	19.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7738	*Eucalyptus siderophloia*	Grey Ironbark	160		160	18.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7739	*Acacia disparrima*	Hickory Wattle	210	170	270	16.0	8.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7740	*Acacia disparrima*	Hickory Wattle	160	130	206	15.0	9.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7741	*Acacia disparrima*	Hickory Wattle	170		170	15.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7742	*Corymbia tessellaris*	Moreton Bay Ash	150		150	15.0	5.0	2.0	1.5	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7743	*Acacia disparrima*	Hickory Wattle	110		110	12.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7744	*Acacia leiocalyx*	Early Flowering Black Wattle	130	110	170	15.0	15.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7745	*Alphitonia excelsa*	Red Ash	130		130	15.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7746	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	14.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7747	*Acacia disparrima*	Hickory Wattle	230		230	15.0	13.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7748	*Acacia disparrima*	Hickory Wattle	100	80	128	12.0	8.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7749	*Corymbia tessellaris*	Moreton Bay Ash	110		110	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7750	*Alphitonia excelsa*	Red Ash	170		170	15.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7751	*Alphitonia excelsa*	Red Ash	140		140	13.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7752	*Alphitonia excelsa*	Red Ash	120		120	11.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7753	*Alphitonia excelsa*	Red Ash	170		170	19.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7754	*Eucalyptus tereticornis*	Forest Red Gum	100		100	16.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7755	*Acacia disparrima*	Hickory Wattle	180		180	14.0	10.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7756	*Acacia disparrima*	Hickory Wattle	120		120	14.0	8.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7757	*Acacia disparrima*	Hickory Wattle	130		130	12.0	10.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7758	*Allocasuarina littoralis*	Black Sheoak	130		130	16.0	8.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7759	*Allocasuarina littoralis*	Black Sheoak	100		100	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7760	*Acacia disparrima*	Hickory Wattle	170		170	14.0	6.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7761	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	13.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7762	*Eucalyptus siderophloia*	Grey Ironbark	200		200	22.0	13.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7763	*Eucalyptus siderophloia*	Grey Ironbark	270		270	23.0	15.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7764	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	13.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7765	*Eucalyptus tereticornis*	Forest Red Gum	330		330	23.0	13.0	4.0	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7766	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	15.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7767	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	15.0	8.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7768	*Alphitonia excelsa*	Red Ash	150		150	16.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7769	*Alphitonia excelsa*	Red Ash	110		110	16.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7770	*Acacia disparrima*	Hickory Wattle	130		130	15.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7771	*Eucalyptus tereticornis*	Forest Red Gum	240		240	23.0	11.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7772	*Alphitonia excelsa*	Red Ash	120		120	16.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7773	*Acacia disparrima*	Hickory Wattle	130		130	15.0	9.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7774	*Eucalyptus tereticornis*	Forest Red Gum	300		300	23.0	12.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7775	*Melaleuca viminalis*	Weeping Bottlebrush	200		200	16.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7776	*Alphitonia excelsa*	Red Ash	150		150	15.0	10.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7777	*Alphitonia excelsa*	Red Ash	150		150	13.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7778	*Eucalyptus tereticornis*	Forest Red Gum	430		430	22.0	16.0	5.2	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7779	*Lophostemon suaveolens*	Swamp Box	240		240	16.0	8.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7780	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	15.0	9.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7781	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	16.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7782	*Allocasuarina littoralis*	Black Sheoak	150		150	16.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7783	*Allocasuarina littoralis*	Black Sheoak	100	70, 70	141	13.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7784	*Eucalyptus siderophloia*	Grey Ironbark	200		200	20.0	7.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7785	*Allocasuarina littoralis*	Black Sheoak	120		120	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7786	*Corymbia citriodora*	Spotted Gum	320		320	22.0	14.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7787	*Acacia disparrima*	Hickory Wattle	100	100, 80	162	4.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7788	*Corymbia citriodora*	Spotted Gum	270		270	20.0	13.0	3.2	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7789	*Alphitonia excelsa*	Red Ash	220		220	14.0	13.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7790	*Petalostigma pubescens*	Quinine Bush	170		170	3.0	2.0	2.0	1.6	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7791	*Eucalyptus siderophloia*	Grey Ironbark	260		260	20.0	13.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7792	*Acacia leiocalyx*	Early Flowering Black Wattle	100		100	12.0	6.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7793	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	13.0	7.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7794	*Corymbia citriodora*	Spotted Gum	290		290	22.0	11.0	3.5	2.0	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7795	*Corymbia citriodora*	Spotted Gum	280		280	25.0	2.0	3.4	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7796	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	15.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7797	*Acacia leiocalyx*	Early Flowering Black Wattle	110		110	8.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7798	*Eucalyptus siderophloia*	Grey Ironbark	120		120	15.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7799	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	14.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7800	*Eucalyptus tereticornis*	Forest Red Gum	120		120	16.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7801	*Acacia leiocalyx*	Early Flowering Black Wattle	120		120	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7802	*Eucalyptus tereticornis*	Forest Red Gum	190		190	18.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7803	*Corymbia citriodora*	Spotted Gum	270		270	20.0	14.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7804	*Eucalyptus tereticornis*	Forest Red Gum	240		240	20.0	11.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7805	*Alphitonia excelsa*	Red Ash	110		110	6.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7806	*Alphitonia excelsa*	Red Ash	120		120	10.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7807	*Acacia disparrima*	Hickory Wattle	130	120	177	10.0	5.0	2.1	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7808	*Acacia disparrima*	Hickory Wattle	100		100	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7809	*Acacia fimbriata*	Fringed Wattle	120		120	13.0	9.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7810	*Lophostemon suaveolens*	Swamp Box	210		210	16.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7811	*Acacia fimbriata*	Fringed Wattle	110		110	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7812	*Lophostemon suaveolens*	Swamp Box	190	180	262	16.0	8.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7813	*Eucalyptus tereticornis*	Forest Red Gum	120		120	16.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7814	*Acacia disparrima*	Hickory Wattle	200	190, 130	305	14.0	15.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7815	*Eucalyptus tereticornis*	Forest Red Gum	110		110	16.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7816	*Eucalyptus tereticornis*	Forest Red Gum	140		140	16.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7817	*Alphitonia excelsa*	Red Ash	120		120	12.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7818	*Acacia fimbriata*	Fringed Wattle	80	80, 80, 70, 40	160	12.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7819	*Alphitonia excelsa*	Red Ash	100		100	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7820	*Alphitonia excelsa*	Red Ash	100		100	6.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7821	*Alphitonia excelsa*	Red Ash	100		100	6.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7822	*Alphitonia excelsa*	Red Ash	160		160	6.0	7.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7823	*Lophostemon suaveolens*	Swamp Box	110	80, 60	149	15.0	6.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7824	*Lophostemon suaveolens*	Swamp Box	170		170	16.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7825	*Acacia disparrima*	Hickory Wattle	170		170	16.0	7.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7826	*Eucalyptus tereticornis*	Forest Red Gum	170		170	18.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7827	*Acacia disparrima*	Hickory Wattle	200	130, 190	305	15.0	8.0	3.7	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7828	*Alphitonia excelsa*	Red Ash	110		110	12.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7829	*Lophostemon suaveolens*	Swamp Box	200		200	16.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7830	*Lophostemon suaveolens*	Swamp Box	120		120	8.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7831	*Alphitonia excelsa*	Red Ash	110		110	14.0	5.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7832	*Eucalyptus tereticornis*	Forest Red Gum	160		160	16.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for basin works
7833	*Corymbia citriodora*	Spotted Gum	200		200	16.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7834	*Corymbia citriodora*	Spotted Gum	380		380	24.0	14.0	4.6	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7835	*Corymbia citriodora*	Spotted Gum	420		420	20.0	19.0	5.0	2.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7836	*Corymbia citriodora*	Spotted Gum	110		110	15.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7837	*Lophostemon suaveolens*	Swamp Box	270		270	17.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7838	**DEAD/STAG**		540		540	18.0	8.0	6.5	2.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	Small	-	-	-	possum observed	Retain
7839	*Corymbia citriodora*	Spotted Gum	140		140	16.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7840	*Lophostemon suaveolens*	Swamp Box	200	180	269	16.0	9.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7841	*Corymbia citriodora*	Spotted Gum	160		160	18.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7842	*Corymbia citriodora*	Spotted Gum	280		280	24.0	15.0	3.4	1.9	Regular	-	-	Die-back	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7843	*Corymbia citriodora*	Spotted Gum	220		220	16.0	11.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7844	*Lophostemon suaveolens*	Swamp Box	160		160	14.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7845	*Corymbia intermedia*	Pink Bloodwood	190		190	16.0	6.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7846	*Lophostemon suaveolens*	Swamp Box	100	80	128	10.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7847	*Lophostemon suaveolens*	Swamp Box	220		220	15.0	6.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7848	*Lophostemon suaveolens*	Swamp Box	210		210	16.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7849	*Corymbia citriodora*	Spotted Gum	250		250	20.0	10.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7850	*Lophostemon suaveolens*	Swamp Box	190		190	17.0	8.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7851	*Lophostemon suaveolens*	Swamp Box	190		190	16.0	5.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7852	*Lophostemon suaveolens*	Swamp Box	130		130	8.0	3.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7853	*Lophostemon suaveolens*	Swamp Box	100		100	12.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7854	*Corymbia citriodora*	Spotted Gum	180		180	18.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7855	*Corymbia citriodora*	Spotted Gum	200		200	19.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7856	*Alphitonia excelsa*	Red Ash	130		130	15.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7857	*Lophostemon suaveolens*	Swamp Box	140		140	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7858	*Lophostemon suaveolens*	Swamp Box	110		110	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7859	*Corymbia citriodora*	Spotted Gum	260		260	20.0	10.0	3.1	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7860	*Corymbia citriodora*	Spotted Gum	320		320	20.0	12.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7861	*Corymbia citriodora*	Spotted Gum	300		300	17.0	10.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7862	*Corymbia citriodora*	Spotted Gum	230		230	20.0	19.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7863	*Alphitonia excelsa*	Red Ash	130		130	13.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7864	*Eucalyptus tereticornis*	Forest Red Gum	140		140	14.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7865	*Acacia leiocalyx*	Early Flowering Black Wattle	130		130	13.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7866	*Alphitonia excelsa*	Red Ash	140		140	11.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7867	*Alphitonia excelsa*	Red Ash	130		130	12.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7868	*Acacia leiocalyx*	Early Flowering Black Wattle	140		140	13.0	10.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7869	*Lophostemon suaveolens*	Swamp Box	240		240	16.0	10.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7870	*Lophostemon suaveolens*	Swamp Box	260	250	361	18.0	15.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7871	*Corymbia citriodora*	Spotted Gum	160		160	16.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7872	*Corymbia citriodora*	Spotted Gum	110		110	17.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7873	*Lophostemon suaveolens*	Swamp Box	350		350	18.0	17.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7874	*Melaleuca quinquenervia*	Broad-leaved Paperbark	140		140	15.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7875	*Melaleuca quinquenervia*	Broad-leaved Paperbark	130		130	9.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7876	*Melaleuca quinquenervia*	Broad-leaved Paperbark	180	110	211	13.0	5.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7877	*Lophostemon suaveolens*	Swamp Box	140		140	13.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7878	*Lophostemon suaveolens*	Swamp Box	140	130	191	14.0	6.0	2.3	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7879	*Acacia disparrima*	Hickory Wattle	240		240	15.0	8.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7880	*Lophostemon suaveolens*	Swamp Box	130		130	15.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7881	*Eucalyptus tereticornis*	Forest Red Gum	270		270	20.0	17.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7882	*Corymbia citriodora*	Spotted Gum	170		170	20.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7883	*Acacia disparrima*	Hickory Wattle	180		180	10.0	9.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7884	*Melaleuca quinquenervia*	Broad-leaved Paperbark	180		180	15.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7885	*Melaleuca quinquenervia*	Broad-leaved Paperbark	210		210	13.0	7.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7886	*Melaleuca quinquenervia*	Broad-leaved Paperbark	270		270	17.0	10.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7887	*Melaleuca quinquenervia*	Broad-leaved Paperbark	190		190	16.0	15.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7888	*Eucalyptus tereticornis*	Forest Red Gum	200		200	18.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7889	*Melaleuca quinquenervia*	Broad-leaved Paperbark	160		160	17.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7890	*Lophostemon suaveolens*	Swamp Box	110		110	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7891	*Melaleuca quinquenervia*	Broad-leaved Paperbark	160		160	15.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7892	*Acacia disparrima*	Hickory Wattle	200		200	16.0	5.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7893	*Alphitonia excelsa*	Red Ash	140		140	16.0	6.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7894	*Melaleuca quinquenervia*	Broad-leaved Paperbark	140		140	14.0	5.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7895	*Corymbia citriodora*	Spotted Gum	130		130	12.0	14.0	2.0	1.4	Regular	-	-	-	-	-	Typical	Major	-	-	-	Typical	-	-	-	-	-	-		Retain
7896	*Eucalyptus tereticornis*	Forest Red Gum	110		110	14.0	4.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7897	*Acacia disparrima*	Hickory Wattle	190		190	14.0	9.0	2.3	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7898	*Corymbia citriodora*	Spotted Gum	150		150	16.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7899	*Acacia disparrima*	Hickory Wattle	160		160	16.0	9.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7900	*Eucalyptus tereticornis*	Forest Red Gum	160		160	16.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7901	*Eucalyptus tereticornis*	Forest Red Gum	300		300	20.0	14.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7902	*Eucalyptus tereticornis*	Forest Red Gum	250		250	20.0	13.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7903	*Lophostemon suaveolens*	Swamp Box	130	80	153	12.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7904	*Corymbia citriodora*	Spotted Gum	170		170	14.0	8.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7905	*Lophostemon suaveolens*	Swamp Box	130		130	13.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7906	*Corymbia citriodora*	Spotted Gum	110		110	16.0	3.0	2.0	1.3	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7907	*Corymbia citriodora*	Spotted Gum	220		220	22.0	18.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7908	*Lophostemon suaveolens*	Swamp Box	130		130	15.0	4.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7909	*Alphitonia excelsa*	Red Ash	150		150	17.0	5.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7910	*Corymbia intermedia*	Pink Bloodwood	180		180	16.0	6.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7911	*Alphitonia excelsa*	Red Ash	140		140	17.0	7.0	2.0	1.4	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7912	*Lophostemon suaveolens*	Swamp Box	270		270	19.0	7.0	3.2	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7913	*Corymbia citriodora*	Spotted Gum	360		360	22.0	15.0	4.3	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7914	*Lophostemon suaveolens*	Swamp Box	170		170	14.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7915	*Lophostemon suaveolens*	Swamp Box	200		200	18.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7916	*Lophostemon suaveolens*	Swamp Box	170		170	15.0	5.0	2.0	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain

Specimen Details										Canopy Condition Details							Trunk Condition Details					Fauna Details and Habitat Value								
Tree ID	Botanical Name	Common Name	Trunk DBH (mm)	Additional Trunks DBH (mm)	Total DBH (mm) [AS 4970-2009]	Height (m)	Spread (m)	Tree Protection Zone (m)	Structural Root Zone (m)	Canopy Form	Spreading	Thinning	Die-Back	Epicormic Growth	Lopped	Canopy Health	Leaning	Vines	Trunk Damage	Fire Damage	Trunk Health	Scats	Scratches	Hollows	Nest	Termite Nest	Habitat Value	Additional Notes	Retention Status
7917	*Lophostemon suaveolens*	Swamp Box	180		180	16.0	8.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7918	*Acacia disparrima*	Hickory Wattle	240		240	18.0	15.0	2.9	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7919	*Melaleuca quinquenervia*	Broad-leaved Paperbark	160		160	13.0	4.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7920	*Angophora subvelutina*	Broadleaf Apple	320		320	22.0	12.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7921	*Angophora subvelutina*	Broadleaf Apple	180		180	18.0	8.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7922	*Angophora subvelutina*	Broadleaf Apple	250		250	18.0	9.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7923	*Angophora subvelutina*	Broadleaf Apple	250		250	18.0	7.0	3.0	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7924	*Angophora subvelutina*	Broadleaf Apple	280		280	18.0	7.0	3.4	1.9	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7925	*Eucalyptus tereticornis*	Forest Red Gum	350		350	22.0	11.0	4.2	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7926	*Acacia disparrima*	Hickory Wattle	150		150	14.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7927	*Angophora subvelutina*	Broadleaf Apple	150		150	18.0	8.0	2.0	1.5	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7928	*Eucalyptus tereticornis*	Forest Red Gum	220		220	22.0	12.0	2.6	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7929	*Corymbia citriodora*	Spotted Gum	200		200	22.0	8.0	2.4	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7930	*Angophora subvelutina*	Broadleaf Apple	280	280	396	22.0	12.0	4.8	2.2	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7931	*Eucalyptus tereticornis*	Forest Red Gum	300		300	24.0	12.0	3.6	2.0	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7932	*Acacia disparrima*	Hickory Wattle	210		210	14.0	8.0	2.5	1.7	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove for trunk sewer
7933	*Corymbia intermedia*	Pink Bloodwood	340		340	24.0	12.0	4.1	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7934	*Eucalyptus tereticornis*	Forest Red Gum	320		320	26.0	12.0	3.8	2.1	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Retain
7935	*Acacia disparrima*	Hickory Wattle	230		230	14.0	7.0	2.8	1.8	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
7936	*Acacia disparrima*	Hickory Wattle	180		180	12.0	8.0	2.2	1.6	Regular	-	-	-	-	-	Typical	-	-	-	-	Typical	-	-	-	-	-	-		Remove
